


**From:** [Pierard, Kevin, NMENV](#)  
**To:** [Andress, Lane, NMENV](#)  
**Subject:** KAFB timeline  
**Date:** Wednesday, September 16, 2020 10:37:40 AM  
**Attachments:** [ABCWUA.BFF\\_CorrectiveAction\\_Timeline\\_09032020.pdf](#)

KAFB-BFFS  
ST106-SS-111  
DRAFT Timeline from  
ABCWUA  
 **ENTERED**

Attached FYI is the timeline ABCWUA came up with.

Kevin Pierard, Chief  
Hazardous Waste Bureau  
NM Environment Department  
2905 Rodeo Park Drive East, Bldg. 1  
Santa Fe, NM. 87505  
(505) 476-6035  
[kevin.pierard@state.nm.us](mailto:kevin.pierard@state.nm.us)  
<https://www.env.nm.gov/>


KAFB5149



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Notes	2019				2020				2021				2022				2023						
								Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1				
1		<b>RCRA Facility Investigation</b>	<b>1780 days</b>	<b>Wed 8/29/18</b>	<b>Tue 6/24/25</b>																									
2		NMED Review of Phase I RFI Report	536 days	Wed 8/29/18	Wed 9/16/20		NMED response pending																							
3		<b>Source Area Characterization</b>	<b>580 days</b>	<b>Fri 10/25/19</b>	<b>Thu 1/13/22</b>																									
4		Source Area Characterization Report	1 day	Fri 10/25/19	Fri 10/25/19																									
5		NMED Disapproval of Source Area Characterization Report	1 day	Mon 8/17/20	Mon 8/17/20																									
6		Revised Source Area Characterization Report	98 days	Tue 8/18/20	Thu 12/31/20	5																								
7		NMED Review of Revised Source Area Characterization Report	270 days	Fri 1/1/21	Thu 1/13/22	6																								
8		<b>Shallow Soil Vapor</b>	<b>1018 days</b>	<b>Fri 11/8/19</b>	<b>Tue 10/3/23</b>																									
9		Shallow Soil Vapor Work Plan	143 days	Fri 11/8/19	Tue 5/26/20																									
10		NMED Disapproval of Shallow Soil Vapor Work Plan	1 day	Tue 5/26/20	Tue 5/26/20																									
11		Revised Shallow Soil Vapor Work Plan	138 days	Fri 8/14/20	Tue 2/23/21																									
12		NMED Review of Revised Shallow Soil Vapor Work Plan	270 days	Wed 2/24/21	Tue 3/8/22	11																								
13		Drilling and installation of new soil vapor monitoring points	45 days	Wed 3/9/22	Tue 5/10/22	12																								
14		Sampling of new soil vapor monitoring points (8 quarters per permit)	365 days	Wed 5/11/22	Tue 10/3/23	13																								
15		<b>Groundwater Monitoring Data Gaps</b>	<b>511 days</b>	<b>Tue 7/14/20</b>	<b>Tue 6/28/22</b>																									
16		NMED Approval with Mods of Data Gap Groundwater Monitoring Wells Work Plan	1 day	Tue 7/14/20	Tue 7/14/20																									
17		Replacement Pages and Proposed Well Locations - Data Gap Groundwater Monitoring Wells Work Plan	45 days	Wed 7/15/20	Tue 9/15/20	16																								
18		NMED Review of Replacement Pages and Proposed Well Locations	30 days	Wed 9/16/20	Tue 10/27/20	17																								
19		Investigation Report - Summary of Installation and Sampling of Data Gap Groundwater Monitoring Wells	165 days	Wed 10/28/20	Tue 6/15/21	18																								
20		NMED Review of Data Gap Groundwater Monitoring Well Investigation Report	270 days	Wed 6/16/21	Tue 6/28/22	19																								
21		<b>Phase II RFI Report</b>	<b>180 days</b>	<b>Wed 10/4/23</b>	<b>Tue 6/11/24</b>	4,8,15,23																								
22		NMED Review of Phase II RFI Report	270 days	Wed 6/12/24	Tue 6/24/25																									
23		<b>Interim Measures/Pilot Tests</b>	<b>629 days</b>	<b>Tue 1/21/20</b>	<b>Fri 6/17/22</b>																									
24		Work Plan for Phase 4 Sampling EDB In Situ Bioremediation Pilot Test	143 days	Tue 2/18/20	Thu 9/3/20		This document is not available in the admin record																							
25		Revised EBD In Situ Bioremediation Pilot Test Report	399 days	Tue 6/23/20	Fri 12/31/21	24																								
26		NMED Review of Revised EDB In Situ Bioremediation Pilot Test Report	120 days	Mon 1/3/22	Fri 6/17/22	25																								
27		Bioventing Pilot Test Construction Report	163 days	Tue 1/21/20	Thu 9/3/20																									
28		<b>Corrective Measures Evaluation</b>	<b>1247 days</b>	<b>Wed 6/25/25</b>	<b>Thu 4/4/30</b>																									
29		NMED Acceptance of RFI Report and Direction to Submit Corrective Measures Work Plan	1 day	Wed 6/25/25	Wed 6/25/25	22,2																								
30		KAFB Submit Corrective Measures Evaluation Work Plan	90 days	Thu 6/26/25	Wed 10/29/25	29																								
31		NMED Review of CME Work Plan	360 days	Thu 3/5/26	Wed 7/21/27	30																								
32		Corrective Measures Evaluation Report	90 days	Thu 7/22/27	Wed 11/24/27	31																								
33		NMED Review of CME Report	480 days	Thu 3/30/28	Wed 1/30/30	32																								
34		NMED Recommends Remedy(ies)	1 day	Thu 1/31/30	Thu 1/31/30	33																								
35		Public Review and Comment of Selected Final Remedy	45 days	Fri 2/1/30	Thu 4/4/30	34																								
36		<b>Remedy Selection</b>	<b>90 days</b>	<b>Fri 4/5/30</b>	<b>Thu 8/8/30</b>	<b>35</b>																								

Project: BFF\_CorrectiveAction\_Tim Date: Wed 9/16/20

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Critical	Critical
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Critical Split	Critical
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Late	Progress	Late

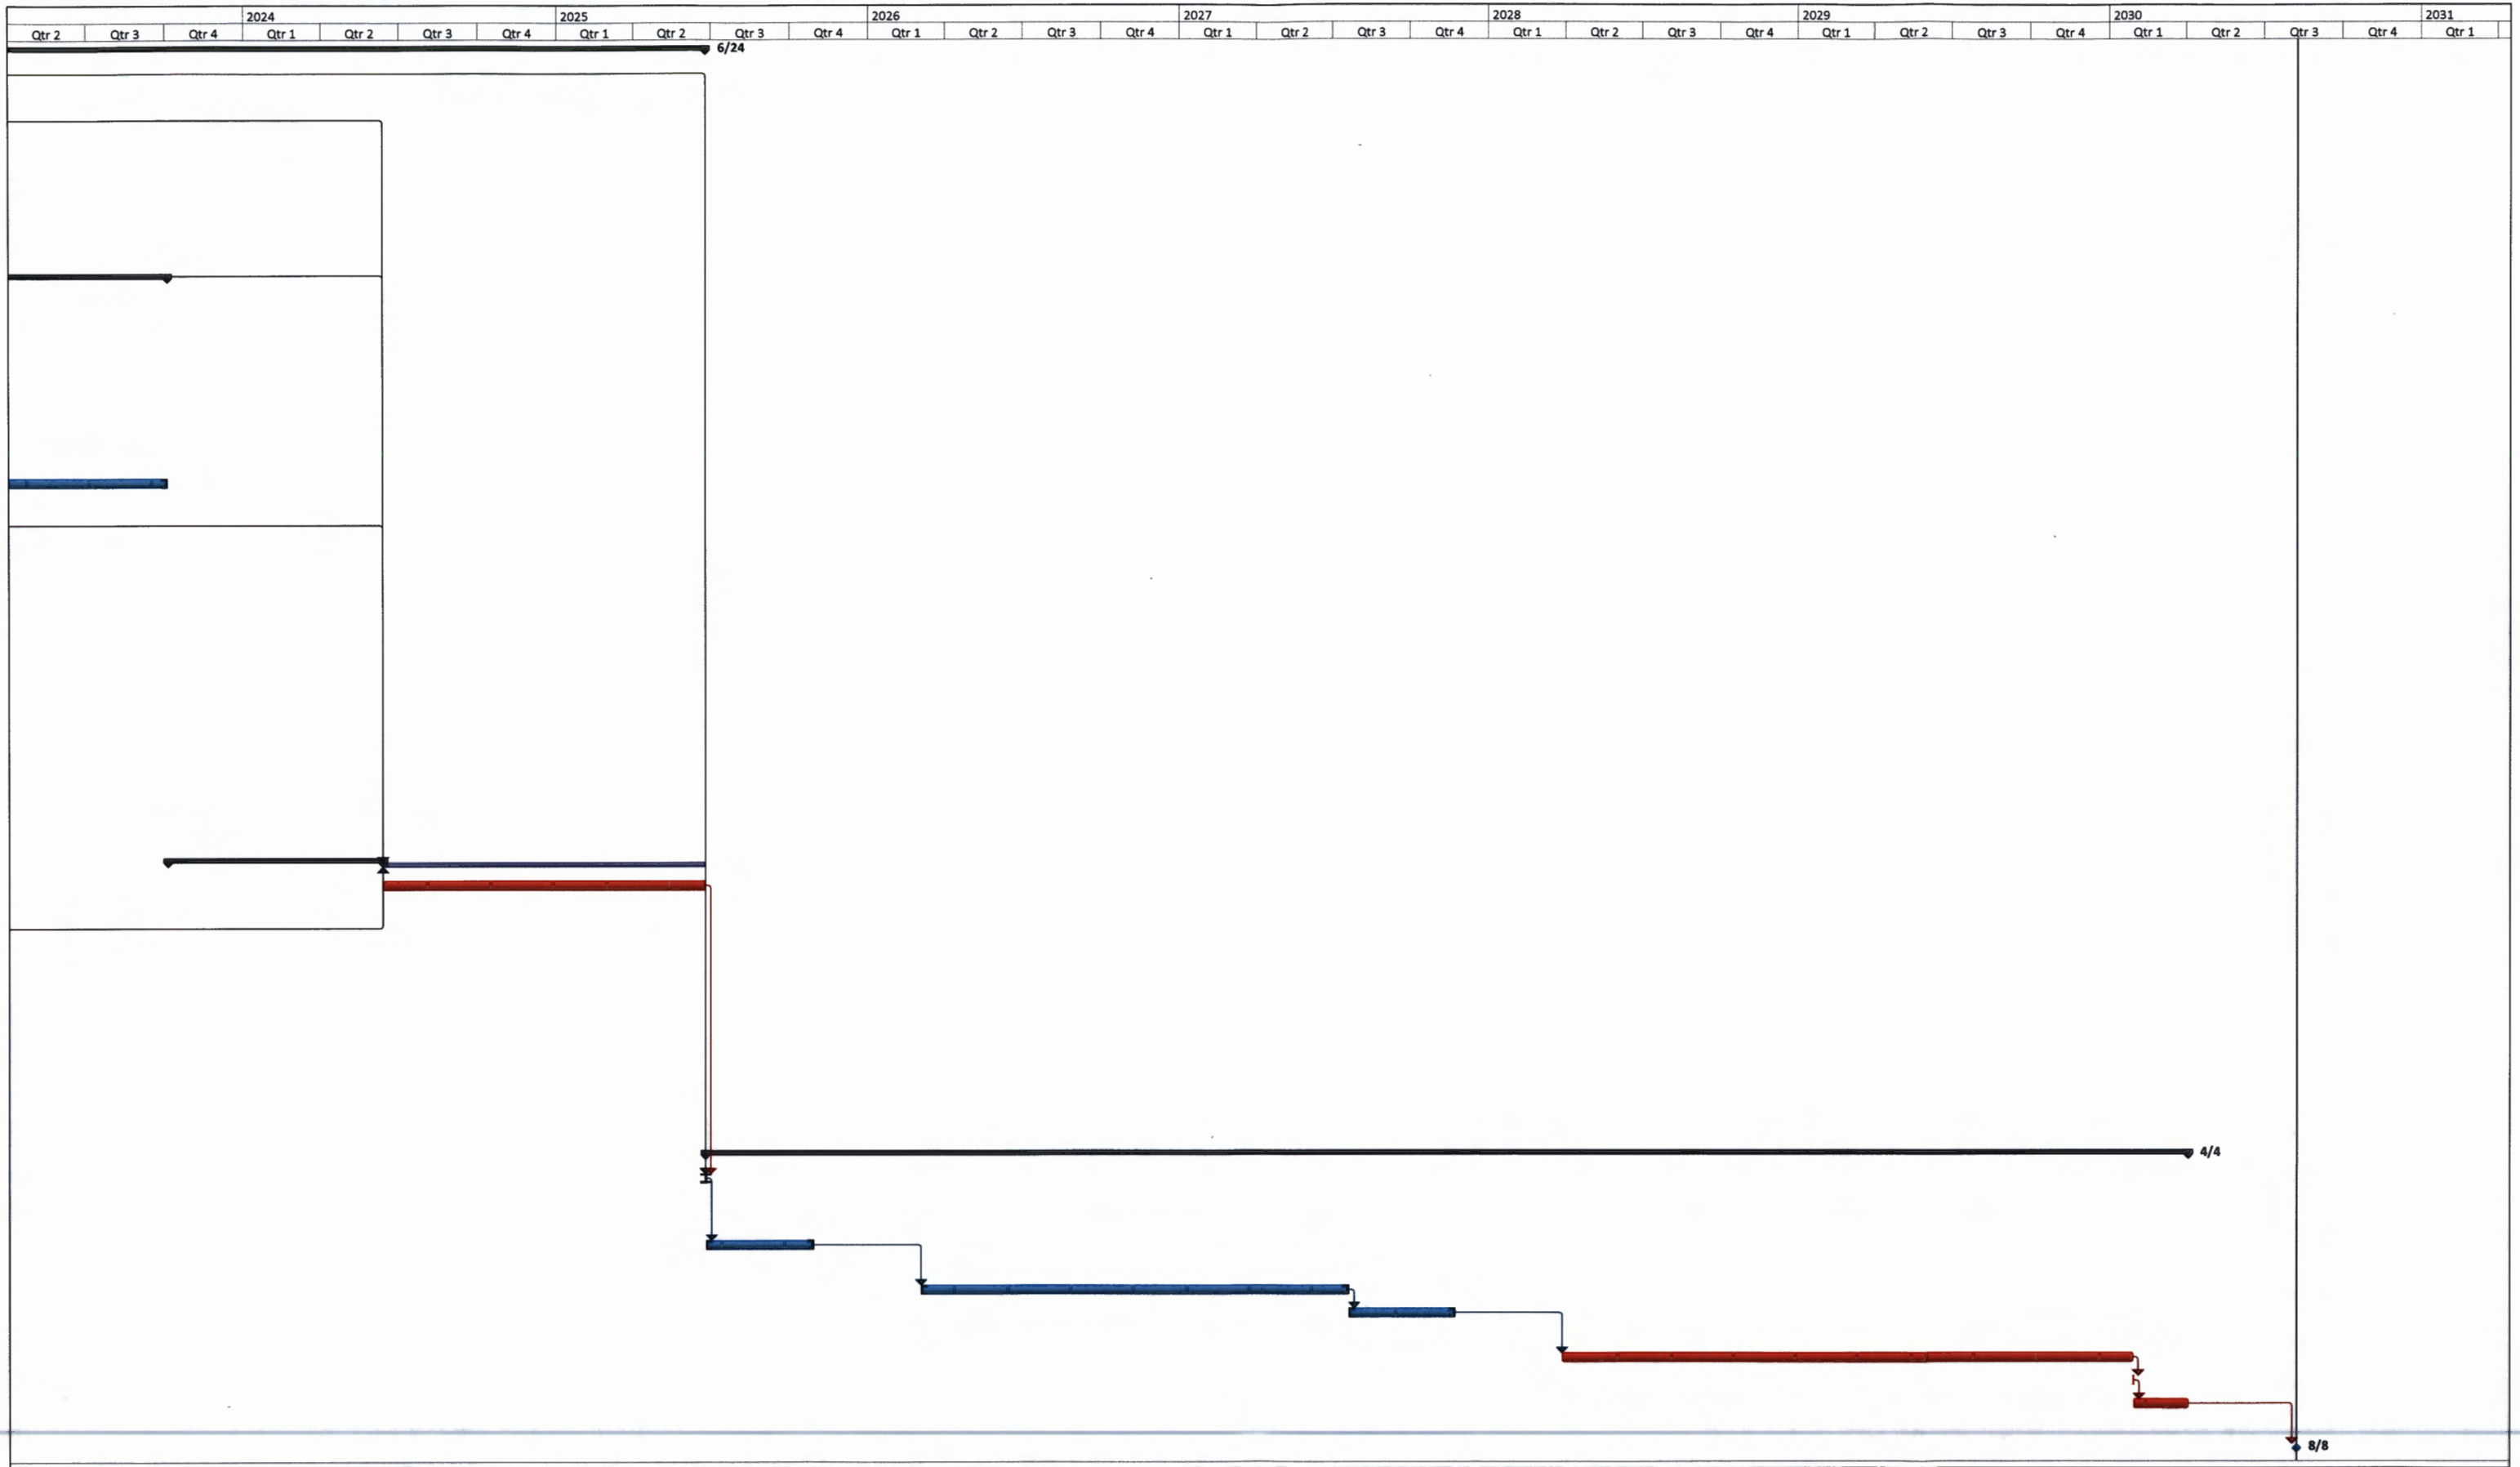

Project: BFF_CorrectiveAction_Tim Date: Wed 9/16/20	Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Critical	Progress
	Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Critical Split	
	Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Late		
