


SEPT 1992

**LIBRARY COPY**



Los Alamos National Laboratory  
**Environmental Restoration**

A Department of Energy environmental cleanup program

**FY 92 UPDATE**

**OPERABLE UNIT  
MILESTONES AND SCHEDULES**

**FOR COMPLIANCE WITH  
HAZARDOUS AND SOLID WASTE AMENDMENTS  
MODULE**



12358


**Los Alamos National Laboratory  
ENVIRONMENTAL RESTORATION PROGRAM  
OPERABLE UNITS (OUs)**

<b>OU</b>	<b>Project Leader</b>	<b>Group</b>	<b>OU</b>	<b>Title</b>
<u>Work plan due to EPA May 1991</u>				
	Gary Eller	INC-DO	1106	TA-21
<u>Eight work plans due to EPA May 1992</u>				
	Jim Aldrich	EES-1	1071	TAs-0, -19, -26, -73, -74
	Ron Conrad	EM-8	1078	TA-1
	(Carl Newton***	EES-3	1078	TA-1)
	Jim Aldrich*	EES-1	1079	TAs-10, -31, -32, -45
	Keith Dowler	CLS-1	1122	TA-33, -70
	Allyn Pratt	EES-3	1129	TAs-4, -5, -35, -42, -48, -52, -55, -63, -66
	Gary Eller	INC-DO	1144	TA-49
	Cheryl Rofer**	EES-1	1147	TA-50
	John Krueger	EM-13	1148	TAs-51, -54
<u>Ten work plans due to EPA May 1993</u>				
	Brad Martin	CLS-DO	1082	TAs-11, -13, -16, -24, -25, -28, -37
	Al Ogard	INC-7	1086	TA-15
	Gene Gould	MEE-4	1093	TAs-18, -27, -65
	Pat Longmire	INC-4	1098	TAs-2, -41
	Cheryl Rofer	EES-1	1111	TAs-6, -7, -22, -40, -58, -62
	Ed Griggs	CLS-DO	1114	TAs-3, -30, -59, -60, -61, -64
	Sharad Kelkar	EES-4	1130	TAs-36, -68, -71
	Gene Gould**	MEE-4	1132	TA-39
	Roy Michelotti	CLS-6	1140	TA-46
	Tracy Glatzmaier	EES-5	1157	TAs-8, -9, -23, 69
<u>Four work plans due to EPA May 1994</u>				
	Calvin Martell**	CLS-1	1085	TAs-12, -14, -67
	Gene Gould**	MEE-4	1100	TAs-20, 53, 72
	Gary Allen**	CLS-7	1136	TA-43
	Sharad Kelkar**	EES-4	1154	TA-57
<u>One work plan due to EPA May 1995</u>				
	TBD	EM-13	1049	Canyons

\*Effective August 1, 1992.

\*\*Effective immediately.

\*\*\*Effective October 1, 1992.

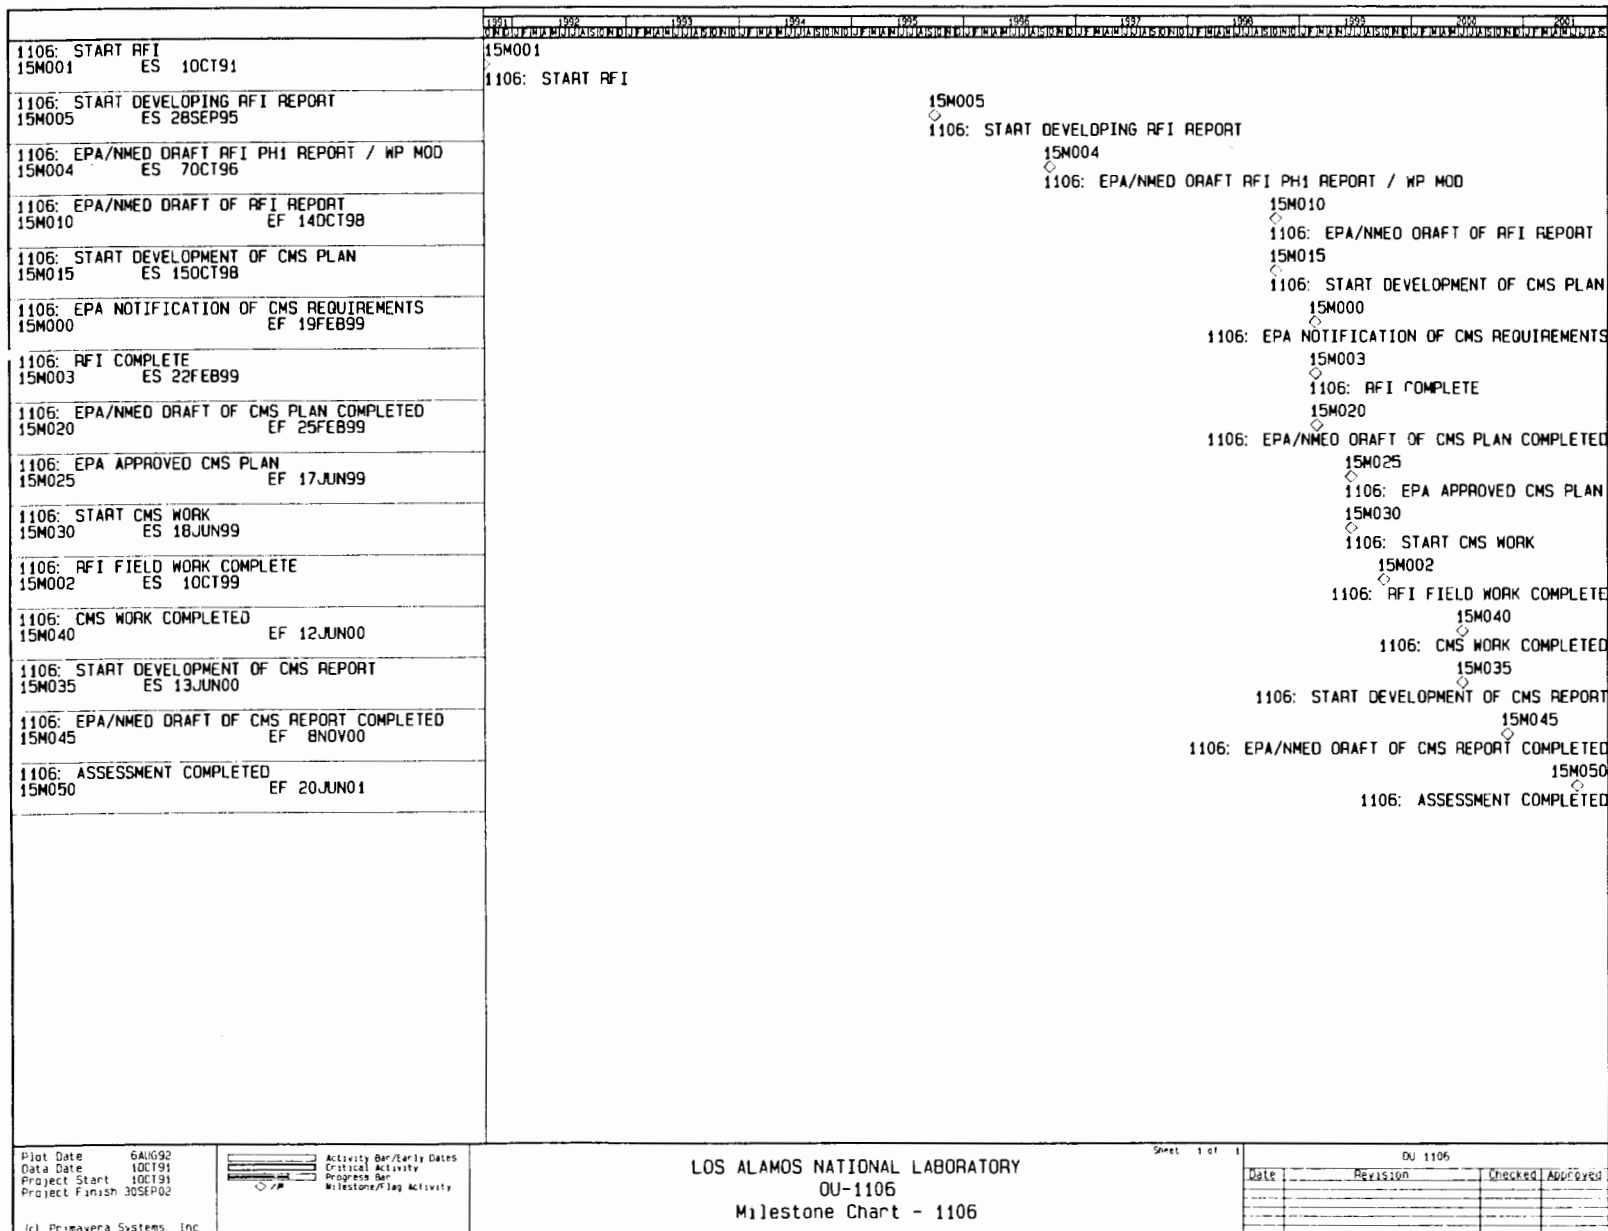

LANL INC-DO G. ELLER  
 REPORT DATE 6AUG92 RUN NO. 134  
 17:43  
 1106 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

ADS 1106: TA-21  
 START DATE 10CT91  
 DATA DATE 10CT91

TBS 2/17/92  
 FIN DATE 30SEP02  
 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
150000	250	250	0	1106: Asmt RFI Manage ADS : FY92	10CT91	30SEP92
150002	250	250	0	1106: Asmt RFI Ph1 Field Work: SQ1 FY92 GCHAR	10CT91	30SEP92
150025	250	250	0	1106: Asmt RFI Ph1 MDA B Pilot: SQ1 FY92 Pilot	10CT91	30SEP92
151305	250	250	0	1106: Cond General Bench/Pilot Studies FY92(LOE)	10CT91	30SEP92
620010	250	250	0	1106: CONDUCT VCA FY-92	10CT91	30SEP92
15M001	0	0	0	1106: START RFI	10CT91	
150165	451	451	0	1106: Asmt RFI Ph1 Field Work : SQ2 12.3 Geomp	2DEC91	20SEP93
150160	43	43	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ2 12.4 Rnd1	11DEC91*	13FEB92
150175	34	34	0	1106: Asmt RFI Ph1 Field Work : SQ2 12.4 Rnd1	14FEB92	2APR92
150060	1	1	0	1106: Asmt RFI Ph1 Field Work : SQ1 12.6 MW 1	2MAR92*	2MAR92
150065	52	52	0	1106: Asmt RFI Ph1 Sample Anal: SQ1 12.6 MW 1	2MAR92	12MAY92
150180	118	118	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 12.4 Rnd1	10MAR92	24AUG92
150185	18	18	0	1106: Asmt RFI Ph1 Field Work : SQ2 13.2 Rnd1	10MAR92	2APR92
150190	118	118	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 13.2 Rnd1	10MAR92	24AUG92
150070	49	49	0	1106: Asmt RFI Ph1 Field Work : SQ1 12.6 MWP 1	2APR92	10JUN92
150075	100	100	0	1106: Asmt RFI Ph1 Sample Anal: SQ1 12.6 MWP 1	2APR92	21AUG92
150200	44	44	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ2 13.2 Rnd2	6APR92*	5JUN92
150745	66	66	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ6 12.5 Vado	11MAY92*	12AUG92
150215	23	23	0	1106: Asmt RFI Ph1 Field Work : SQ2 12.4 Rnd2	1JUN92	1JUL92
150205	30	30	0	1106: Asmt RFI Ph1 Field Work : SQ2 13.2 Rnd2	8JUN92	20JUL92
150220	114	114	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 12.4 Rnd2	8JUN92	18NOV92
150210	139	139	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 13.2 Rnd2	12JUN92	5JAN93
150410	13	13	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.2 Outf	13JUL92	29JUL92
150080	47	47	0	1106: Asmt RFI Ph1 Field Work : SQ1 12.6 MWS 1	14JUL92	17SEP92
150085	98	98	0	1106: Asmt RFI Ph1 Sample Anal: SQ1 12.6 MWS 1	14JUL92	30DEC92
150415	90	90	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.2 Outf	21JUL92	30NOV92
150420	11	11	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.3 Outf	22JUL92	5AUG92
150425	82	82	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.3 Outf	29JUL92	24NOV92
600000	245	245	0	1106: Conduct VCA (LOE)	30JUL92*	23JUL93
150430	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.4 Outf	3AUG92	10AUG92

TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 1OCT91 PAGE NO. 2

DATA DATE 1OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
150435	64	64	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.4 Outf	5AUG92	4NOV92
150450	7	7	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.6 Outf	6AUG92	14AUG92
150440	4	4	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.5 Outf	7AUG92	12AUG92
150445	71	71	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.5 Outf	10AUG92	19NOV92
150455	71	71	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.6 Outf	11AUG92	20NOV92
150470	7	7	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.8 Outf	12AUG92	20AUG92
150460	3	3	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.7 Outf	13AUG92	17AUG92
150750	24	24	0	1106: Asmt RFI Ph1 Field Work : SQ6 12.5 DP-3	13AUG92	16SEP92
150465	54	54	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.7 Outf	14AUG92	30OCT92
150475	75	75	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.8 Outf	17AUG92	4DEC92
150480	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ2 15.9 Outf	17AUG92	24AUG92
150751	120	120	0	1106: Asmt RFI PH1 Sample Anal: SQ6 12.5 DP-3	19AUG92	16FEB93
150485	72	72	0	1106: Asmt RFI Ph1 Sample Anal: SQ2 15.9 Outf	20AUG92	4DEC92
150195	44	44	0	1106: Asmt RFI Ph1 Data Assmt : SQ2 Seq2 Rnd1	25AUG92	27OCT92
150755	36	36	0	1106: Asmt RFI Ph1 Field Work : SQ6 12.5 DP-4	28AUG92	20OCT92
150756	118	118	0	1106: Asmt RFI PH1 Sample Anal: SQ6 12.5 DP-4	3SEP92	1MAR93
150775	19	19	0	1106: Asmt RFI Ph1 Field Work : SQ6 12.5 V-DP	24SEP92	21OCT92
150776	39	39	0	1106: Asmt RFI PH1 Sample Anal: SQ7 12.5 V-DP	24SEP92	19NOV92
150005	249	249	0	1106: Asmt RFI Manage ADS : FY93	1OCT92	30SEP93
150007	249	249	0	1106: Asmt RFI PH1 Field Work: SQ1 FY93 GCHAR	1OCT92	30SEP93
150030	249	249	0	1106: Asmt RFI Ph1 MDA B Pilot: SQ1 FY93 Pilot	1OCT92	30SEP93
151310	249	249	0	1106: Cond General Bench/Pilot Studies FY93(LOE)	1OCT92	30SEP93
620015	249	249	0	1106: CONDUCT VCA FY-93	1OCT92	30SEP93
150170	44	44	0	1106: Asmt RFI Ph1 Data Assmt : SQ2 12.3 Geomp	6OCT92	10DEC92
150090	2	2	0	1106: Asmt RFI Ph2 Field Work : SQ1 12.6 QWF 2	5NOV92	6NOV92
150095	52	52	0	1106: Asmt RFI Ph2 Sample Anal: SQ1 12.6 QWF 2	5NOV92	26JAN93
150500	43	43	0	1106: Asmt RFI Ph1 Data Assmt : SQ2 Surf Assmt	7DEC92	9FEB93
150245	44	44	0	1106: Asmt RFI Ph1 Data Assmt : SQ2 Seq2 Rnd2	6JAN93	10MAR93
150100	2	2	0	1106: Asmt RFI Ph2 Field Work : SQ1 12.6 QWW 2	3FEB93	4FEB93
150105	53	53	0	1106: Asmt RFI Ph2 Sample Anal: SQ1 12.6 QWW 2	3FEB93	19APR93

TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10OCT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
150795	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ6 12.5 Vado	2MAR93	30APR93
150110	2	2	0	1106: Asmt RFI Ph2 Field Work : SQ1 12.6 QWP 2	6MAY93	7MAY93
150250	121	121	0	1106: Asmt RFI Ph1 Tech Memo : SQ2 Seq2 All	8JUL93*	4JAN94
150115	53	53	0	1106: Asmt RFI Ph2 Sample Anal: SQ1 12.6 QWP 2	8SEP93*	23NOV93
150010	250	250	0	1106: Asmt RFI Manage ADS : FY94	1OCT93	3OCT94
150012	250	250	0	1106: Asmt RFI PH1 Field Work: SQ1 FY94 GCHAR	1OCT93	3OCT94
150035	250	250	0	1106: Asmt RFI Ph1 MDA B Pilot: SQ1 FY94 Pilot	1OCT93	3OCT94
150120	2	2	0	1106: Asmt RFI Ph2 Field Work : SQ1 12.6 QWS 2	1OCT93*	4OCT93
150125	53	53	0	1106: Asmt RFI Ph2 Sample Anal: SQ1 12.6 QWS 2	1OCT93*	20DEC93
150800	20	20	0	1106: Asmt RFI Ph1 Field Work : SQ6 16.7 Subs	1OCT93*	29OCT93
150805	121	121	0	1106: Asmt RFI Ph1 Sample Anal: SQ6 16.7 Subs	1OCT93	31MAR94
151315	250	250	0	1106: Cond General Bench/Pilot Studies FY94(LOE)	1OCT93	3OCT94
600019	250	250	0	1106: Conduct VCA (LOE)	1OCT93*	3OCT94
620020	250	250	0	1106: CONDUCT VCA FY-94	1OCT93	3OCT94
150171	44	44	0	1106: Asmt RFI PH1 Data Assmt: SQ2 12.3 Geomp	5OCT93	9DEC93
150130	193	193	0	1106: Asmt RFI Ph3 Field Work : SQ1 12.6 YW3 3	12JAN94	17OCT94
150135	245	245	0	1106: Asmt RFI Ph3 Sample Anal: SQ1 12.6 YW3 3	12JAN94	5JAN95
150820	66	66	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ7 Mda Init	1MAR94*	1JUN94
150255	45	45	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ3 Mob	1APR94*	3JUN94
150810	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ6 16.7 Subs	1APR94	2JUN94
150760	17	17	0	1106: Asmt RFI Ph1 Field Work : SQ7 12.5 DP-1	2JUN94	24JUN94
150761	126	126	0	1106: Asmt RFI PH1 Sample Anal: Sq7 12.5 DP-1	2JUN94	2DEC94
150815	121	121	0	1106: Asmt RFI Ph1 Tech Memo: SQ6 Seq5 All	3JUN94*	28NOV94
150225	16	16	0	1106: Asmt RFI Ph1 Field Work : SQ3 16.1 Surf	6JUN94	27JUN94
150230	85	85	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.1 Surf	9JUN94	7OCT94
150765	17	17	0	1106: Asmt RFI Ph1 Field Work : SQ7 12.5 DP-2	15JUN94	8JUL94
150766	126	126	0	1106: Asmt RFI Ph1 Sample Anal: SQ7 12.5 DP-2	15JUN94	15DEC94
150490	5	5	0	1106: Asmt RFI Ph1 Field Work : SQ3 15.10 Outf	17JUN94	23JUN94
150495	62	62	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 15.10 Outf	21JUN94	16SEP94
150260	30	30	0	1106: Asmt RFI Ph1 Field Work: SQ3 12.6 Well	23JUN94	4AUG94

LANL INC-DO G. ELLER

FINEST HOUR

ADS 1106: TA-21

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 134

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 30SEP02

17:43

1106 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
150265	96	96	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 12.6 Well	23JUN94	8NOV94
150770	17	17	0	1106: Asmt RFI Ph1 Field Work : SQ7 12.5 DP-5	28JUN94	21JUL94
150771	126	126	0	1106: Asmt RFI PH1 Sample Anal: SQ7 12.5 DP-5	28JUN94	30DEC94
150270	8	8	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.4 Surf	11JUL94	20JUL94
150780	17	17	0	1106: Asmt RFI Ph1 Field Work : SQ7 12.5 U-DP	12JUL94	3AUG94
150781	48	48	0	1106: Asmt RFI PH1 Sample Anal: Sq7 12.5 U-DP	12JUL94	16SEP94
150275	74	74	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.4 Surf	13JUL94	26OCT94
150280	8	8	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.5 Surf	15JUL94	26JUL94
150290	3	3	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.7 Surf	18JUL94	20JUL94
150295	9	9	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.8 Surf	19JUL94	29JUL94
150285	76	76	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.5 Surf	20JUL94	4NOV94
150305	10	10	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.6 Surf	22JUL94	4AUG94
150785	17	17	0	1106: Asmt RFI Ph1 Field Work : SQ7 12.5 T-DP	25JUL94	16AUG94
150790	39	39	0	1106: Asmt RFI Ph1 Sample Anal: SQ7 12.5 Vado	25JUL94	16SEP94
150300	70	70	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.8 Surf	26JUL94	2NOV94
150315	11	11	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.2 Surf	28JUL94	11AUG94
150310	72	72	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.6 Surf	1AUG94	10NOV94
150325	10	10	0	1106: Asmt RFI Ph1 Field Work: SQ3 16.3 Surf	4AUG94	17AUG94
150320	78	78	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.2 Surf	5AUG94	29NOV94
150825	24	24	0	1106: Asmt RFI Ph1 Field Work : SQ7 16.3 Ssurf	5AUG94	8SEP94
150830	134	134	0	1106: Asmt RFI Ph1 Sample Anal: SQ7 16.3 Ssurf	5AUG94	22FEB95
150330	72	72	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 16.3 Surf	12AUG94	28NOV94
150340	7	7	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.2 Surf	15AUG94	23AUG94
150345	70	70	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.2 Surf	18AUG94	30NOV94
150350	5	5	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.3 Surf	22AUG94	26AUG94
150390	41	41	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.7 Surf	22AUG94	19OCT94
150355	68	68	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.3 Surf	24AUG94	2DEC94
150360	3	3	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.4 Surf	25AUG94	29AUG94
150370	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.5 Surf	25AUG94	1SEP94
150365	54	54	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.4 Surf	26AUG94	14NOV94

LANL INC-DO G. ELLER

FINEST HOUR

ADS 1106: TA-21

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 134

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 30SEP92

17:43

1106 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
150375	73	73	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.5 Surf	29AUG94	14DEC94
150380	4	4	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.6 Surf	31AUG94	6SEP94
150385	54	54	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.6 Surf	2SEP94	21NOV94
150395	108	108	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.7 Surf	6SEP94	14FEB95
150840	12	12	0	1106: Asmt RFI Ph1 Field Work : SQ7 16.6 Ssurf	8SEP94	23SEP94
150845	92	92	0	1106: Asmt RFI Ph1 Sample Anal: SQ7 16.6 Ssurf	8SEP94	25JAN95
151010	247	247	0	1106: Assmt - Conduct VCA (LOE)	30CT94*	28SEP95
150015	247	247	0	1106: Asmt RFI Manage ADS : FY95	4OCT94	29SEP95
150017	247	247	0	1106: Asmt RFI PH1 Field Work: SQ1 FY95 GCHAR	4OCT94	29SEP95
150040	247	247	0	1106: Asmt RFI Ph2 MDA B Pilot: SQ1 FY95 Pilot	4OCT94	29SEP95
151320	247	247	0	1106: Cond General Bench/Pilot Studies FY95(LOE)	4OCT94	29SEP95
620025	247	247	0	1106: CONDUCT VCA FY-95	4OCT94	29SEP95
150400	10	10	0	1106: Asmt RFI Ph1 Field Work : SQ3 14.8 Surf	5OCT94	19OCT94
150405	77	77	0	1106: Asmt RFI Ph1 Sample Anal: SQ3 14.8 Surf	7OCT94	2FEB95
150335	43	43	0	1106: Asmt RFI Ph1 Data Assmt: SQ3 MDA Assmt	30NOV94	2FEB95
150794	44	44	0	1106: Asmt RFI PH1 Data Assmt: Sq7 12.5 VADOS	3JAN95	7MAR95
150140	194	194	0	1106: Asmt RFI Ph3 Field Work : SQ1 12.6 YW4 3	9JAN95	13OCT95
150145	246	246	0	1106: Asmt RFI Ph3 Sample Anal: SQ1 12.6 YW4 3	9JAN95	3JAN96
150850	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ7 16.6 Ssurf	26JAN95	29MAR95
150336	44	44	0	1106: Asmt RFI PH1 Data Assmt: SQ3 Surf Assmt	15FEB95	18APR95
150835	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ7 16.3 Ssurf	23FEB95	25APR95
150859	66	66	0	1106: Asmt RFI PH1 Con/Mob/Dem: Sq8 MDA INIT	1MAR95*	1JUN95
150504	44	44	0	1106: Asmt RFI Ph1 Con/Mob/Dem: SQ4 Seq4 Mob	3APR95*	2JUN95
150337	121	121	0	1106: Asmt RFI PH1 Tech Memo: SQ3 Seq T-Memo	19APR95	10OCT95
150855	121	121	0	1106: Asmt RFI Ph1 Tech Memo: SQ7 Mdaut Init	26APR95	17OCT95
150860	35	35	0	1106: Asmt RFI Ph1 Field Work : SQ8 16.2 Ssurf	2JUN95	21JUL95
150865	172	172	0	1106: Asmt RFI Ph1 Sample Anal: SQ8 16.2 Ssurf	2JUN95	12FEB96
150505	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ4 17.2 Subu	5JUN95	12JUN95
150515	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ4 17.3 Subu	7JUN95	14JUN95
150510	67	67	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 17.2 Subu	8JUN95	12SEP95



TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 1OCT91 PAGE NO. 6

DATA DATE 10OCT91 PAGE NO. 6

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
150520	68	68	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 17.3 Subu	9JUN95	14SEP95
150525	7	7	0	1106: Asmt RFI Ph1 Field Work : SQ4 17.4 Subu	12JUN95	20JUN95
150530	73	73	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 17.4 Subu	14JUN95	26SEP95
150535	7	7	0	1106: Asmt RFI Ph1 Field Work : SQ4 17.5 Subu	19JUN95	27JUN95
150555	20	20	0	1106: Asmt RFI Ph1 Field Work : SQ4 18.8 D&D	19JUN95	17JUL95
150540	76	76	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 17.5 Subu	20JUN95	5OCT95
150560	96	96	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 18.8 D&D	21JUN95	6NOV95
150545	4	4	0	1106: Asmt RFI Ph1 Field Work : SQ4 17.6 Subu	23JUN95	28JUN95
150550	65	65	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 17.6 Subu	27JUN95	27SEP95
150565	6	6	0	1106: Asmt RFI Ph1 Field Work : SQ4 18.9 D&D	17JUL95	24JUL95
150570	75	75	0	1106: Asmt RFI Ph1 Sample Anal: SQ4 18.9 D&D	17JUL95	31OCT95
150880	23	23	0	1106: Asmt RFI Ph1 Field Work : SQ8 16.8 Ssurf	21JUL95	22AUG95
150885	131	131	0	1106: Asmt RFI Ph1 Sample Anal: SQ8 16.8 Ssurf	21JUL95	1FEB96
15M005	0	0	0	1106: START DEVELOPING RFI REPORT	28SEP95*	
150020	249	249	0	1106: Asmt RFI Manage ADS : FY96	2OCT95	30SEP96
150022	249	249	0	1106: Asmt RFI PH1 Field Work: SQ1 FY96 GCHAR	2OCT95	30SEP96
150045	249	249	0	1106: Asmt RFI Ph2 MDA B Pilot: SQ1 FY96 Pilot	2OCT95	30SEP96
151325	249	249	0	1106: Cond General Bench/Pilot Studies FY96(LOE)	2OCT95	30SEP96
620030	249	249	0	1106: CONDUCT VCA FY-96	2OCT95	30SEP96
150575	44	44	0	1106: Asmt RFI Ph1 Data Assmt : SQ4 Subsf Asmt	7NOV95	16JAN96
150895	66	66	0	1106: Asmt RFI Ph2 Con/Mob/Dem: SQ9 Mda Subs 2	11DEC95*	18MAR96
150150	199	199	0	1106: Asmt RFI Ph3 Field Work : SQ1 12.6 YW5 3	3JAN96	15OCT96
150155	251	251	0	1106: Asmt RFI Ph3 Sample Anal: SQ1 12.6 YW5 3	3JAN96	3JAN97
150580	121	121	0	1106: Asmt RFI Ph1 Tech Memo : SQ4 Seq T-Memo	17JAN96	8JUL96
150890	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ8 16.8 Ssurf	2FEB96	4APR96
150870	44	44	0	1106: Asmt RFI Ph1 Data Assmt: SQ8 16.2 Ssurf	13FEB96	15APR96
151005	245	245	0	1106: Develop NEPA Documentation for RFI Report	6MAR96*	27FEB97
150930	85	85	0	1106: Asmt RFI Ph2 Field Work : SQ10 16.3 Subsf	19MAR96	17JUL96
150935	200	200	0	1106: Asmt RFI Ph2 Sample Anal: SQ10 16.3 Subsf	19MAR96	6JAN97
150590	44	44	0	1106: Asmt RFI Ph2 Con/Mob/Dem: SQ5 13.2 Filt	1APR96*	31MAY96

TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10OCT91 PAGE NO. 7

DATA DATE 10OCT91 PAGE NO. 7

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
150875	121	121	0	1106: Asmt RFI Ph1 Tech Memo: SQ8 Mdaab Init	16APR96	4OCT96
150595	9	9	0	1106: Asmt RFI Ph2 Field Work : SQ5 13.2 Filt	3JUN96	13JUN96
150600	92	92	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 13.2 Filt	3JUN96	10OCT96
150605	6	6	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.4 Surf	14JUN96	21JUN96
150610	74	74	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.4 Surf	14JUN96	27SEP96
150615	6	6	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.5 Surf	21JUN96	28JUN96
150620	74	74	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.5 Surf	21JUN96	4OCT96
150625	5	5	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.7 Surf	25JUN96	1JUL96
150635	5	5	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.8 Surf	27JUN96	3JUL96
150630	61	61	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.7 Surf	28JUN96	24SEP96
150645	5	5	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.6 Surf	1JUL96	8JUL96
150640	61	61	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.8 Surf	2JUL96	26SEP96
150655	5	5	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.2 Surf	3JUL96	10JUL96
150650	61	61	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.6 Surf	5JUL96	30SEP96
150665	6	6	0	1106: Asmt RFI Ph2 Field Work : SQ5 16.3 Surf	8JUL96	15JUL96
150660	62	62	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.2 Surf	9JUL96	30OCT96
150670	65	65	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 16.3 Surf	11JUL96	10OCT96
150675	3	3	0	1106: Asmt RFI Ph2 Field Work : SQ5 14.2 Surf	16JUL96	18JUL96
150680	68	68	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 14.2 Surf	16JUL96	21OCT96
150685	3	3	0	1106: Asmt RFI Ph2 Field Work : SQ5 14.6 Surf	18JUL96	22JUL96
150690	66	66	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 14.6 Surf	18JUL96	21OCT96
150695	4	4	0	1106: Asmt RFI Ph2 Field Work : SQ5 14.7 Surf	22JUL96	25JUL96
150700	69	69	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 14.7 Surf	22JUL96	28OCT96
150705	11	11	0	1106: Asmt RFI Ph2 Field Work : SQ5 17.2 Subu	25JUL96	8AUG96
150710	86	86	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 17.2 Subu	25JUL96	26NOV96
150715	3	3	0	1106: Asmt RFI Ph2 Field Work : SQ5 17.3 Subu	8AUG96	12AUG96
150720	67	67	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 17.3 Subu	8AUG96	13NOV96
150725	20	20	0	1106: Asmt RFI Ph2 Field Work : SQ5 17.5 Subu	12AUG96	9SEP96
150730	99	99	0	1106: Asmt RFI Ph2 Sample Anal: SQ5 17.5 Subu	12AUG96	7JAN97
150021	249	249	0	1106: Asmt RFI Manage ADS: FY97	1OCT96	30SEP97

-----

LANL	INC-DO	G. ELLER	FINEST HOUR	ADS 1106: TA-21	TBS 2/17/92
REPORT DATE	6AUG92	RUN NO. 134	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 30SEP02
	17:43				
1106 SCHEDULE REPORT BY	EARLY START			DATA DATE 10CT91	PAGE NO. 8

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
150027	249	249	0	1106: Asmt RFI PH1 Field Work: SQ1 FY97 GCHAR	10CT96	30SEP97
150046	249	249	0	1106: Asmt RFI Ph2 MDA B Pilot: SQ1 FY97 Pilot	10CT96	30SEP97
620035	249	249	0	1106: CONDUCT VCA FY-97	10CT96	30SEP97
15H004	0	0	0	1106: EPA/NMED DRAFT RFI PH1 REPORT / WP MOD	70CT96	
150156	199	199	0	1106: Asmt RFI PH3 Field Work: SQ1 12.6 YW5 3	27DEC96	90CT97
150157	250	250	0	1106: Asmt RFI PH3 Sample Anal:SQ1 12.6 YW5 3	27DEC96	29DEC97
150940	66	66	0	1106: Asmt RFI Ph2 Data Assmt: SQ10 16.3 Subsf	7JAN97	10APR97
150735	44	44	0	1106: Asmt RFI Ph2 Data Assmt: SQ5 Surf Subsq	8JAN97	12MAR97
151065	110	110	0	1106: Conduct RFI Report Investigation Analysis	28FEB97	4AUG97
150965	66	66	0	1106: Asmt RFI Ph2 Con/Mob/Dem: SQ10 SW MDA MOB	3MAR97*	3JUN97
150740	121	121	0	1106: Asmt RFI Ph2 Tech Memo: SQ5 Surf Subsq	13MAR97	2SEP97
150945	121	121	0	1106: Asmt RFI Ph2 Tech Memo: SQ10 LW MDA 2	11APR97	10CT97
150915	41	41	0	1106: Asmt RFI Ph2 Field Work : SQ10 16.7 Subsf	4JUN97	31JUL97
150920	185	185	0	1106: Asmt RFI Ph2 Sample Anal: SQ10 16.7 Subsf	4JUN97	4MAR98
150950	19	19	0	1106: Asmt RFI Ph2 Field Work : SQ10 16.6 Subsf	31JUL97	26AUG97
150955	111	111	0	1106: Asmt RFI Ph2 Sample Anal: SQ10 16.6 Subsf	31JUL97*	13JAN98
151070	132	132	0	1106: Prepare Internal Draft of RFI Report	5AUG97	18FEB98
150970	16	16	0	1106: Asmt RFI Ph2 Field Work : SQ10 16.8 Subsf	26AUG97	17SEP97
150985	16	16	0	1106: Asmt RFI Ph2 Field Work : SQ10 16.2 Subsf	17SEP97	8OCT97
150990	95	95	0	1106: Asmt RFI Ph2 Sample Anal: SQ10 16.2 Subsf	17SEP97	6FEB98
150975	101	101	0	1106: Asmt RFI Ph2 Sample Anal: SQ10 16.8 Subsf	18SEP97	18FEB98
150026	249	249	0	1106: Asmt RFI Manage ADS: FY98	10CT97	30SEP98
150032	249	249	0	1106: Asmt RFI PH1 Field Work: SQ1 FY98 GCHAR	10CT97	30SEP98
150047	249	249	0	1106: Asmt RFI PH3 MDA B Pilot: SQ1 FY98 Pilot	10CT97	30SEP98
620040	249	249	0	1106: CONDUCT VCA FY-98	10CT97	30SEP98
150158	194	194	0	1106: Asmt RFI PH3 Field Work: SQ1 12.6 YW5 3	17DEC97	24SEP98
150159	245	245	0	1106: Asmt RFI PH3 Sample Anal:SQ1 12.6 YW5 3	17DEC97	10DEC98
150960	44	44	0	1106: Asmt RFI Ph2 Data Assmt: SQ10 16.6 Subsf	14JAN98	18MAR98
150995	44	44	0	1106: Asmt RFI Ph2 Data Assmt: SQ10 16.2 Subsf	9FEB98	10APR98
150980	44	44	0	1106: Asmt RFI Ph2 Data Assmt: SQ10 16.8 Subsf	19FEB98	21APR98

-----

LANL INC-DO	G. ELLER	FINEST HOUR	ADS 1106: TA-21	TBS 2/17/92
REPORT DATE	6AUG92 RUN NO. 134	ENVIRONMENTAL RESTORATION	START DATE	10CT91 FIN DATE 30SEP02
	17:43			
1106 SCHEDULE REPORT BY EARLY START			DATA DATE	10CT91 PAGE NO. 9

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
151075	20	20	0	1106: LANL/VE Review Internal Draft of RFI Rpt	23FEB98	20MAR98
150925	44	44	0	1106: Asmt RFI Ph2 Data Assmt: SQ10 16.7 Subsf	5MAR98	5MAY98
151080	40	40	0	1106:Incorp LANL Rev Comments Intern Dft RFI Rpt	23MAR98	15MAY98
150961	121	121	0	1106: Asmt RFI PH2 Tech Memo: Sq10 MDAAB Subs	6MAY98	27OCT98
151085	20	20	0	1106: Publish DOE Draft of RFI Report	18MAY98	15JUN98
151090	22	22	0	1106: Conduct Review of DOE Draft of RFI Report	16JUN98	16JUL98
151095	40	40	0	1106: Incorp DOE Rev Comments DOE Dft RFI Rpt	21JUL98	15SEP98
151115	245	245	0	1106: Cond Bench/Pilot Studies for CMS Plan(LOE)	6AUG98	30JUL99
151120	35	35	0	1106: Establish Current Situation for CMS Plan	6AUG98	24SEP98
151125	35	35	0	1106: Establish CA Objectives for CMS Plan	6AUG98	24SEP98
151130	35	35	0	1106: Develop Screening Technologies for CMS Pla	6AUG98	24SEP98
151135	245	245	0	1106: Develop NEPA Documentation for CMS Plan	6AUG98	30JUL99
151100	20	20	0	1106: Publish EPA/NMED Draft of RFI Report	16SEP98	14OCT98
151140	15	15	0	1106: Develop Alternatives for CMS Plan	25SEP98	16OCT98
150031	249	249	0	1106: Asmt RFI Manage ADS: FY99	10CT98	30SEP99
150037	249	249	0	1106: Asmt RFI PH1 Field Work: SQ1 FY99 GCHAR	10CT98	30SEP99
150048	249	249	0	1106: Asmt RFI PH3 MDA B Pilot: SQ1 FY99 Pilot	10CT98	30SEP99
151045	249*	249*	0	1106: Manage ADS FY-99 (LOE)	10CT98*	30SEP99
620045	249	249	0	1106: CONDUCT VCA FY-99	10CT98	30SEP99
15M010	0	0	0	1106: EPA/NMED DRAFT OF RFI REPORT		14OCT98
151105	44	44	0	1106: Conduct EPA Review of RFI Report	15OCT98	18DEC98
15M015	0	0	0	1106: START DEVELOPMENT OF CMS PLAN	15OCT98*	
151110	43	43	0	1106: Conduct NMED Review of RFI Report	16OCT98	18DEC98
151150	10	10	0	1106: Develop Internal Draft of CMS Plan	19OCT98	30OCT98
151155	10	10	0	1106: LANL/VE Review Internal Draft of CMS Plan	2NOV98	16NOV98
151165	10	10	0	1106:Incorp LANL REV Comments Intern Dft CMS Pl	17NOV98	2DEC98
151170	5	5	0	1106: Publish DOE Draft of CMS Plan	3DEC98	9DEC98
151175	22	22	0	1106: Conduct Review of DOE Draft of CMS Plan	10DEC98	13JAN99
151145	20	20	0	1106: Incorporate EPA/NMED Comments on RFI Rpt	21DEC98	21JAN99
151180	20	20	0	1106: Incorp DOE Rev Comments DOE Dft of CMS Pl	14JAN99	11FEB99

TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 1OCT91 PAGE NO. 10


ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
151160	20	20	0	1106: Publish Final RFI Report	22JAN99	19FEB99
151185	10	10	0	1106: Publish EPA/NMED Draft of CMS Plan	11FEB99	25FEB99
15M000	0	0	0	1106: EPA NOTIFICATION OF CMS REQUIREMENTS		19FEB99
15M003	0	0	0	1106: RFI COMPLETE	22FEB99	
15M020	0	0	0	1106: EPA/NMED DRAFT OF CMS PLAN COMPLETED		25FEB99
151190	44	44	0	1106: Conduct EPA Review of CMS Plan	26FEB99	28APR99
151195	44	44	0	1106: Conduct NMED Review of CMS Plan	26FEB99	28APR99
151200	20	20	0	1106: Incorporate EPA/NMED Comments on CMS Plan	29APR99	26MAY99
151205	10	10	0	1106: Publish Final CMS Plan	27MAY99	10JUN99
151210	5	5	0	1106: EPA Approves CMS Plan	11JUN99	17JUN99
15M025	0	0	0	1106: EPA APPROVED CMS PLAN		17JUN99
151215	245	245	0	1106: Conduct CMS Bench/Pilot Studies (LOE)	18JUN99	12JUN00
15M030	0	0	0	1106: START CMS WORK	18JUN99	
151050	249	249	0	1106: Manage ADS During FY-00 (LOE)	1OCT99	29SEP00
620050	249	249	0	1106: CONDUCT VCA FY-00	1OCT99	29SEP00
15M002	0	0	0	1106: RFI FIELD WORK COMPLETE	1OCT99	
15M040	0	0	0	1106: CMS WORK COMPLETED		12JUN00
151220	30	30	0	1106: Conduct Technical Evaluation for CMS Rpt	13JUN00	25JUL00
151225	30	30	0	1106: Cond Environmental Evaluation for CMS Rpt	13JUN00	25JUL00
151230	30	30	0	1106: Cond Human Health Evaluation for CMS Rpt	13JUN00	25JUL00
151235	30	30	0	1106: Cond Community Relations Eval for CMS Rpt	13JUN00	25JUL00
151240	30	30	0	1106: Conduct Cost Evaluation for CMS Report	13JUN00	25JUL00
151245	30	30	0	1106: Develop NEPA Documentation for CMS Report	13JUN00	25JUL00
15M035	0	0	0	1106: START DEVELOPMENT OF CMS REPORT	13JUN00	
151250	10	10	0	1106: Prepare Internal Draft of CMS Report	26JUL00	8AUG00
151255	10	10	0	1106: LANL/VE Review Internal Draft of CMS Rpt	4AUG00	17AUG00
151260	35	35	0	1106:Incorp LANL Rev Comments Intern Dft CMS Rpt	18AUG00	6OCT00
151055	248	248	0	1106: Manage ADS During FY-01 (LOE)	2OCT00	28SEP01
620055	248	248	0	1106: CONDUCT VCA FY-01	2OCT00	28SEP01
151265	10	10	0	1106: Publish DOE Draft of CMS Report	6OCT00	20OCT00

-----

LANL INC-DO G. ELLER	FINEST HOUR	ADS 1106: TA-21	TBS 2/17/92
REPORT DATE 6AUG92 RUN NO. 134	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 30SEP02
17:43			
1106 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91	PAGE NO. 11

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
151270	22	22	0	1106: Conduct Review of DOE Draft of CMS Report	23OCT00	22NOV00
15M045	0	0	0	1106: EPA/NMED DRAFT OF CMS REPORT COMPLETED		8NOV00
151275	10	10	0	1106: Incorp. DOE Rev Comments DOE Dft CMS Rpt	22NOV00	7DEC00
151280	10	10	0	1106: Publish EPA/NMED Draft of CMS Report	8DEC00	21DEC00
151285	120	120	0	1106: Conduct EPA Review of CMS Report	22DEC00	15JUN01
151290	120	120	0	1106: Conduct NMED Review of CMS Report	22DEC00	15JUN01
151295	20	20	0	1106: Incorporate EPA/NMED Comments on CMS Rpt	18JUN01	16JUL01
15M050	0	0	0	1106: ASSESSMENT COMPLETED		20JUN01
151300	10	10	0	1106: Publish Final CMS Report	17JUL01	30JUL01
151060	249	249	0	1106: MANAGE ADS FY-02	(LOE) 1OCT01*	30SEP02

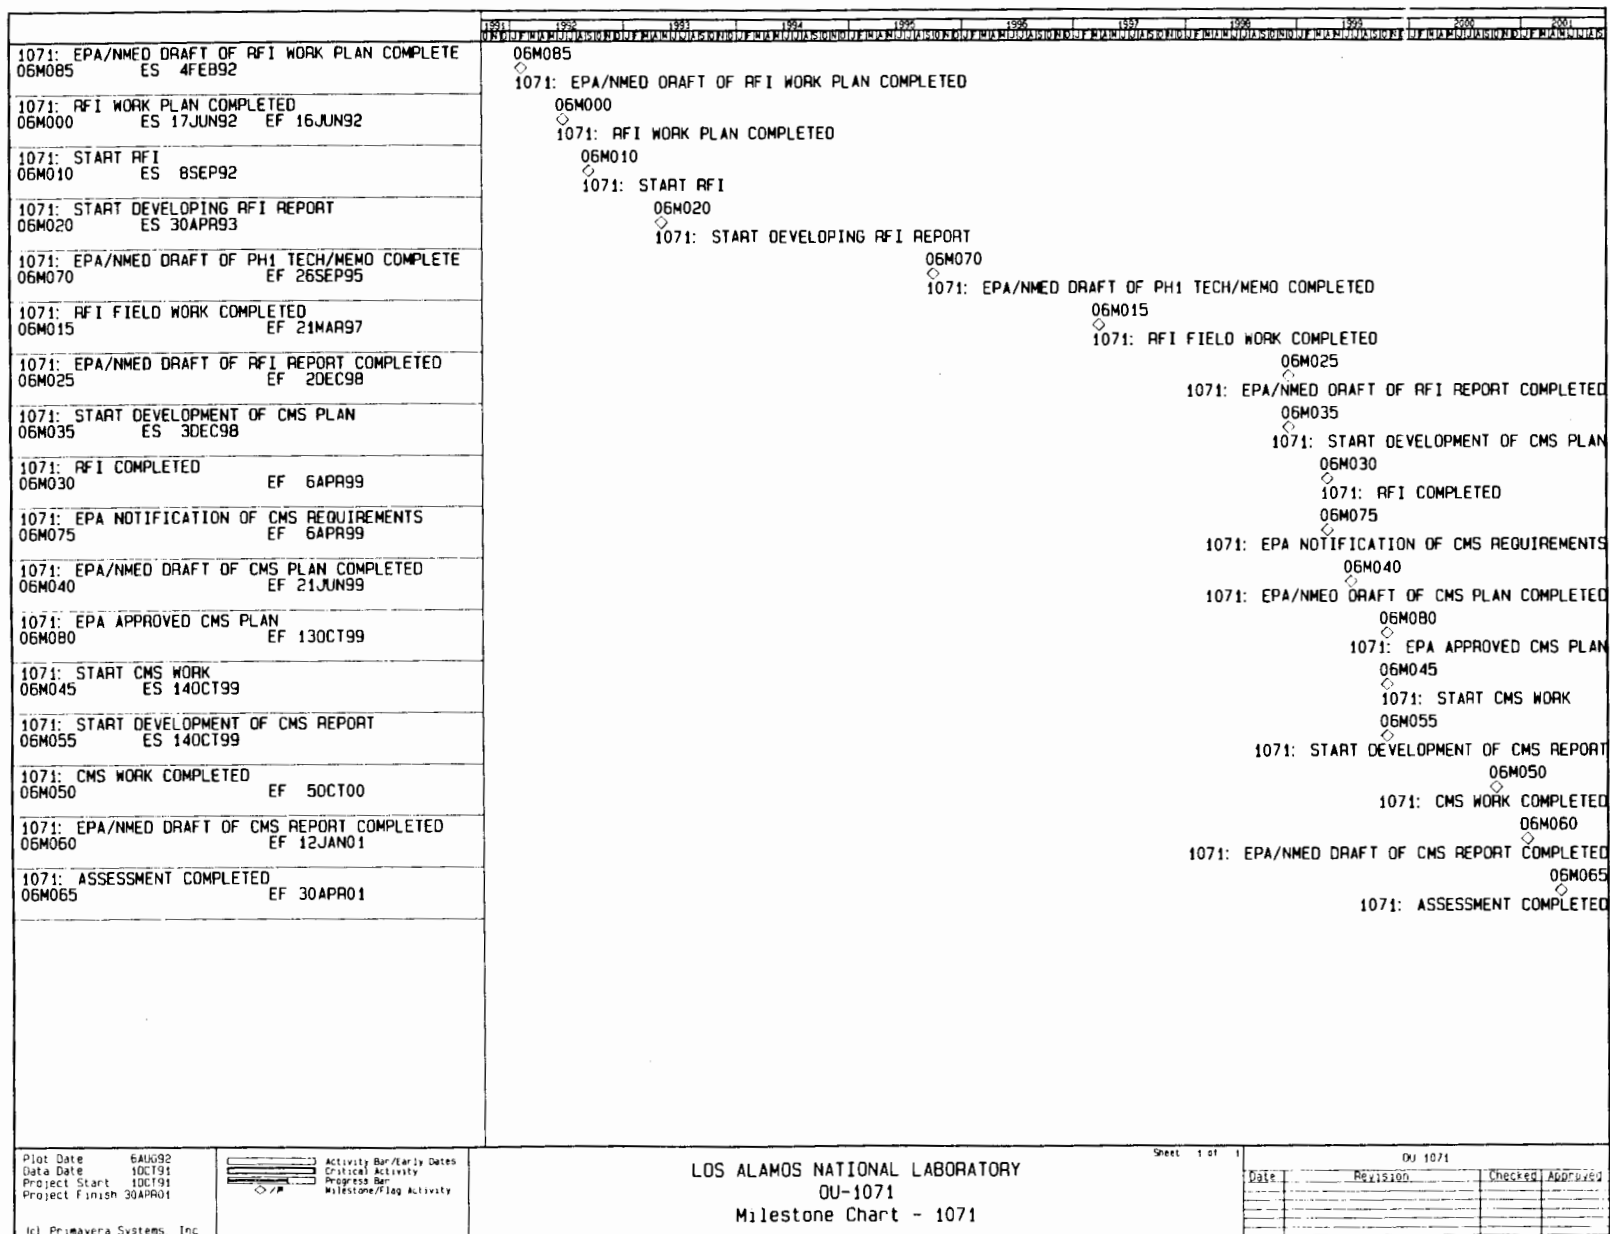

-----

LANL EES-1 JIM ALDRICH	FINEST HOUR	1071: TA-0 19 26 73 74 TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 178	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 30APR91
15:47		
1071 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91 PAGE NO. 1

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START FINISH
060000	22	22	0	1071:DOE/LANL/VE Review Internal Draft RFI WP	10CT91 31OCT91
060035	250	250	0	1071: Manage ADS During FY-92 (LOE)	10CT91 30SEP92
060457	32	32	0	1071: Develop General Schedule	15OCT91* 2DEC91
060005	20	20	0	1071: Revise Internal Dft RFI WP & Dev. DOE Dft	1NOV91 3DEC91
060010	10	10	0	1071: DOE Review DOE Draft RFI WP	4DEC91 17DEC91
060015	30	30	0	1071: Revise DOE Dft RFI WP & Dev EPA/NMED Dft	18DEC91 3FEB92
060456	22	22	0	1071: Develop Detailed Field Schedule	2JAN92* 3FEB92
060020	44	44	0	1071: Regulatory Review Draft RFI Work Plan	4FEB92 6APR92
06M085	0	0	0	1071: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED	4FEB92
060025	40	40	0	1071: Incorporate EPA/NMED Comments	7APR92 2JUN92
060485	10	10	0	1071: Issue Final RFI Work Plan	3JUN92 16JUN92
06M000	0	0	0	1071: RFI WORK PLAN COMPLETED	17JUN92 16JUN92
060470	62	62	0	1071: Prepare for Field Work	8SEP92* 8DEC92
06M010	0	0	0	1071: START RFI	8SEP92*
060040	249	249	0	1071: Manage ADS During FY-93 (LOE)	10CT92 30SEP93
065010	248	248	0	1071: Conduct VCA (LOE) - FY 93	10CT92* 29SEP93
060435	245	245	0	1071: Assmt - Conduct VCA (LOE)	1FEB93 25JAN94
060475	63	63	0	1071: Write PH1 Contract, Mobilize for RFI	1FEB93* 29APR93
060225	100	100	0	1071: Prepare NEPA/Environmental Information	30APR93* 21SEP93
06M020	0	0	0	1071: START DEVELOPING RFI REPORT	30APR93*
060100	327	327	0	1071: Conduct RFI PH1 Field Work	16AUG93 8DEC94
060105	357	357	0	1071: Conduct RFI PH1 Sample Analysis	16AUG93* 25JAN95
060045	246	246	0	1071: Manage ADS During FY-94 (LOE)	10CT93 27SEP94
065015	248	248	0	1071: Conduct VCA (LOE) - FY 94	10CT93* 29SEP94
060110	367	367	0	1071: Conduct RFI PH1 Data Assessment	13JAN94 30JUN95
060050	244	244	0	1071: Manage ADS During FY-95 (LOE)	28SEP94 20SEP95
065020	248	248	0	1071: Conduct VCA (LOE) - FY 95	30CT94* 29SEP95
060120	20	20	0	1071: Demobilize RFI PH1 Field Work	9DEC94 10JAN95
060115	60	60	0	1071: Write Draft RFI PH1 Report/WP Modification	3JUL95 26SEP95
060055	246	246	0	1071: Manage ADS During FY-96 (LOE)	21SEP95 16SEP96



LANL EES-1	JIM ALDRICH	FINEST HOUR	1071: TA-0	19 26 73 74	TBS	2/17/92
REPORT DATE	5AUG92	RUN NO. 178	ENVIRONMENTAL RESTORATION	START DATE	10CT91	FIN DATE 30APR01
	15:47					
1071 SCHEDULE	REPORT BY	EARLY START	DATA DATE	10CT91	PAGE NO.	2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
06M070	0	0	0	1071: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		26SEP95
060125	22	22	0	1071: EPA/NMED Rev PH1 Tech Memo/WP Modification	27SEP95	27OCT95
060130	22	22	0	1071: DOE/LANL Review PH1 Report/Wp Modification	27SEP95	27OCT95
060131	20	20	0	1071: DOE/LANL Revise Draft RFI PH1 Report	27SEP95	25OCT95
060135	20	20	0	1071: Write PH2 Contract; Mobilize for RFI	27SEP95	25OCT95
065025	248	248	0	1071: Conduct VCA (LOE) - FY 96	20CT95*	27SEP96
060140	327	327	0	1071: Conduct RFI PH2 Field Work	26OCT95	21FEB97
060145	357	357	0	1071: Conduct RFI PH2 Sample Analysis	26OCT95	4APR97
060155	367	367	0	1071: Conduct RFI PH2 Data Assessment	26OCT95	18APR97
060060	245	245	0	1071: Manage ADS During FY-97 (LOE)	17SEP96	10SEP97
510000	187	187	0	1071: Conduct VCA (LOE) - FY 97	10CT96*	2JUL97
060150	20	20	0	1071: Demoblize RFI PH2 Field Work	24FEB97	21MAR97
06M015	0	0	0	1071: RFI FIELD WORK COMPLETED		21MAR97
060215	100	100	0	1071: Conduct RFI Report Facility Investigation	21APR97	10SEP97
060220	110	110	0	1071: Conduct RFI Report Investigation Analysis	21APR97	24SEP97
060065	245	245	0	1071: Manage ADS During FY-98 (LOE)	11SEP97	3SEP98
060235	132	132	0	1071: Prepare Internal Draft of RFI Report	25SEP97	9APR98
510005	245	245	0	1071: Conduct VCA (LOE) - FY 98	10CT97*	24SEP98
060240	20	20	0	1071: LANL/VE Review Internal Draft of RFI Rpt	10APR98	7MAY98
060245	40	40	0	1071:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	8MAY98	6JUL98
060250	20	20	0	1071: Publish DOE Draft of RFI Report	7JUL98	3AUG98
060255	22	22	0	1071: Conduct Review of DOE Draft of RFI Report	4AUG98	2SEP98
060260	40	40	0	1071:Incorp. DOE Rev. Comments DOE Dft RFI Rpt	3SEP98	30OCT98
060070	245	245	0	1071: Manage ADS During FY-99 (LOE)	4SEP98	30AUG99
060265	20	20	0	1071: Publish EPA/NMED Draft of RFI Report	2NOV98	2DEC98
06M025	0	0	0	1071: EPA/NMED DRAFT OF RFI REPORT COMPLETED		2DEC98
060270	44	44	0	1071: Conduct EPA Review of RFI Report	3DEC98	8FEB99
060275	44	44	0	1071: Conduct NMED Review of RFI Report	3DEC98	8FEB99
060280	245	245	0	1071:Conduct Bench/Pilot Studies for CMS Pl(LOE)	3DEC98	24NOV99
060285	35	35	0	1071: Establish Current Situation for CMS Plan	3DEC98	26JAN99

LANL EES-1 JIM ALDRICH  
 REPORT DATE 5AUG92 RUN NO. 178  
 15:47  
 1071 SCHEDULE REPORT BY EARLY START


FINEST HOUR  
 ENVIRONMENTAL RESTORATION

1071: TA-0 19 26 73 74 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 30APR01  
 DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
060290	35	35	0	1071: Establish CA Objectives for CMS Plan	3DEC98	26JAN99
060295	35	35	0	1071: Develop Screening Technologies for CMS Pl	3DEC98	26JAN99
060300	245	245	0	1071: Develop NEPA Documentation for CMS Plan	3DEC98	24NOV99
06M035	0	0	0	1071: START DEVELOPMENT OF CMS PLAN	3DEC98	
060305	15	15	0	1071: Develop Alternatives for CMS Plan	27JAN99	17FEB99
060495	20	20	0	1071: Incorporate EPA/NMED Comments on RFI Rpt	9FEB99	9MAR99
060310	10	10	0	1071: Develop Internal Draft of CMS Plan	18FEB99	3MAR99
060315	10	10	0	1071: LANL/VE Review Internal Draft of CMS Pl	4MAR99	17MAR99
060500	20	20	0	1071: Publish Final RFI Report	10MAR99	6APR99
060320	10	10	0	1071:Incorp. LANL REV Comments Intern Dft CMS Pl	18MAR99	31MAR99
060325	5	5	0	1071: Publish DOE Draft of CMS Plan	1APR99	7APR99
06M030	0	0	0	1071: RFI COMPLETED		6APR99
06M075	0	0	0	1071: EPA NOTIFICATION OF CMS REQUIREMENTS		6APR99
060330	22	22	0	1071: Conduct Review of DOE Draft of CMS Plan	8APR99	7MAY99
060335	20	20	0	1071:Incorp. DOE Rev.Comments DOE Dft of CMS Pl	10MAY99	7JUN99
060340	10	10	0	1071: Publish EPA/NMED Draft of CMS Plan	8JUN99	21JUN99
06M040	0	0	0	1071: EPA/NMED DRAFT OF CMS PLAN COMPLETED		21JUN99
060345	44	44	0	1071: Conduct EPA Review of CMS Plan	22JUN99	23AUG99
060350	44	44	0	1071: Conduct NMED Review of CMS Plan	22JUN99	23AUG99
060505	20	20	0	1071: Incorporate EPA/NMED Comments on CMS Plan	24AUG99	21SEP99
060075	155	155	0	Manage ADS During FY-2000	31AUG99	17APR00
060510	10	10	0	1071: Publish Final CMS Plan	22SEP99	5OCT99
060515	5	5	0	1071: EPA Approves CMS Plan	6OCT99	13OCT99
06M080	0	0	0	1071: EPA APPROVED CMS PLAN		13OCT99
060355	245	245	0	1071: Conduct CMS Bench/Pilot Studies (LOE)	14OCT99	5OCT00
060360	30	30	0	1071: Conduct Technical Evaluation for CMS Rpt	14OCT99	29NOV99
060365	30	30	0	1071: Conduct Environmental Eval for CMS Report	14OCT99	29NOV99
060370	30	30	0	1071: Conduct Human Health Eval for CMS Report	14OCT99	29NOV99
060375	30	30	0	1071: Conduct Community Relations Eval. CMS Rpt	14OCT99	29NOV99
060380	30	30	0	1071: Conduct Cost Evaluation for CMS Report	14OCT99	29NOV99

LANL EES-1 JIM ALDRICH  
 REPORT DATE 5AUG92 RUN NO. 178 ENVIRONMENTAL RESTORATION  
 1071 SCHEDULE REPORT BY EARLY START  
 1071: TA-0 19 26 73 74 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 30APR01  
 DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
060385	30	30	0	1071: Develop NEPA Documentation for CMS Report	14OCT99	29NOV99
06M045	0	0	0	1071: START CMS WORK	14OCT99	
06M055	0	0	0	1071: START DEVELOPMENT OF CMS REPORT	14OCT99	
060390	10	10	0	1071: Prepare Internal Draft of CMS Report	30NOV99	13DEC99
060395	10	10	0	1071: LANL/VE Review Internal Draft of CMS Rpt	14DEC99	29DEC99
060400	35	35	0	1071:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	17AUG00	5OCT00
06M050	0	0	0	1071: CMS WORK COMPLETED		5OCT00
060405	10	10	0	1071: Publish DOE Draft of CMS Report	6OCT00	20OCT00
060410	22	22	0	1071: Conduct Review of DOE Draft of CMS Report	23OCT00	22NOV00
060415	22	22	0	1071:Incorp. DOE Rev Comments DOE Dft CMS Report	27NOV00	28DEC00
060420	10	10	0	1071: Publish EPA/NMED Draft of CMS Report	29DEC00	12JAN01
06M060	0	0	0	1071: EPA/NMED DRAFT OF CMS REPORT COMPLETED		12JAN01
060425	44	44	0	1071: Conduct EPA Review of CMS Report	16JAN01	19MAR01
060430	44	44	0	1071: Conduct NMED Review of CMS Report	16JAN01	19MAR01
060520	20	20	0	1071: Incorporate EPA/NMED Comments on CMS Rpt	20MAR01	16APR01
060530	10	10	0	1071: Publish Final CMS Report	17APR01	30APR01
06M065	0	0	0	1071: ASSESSMENT COMPLETED		30APR01

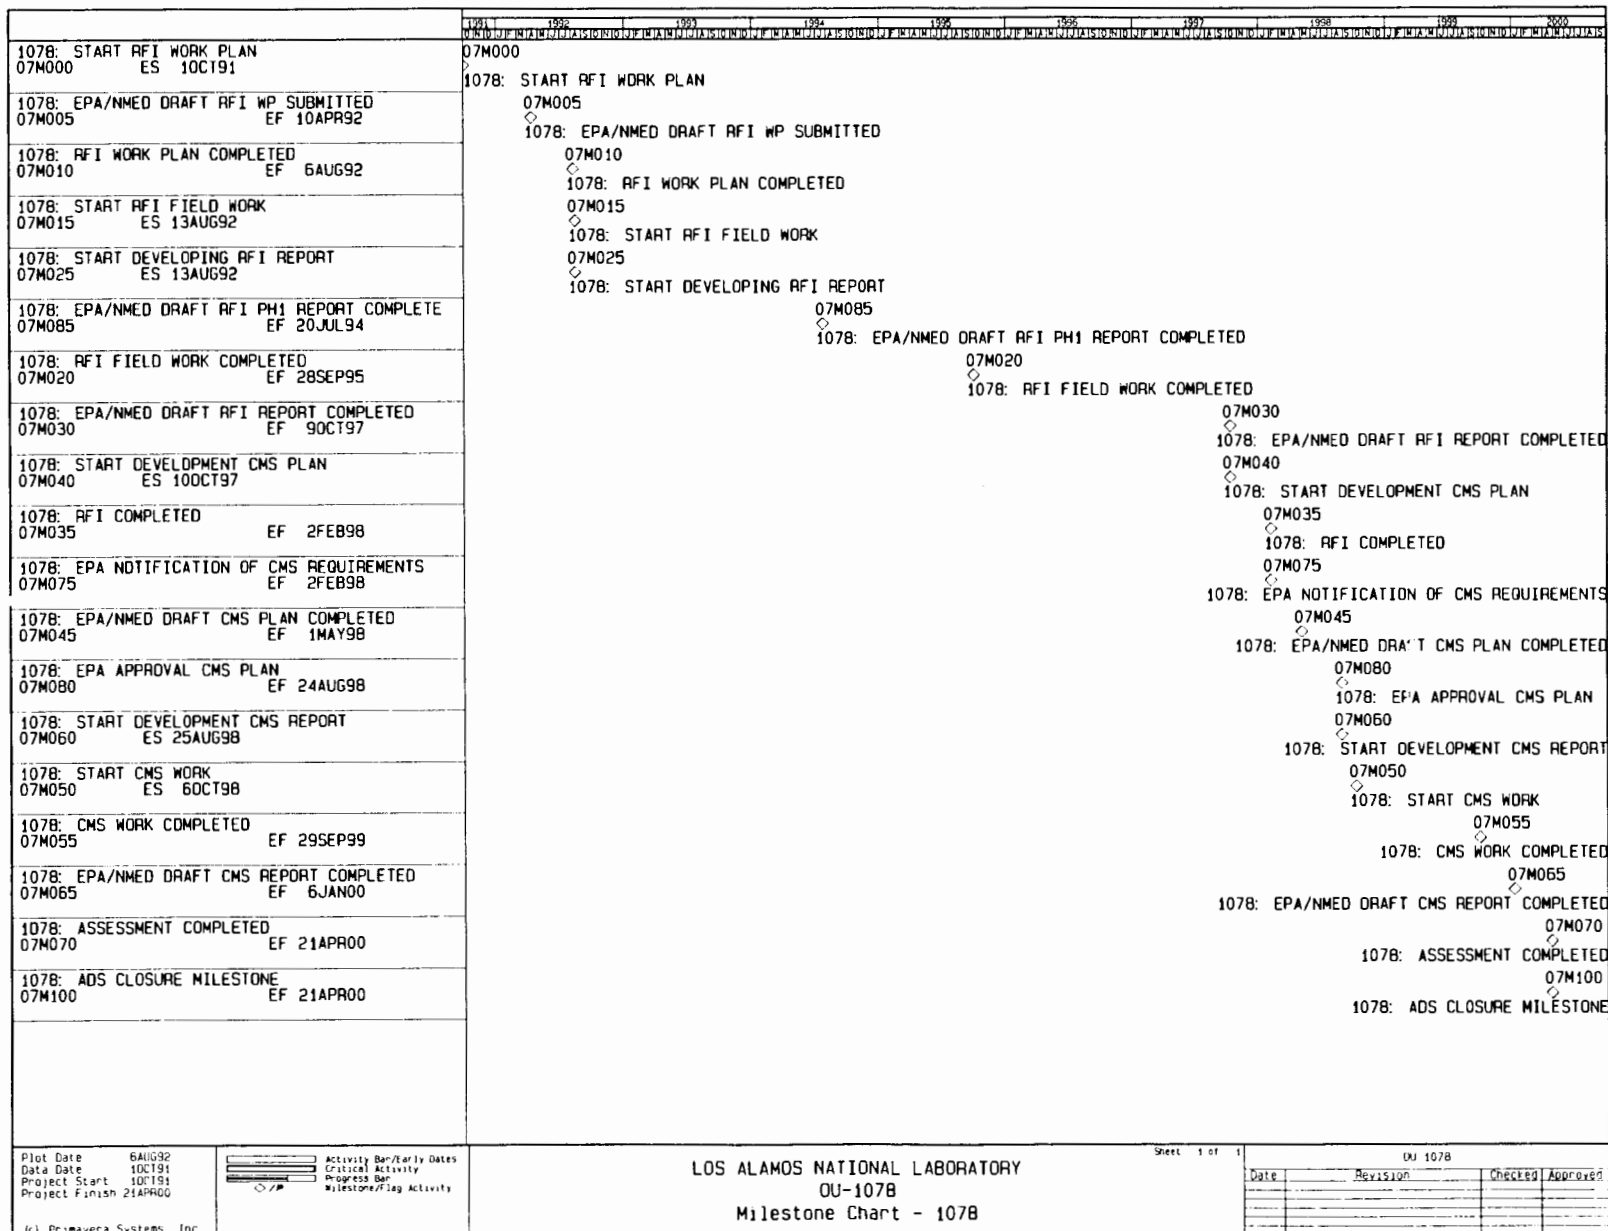

LANL EM-8 R. CONRAD  
 REPORT DATE 5AUG92 RUN NO. 145 ENVIRONMENTAL RESTORATION  
 15:48  
 1078 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ADS 1078: TA-1  
 START DATE 10CT91 FIN DATE 21APR00  
 DATA DATE 10CT91 PAGE NO. 1

TBS 2/17/92

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
070010	40	40	0	1078: Determine Data Needs RFI WP	10CT91	27NOV91
070040	68	68	0	1078: Develop Health & Safety Plan RFI WP	10CT91	14JAN92
070090	250	250	0	1078: MANAGE ADS FY-92 (LOE)	10CT91	30SEP92
070575	60	60	0	1078: Conduct VCA - Assessment FY-92 (LOE)	10CT91	31DEC91
070580	60	60	0	1078: Bench/Pilot Studies RFI WP	10CT91	31DEC91
07M000	0	0	0	1078: START RFI WORK PLAN	10CT91*	
070015	24	24	0	1078: Dft Samp Pl Hillside Aggr RFI WP	9OCT91	12NOV91
070020	24	24	0	1078: Dft Samp Pl Non-Hillside Aggr RFI WP	16OCT91	19NOV91
070025	24	24	0	1078: Dft Samp Pl for SWMU'S RFI WP	21OCT91	22NOV91
070050	21	21	0	1078: Develop NEPA Documentation RFI WP	30OCT91	2DEC91
070030	4	4	0	1078: Review Draft Sampling Plans RFI WP	19NOV91	22NOV91
070035	5	5	0	1078: Finalize Sampling Plans RFI WP	25NOV91	3DEC91
070055	15	15	0	1078: Develop Internal Draft RFI WP	10DEC91*	2JAN92
070060	22	22	0	1078: DOE/LANL/VE Rev Internal Drft RFI WP	17DEC91	21JAN92
070045	75	75	0	1078: Develop Management Plan RFI WP	10JAN92	27APR92
070065	15	15	0	1078: Inc DOE/LANL Comment Int Drft RFI WP	15JAN92	4FEB92
070070	15	15	0	1078: DOE Review DOE Draft RFI WP	5FEB92	26FEB92
070075	37	37	0	1078: Inc DOE Commnt Issue EPA/NMED RFI WP	20FEB92	10APR92
07M005	0	0	0	1078: EPA/NMED DRAFT RFI WP SUBMITTED		10APR92
070080	62	62	0	1078: EPA Review Draft RFI WP	13APR92	9JUL92
070085	62	62	0	1078: NMED Review Draft RFI WP	13APR92	9JUL92
070510	24	24	0	1078: Write Contracts and Mobilize RFI PH1	10JUL92	12AUG92
070515	10	10	0	1078: Inc EPA/NMED Comments RFI WP	10JUL92	23JUL92
070520	20	20	0	1078: Issue Final RFI WP	10JUL92	6AUG92
07M010	0	0	0	1078: RFI WORK PLAN COMPLETED		6AUG92
070155	245	245	0	1078: Field Work RFI PH1	13AUG92	6AUG93
070290	100	100	0	1078: Prep NEPA Environmental Info RFI RPT	13AUG92*	11JAN93
07M015	0	0	0	1078: START RFI FIELD WORK	13AUG92	
07M025	0	0	0	1078: START DEVELOPING RFI REPORT	13AUG92	
070095	249	249	0	1078: MANAGE ADS FY-93 (LOE)	10CT92	30SEP93

LANL EM-8 R. CONRAD

FINEST HOUR

ADS 1078: TA-1

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 145

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 21APR00

15:48

1078 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
070150	249	249	0	1078: RFI Bench/Pilot Studies (LOE)	10CT92*	30SEP93
070505	249	249	0	1078: Conduct VCA - Assessment FY-93 (LOE)	10CT92*	30SEP93
070160	245	245	0	1078: Sample Analysis RFI PH1	9FEB93*	1FEB94
070165	245	245	0	1078: Data Assessment RFI PH1	4MAR93*	24FEB94
070175	20	20	0	1078: Demobilize Field Work RFI PH1	9AUG93	3SEP93
070100	249	249	0	1078: MANAGE ADS FY-94 (LOE)	10CT93	30SEP94
600290	249	249	0	1078: Conduct VCA - FY-94 (LOE)	10CT93	30SEP94
070170	60	60	0	1078: Write Draft Report / WP Mod RFI PH1	25FEB94	19MAY94
070185	22	22	0	1078: DOE/LANL Rev Report/WP Mod RFI PH1	20MAY94	21JUN94
070187	20	20	0	1078: Inc DOE/LANL Comments Rpt/WP RFI PH1	22JUN94	20JUL94
07M085	0	0	0	1078: EPA/NMED DRAFT RFI PH1 REPORT COMPLETED		20JUL94
070180	22	22	0	1078: EPA/NMED Review RPT / WP Mod RFI PH1	21JUL94	19AUG94
070183	40	40	0	1078: Inc EPA/NMED Comments Rpt/WP RFI PH1	22AUG94	18OCT94
070105	248	248	0	1078: MANAGE ADS FY-95 (LOE)	30CT94	29SEP95
600294	248	248	0	E078: Conduct VCA - FY-95 (LOE)	30CT94	29SEP95
070190	20	20	0	1078: Write Contracts and Mobilize RFI PH2	4OCT94	1NOV94
070189	10	10	0	1078: Issue Final Report/WP Mod RFI PH1	19OCT94	1NOV94
070195	205	205	0	1078: Field Work RFI PH2	2NOV94	30AUG95
070200	235	235	0	1078: Sample Analysis RFI PH2	2NOV94	13OCT95
070210	245	245	0	1078: Data Assessment RFI PH2	2NOV94	27OCT95
070205	20	20	0	1078: Demoblize Field Work RFI PH2	31AUG95	28SEP95
07M020	0	0	0	1078: RFI FIELD WORK COMPLETED		28SEP95
070110	249	249	0	1078: MANAGE ADS FY-96 (LOE)	20CT95	30SEP96
600298	249	249	0	1078: Conduct VCA - FY-96 (LOE)	20CT95	30SEP96
070280	100	100	0	1078: Facility Investigation RFI RPT	30OCT95	27MAR96
070300	132	132	0	1078: Prepare Internal Draft RFI RPT	28MAR96	20CT96
070115	249	249	0	1078: MANAGE ADS FY-97 (LOE)	10CT96	30SEP97
070285	110	110	0	1078: Investigation Analysis RFI RPT	30CT96	18MAR97
520000	189	189	0	1078: Conduct VCA - Remediation FY-97 (LOE)	2JAN97*	30SEP97
070305	22	22	0	1078: DOE/LANL/VE Rev Internal Drft RFI RPT	19MAR97	17APR97

LANL EM-8 R. CONRAD

FINEST HOUR

ADS 1078: TA-1

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 145

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 21APR00

15:48

1078 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
070310	40	40	0	1078: Inc DOE/LANL Comments Int Dft RFI RPT	18APR97	13JUN97
070315	10	10	0	1078: Issue DOE Draft RFI RPT	16JUN97	27JUN97
070320	22	22	0	1078: DOE Review DOE Draft RFI RPT	30JUN97	30JUL97
070325	40	40	0	1078: Inc DOE Comments DOE Draft RFI RPT	31JUL97	25SEP97
070330	10	10	0	1078: Issue EPA/NMED Draft RFI RPT	26SEP97	9OCT97
070120	249	249	0	1078: MANAGE ADS FY-98 (LOE)	10CT97	30SEP98
520005	249	249	0	1078: Conduct VCA - Remediation FY-98 (LOE)	10CT97	30SEP98
07M030	0	0	0	1078: EPA/NMED DRAFT RFI REPORT COMPLETED		9OCT97
070335	44	44	0	1078: EPA Review RFI RPT	10OCT97*	16DEC97
070340	44	44	0	1078: NMED Review RFI RPT	10OCT97	16DEC97
070345	245	245	0	1078: Conduct Bench/Pilot Studies CMS PLN(LOE)	10OCT97	5OCT98
070350	35	35	0	1078: Establish Current Situation CMS PLN	10OCT97	3DEC97
070355	35	35	0	1078: Establish CA Objectives CMS PLN	10OCT97	3DEC97
070360	35	35	0	1078: Develop Screening Technology CMS PLN	10OCT97	3DEC97
070365	35	35	0	1078: Develop NEPA Documentation CMS PLN	10OCT97	3DEC97
07M040	0	0	0	1078: START DEVELOPMENT CMS PLAN	10OCT97	
070370	15	15	0	1078: Develop Alternatives CMS PLN	4DEC97	24DEC97
070540	20	20	0	1078: Inc EPA/NMED Comments RFI RPT	17DEC97	19JAN98
070375	10	10	0	1078: Develop Internal Draft CMS PLN	29DEC97	13JAN98
070380	10	10	0	1078: DOE/LANL/VE Rev Internal Drft CMS PLN	14JAN98	27JAN98
070545	10	10	0	1078: Issue Final RFI RPT	20JAN98	2FEB98
070385	10	10	0	1078: Inc DOE/LANL Comments Int Dft CMS PLN	28JAN98	10FEB98
07M035	0	0	0	1078: RFI COMPLETED		2FEB98
07M075	0	0	0	1078: EPA NOTIFICATION OF CMS REQUIREMENTS		2FEB98
070390	5	5	0	1078: Issue DOE Draft CMS PLN	11FEB98	18FEB98
070395	22	22	0	1078: DOE Review DOE Draft CMS PLN	19FEB98	20MAR98
070400	20	20	0	1078: Inc DOE Comments DOE Draft CMS PLN	23MAR98	17APR98
070405	10	10	0	1078: Issue EPA/NMED Draft CMS PLN	20APR98	1MAY98
07M045	0	0	0	1078: EPA/NMED DRAFT CMS PLAN COMPLETED		1MAY98
070410	44	44	0	1078: EPA Review CMS PLN	4MAY98	6JUL98

LANL EM-8 R. CONRAD

FINEST HOUR

ADS 1078: TA-1

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 145

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 21APR00


15:48

1078 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
070415	44	44	0	1078: NMED Review	CMS PLN	4MAY98	6JUL98
070550	20	20	0	1078: Inc EPA/NMED Comments	CMS PLN	7JUL98	3AUG98
070555	10	10	0	1078: Issue Final	CMS PLN	4AUG98	17AUG98
070560	5	5	0	1078: EPA Approval	CMS PLN	18AUG98	24AUG98
07M080	0	0	0	1078: EPA APPROVAL CMS PLAN			24AUG98
070425	30	30	0	1078: Technical Evaluation	CMS RPT	25AUG98	6OCT98
070430	30	30	0	1078: Environmental Evaluation	CMS RPT	25AUG98	6OCT98
070435	30	30	0	1078: Human Health Evaluation	CMS RPT	25AUG98	6OCT98
070440	30	30	0	1078: Community Relations Eval	CMS RPT	25AUG98	6OCT98
070445	30	30	0	1078: Cost Evaluation	CMS RPT	25AUG98	6OCT98
070450	30	30	0	1078: Develop NEPA Documentation	CMS RPT	25AUG98	6OCT98
07M060	0	0	0	1078: START DEVELOPMENT CMS REPORT		25AUG98	
070125	140	140	0	1078: MANAGE ADS FY-99	(LOE)	10CT98	27APR99
070420	245	245	0	1078: CMS Bench/Pilot Studies	(LOE)	6OCT98	29SEP99
07M050	0	0	0	1078: START CMS WORK		6OCT98*	
070455	10	10	0	1078: Prepare Internal Draft	CMS RPT	7OCT98	21OCT98
070460	10	10	0	1078: DOE/LANL/VE Review Int Draft	CMS RPT	22OCT98	4NOV98
070465	35	35	0	1078: Inc DOE/LANL Comments Int Dft	CMS RPT	11AUG99	29SEP99
07M055	0	0	0	1078: CMS WORK COMPLETED			29SEP99
070470	10	10	0	1078: Issue DOE Draft	CMS RPT	30SEP99	14OCT99
070475	22	22	0	1078: DOE Review DOE Draft	CMS RPT	15OCT99	16NOV99
070480	22	22	0	1078: Inc DOE Comments DOE Draft	CMS RPT	17NOV99	20DEC99
070485	10	10	0	1078: Issue EPA/NMED Draft	CMS RPT	21DEC99	6JAN00
07M065	0	0	0	1078: EPA/NMED DRAFT CMS REPORT COMPLETED			6JAN00
070490	44	44	0	1078: EPA Review	CMS RPT	7JAN00	10MAR00
070500	44	44	0	1078: NMED Review	CMS RPT	7JAN00	10MAR00
070565	20	20	0	1078: Inc EPA/NMED Comments	CMS RPT	13MAR00	7APR00
070570	10	10	0	1078: Issue Final	CMS RPT	10APR00	21APR00
07M070	0	0	0	1078: ASSESSMENT COMPLETED			21APR00
07M100	0	0	0	1078: ADS CLOSURE MILESTONE			21APR00



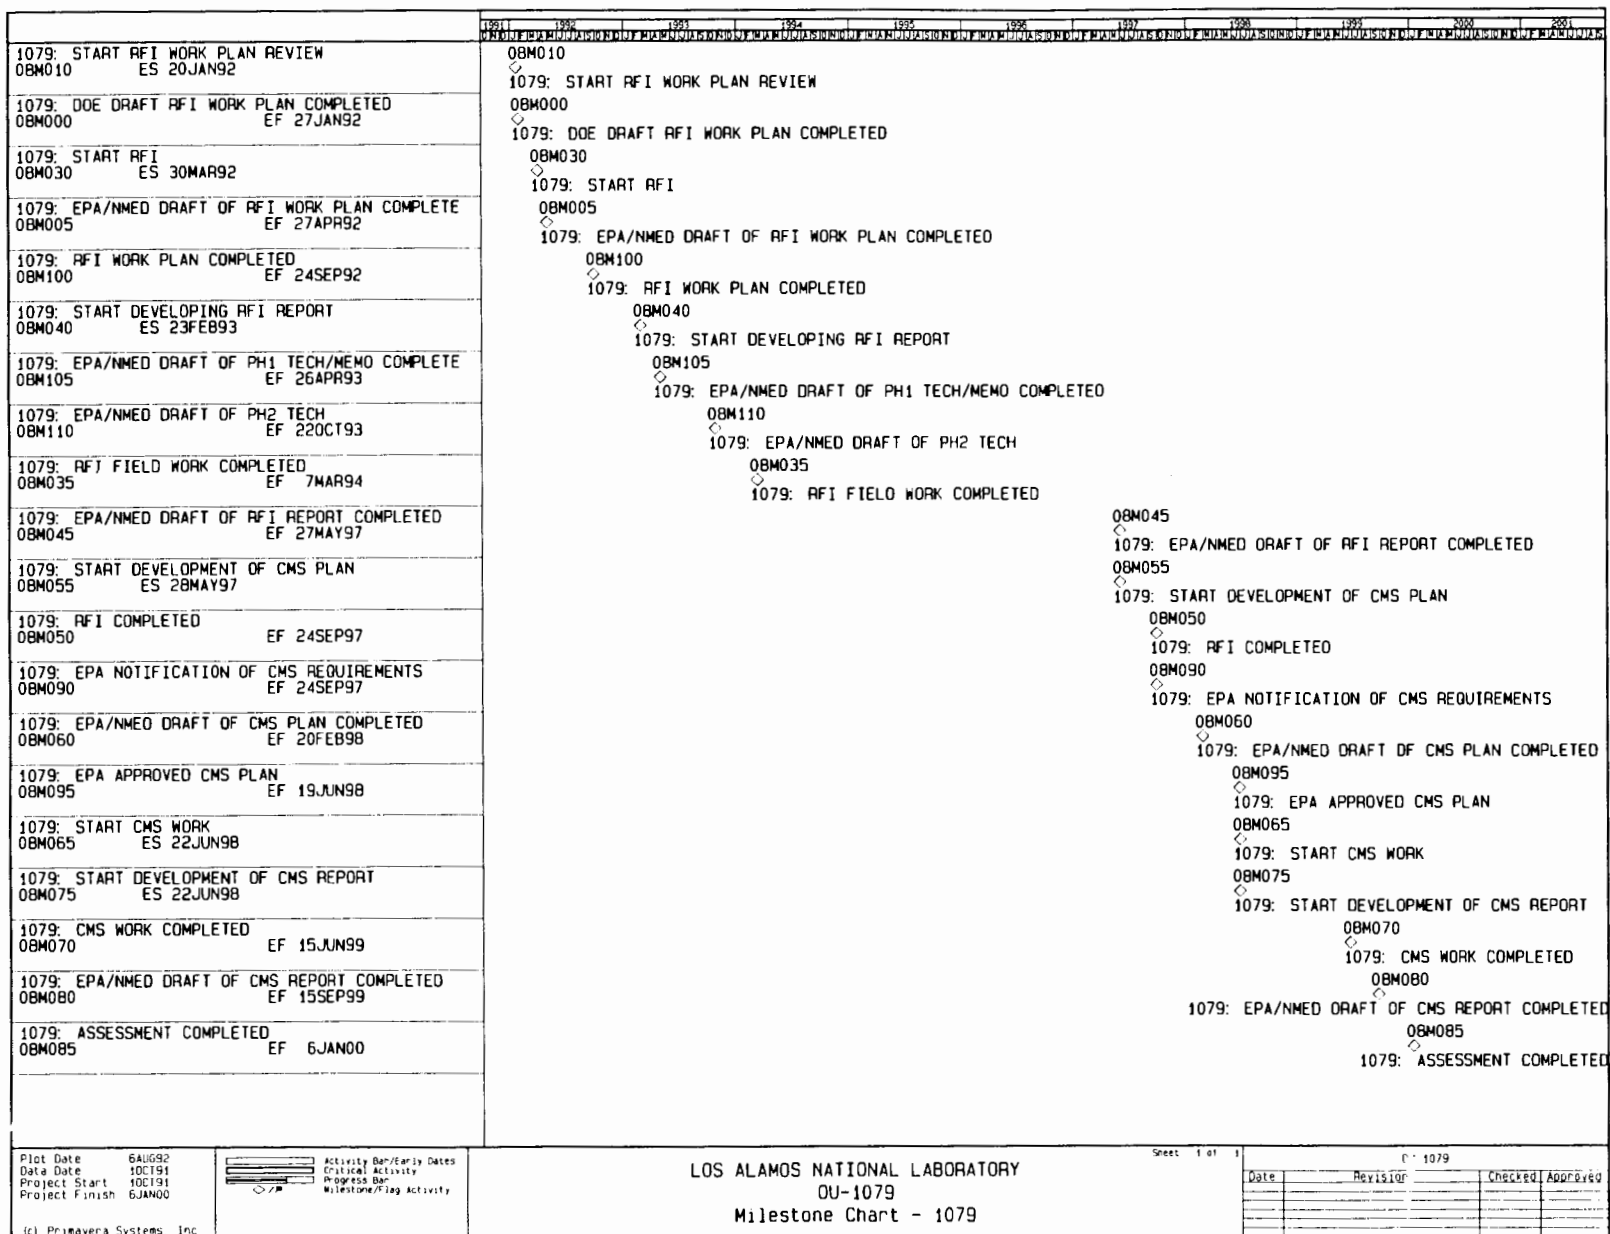

LANL EES-1 J. ALDRICH  
 REPORT DATE 6AUG92 RUN NO. 157 ENVIRONMENTAL RESTORATION  
 1079 SCHEDULE REPORT BY EARLY START  
 ADS 1079: TA-10 31 32 45 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 6JAN00  
 DATA DATE 10CT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
080000	55	55	0	1079: Develop Internal Draft Work Plan	10CT91	20DEC91
080390	246	246	0	1079: Manage ADS During FY-92 (LOE)	10CT91	24SEP92
080055	246	246	0	1079: Develop NEPA Documentation for RFI WP	23OCT91*	16OCT92
080005	12	12	0	1079: Conduct LANL/VE Rev of Int Draft Work Plan	23DEC91	10JAN92
080510	61	61	0	1079: Write Ph1 Contracts for RFI	2JAN92*	30MAR92
080010	10	10	0	1079: Incorp. LANL Comments & Dev.DOE Dft RFI WP	14JAN92	27JAN92
080130	10	10	0	1079: Publish DOE Draft of RFI WP	14JAN92	27JAN92
08M010	0	0	0	1079: START RFI WORK PLAN REVIEW	20JAN92*	
08M000	0	0	0	1079: DOE DRAFT RFI WORK PLAN COMPLETED		27JAN92
080015	19	19	0	1079: Conduct DOE Review of DOE Draft RFI WP	28JAN92	24FEB92
080160	64	64	0	1079: Mobilize for RFI	3FEB92	1MAY92
080020	25	25	0	1079: Incorporate DOE Comments into DOE RFI WP	18FEB92	23MAR92
080025	25	25	0	1079: Publish EPA/NMED Draft for RFI WP	24MAR92	27APR92
08M030	0	0	0	1079: START RFI	30MAR92*	
08M005	0	0	0	1079: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		27APR92
080030	58	58	0	1079: Conduct EPA Review of RFI WP	28APR92	20JUL92
080035	58	58	0	1079: Conduct NMED Review of RFI WP	28APR92	20JUL92
080170	105	105	0	1079: Conduct RFI PH1 Field Work	4MAY92	30SEP92
080515	30	30	0	1079: Incorporate EPA/NMED Comments for RFI WP	21JUL92	31AUG92
080520	17	17	0	1079: Publish Final RFI Work Plan	1SEP92	24SEP92
080410	84	84	0	1079: Write PH2 Contract; Mobilize for RFI	24SEP92*	29JAN93
08M100	0	0	0	1079: RFI WORK PLAN COMPLETED		24SEP92
080040	246	246	0	1079:Conduct Bench/Pilot Studies for RFI WP(LOE)	10CT92*	27SEP93
080045	246	246	0	3079:Conduct Voluntary C.Actions for RFI WP(LOE)	10CT92*	27SEP93
080175	40	40	0	1079: Conduct RFI PH1 Sample Analysis	10CT92	1DEC92
080455	245	245	0	1079: Manage ADS During FY-93 (LOE)	10CT92*	24SEP93
080580	20	20	0	1079: Demobilize RFI PH1 Field Work	10CT92	29OCT92
600330	245	245	0	1079: VCA FY-93	10CT92*	24SEP93
080180	55	55	0	1079: Conduct RFI PH1 Data Assessment	2DEC92	23FEB93
080435	100	100	0	1079: Develop NEPA Documentation for RFI Report	23FEB93	14JUL93

-----

LANL EES-1 J. ALDRICH	FINEST HOUR	ADS 1079: TA-10 31 32 45 TBS 2/17/92
REPORT DATE 6AUG92 RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 6JAN00
17:54		
1079 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91 PAGE NO. 2

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
08M040	0	0	0	1079: START DEVELOPING RFI REPORT	23FEB93	
080185	44	44	0	1079: Write RFI PH1 Tech Memo/WP Modification	24FEB93	26APR93
08M105	0	0	0	1079: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		26APR93
080400	22	22	0	1079: EPA/NMED Rev PH1 Tech Memo/WP Modification	27APR93	26MAY93
080405	22	22	0	1079: DOE Review PH1 Tech Memo/WP Modification	27APR93	26MAY93
080415	105	105	0	1079: Conduct RFI PH2 Field Work	1SEP93*	4FEB94
080460	246	246	0	1079: Manage ADS During FY-94 (LOE)	27SEP93	20SEP94
080625	20	20	0	1079: DOE Review Ph2 Tech Memo	27SEP93*	22OCT93
600334	246	246	0	1079: VCA FY-94	27SEP93	20SEP94
080090	20	20	0	E079: Develop Data Quality Objectives for RFI WP	10CT93*	28OCT93
08M110	0	0	0	1079: EPA/NMED DRAFT OF PH2 TECH		22OCT93
080620	23	23	0	1079: EPA/NMED Rev Ph2 Tech Memo	25OCT93	29NOV93
080420	40	40	0	1079: Conduct RFI PH2 Sample Analysis	7FEB94	4APR94
080430	20	20	0	1079: Demoblize RFI PH2 Field Work	7FEB94	7MAR94
080395	20	20	0	1079: Demobilize RFI PH1 Field Work	15FEB94	15MAR94
08M035	0	0	0	1079: RFI FIELD WORK COMPLETED		7MAR94
080585	36	36	0	1079: Write RFI PH2 Tech Memo/WP Modification	8MAR94	26APR94
080425	56	56	0	1079: Conduct RFI PH2 Data Assessment	5APR94	22JUN94
080590	61	61	0	1079: Write PH3 Contract; Mobilize for RFI	27APR94*	22JUL94
080595	105	105	0	1079: Conduct RFI PH3 Field Work	25JUL94	28DEC94
080465	244	244	0	1079: Manage ADS During FY-95 (LOE)	21SEP94	14SEP95
600338	245	245	0	1079: VCA FY-95	21SEP94	15SEP95
080600	40	40	0	1079: Conduct RFI PH3 Sample Analysis	29DEC94	27FEB95
080605	56	56	0	1079: Conduct RFI PH3 Data Assessment	28FEB95	16MAY95
080610	20	20	0	1079: Demobilize RFI PH3 Field Work	17MAY95	14JUN95
080470	246	246	0	1079: Manage ADS During FY-96 (LOE)	15SEP95	10SEP96
600342	245	245	0	1079: VCA FY-96	6OCT95	30SEP96*
080190	100	100	0	1079: Conduct RFI Report Facility Investigation	11OCT95	8MAR96
080195	110	110	0	1079: Conduct RFI Report Investigation Analysis	11OCT95	22MAR96
080200	132	132	0	1079: Prepare Internal Draft of RFI Report	25MAR96	27SEP96

LANL EES-1 J. ALDRICH

FINEST HOUR

ADS 1079: TA-10 31 32 45 TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 157  
17:54

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 6JAN00

1079 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
080475	245	245	0	1079: Manage ADS During FY-97 (LOE)	11SEP96	4SEP97
080205	20	20	0	1079: LANL/VE Review Internal Draft of RFI Rpt	30SEP96	28OCT96
080210	40	40	0	1079: Incorporate LANL Rev.Commts Intern Dft RFI Rpt	29OCT96	30DEC96
080215	20	20	0	1079: Publish DOE Draft of RFI Report	31DEC96	29JAN97
530000	189	189	0	1079: CONDUCT VCA (LOE) FY-97	2JAN97*	30SEP97
080220	22	22	0	1079: Conduct Review of DOE Draft of RFI Report	30JAN97	3MAR97
080225	40	40	0	1079: Incorporate DOE Rev. Commts. DOE Draft RFI Rpt	4MAR97	28APR97
080230	20	20	0	1079: Publish EPA/NMED Draft of RFI Report	29APR97	27MAY97
08M045	0	0	0	1079: EPA/NMED DRAFT OF RFI REPORT COMPLETED		27MAY97
080235	44	44	0	1079: Conduct EPA Review of RFI Report	28MAY97	29JUL97
080240	44	44	0	1079: Conduct NMED Review of RFI Rpt	28MAY97	29JUL97
080245	245	245	0	1079: Conduct Bench/Pilot Studies for CMS Pl (LOE)	28MAY97	20MAY98
080250	35	35	0	1079: Establish Current Situation for CMS Plan	28MAY97	16JUL97
080255	35	35	0	1079: Establish CA Objectives for CMS Plan	28MAY97	16JUL97
080260	35	35	0	1079: Develop Screening Technologies for CMS Pl	28MAY97	16JUL97
080445	245	245	0	1079: Develop NEPA Documentation for CMS Plan	28MAY97	20MAY98
08M055	0	0	0	1079: START DEVELOPMENT OF CMS PLAN	28MAY97	
080265	35	35	0	1079: Develop Alternatives for CMS Plan	17JUL97	4SEP97
080540	20	20	0	1079: Incorporate EPA/NMED Comments on RFI Rpt	30JUL97	26AUG97
080545	20	20	0	1079: Publish Final RFI Report	27AUG97	24SEP97
080270	35	35	0	1079: Develop Internal Draft of CMS Plan	5SEP97	24OCT97
080480	245	245	0	1079: Manage ADS During FY-98 (LOE)	5SEP97	28AUG98
08M050	0	0	0	1079: RFI COMPLETED		24SEP97
08M090	0	0	0	1079: EPA NOTIFICATION OF CMS REQUIREMENTS		24SEP97
530005	249	249	0	1079: Conduct VCA (LOE) FY-98	1OCT97	30SEP98
080275	10	10	0	1079: LANL/VE Review Internal Draft of CMS Pl	27OCT97	7NOV97
080280	10	10	0	1079: Incorporate LANL REV Commts Intern Dft CMS Pln	11NOV97	26NOV97
080285	5	5	0	1079: Publish DOE Draft of CMS Plan	27NOV97	3DEC97
080290	22	22	0	1079: Conduct Review of DOE Draft of CMS Plan	4DEC97	7JAN98
080295	20	20	0	1079: Incorporate DOE Rev.Commts DOE Dft.of CMS Pl	8JAN98	5FEB98

-----

LANL EES-1 J. ALDRICH	FINEST HOUR	ADS 1079: TA-10 31 32 45 TBS 2/17/92
REPORT DATE 6AUG92 RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 1OCT91 FIN DATE 6JAN00
17:54		
1079 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91 PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
080300	10	10	0	1079: Publish EPA/NMED Draft of CMS Plan	6FEB98	20FEB98
08M060	0	0	0	1079: EPA/NMED DRAFT OF CMS PLAN COMPLETED		20FEB98
080305	44	44	0	1079: Conduct EPA Review of CMS Plan	23FEB98	23APR98
080310	44	44	0	1079: Conduct NMED Review of CMS Plan	23FEB98	23APR98
080550	20	20	0	1079: Incorporate EPA/NMED Comments on CMS Plan	24APR98	21MAY98
080555	10	10	0	1079: Publish Final CMS Plan	22MAY98	5JUN98
080560	10	10	0	1079: EPA Approves CMS Plan	8JUN98	19JUN98
08M095	0	0	0	1079: EPA APPROVED CMS PLAN		19JUN98
080315	245	245	0	1079: Conduct CMS Bench/Pilot Studies (LOE)	22JUN98	15JUN99
080320	30	30	0	1079: Conduct Technical Evaluation for CMS Rpt	22JUN98	3AUG98
080325	30	30	0	1079: Conduct Environmental Eval for CMS Report	22JUN98	3AUG98
080330	30	30	0	1079: Conduct Human Health Eval for CMS Report	22JUN98	3AUG98
080335	30	30	0	1079: Cond Community Relations Eval. for CMS Rpt	22JUN98	3AUG98
080340	30	30	0	1079: Conduct Cost Evaluation for CMS Report	22JUN98	3AUG98
080450	30	30	0	1079: Develop NEPA Documentation for CMS Report	22JUN98	3AUG98
08M065	0	0	0	1079: START CMS WORK	22JUN98	
08M075	0	0	0	1079: START DEVELOPMENT OF CMS REPORT	22JUN98	
080345	163	163	0	1079: Prepare Internal Draft of CMS Report	4AUG98	1APR99
080485	245	245	0	1079: Manage ADS During FY-99 (LOE)	7OCT98	30SEP99*
080350	10	10	0	1079: LANL/VE Review Internal Draft of CMS Rpt	2APR99	15APR99
080355	35	35	0	1079: Incorp. LANL Rev Commts Intern. Dft CMS Rp	27APR99	15JUN99
08M070	0	0	0	1079: CMS WORK COMPLETED		15JUN99
080360	10	10	0	1079: Publish DOE Draft of CMS Report	16JUN99	29JUN99
080365	22	22	0	1079: Conduct Review of DOE Draft of CMS Report	30JUN99	30JUL99
080370	22	22	0	1079: Incorp. DOE Rev Comments DOE Dft CMS Rpt	2AUG99	31AUG99
080375	10	10	0	1079: Publish EPA/NMED Draft of CMS Report	1SEP99	15SEP99
08M080	0	0	0	1079: EPA/NMED DRAFT OF CMS REPORT COMPLETED		15SEP99
080380	44	44	0	1079: Conduct EPA Review of CMS Report	16SEP99	18NOV99
080385	44	44	0	1079: Conduct NMED Review of CMS Rpt	16SEP99	18NOV99
080565	20	20	0	1079: Incorporate EPA/NMED Comments on CMS Rpt	19NOV99	20DEC99

-----  
LANL EES-1 J. ALDRICH

FINEST HOUR

ADS 1079: TA-10 31 32 45 TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 157

ENVIRONMENTAL RESTORATION


START DATE 1OCT91 FIN DATE 6JAN00

17:54

1079 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 5

-----  
ACTIVITY ID      ORIG DUR    REM DUR      %      ACTIVITY DESCRIPTION      SCHEDULED START    FINISH  
-----  
080570      10    10      0      1079: Publish Final CMS Report      21DEC99    6JAN00  
08M085      0    0      0      1079: ASSESSMENT COMPLETED      6JAN00  
-----

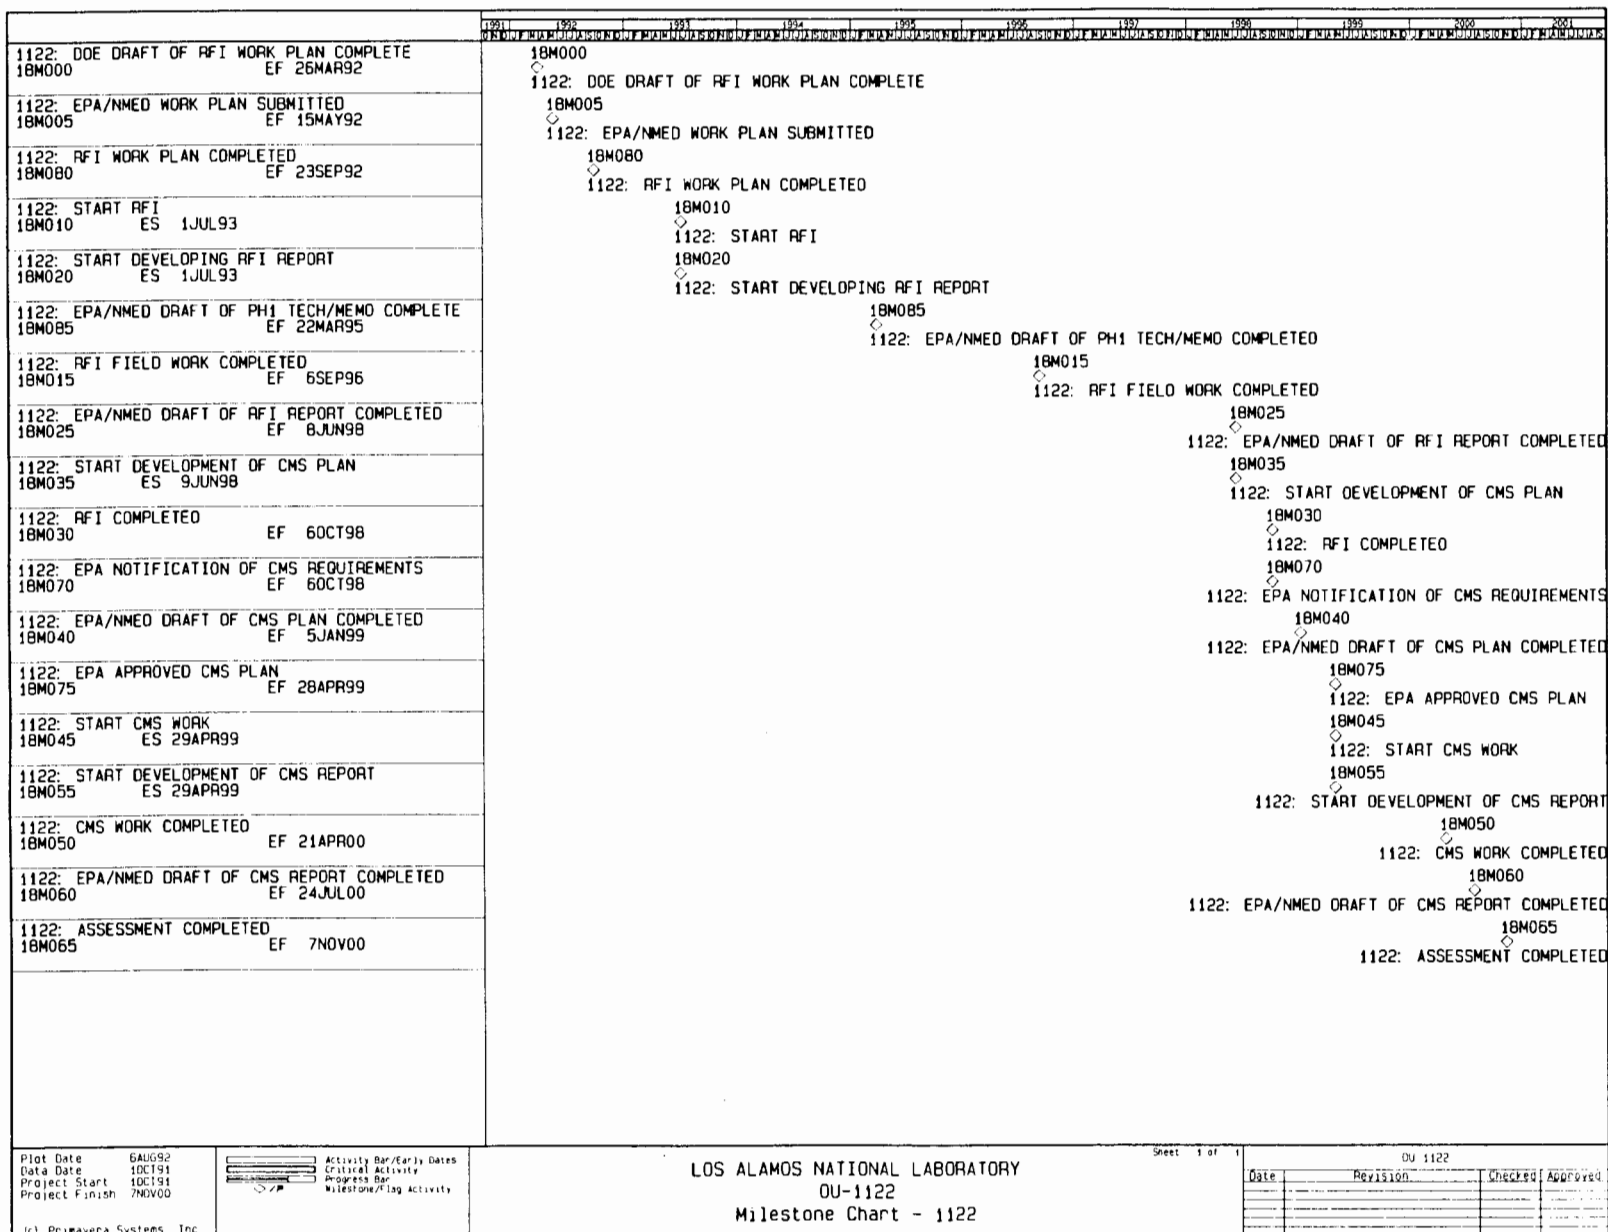

Plot Date 6AUG92  
Data Date 10C191  
Project Start 10C191  
Project Finish 7NOV00

Activity Bar/Early Dates  
Critical Activity  
Progress Bar  
Milestone/Flag Activity

LOS ALAMOS NATIONAL LABORATORY  
OU-1122  
Milestone Chart - 1122

Sheet 1 of 1

DU 1122			
Date	Revision	Checked	Approved

LANL CLS-1 KEITH DOWLER

FINEST HOUR

ADS 1122:TA-33, 70

BASELINE

REPORT DATE 6AUG92 RUN NO. 127

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 7NOV00

16:29

1122 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
180055	250	250	0	1122: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
180060	30	30	0	1122: Develop Management Plan for RFI Work Plan	10CT91	13NOV91
180070	10	10	0	1122: Write Final QA Plan	10CT91	15OCT91
180080	10	10	0	1122: Write Final Health and Safety Plan	10CT91	15OCT91
180100	10	10	0	1122: Write Final Records Management Plan	10CT91	15OCT91
180605	245	245	0	1122:Conduct Voluntary C. Actions for RFI WP LOE	10CT91	23SEP92
180610	245	245	0	1122: Cond Bench/Pilot Studies for RFI WP (LOE)	10CT91	23SEP92
180155	50	50	0	1122: Develop Internal Draft RFI Work Plan	14NOV91	30JAN92
180160	19	19	0	1122: LANL/VE Review Internal Draft RFI WP	31JAN92	27FEB92
180165	20	20	0	1122: Write DOE Draft RFI Work Plan	28FEB92	26MAR92
18M000	0	0	0	1122: DOE DRAFT OF RFI WORK PLAN COMPLETE		26MAR92
180170	21	21	0	1122: DOE Review DOE Draft Work Plan	27MAR92	24APR92
180175	15	15	0	1122: Incorporate DOE Comments/Write EPA/NMED Dft WP	27APR92	15MAY92
18M005	0	0	0	1122: EPA/NMED WORK PLAN SUBMITTED		15MAY92
180180	44	44	0	1122: Conduct NMED Review of RFI Work Plan	18MAY92	20JUL92
180185	44	44	0	1122: Conduct EPA Review of RFI Work Plan	18MAY92	20JUL92
180615	30	30	0	1122: Develop NEPA Documentation for RFI WP	29JUN92*	10AUG92
180540	45	45	0	1122: Write Ph1 Contracts for RFI	21JUL92	22SEP92
180545	20	20	0	1122: Incorporate EPA/NMED Comments for RFI WP	21JUL92	17AUG92
180550	10	10	0	1122: Publish Final RFI Work Plan	18AUG92	31AUG92
18M080	0	0	0	1122: RFI WORK PLAN COMPLETED		23SEP92
180105	249	249	0	1122: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
180700	158	158	0	1122: Detailed Field Planning	10CT92*	21MAY93
180190	20	20	0	1122: Mobilize for RFI	1JUL93	29JUL93
180195	245	245	0	1122: Conduct RFI Bench/Pilot Studies (LOE)	1JUL93	23JUN94
180200	327	327	0	1122: Conduct RFI PH1 Field Work	1JUL93	20OCT94
180205	357	357	0	1122: Conduct RFI PH1 Sample Analysis	1JUL93	6DEC94
180210	367	367	0	1122: Conduct RFI PH1 Data Assessment	1JUL93	20DEC94
180325	100	100	0	1122: Develop NEPA Documentation for RFI Report	1JUL93	22NOV93
180535	245	245	0	1122: Assmt - Conduct VCA (LOE)	1JUL93	23JUN94



-----

LANL CLS-1 KEITH DOWLER	FINEST HOUR	ADS 1122:TA-33, 70	BASLINE
REPORT DATE 6AUG92 RUN NO. 127	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 7NOV00
16:29		DATA DATE 1OCT91	PAGE NO. 2
1122 SCHEDULE REPORT BY EARLY START			

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START FINISH
18M010	0	0	0	1122: START RFI	1JUL93*
18M020	0	0	0	1122: START DEVELOPING RFI REPORT	1JUL93
180110	250	250	0	1122: Manage ADS During FY-94 (LOE)	10CT93 30SEP94
180115	247	247	0	1122: Manage ADS During FY-95 (LOE)	30CT94 29SEP95
180220	20	20	0	1122: Demobilize RFI PH1 Field Work	21OCT94 18NOV94
180215	60	60	0	1122: Write RFI PH1 Tech Memo/WP Modification	21DEC94 22MAR95
18M085	0	0	0	1122: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED	22MAR95
180225	22	22	0	1122: EPA/NMED Rev PH1 Tech Memo/WP Modification	23MAR95 21APR95
180230	22	22	0	1122: DOE Review PH1 Tech Memo/WP Modification	23MAR95 21APR95
180235	20	20	0	1122: Write PH2 Contract; Mobilize for RFI	23MAR95 19APR95
180240	327	327	0	1122: Conduct RFI PH2 Field Work	20APR95 8AUG96
180245	357	357	0	1122: Conduct RFI PH2 Sample Analysis	20APR95 20SEP96
180255	367	367	0	1122: Conduct RFI PH2 Data Assessment	20APR95 4OCT96
180120	249	249	0	1122: Manage ADS During FY-96 (LOE)	20CT95 30SEP96
180250	20	20	0	1122: Demoblize RFI PH2 Field Work	9AUG96 6SEP96
18M015	0	0	0	1122: RFI FIELD WORK COMPLETED	6SEP96
180315	100	100	0	1122: Conduct RFI Report Facility Investigation	23SEP96 20FEB97
180320	110	110	0	1122: Conduct RFI Report Investigation Analysis	23SEP96 6MAR97
180125	249	249	0	1122: Manage ADS During FY-97 (LOE)	10CT96 30SEP97
630000	189	189	0	1122: Conduct VCA (LOE)	2JAN97* 30SEP97
180335	132	132	0	1122: Prepare Internal Draft of RFI Report	7MAR97 11SEP97
180340	40	40	0	1122: LANL/VE Review Internal Draft of RFI Rpt	12SEP97 7NOV97
180130	249	249	0	1122: Manage ADS During FY-98 (LOE)	10CT97 30SEP98
630005	245	245	0	1122: Conduct VCA (LOE)	10CT97 24SEP98
180345	40	40	0	1122:Incorp.LANL Rev.Comments Intern RFI Dft Rpt	11NOV97 13JAN98
180350	20	20	0	1122: Publish DOE Draft of RFI Report	14JAN98 10FEB98
180355	22	22	0	1122: Conduct Review of DOE Draft of RFI Report	11FEB98 13MAR98
180360	40	40	0	1122:Incorp DOE Rev Comments into DOE Dft RFI Rpt	16MAR98 8MAY98
180365	20	20	0	1122: Publish EPA/NMED Draft of RFI Report	11MAY98 8JUN98
18M025	0	0	0	1122: EPA/NMED DRAFT OF RFI REPORT COMPLETED	8JUN98

BASELINE

START DATE 1OCT91 FIN DATE 7NOV00

DATA DATE 1OCT91 PAGE NO. 3


ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
180370	44	44	0	1122: Conduct EPA Review of RFI Report	9JUN98	10AUG98
180375	44	44	0	1122: Conduct NMED Review of RFI Rpt	9JUN98	10AUG98
180380	245	245	0	1122: Conduct Bench/Pilot Studies for CMS Pl LOE	9JUN98	2JUN99
180385	35	35	0	1122: Establish Current Situation for CMS Plan	9JUN98	28JUL98
180390	35	35	0	1122: Establish CA Objectives for CMS Plan	9JUN98	28JUL98
180395	35	35	0	1122: Develop Screening Technologies for CMS Pl.	9JUN98	28JUL98
180400	245	245	0	1122: Develop NEPA Documentation for CMS Plan	9JUN98	2JUN99
18M035	0	0	0	1122: START DEVELOPMENT OF CMS PLAN	9JUN98	
180405	15	15	0	1122: Develop Alternatives for CMS Plan	29JUL98	18AUG98
180570	20	20	0	1122: Incorporate EPA/NMED Comments on RFI Rpt	11AUG98	8SEP98
180410	15	15	0	1122: Develop Internal Draft of CMS Plan	19AUG98	9SEP98
180575	20	20	0	1122: Publish Final RFI Report	9SEP98	6OCT98
180415	10	10	0	1122: LANL/VE Review Internal Draft of CMS Plan	10SEP98	23SEP98
180420	10	10	0	1122:Incorp LANL REV Commts Intern Dft CMS Pl	24SEP98	7OCT98
180135	249	249	0	1122: Manage ADS During FY-99 (LOE)	1OCT98	30SEP99
18M030	0	0	0	1122: RFI COMPLETED		6OCT98
18M070	0	0	0	1122: EPA NOTIFICATION OF CMS REQUIREMENTS		6OCT98
180425	5	5	0	1122: Publish DOE Draft of CMS Plan	8OCT98	15OCT98
180430	22	22	0	1122: Conduct Review of DOE Draft of CMS Plan	16OCT98	17NOV98
180435	20	20	0	1122:Incorp. DOE Rev.Commts into DOE Dft CMS Pl	18NOV98	17DEC98
180440	10	10	0	1122: Publish EPA/NMED Draft of CMS Plan	18DEC98	5JAN99
18M040	0	0	0	1122: EPA/NMED DRAFT OF CMS PLAN COMPLETED		5JAN99
180445	44	44	0	1122: Conduct EPA Review of CMS Plan	6JAN99	10MAR99
180450	44	44	0	1122: Conduct NMED Review of CMS Plan	6JAN99	10MAR99
180580	20	20	0	1122: Incorporate EPA/NMED Comments on CMS Plan	11MAR99	7APR99
180585	10	10	0	1122: Publish Final CMS Plan	8APR99	21APR99
180590	5	5	0	1122: EPA Approves CMS Plan	22APR99	28APR99
18M075	0	0	0	1122: EPA APPROVED CMS PLAN		28APR99
180455	245	245	0	1122: Conduct CMS Bench/Pilot Studies (LOE)	29APR99	21APR00
180460	30	30	0	1122: Conduct Technical Evaluation for CMS Rpt	29APR99	10JUN99

-----

LANL CLS-1 KEITH DOWLER	FINEST HOUR	ADS 1122:TA-33, 70	BASELINE
REPORT DATE 6AUG92 RUN NO. 127	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 7NOV00
16:29		DATA DATE 1OCT91	PAGE NO. 4
1122 SCHEDULE REPORT BY EARLY START			

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
180465	30	30	0	1122: Conduct Environ Evaluation for CMS Report	29APR99	10JUN99
180470	30	30	0	1122: Conduct Human Health Eval for CMS Rpt	29APR99	10JUN99
180475	30	30	0	1122: Conduct Community Relations Eval. CMS Rpt	29APR99	10JUN99
180480	30	30	0	1122: Conduct Cost Evaluation for CMS Report	29APR99	10JUN99
180485	30	30	0	1122: Develop NEPA Documentation for CMS Report	29APR99	10JUN99
18M045	0	0	0	1122: START CMS WORK	29APR99	
18M055	0	0	0	1122: START DEVELOPMENT OF CMS REPORT	29APR99	
180490	10	10	0	1122: Prepare Internal Draft of CMS Report	11JUN99	24JUN99
180495	10	10	0	1122: LANL/VE Review Internal Draft of CMS Rpt	25JUN99	9JUL99
180500	35	35	0	1122:Incorp.LANL Rev Commt Intern Dft CMS Rpt	6MAR00	21APR00
18M050	0	0	0	1122: CMS WORK COMPLETED		21APR00
180505	10	10	0	1122: Publish DOE Draft of CMS Report	24APR00	5MAY00
180510	22	22	0	1122: Conduct Review of DOE Draft of CMS Report	8MAY00	7JUN00
180515	22	22	0	1122: Incorp. DOE Rev Commt into DOE Dft CMS Rpt	8JUN00	10JUL00
180520	10	10	0	1122: Publish EPA/NMED Draft of CMS Report	11JUL00	24JUL00
18M060	0	0	0	1122: EPA/NMED DRAFT OF CMS REPORT COMPLETED		24JUL00
180525	44	44	0	1122: Conduct EPA Review of CMS Report	25JUL00	25SEP00
180530	44	44	0	1122: Conduct NMED Review of CMS Rpt	25JUL00	25SEP00
180595	20	20	0	1122: Incorporate EPA/NMED Comments on CMS Rpt	26SEP00	24OCT00
180600	10	10	0	1122: Publish Final CMS Report	25OCT00	7NOV00
18M065	0	0	0	1122: ASSESSMENT COMPLETED		7NOV00

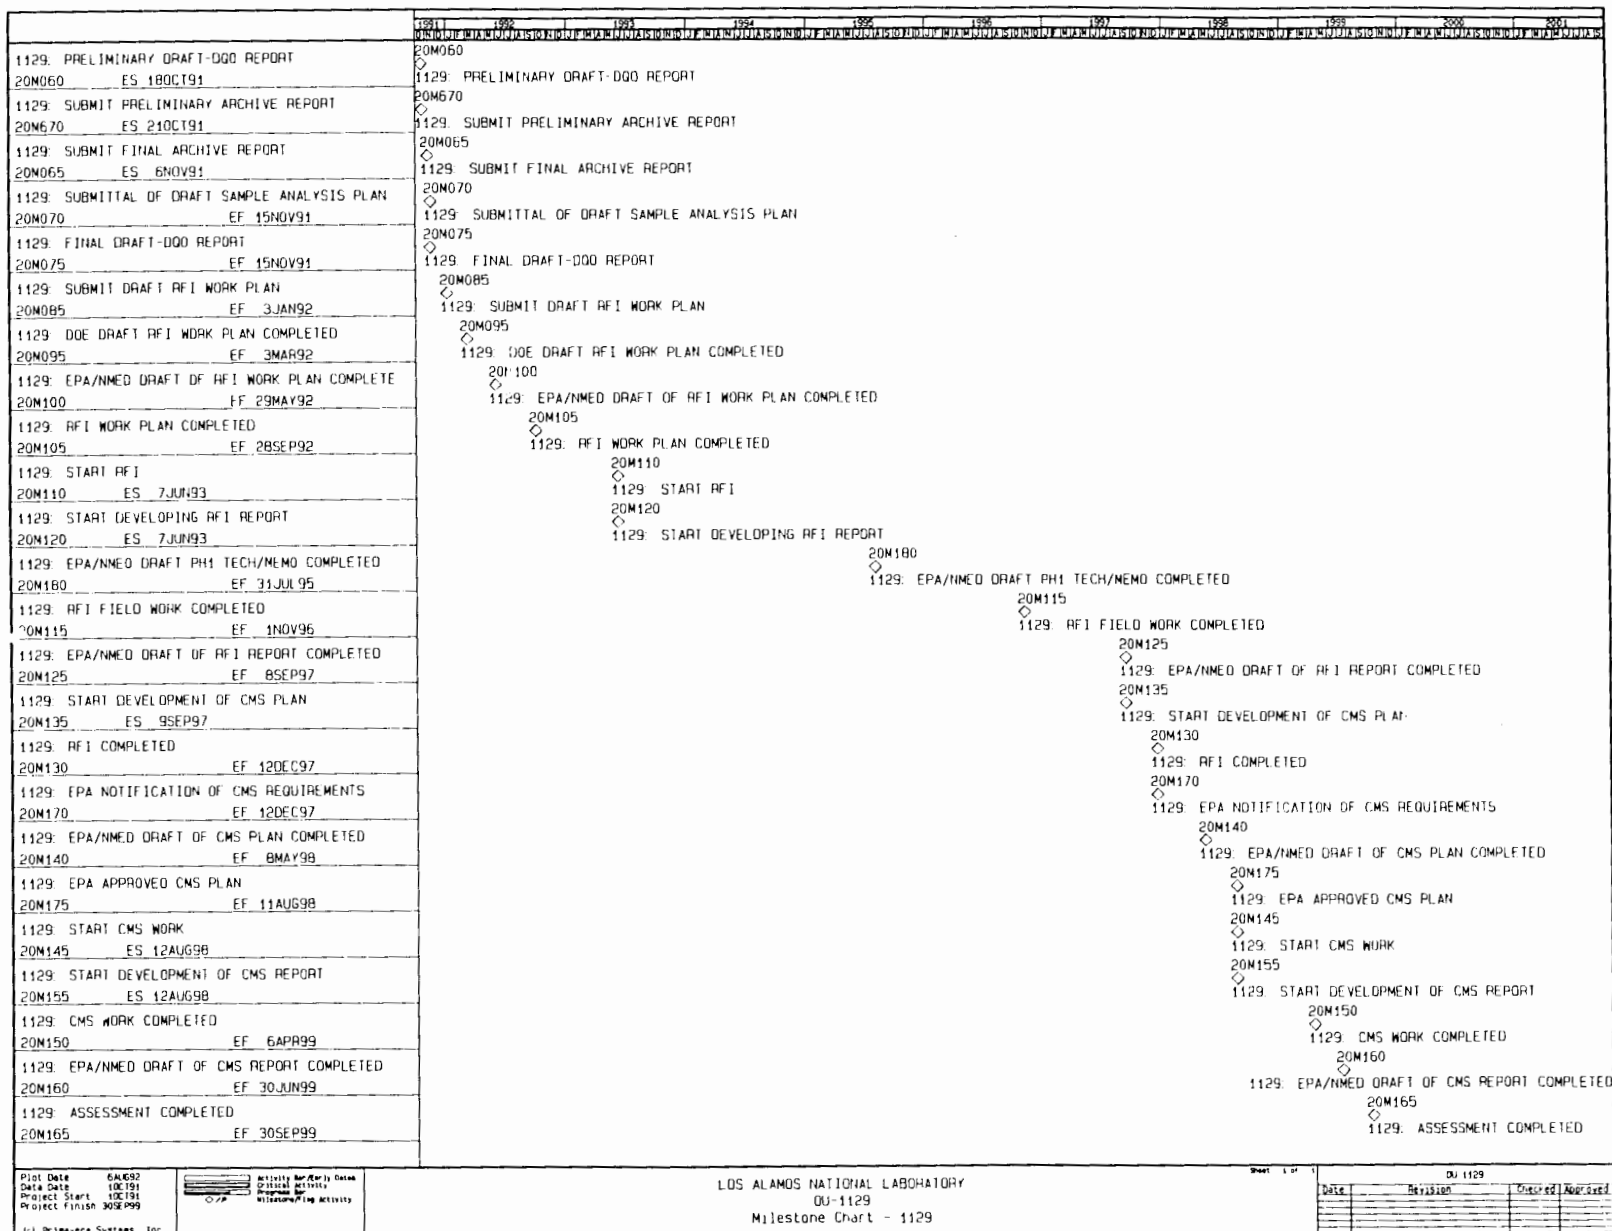

LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&66

REPORT DATE 6AUG92 RUN NO. 14  
16:40

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 30SEP99

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
200000	32	32	0	1129: Scope RFI Work Plan	1OCT91	15NOV91
200005	34	34	0	1129: Conduct Archive Search for RFI Work Plan	1OCT91	19NOV91
200010	12	12	0	1129: Assmt RFI WP-OU 1129 DOE Draft	1OCT91	17OCT91
200015	12	12	0	1129: Assmt RFI WP-OU 1129 EPA/EID DRAFT	1OCT91	17OCT91
200020	5	5	0	1129: Conduct Bench/Pilot Studies	1OCT91	8OCT91
200025	5	5	0	1129: Conduct Vol Corrective Actions	1OCT91	8OCT91
200120	245	245	0	1129: Cond Bench/Pilot Studies for RFI WP (LOE)	1OCT91	23SEP92
200125	245	245	0	1129: Cond Voluntary C.Actions for RFI WP (LOE)	1OCT91	23SEP92
200135	246	246	0	1129: Manage ADS During FY-92 (LOE)	1OCT91	24SEP92
200380	245	245	0	1129: Conduct RFI Bench/Pilot Studies (LOE)	1OCT91	23SEP92
205005	246	246	0	CONDUCT VCA (LOE) FY-92	1OCT91	24SEP92
200030	14	14	0	1129: Prepare Management Plan	18OCT91	6NOV91
200035	20	20	0	1129: Develop Data Quality Objectives for RFI WP	18OCT91	15NOV91
200045	30	30	0	1129: Prepare RFI WP QA, H&S, CR, and RMP	18OCT91	3DEC91
200055	20	20	0	1129: Prepare RFI Sampling Plans	18OCT91	15NOV91
20M060	0	0	0	1129: PRELIMINARY DRAFT-DQO REPORT	18OCT91	
20M670	0	0	0	1129: SUBMIT PRELIMINARY ARCHIVE REPORT	21OCT91	
200140	245	245	0	1129: Develop NEPA Documentation for RFI WP	30OCT91*	22OCT92
200145	40	40	0	1129: Locate Existing Data for RFI WP	30OCT91	31DEC91
20M065	0	0	0	1129: SUBMIT FINAL ARCHIVE REPORT	6NOV91	
200050	30	30	0	1129: Prepare RFI WP NEPA Documentation	15NOV91	2JAN92*
20M070	0	0	0	1129: SUBMITTAL OF DRAFT SAMPLE ANALYSIS PLAN		15NOV91
20M075	0	0	0	1129: FINAL DRAFT-DQO REPORT		15NOV91
200080	20	20	0	1129: Prepare RFI WP Internal Draft	4DEC91	3JAN92
200155	38	38	0	1129: Analyze Existing Data for RFI WP	2JAN92	26FEB92
20M085	0	0	0	1129: SUBMIT DRAFT RFI WORK PLAN		3JAN92
200090	20	20	0	1129: LANL/VE Review Internal Draft of RFI WP	6JAN92	3FEB92
200095	20	20	0	1129: Comment Resolution LANL Review Dft RFI WP	4FEB92	3MAR92
200165	20	20	0	1129: Draft Existing Data Report for RFI WP	27FEB92	25MAR92
20M095	0	0	0	1129: DOE DRAFT RFI WORK PLAN COMPLETED		3MAR92

LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&66

REPORT DATE 6AUG92 RUN NO. 14

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 30SEP99

16:40

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
200100	22	22	0	1129: DOE Review of Draft RFI Work Plan	4MAR92	2APR92
200175	40	40	0	1129: Determine Data Needs for RFI WP	26MAR92	20MAY92
200180	20	20	0	1129: Write Community Relations Plan for RFI WP	26MAR92	22APR92
200185	90	90	0	1129: Write Records Management Plan for RFI WP	26MAR92	31JUL92
200105	20	20	0	1129: Comment Resolution-DOE Revision Dft RFI WP	3APR92	30APR92
200280	21	21	0	1129: Publish EPA/NMED Draft of RFI Work Plan	27APR92*	26MAY92
200110	20	20	0	1129: Publish EPA/NMED Draft RFI Work Plan	1MAY92	29MAY92
20M100	0	0	0	1129: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		29MAY92
200285	44	44	0	1129: Conduct NMED Review of RFI WP	1JUN92	31JUL92
200290	44	44	0	1129: Conduct EPA Review of RFI Work Plan	1JUN92	31JUL92
200195	93	93	0	1129: Develop Data Quality Objectives for RFI WP	3AUG92*	16DEC92
200605	20	20	0	1129: Incorporate EPA/NMED Comments for RFI WP	3AUG92	28AUG92
200610	20	20	0	1129: Publish Final RFI Work Plan	31AUG92	28SEP92
200150	245	245	0	1129: Manage ADS During FY-93 (LOE)	25SEP92	20SEP93
205010	245	245	0	CONDUCT VCA (LOE) FY-93	25SEP92	20SEP93
20M105	0	0	0	1129: RFI WORK PLAN COMPLETED		28SEP92
200600	45	45	0	1129: Write PH1 Contracts for RFI	10CT92*	8DEC92
200115	124	124	0	1129: Regulatory Review of OU1129 Draft RFI WP	26OCT92*	27APR93
200245	22	22	0	1129: LANL/VE Review Internal Draft RFI WP	16DEC92*	20JAN93
200295	190	190	0	1129: Mobilize for RFI	4JAN93*	10CT93
200300	245	245	0	1129: Conduct RFI Bench/Pilot Studies (LOE)	4JAN93	23DEC93
200255	20	20	0	1129:Incorp.LANL Rev Comments Intern Dft RFI WP	21JAN93*	18FEB93
200265	10	10	0	1129: Publish DOE Draft of RFI WP	19FEB93*	4MAR93
200270	22	22	0	1129: Cond DOE Review of DOE Draft of RFI WP	5MAR93*	5APR93
200275	20	20	0	1129: Incorp DOE Rev.Comments into DOE Dft RFIWP	6APR93*	3MAY93
200305	82	82	0	1129: Conduct RFI PH1 Field Work	7JUN93	30SEP93
200310	82	82	0	1129: Conduct RFI PH1 Sample Analysis	7JUN93	30SEP93
200315	82	82	0	1129: Conduct RFI PH1 Data Assessment	7JUN93	30SEP93
200375	82	82	0	1129: Develop NEPA Documentation for RFI Report	7JUN93	30SEP93
20M110	0	0	0	1129: START RFI	7JUN93*	

LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&amp;66

REPORT DATE 6AUG92 RUN NO. 14

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 30SEP99

16:40

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
20M120	0	0	0	1129: START DEVELOPING RFI REPORT	7JUN93	
200595	245	245	0	1129: Assmt - Conduct VCA (LOE)	10JUN93	3JUN94
200160	249	249	0	1129: Manage ADS During FY-94 (LOE)	10CT93*	30SEP94
200306	249	249	0	1129: Conduct RFI PH1 Field Work	10CT93	30SEP94
200311	249	249	0	1129: Conduct RFI PH1 Sample Analysis	10CT93	30SEP94
200316	249	249	0	1129: Conduct RFI PH1 Data Assessment	10CT93	30SEP94
200376	28	28	0	1129: Develop NEPA Documentation for RFI Report	10CT93	10NOV93
205015	249	249	0	CONDUCT VCA (LOE) FY-94	10CT93*	30SEP94
200170	248	248	0	1129: Manage ADS During FY-95 (LOE)	30CT94	29SEP95
200307	100	100	0	1129: Conduct RFI PH1 Field Work	30CT94	2MAR95
200312	130	130	0	1129: Conduct RFI PH1 Sample Analysis	30CT94	13APR95
200317	140	140	0	1129: Conduct RFI PH1 Data Assessment	30CT94	27APR95
205020	248	248	0	CONDUCT VCA (LOE) FY-95	30CT94	29SEP95
200325	20	20	0	1129: Demobilize RFI PH1 Field Work	3MAR95	30MAR95
200320	50	50	0	1129: Write RFI PH1 Tech Memo/WP Modification	31MAR95	9JUN95
200335	20	20	0	1129: DOE Review PH1 Tech Memo/WP Modification	12JUN95	10JUL95
200336	10	10	0	1129: Incorp DOE PH1 Tech Memo/WP Mod. Comments	11JUL95	24JUL95
200337	5	5	0	1129: Issue EPA/NMED Draft PH1 Tech Memo/WP	25JUL95	31JUL95
20M180	0	0	0	1129: EPA/NMED DRAFT PH1 TECH/MEMO COMPLETED		31JUL95
200330	20	20	0	1129: EPA/NMED Rev PH1 Tech Memo/WP Modification	1AUG95	28AUG95
200331	10	10	0	1129: Incorp EPA/NMED PH1 Tech Memo/WP Comments	29AUG95	12SEP95
200332	5	5	0	1129: Issue Final EPA/NMED PH1 Tech Memo/WP Rpt	13SEP95	19SEP95
200340	15	15	0	1129: Write PH2 Contract; Mobilize for RFI	20SEP95	11OCT95
200190	249	249	0	1129: Manage ADS During FY-96 (LOE)	20CT95	30SEP96
205025	249	249	0	CONDUCT VCA (LOE) FY-96	20CT95	30SEP96
200345	245	245	0	1129: Conduct RFI PH2 Field Work	12OCT95	30CT96
200350	275	275	0	1129: Conduct RFI PH2 Sample Analysis	12OCT95	18NOV96
200370	285	285	0	1129: Conduct RFI PH2 Data Assessment	12OCT95	4DEC96
200200	249	249	0	1129: Manage ADS During FY-97 (LOE)	10CT96	30SEP97
205030	249	249	0	CONDUCT VCA (LOE) FY-97	10CT96	30SEP97

LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&66

REPORT DATE 6AUG92 RUN NO. 14  
16:40

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 30SEP99

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
640000	249	249	0	CONDUCT VCA - FY97	1OCT96*	30SEP97
200355	20	20	0	1129: Demoblize RFI PH2 Field Work	4OCT96	1NOV96
200360	80	80	0	1129: Conduct RFI Report Facility Investigation	4OCT96	4FEB97
200365	90	90	0	1129: Conduct RFI Report Investigation Analysis	4OCT96	19FEB97
20M115	0	0	0	1129: RFI FIELD WORK COMPLETED		1NOV96
200385	90	90	0	1129: Prepare Internal Draft of RFI Report	4NOV96	19MAR97
200395	20	20	0	1129: LANL/VE Review Internal Draft of RFI Rpt	20MAR97	16APR97
200405	20	20	0	1129:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	17APR97	14MAY97
200410	20	20	0	1129: Publish DOE Draft of RFI Report	15MAY97	12JUN97
200415	20	20	0	1129: Conduct Review of DOE Draft of RFI Report	13JUN97	11JUL97
200420	20	20	0	1129: Incorp. DOE Rev. Comments DOE Drft RFI Rpt	14JUL97	8AUG97
200425	20	20	0	1129: Publish EPA/NMED Draft of RFI Report	11AUG97	8SEP97
20M125	0	0	0	1129: EPA/NMED DRAFT OF RFI REPORT COMPLETED		8SEP97
200430	40	40	0	1129: Conduct EPA Review of RFI Report	9SEP97	4NOV97
200435	40	40	0	1129: Conduct NMED Review of RFI Rpt	9SEP97	4NOV97
200440	245	245	0	1129: Conduct Bench/Pilot Studies for CMS Pl LOE	9SEP97	1SEP98
200445	30	30	0	1129: Establish Current Situation for CMS Plan	9SEP97	21OCT97
200450	30	30	0	1129: Establish CA Objectives for CMS Plan	9SEP97	21OCT97
200455	30	30	0	1129: Develop Screening Technologies for CMS Pl	9SEP97	21OCT97
200460	245	245	0	1129: Develop NEPA Documentation for CMS Plan	9SEP97	1SEP98
20M135	0	0	0	1129: START DEVELOPMENT OF CMS PLAN	9SEP97	
200210	249	249	0	1129: Manage ADS During FY-98 (LOE)	1OCT97	30SEP98
205035	249	249	0	CONDUCT VCA (LOE) FY-98	1OCT97	30SEP98
640005	249	249	0	CONDUCT VCA - FY98	1OCT97	30SEP98
200465	35	35	0	1129: Develop Alternatives for CMS Plan	22OCT97	12DEC97
200630	15	15	0	1129: Incorporate EPA/NMED Comments for RFI Rpt	5NOV97	26NOV97
200635	10	10	0	1129: Publish Final RFI Report	1DEC97	12DEC97
20M130	0	0	0	1129: RFI COMPLETED		12DEC97
20M170	0	0	0	1129: EPA NOTIFICATION OF CMS REQUIREMENTS		12DEC97
200470	35	35	0	1129: Develop Internal Draft of CMS Plan	15DEC97	5FEB98



LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&amp;66

REPORT DATE 6AUG92 RUN NO. 14

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 30SEP99

16:40

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
200475	10	10	0	1129: LANL/VE Review Internal Draft of CMS Plan	6FEB98	20FEB98
200480	10	10	0	1129: Incorp. LANL REV Comments Intern Dft CMSPL	23FEB98	6MAR98
200485	5	5	0	1129: Publish DOE Draft of CMS Plan	9MAR98	13MAR98
200490	20	20	0	1129: Conduct Review of DOE Draft of CMS Plan	16MAR98	10APR98
200495	15	15	0	1129: Incorp. DOE Rev.Comments DOE Dft of CMS PL	13APR98	1MAY98
200500	5	5	0	1129: Publish EPA/NMED Draft of CMS Plan	4MAY98	8MAY98
20M140	0	0	0	1129: EPA/NMED DRAFT OF CMS PLAN COMPLETED		8MAY98
200505	40	40	0	1129: Conduct EPA Review of CMS Plan	11MAY98	7JUL98
200510	40	40	0	1129: Conduct NMED Review of CMS Plan	11MAY98	7JUL98
200640	15	15	0	1129: Incorporate EPA/NMED Comments on CMS Plan	8JUL98	28JUL98
200645	5	5	0	1129: Publish Final CMS Plan	29JUL98	4AUG98
200650	5	5	0	1129: EPA Approves CMS Plan	5AUG98	11AUG98
20M175	0	0	0	1129: EPA APPROVED CMS PLAN		11AUG98
200515	160	160	0	1129: Conduct CMS Bench/Pilot Studies (LOE)	12AUG98	6APR99
200520	30	30	0	1129: Conduct Technical Evaluation for CMS Rpt	12AUG98	23SEP98
200525	30	30	0	1129: Conduct Environmental Eval for CMS Report	12AUG98	23SEP98
200530	30	30	0	1129: Conduct Human Health Eval for CMS Report	12AUG98	23SEP98
200535	30	30	0	1129: Conduct Community Relations Eval CMS Rpt	12AUG98	23SEP98
200540	30	30	0	1129: Conduct Cost Evaluation for CMS Report	12AUG98	23SEP98
200545	30	30	0	1129: Develop NEPA Documentation for CMS Report	12AUG98	23SEP98
20M145	0	0	0	1129: START CMS WORK	12AUG98	
20M155	0	0	0	1129: START DEVELOPMENT OF CMS REPORT	12AUG98	
200550	10	10	0	1129: Prepare Internal Draft of CMS Report	24SEP98	7OCT98
200230	249	249	0	1129: Manage ADS During FY-99 (LOE)	1OCT98	30SEP99
205040	87	87	0	CONDUCT VCA (LOE) FY-99	1OCT98	10FEB99
200555	10	10	0	1129: LANL/VE Review Internal Draft of CMS Rpt	8OCT98	22OCT98
200560	20	20	0	1129:Incorp.LANL Rev Comments Intern Dft CMS Rpt	10MAR99	6APR99
20M150	0	0	0	1129: CMS WORK COMPLETED		6APR99*
200565	10	10	0	1129: Publish DOE Draft of CMS Report	7APR99	20APR99
200570	20	20	0	1129: Conduct Review of DOE Draft of CMS Report	21APR99	18MAY99

LANL EES-13 ALLYN PRATT

FINEST HOUR

ADS 1129:TA-4,5,35,42,48,52,55,63&66

REPORT DATE 6AUG92 RUN NO. 14

ENVIRONMENTAL RESTORATION


START DATE 1OCT91 FIN DATE 30SEP99

16:40

1129 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 6

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
200575	20	20	0	1129: Incorp. DOE Rev Comments DOE Dft CMS Rpt	19MAY99	16JUN99
200580	10	10	0	1129: Publish EPA/NMED Draft of CMS Report	17JUN99	30JUN99
20M160	0	0	0	1129: EPA/NMED DRAFT OF CMS REPORT COMPLETED		30JUN99
200585	40	40	0	1129: Conduct EPA Review of CMS Report	1JUL99	26AUG99
200590	40	40	0	1129: Conduct NMED Review of CMS Report	1JUL99	26AUG99
200655	14	14	0	1129: Incorporate EPA/NMED Comments CMS Report	27AUG99	16SEP99
200660	10	10	0	1129: Publish Final CMS Report	17SEP99	30SEP99
20M165	0	0	0	1129: ASSESSMENT COMPLETED		30SEP99

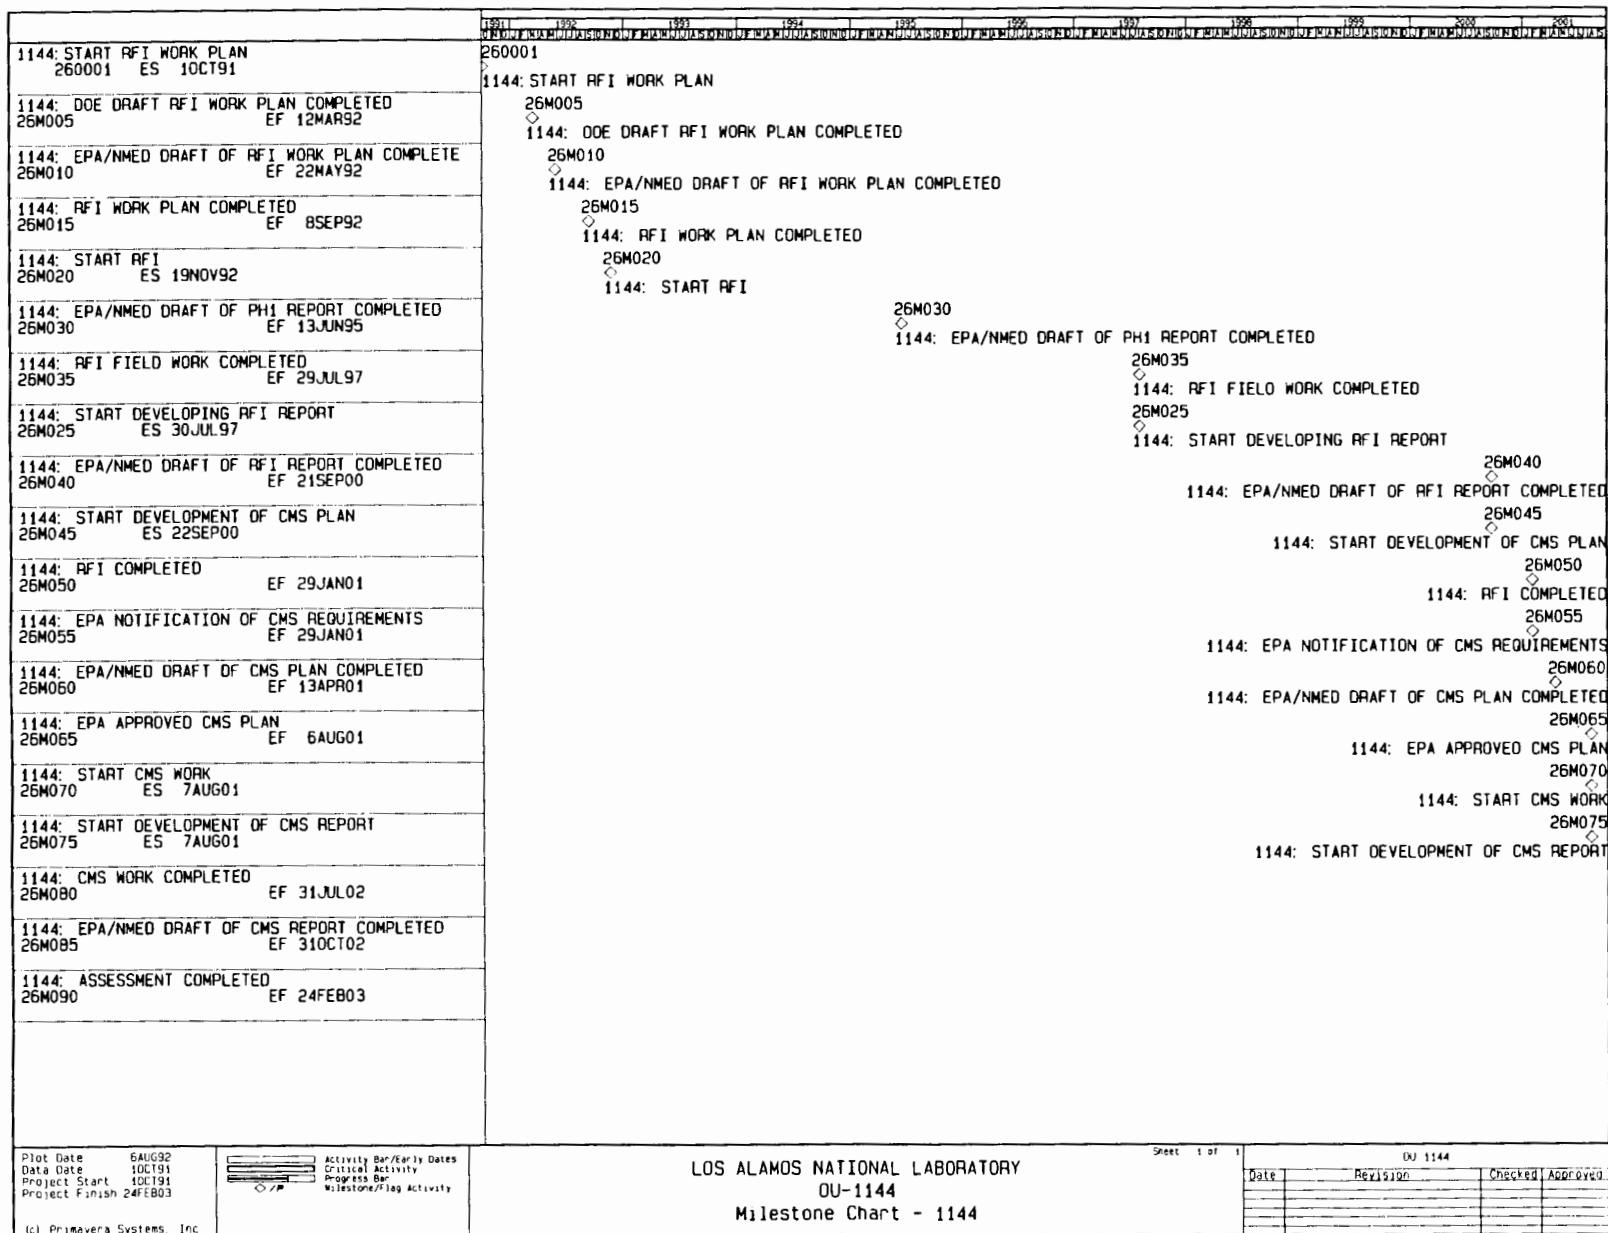

LANL INC-DO G. ELLER  
 REPORT DATE 7AUG92 RUN NO. 53  
 1144 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

ADS 1144: TA-49  
 START DATE 10CT91  
 DATA DATE 10CT91

TBS 2/17/92  
 FIN DATE 24FEB03  
 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
260001	0	0	0	1144:START RFI WORK PLAN	10CT91	
260005	250	250	0	1144:Conduct Voluntary C. Actions for RFI WP LOE	10CT91	30SEP92
260008	20	20	0	1144:Write Community Relations Plan	10CT91	29OCT91
260009	20	20	0	1144:Write Management Plan for RFI WP	10CT91	29OCT91
260010	20	20	0	1144:Write Health and Safety Plan for RFI WP	10CT91	29OCT91
260015	250	250	0	1144: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
260025	250	250	0	1144: Develop NEPA Documentation for RFI WP(LOE)	10CT91	30SEP92
260065	40	40	0	1144: Develop Sampling Plan for RFI WP	10CT91	27NOV91
260090	80	80	0	1144: Develop LANL Internal Draft of RFI WP	10CT91	30JAN92
260095	10	10	0	1144: LANL/VE Review Internal Draft RFI WP	31JAN92	13FEB92
260100	10	10	0	1144: Incorp.LANL Rev Comments Intern Dft RFI WP	14FEB92	28FEB92
260105	9	9	0	1144: Issue DOE Draft of RFI WP	2MAR92	12MAR92
26M005	0	0	0	1144: DOE DRAFT RFI WORK PLAN COMPLETED		12MAR92
260110	11	11	0	1144: Cond DOE Review of DOE Dft of RFI WP	13MAR92	27MAR92
260115	10	10	0	1144:Incorp DOE Rev.Comments into DOE Dft RFI WP	30MAR92	10APR92
260120	30	30	0	1144: Issue EPA/NMED Draft of RFI Work Plan	13APR92	22MAY92
26M010	0	0	0	1144: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		22MAY92
260125	44	44	0	1144: Conduct NMED Review of RFI Work Plan	26MAY92	27JUL92
260130	44	44	0	1144: Conduct EPA Review of RFI Work Plan	26MAY92	27JUL92
260140	20	20	0	1144: Incorporate EPA/NMED Comments for RFI WP	28JUL92	24AUG92
260145	10	10	0	1144: Issue Final RFI Work Plan	25AUG92	8SEP92
26M015	0	0	0	1144: RFI WORK PLAN COMPLETED		8SEP92
260135	46	46	0	1144: Write Ph1 Contracts for RFI;Mobilize	14SEP92	18NOV92
260510	169	169	0	1144: Conduct MDA AB Pilot/Study FY-92 (LOE)	14SEP92	19MAY93
260070	249	249	0	1144: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
26M020	0	0	0	1144: START RFI	19NOV92	
260165	491	491	0	1144: Conduct RFI PH1 Field Work	2FEB93	23JAN95
260170	530	530	0	1144: Conduct RFI PH1 Sample Analysis	2FEB93	20MAR95
260175	530	530	0	1144: Conduct RFI PH1 Data Assessment	2FEB93	20MAR95
260160	250	250	0	1144: Manage ADS During FY-94 (LOE)	10CT93	30SEP94

LANL INC-DO	G. ELLER	FINEST HOUR	ADS 1144: TA-49	TBS 2/17/92
REPORT DATE	7AUG92	RUN NO. 53	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 24FEB03
1144 SCHEDULE	REPORT BY	EARLY START	DATA DATE 10CT91	PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
260185	247	247	0	1144: Manage ADS During FY-95 (LOE)	30OCT94	29SEP95
260195	20	20	0	1144: Demobilize RFI PH1 Field Work	24JAN95	21FEB95
260190	60	60	0	1144: Write RFI PH1 Report/WP Modification	21MAR95	13JUN95
26M030	0	0	0	1144: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		13JUN95
260200	22	22	0	1144: EPA/NMED Rev PH1 Report/WP Modification	14JUN95	14JUL95
260205	22	22	0	1144: DOE Review PH1 Report/WP Modification	14JUN95	14JUL95
260210	20	20	0	1144: Write PH2 Contract; Mobilize for RFI	14JUN95	12JUL95
260215	490	490	0	1144: Conduct RFI PH2 Field Work	13JUL95	30JUN97
260220	490	490	0	1144: Conduct RFI PH2 Sample Analysis	13JUL95	30JUN97
260225	490	490	0	1144: Conduct RFI PH2 Data Assessment	13JUL95	30JUN97
260230	249	249	0	1144: Manage ADS During FY-96 (LOE)	20OCT95	30SEP96
260255	249	249	0	1144: Manage ADS During FY-97 (LOE)	10OCT96	30SEP97
690000	189	189	0	1144: Conduct VCA (LOE)	2JAN97*	30SEP97
260235	100	100	0	1144: Conduct RFI Report Facility Investigation	1JUL97	25NOV97
260240	110	110	0	1144: Conduct RFI Report Investigation Analysis	1JUL97	9DEC97
260245	20	20	0	1144: Demobilize RFI PH2 Field Work	1JUL97	29JUL97
26M035	0	0	0	1144: RFI FIELD WORK COMPLETED		29JUL97
260180	491	491	0	1144: Develop NEPA Documentation for RFI Report	30JUL97	20JUL99
26M025	0	0	0	1144: START DEVELOPING RFI REPORT	30JUL97	
260290	249	249	0	1144: Manage ADS During FY-98 (LOE)	10OCT97	30SEP98
690005	249	249	0	1144: Conduct VCA (LOE)	10OCT97	30SEP98
260155	249	249	0	1144: Assmt - Conduct VCA (LOE)	10OCT98	30SEP99
260410	249	249	0	1144: Manage ADS During FY-99 (LOE)	10OCT98	30SEP99
260250	132	132	0	1144: Prepare Internal Draft of RFI Report	21JUL99	2FEB00
260412	95	95	0	1144: Manage ADS During FY 2000	10OCT99	23FEB00
260260	20	20	0	1144: LANL/VE Review Internal Draft of RFI Rpt	3FEB00	2MAR00
260265	40	40	0	1144:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	3MAR00	27APR00
260270	20	20	0	1144: Issue DOE Draft of RFI Report	28APR00	25MAY00
260275	22	22	0	1144: Conduct DOE Review of DOE Draft of RFI Rpt	26MAY00	27JUN00
260280	40	40	0	1144: Incorp. DOE Rev. Comments DOE Drft RFI Rpt	28JUN00	23AUG00

-----

LANL INC-DO	G. ELLER	FINEST HOUR	ADS 1144: TA-49	TBS 2/17/92
REPORT DATE	7AUG92	RUN NO. 53	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 24FEB03
	7:38			
1144 SCHEDULE	REPORT BY EARLY START		DATA DATE 10CT91	PAGE NO. 3


-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
260285	20	20	0	1144: Issue EPA/NMED Draft of RFI Report	24AUG00	21SEP00
26M040	0	0	0	1144: EPA/NMED DRAFT OF RFI REPORT COMPLETED		21SEP00
260295	44	44	0	1144: Conduct EPA Review of RFI Report	22SEP00	28NOV00
260300	44	44	0	1144: Conduct NMED Review of RFI Report	22SEP00	28NOV00
260305	245	245	0	1144: Conduct Bench/Pilot Studies for CMS Pl (LOE)	22SEP00	17SEP01
260310	35	35	0	1144: Establish Current Situation for CMS Plan	22SEP00	13NOV00
260315	35	35	0	1144: Establish CA Objectives for CMS Plan	22SEP00	13NOV00
260320	35	35	0	1144: Develop Screening Technologies for CMS Pl	22SEP00	13NOV00
26M045	0	0	0	1144: START DEVELOPMENT OF CMS PLAN	22SEP00	
260325	248	248	0	1144: Develop NEPA Documentation for CMS Plan	20CT00*	28SEP01
260330	15	15	0	1144: Develop Alternatives for CMS Plan	14NOV00	6DEC00
260335	20	20	0	1144: Incorporate EPA/NMED Comments on RFI Rpt	29NOV00	28DEC00
260340	10	10	0	1144: Develop Internal Draft of CMS Plan	7DEC00	20DEC00
260345	10	10	0	1144: LANL/VE Review Internal Draft of CMS Plan	21DEC00	8JAN01
260350	20	20	0	1144: Issue Final RFI Report	29DEC00	29JAN01
260355	10	10	0	1144: Incorp. LANL REV Comments Intern Dft CMS Pl	9JAN01	23JAN01
260360	5	5	0	1144: Issue DOE Draft of CMS Plan	24JAN01	30JAN01
26M050	0	0	0	1144: RFI COMPLETED		29JAN01
26M055	0	0	0	1144: EPA NOTIFICATION OF CMS REQUIREMENTS		29JAN01
260365	22	22	0	1144: Conduct DOE Review of Draft of CMS Plan	31JAN01	2MAR01
260370	20	20	0	1144: Incorp DOE Rev Comments DOE Dft of CMS Pl	5MAR01	30MAR01
260375	10	10	0	1144: Issue EPA/NMED Draft of CMS Plan	2APR01	13APR01
26M060	0	0	0	1144: EPA/NMED DRAFT OF CMS PLAN COMPLETED		13APR01
260380	44	44	0	1144: Conduct EPA Review of CMS Plan	16APR01	15JUN01
260385	44	44	0	1144: Conduct NMED Review of CMS Plan	16APR01	15JUN01
260390	20	20	0	1144: Incorporate EPA/NMED Comments on CMS Plan	18JUN01	16JUL01
260395	10	10	0	1144: Issue Final CMS Plan	17JUL01	30JUL01
260400	5	5	0	1144: EPA Approves CMS Plan	31JUL01	6AUG01
26M065	0	0	0	1144: EPA APPROVED CMS PLAN		6AUG01
260405	245	245	0	1144: Conduct CMS Bench/Pilot Studies (LOE)	7AUG01	31JUL02

LANL INC-DO G. ELLER  
 REPORT DATE 7AUG92 RUN NO. 53 ENVIRONMENTAL RESTORATION  
 7:38  
 1144 SCHEDULE REPORT BY EARLY START

ADS 1144: TA-49 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 24FEB03  
 DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
260415	30	30	0	1144: Conduct Technical Evaluation for CMS Rpt	7AUG01	18SEP01
260420	30	30	0	1144: Cond Environmental Evaluation for CMS Rpt	7AUG01	18SEP01
260425	30	30	0	1144: Cond Human Health Evaluation for CMS Rpt	7AUG01	18SEP01
260430	30	30	0	1144: Cond Community Relations Eval.for CMS Rpt	7AUG01	18SEP01
260435	30	30	0	1144: Conduct Cost Evaluation for CMS Report	7AUG01	18SEP01
260440	30	30	0	1144: Develop NEPA Documentation for CMS Report	7AUG01	18SEP01
26M070	0	0	0	1144: START CMS WORK	7AUG01	
26M075	0	0	0	1144: START DEVELOPMENT OF CMS REPORT	7AUG01	
260450	10	10	0	1144: Prepare Internal Draft of CMS Report	19SEP01	20CT01
260455	10	10	0	1144: LANL/VE Rev Internal Draft of CMS Report	30CT01	17OCT01
260460	35	35	0	1144:Incorp LANL Rev Comments Intern.Dft CMS Rpt	12JUN02	31JUL02
26M080	0	0	0	1144: CMS WORK COMPLETED		31JUL02
260465	10	10	0	1144: Issue DOE Draft of CMS Report	1AUG02	14AUG02
260470	22	22	0	1144: Conduct Review of DOE Draft of CMS Report	15AUG02	16SEP02
260475	22	22	0	1144: Incorp. DOE Rev Comments DOE Dft CMS Rpt	17SEP02	17OCT02
260480	10	10	0	1144: Issue EPA/NMED Draft of CMS Report	18OCT02	31OCT02
26M085	0	0	0	1144: EPA/NMED DRAFT OF CMS REPORT COMPLETED		31OCT02
260485	44	44	0	1144: Conduct EPA Review of CMS Report	1NOV02	9JAN03
260490	44	44	0	1144: Conduct NMED Review of CMS Report	1NOV02	9JAN03
260495	20	20	0	1144: Incorporate EPA/NMED Comments on CMS Rpt	10JAN03	7FEB03
260505	10	10	0	1144: Issue Final CMS Report	10FEB03	24FEB03
26M090	0	0	0	1144: ASSESSMENT COMPLETED		24FEB03

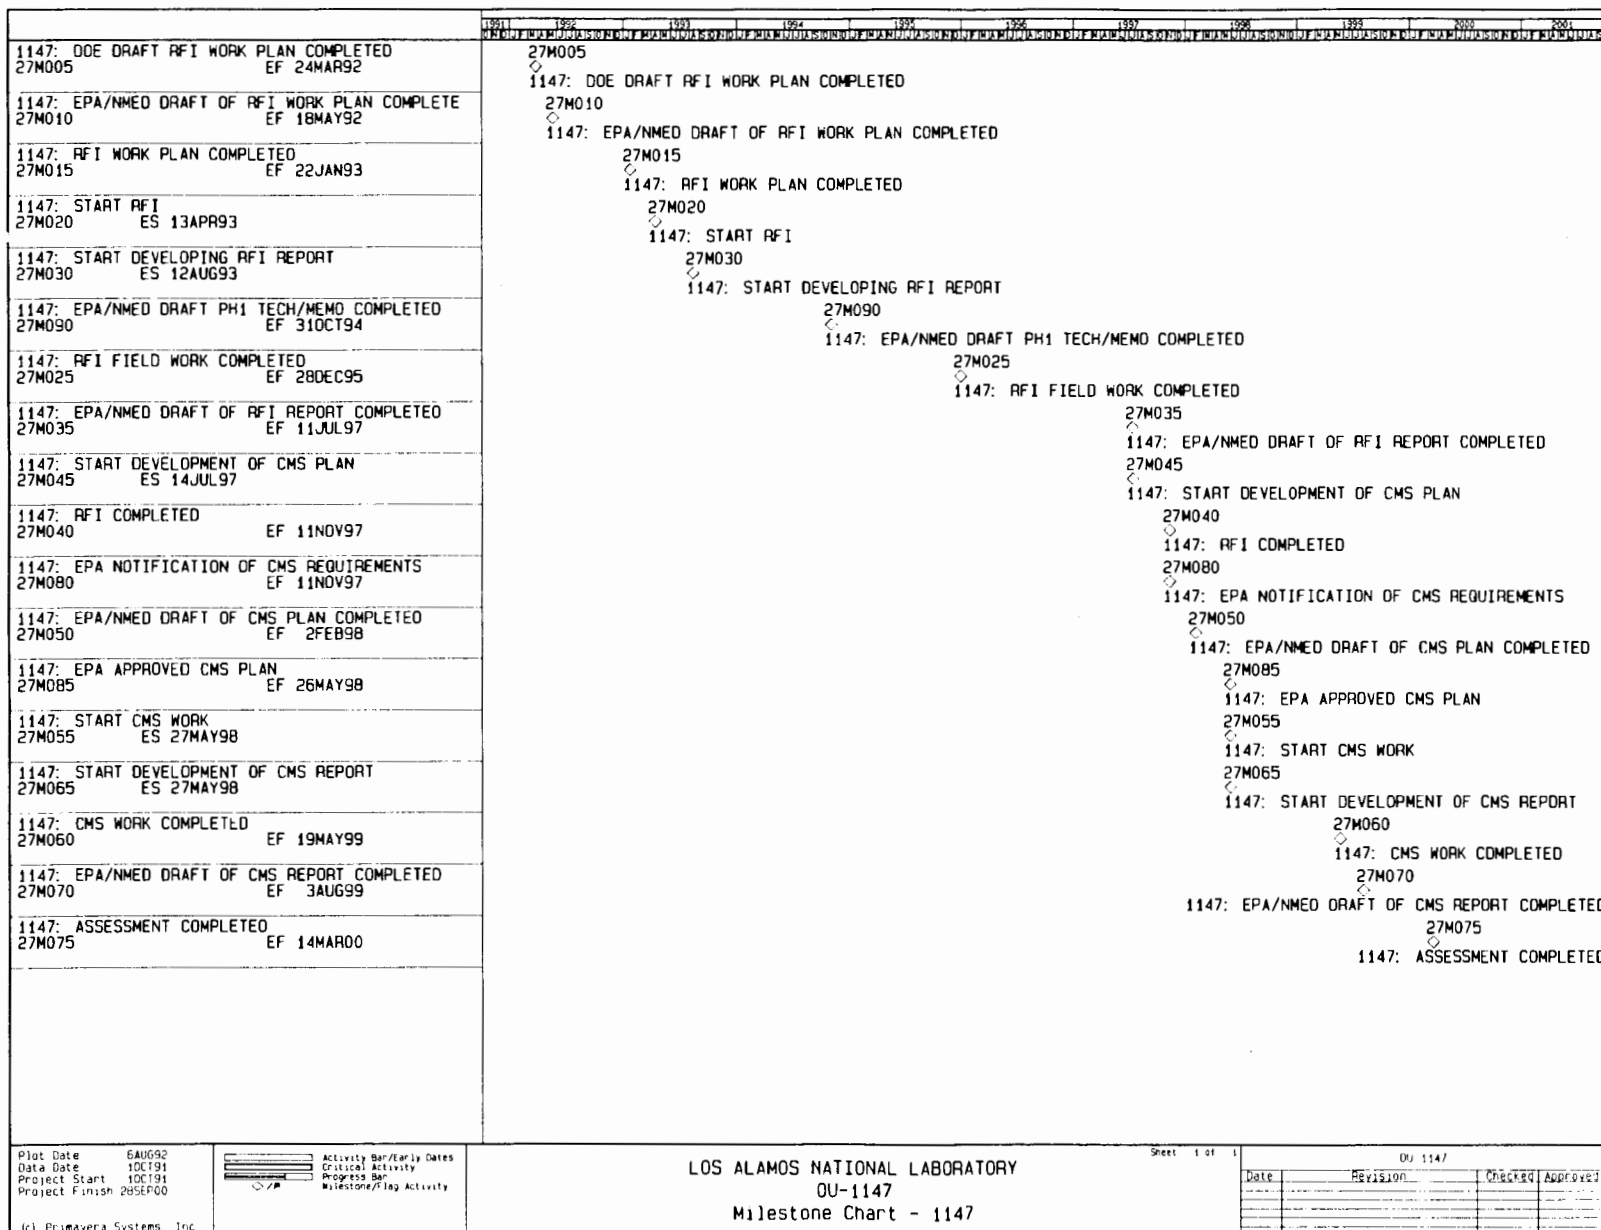



LANL EES-1 C. ROFER

FINEST HOUR

ADS 1147: TA-50

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 25

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 28SEP00

17:58

1147 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
270015	250	250	0	1 523 7	1147: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
270310	65	65	0	1 523 113	1147: Develop NEPA Documentation for RFI WP	10CT91	8JAN92
270590	12	12	0	1 523 1	1147: Scope RFI Work Plan	10CT91	17OCT91
270595	40	40	0	1 523 1	1147: Analyze Existing Data & Deter RFI Data Nds	10CT91	27NOV91
270620	77	77	0	1 523 1	1147: Write RFI Sampling Plans	10CT91	27JAN92
270115	76	76	0	1 523 1 7	1147: Develop LANL Internal Draft of RFI WP	20CT91	27JAN92
270125	20	20	0	1 523 3 7	1147: LANL/VE Review Internal Draft RFI Report	28JAN92	25FEB92
270135	20	20	0	1 523 1 7	1147: Incorp LANL Rev Comments in Int Dft RFI WP	11FEB92	10MAR92
270145	10	10	0	1 523 1 9	1147: Publish DOE Draft of RFI Work Plan	11MAR92	24MAR92
27M005	0	0	0	1 523 1 9	1147: DOE DRAFT RFI WORK PLAN COMPLETED		24MAR92
270150	22	22	0	1 523 1 9	1147: Cond DOE Review of DOE Draft of RFI WP	25MAR92	23APR92
270155	20	20	0	1 523 1 9	1147: Incorp DOE Rev. Comments in DOE Dft RFI WP	21APR92	18MAY92
270160	5	5	0	1 523 110	1147: Publish EPA/NMED Draft of RFI Work Plan	12MAY92	18MAY92
27M010	0	0	0	1 523 110	1147: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		18MAY92
270170	44	44	0	1 523 110	1147: Conduct EPA Review of RFI Work Plan	19MAY92	21JUL92
270030	249	249	0	1 523 7	1147: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
270165	44	44	0	1 523 110	1147: Conduct NMED Review of RFI Work Plan	10CT92*	7DEC92
270530	20	20	0	1 523 110	1147: Incorporate EPA/NMED Comments RFI WP	8DEC92	7JAN93
270525	65	65	0	1 523 210	1147: Write PH1 Contracts for RFI; Mobilize	8JAN93	12APR93
270535	10	10	0	1 523 110	1147: Publish Final RFI Work Plan	8JAN93	22JAN93
27M015	0	0	0	1 523 1	1147: RFI WORK PLAN COMPLETED		22JAN93
27M020	0	0	0	1 523 2	1147: START RFI		13APR93
270185	245	245	0	1 523 2 2	1147: Conduct RFI PH1 Field Work	12AUG93*	4AUG94
270190	245	245	0	1 523 2 4	1147: Conduct RFI PH1 Sample Analysis	12AUG93*	4AUG94
270195	245	245	0	1 523 2 5	1147: Conduct RFI PH1 Data Assessment	12AUG93*	4AUG94
27M030	0	0	0	1 523 3	1147: START DEVELOPING RFI REPORT		12AUG93
270040	250	250	0	1 523 7	1147: Manage ADS During FY-94 (LOE)	10CT93	30SEP94
270200	60	60	0	1 523 2 6	1147: Write RFI PH1 Tech Memo/WP Modification	5AUG94	31OCT94
270205	20	20	0	1 523 2 1	1147: Demobilize RFI PH1 Field Work	5AUG94	1SEP94
270050	247	247	0	1 523 7	1147: Manage ADS During FY-95 (LOE)	30CT94	29SEP95

LANL EES-1 C. ROFER  
 REPORT DATE 6AUG92 RUN NO. 25 ENVIRONMENTAL RESTORATION  
 17:58  
 1147 SCHEDULE REPORT BY EARLY START

ADS 1147: TA-50 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 28SEP00  
 DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
27M090	0	0	0	1 523 2	1147: EPA/NMED DRAFT PH1 TECH/MEMO COMPLETED		31OCT94
270210	22	22	0	1 523 2 6	1147: EPA/NMED Rev PH1 Tech Memo/WP Modification	1NOV94	5DEC94
270215	22	22	0	1 523 2 6	1147: DOE Review PH1 Tech Memo/WP Modification	1NOV94	5DEC94
270220	20	20	0	1 523 2 7	1147: Write PH2 Contract; Mobilize for RFI	1NOV94	1DEC94
270225	245	245	0	1 523 2 8	1147: Conduct RFI PH2 Field Work	2DEC94	28NOV95
270230	245	245	0	1 523 210	1147: Conduct RFI PH2 Sample Analysis	2DEC94	28NOV95
270240	245	245	0	1 523 211	1147: Conduct RFI PH2 Data Assessment	2DEC94	28NOV95
270070	249	249	0	1 523 7	1147: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
270235	20	20	0	1 523 2 7	1147: Demoblize RFI PH2 Field Work	29NOV95	28DEC95
270300	100	100	0	1 523 3 1	1147: Conduct RFI Report Facility Investigation	29NOV95	23APR96
270305	110	110	0	1 523 3 2	1147: Conduct RFI Report Investigation Analysis	29NOV95	7MAY96
27M025	0	0	0	1 523 2	1147: RFI FIELD WORK COMPLETED		28DEC95
270320	132	132	0	1 523 3 8	1147: Prepare Internal Draft of RFI Report	8MAY96	14NOV96
270080	249	249	0	1 523 7	1147: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
270325	20	20	0	1 523 3 4	1147: LANL/VE Review Internal Draft of RFI Rpt	15NOV96	16DEC96
270330	40	40	0	1 523 3 4	1147: Incorp.LANL Rev.Comments Int Dft RFI Rpt	17DEC96	14FEB97
700000	189	189	0	1 523 8	2113: Remed - Conduct VCA (LOE)	2JAN97*	30SEP97
270335	20	20	0	1 523 3 5	1147: Publish DOE Draft of RFI Report	18FEB97	17MAR97
270340	22	22	0	1 523 3 6	1147: Conduct DOE Review of DOE Draft of RFI Rpt	18MAR97	16APR97
270345	40	40	0	1 523 3 6	1147: Incorp. DOE Rev. Comments DOE Drft RFI Rpt	17APR97	12JUN97
270350	20	20	0	1 523 3 7	1147: Publish EPA/NMED Draft of RFI Report	13JUN97	11JUL97
27M035	0	0	0	1 523 3 7	1147: EPA/NMED DRAFT OF RFI REPORT COMPLETED		11JUL97
270355	44	44	0	1 523 3 7	1147: Conduct EPA Review of RFI Report	14JUL97	12SEP97
270360	44	44	0	1 523 3 7	1147: Conduct NMED Review of RFI Report	14JUL97	12SEP97
270365	245	245	0	1 523 4 5	1147:Cond Bench/Pilot Studies for CMS Plan (LOE)	14JUL97	7JUL98
270370	35	35	0	1 523 4 1	1147: Establish Current Situation for CMS Plan	14JUL97	29AUG97
270375	35	35	0	1 523 4 2	1147: Establish CA Objectives for CMS Plan	14JUL97	29AUG97
270380	35	35	0	1 523 4 3	1147: Dev Screening Technologies for CMS Plan	14JUL97	29AUG97
270385	245	245	0	1 523 413	1147: Develop NEPA Documentation for CMS Plan	14JUL97	7JUL98
27M045	0	0	0	1 523 4	1147: START DEVELOPMENT OF CMS PLAN	14JUL97	

LANL EES-1 C. ROFER

FINEST HOUR

ADS 1147: TA-50

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 25  
17:58

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 28SEP00

1147 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
270390	15	15	0	1 523 4 4	1147: Develop Alternatives for CMS Plan	2SEP97	22SEP97
270555	20	20	0	1 523 3 7	1147: Incorporate EPA/NMED Comments on RFI Rpt	15SEP97	10OCT97
270395	10	10	0	1 523 4 6	1147: Develop Internal Draft of CMS Plan	23SEP97	6OCT97
270090	249	249	0	1 523 7	1147: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
700005	249	249	0	1 523 8	2113: Remed - Conduct VCA (LOE)	10CT97	30SEP98
270400	10	10	0	1 523 4 6	1147: LANL/VE Review Internal Draft of CMS Plan	7OCT97	21OCT97
270560	20	20	0	1 523 3 7	1147: Publish Final RFI Report	14OCT97	11NOV97
270405	10	10	0	1 523 4 6	1147:Incorp. LANL REV Comments Intern Dft CMS PL	22OCT97	4NOV97
270410	5	5	0	1 523 4 8	1147: Publish DOE Draft of CMS Plan	5NOV97	12NOV97
27M040	0	0	0	1 523 3	1147: RFI COMPLETED		11NOV97
27M080	0	0	0	1 523 6	1147: EPA NOTIFICATION OF CMS REQUIREMENTS		11NOV97
270415	22	22	0	1 523 4 8	1147: Conduct DOE Review of Draft of CMS Plan	13NOV97	16DEC97
270420	20	20	0	1 523 4 8	1147:Incorp. DOE Rev.Comments DOE Dft.of CMS PL	17DEC97	19JAN98
270425	10	10	0	1 523 4 9	1147: Publish EPA/NMED Draft of CMS Plan	20JAN98	2FEB98
27M050	0	0	0	1 523 4 9	1147: EPA/NMED DRAFT OF CMS PLAN COMPLETED		2FEB98
270430	44	44	0	1 523 4 9	1147: Conduct EPA Review of CMS Plan	3FEB98	6APR98
270435	44	44	0	1 523 4 9	1147: Conduct NMED Review of CMS Plan	3FEB98	6APR98
270565	20	20	0	1 523 4 9	1147: Incorporate EPA/NMED Comments on CMS Plan	7APR98	4MAY98
270570	10	10	0	1 523 4 9	1147: Publish Final CMS Plan	5MAY98	18MAY98
270575	5	5	0	1 523 4 9	1147: EPA Approves CMS Plan	19MAY98	26MAY98
27M085	0	0	0	1 523 4	1147: EPA APPROVED CMS PLAN		26MAY98
270440	245	245	0	1 523 5 1	1147: Conduct CMS Bench/Pilot Studies (LOE)	27MAY98	19MAY99
270445	30	30	0	1 523 6 1	1147:Conduct Technical Evaluation for CMS Report	27MAY98	8JUL98
270450	30	30	0	1 523 6 2	1147: Cond Envir Evaluation for CMS Report	27MAY98	8JUL98
270455	30	30	0	1 523 6 3	1147: Conduct Human Health Eval for CMS Report	27MAY98	8JUL98
270460	30	30	0	1 523 6 4	1147: Cond Comm Relations Eval.for CMS Report	27MAY98	8JUL98
270465	30	30	0	1 523 6 5	1147: Conduct Cost Evaluation for CMS Report	27MAY98	8JUL98
270470	30	30	0	1 523 613	1147: Develop NEPA Documentation for CMS Report	27MAY98	8JUL98
27M055	0	0	0	1 523 5	1147: START CMS WORK	27MAY98	
27M065	0	0	0	1 523 6	1147: START DEVELOPMENT OF CMS REPORT	27MAY98	

LANL EES-1 C. ROFER

FINEST HOUR

ADS 1147: TA-50

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 25

ENVIRONMENTAL RESTORATION


START DATE 10CT91 FIN DATE 28SEP00

17:58

1147 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
270475	10	10	0	1 523 610	1147: Prepare Internal Draft of CMS Report	9JUL98	22JUL98
270480	10	10	0	1 523 6 6	1147: LANL/VE Review Internal Draft of CMS Rpt	23JUL98	5AUG98
270110	249	249	0	1 523 7	1147: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
270485	35	35	0	1 523 6 6	1147:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	1APR99	19MAY99
27M060	0	0	0	1 523 5	1147: CMS WORK COMPLETED		19MAY99
270490	10	10	0	1 523 6 8	1147: Publish DOE Draft of CMS Report	20MAY99	3JUN99
270495	22	22	0	1 523 6 8	1147: Conduct Review of DOE Draft of CMS Report	4JUN99	6JUL99
270500	10	10	0	1 523 6 8	1147:Incorp. DOE Rev Comments DOE Dft CMS Report	7JUL99	20JUL99
270505	10	10	0	1 523 6 9	1147: Publish EPA/NMED Draft of CMS Report	21JUL99	3AUG99
27M070	0	0	0	1 523 6	1147: EPA/NMED DRAFT OF CMS REPORT COMPLETED		3AUG99
270510	120	120	0	1 523 6 9	1147: Conduct EPA Review of CMS Report	4AUG99	31JAN00
270515	120	120	0	1 523 6 9	1147: Conduct NMED Review of CMS Report	4AUG99	31JAN00
270112	248	248	0	1 523 7	1147: Manage ADS During FY 2000 (LOE)	10CT99	28SEP00
270580	20	20	0	1 523 6 9	1147: Incorporate EPA/NMED Comments on CMS Rpt	1FEB00	29FEB00
270585	10	10	0	1 523 4 9	1147: Publish Final CMS Plan	1MAR00	14MAR00
27M075	0	0	0	1 523 8	1147: ASSESSMENT COMPLETED		14MAR00

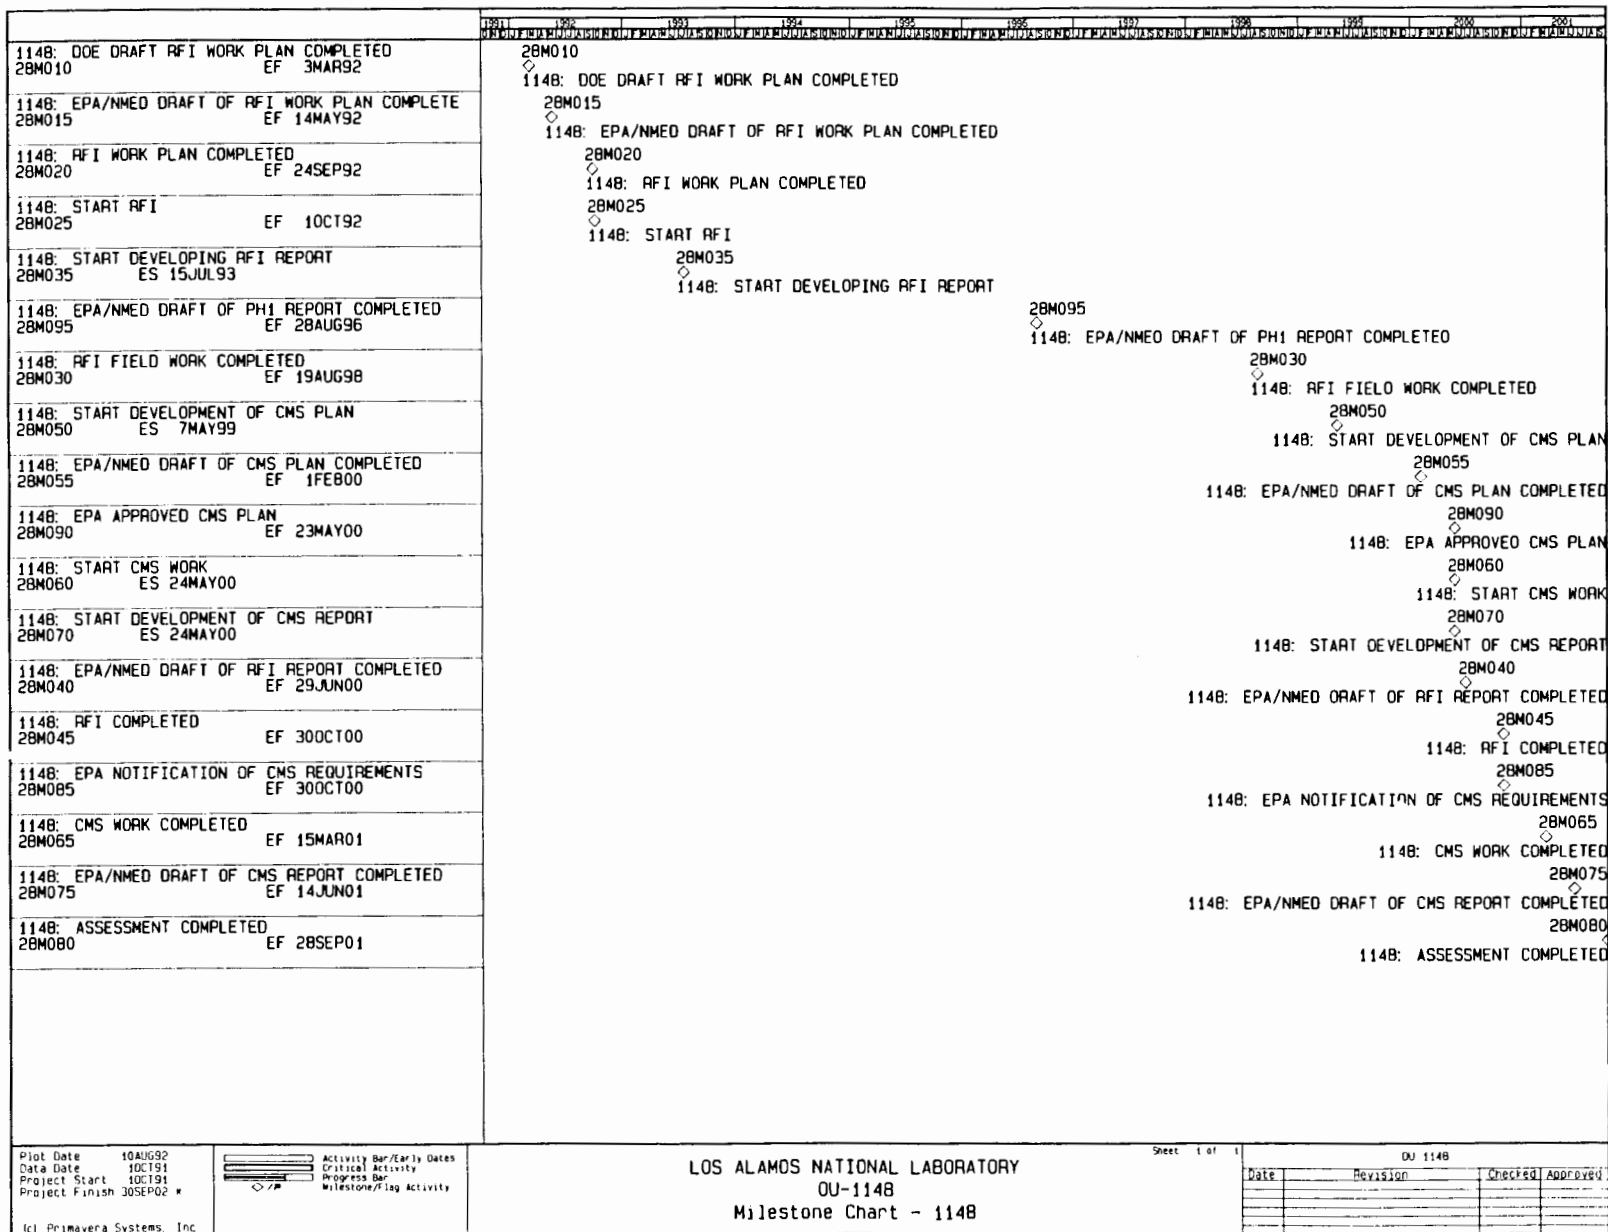

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02\*

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED	
						START	FINISH
280090	63	63	0	1148: Sect 8: QA Project Plan	RFI WP	10CT91	6JAN92
280095	63	63	0	1148: Sect 9: Health & Safety Plan	RFI WP	10CT91	6JAN92
280100	63	63	0	1148: Sect10: Records Mgt Plan	RFI WP	10CT91	6JAN92
280160	250	250	0	1148: Cond Bench/Pilot Studies	RFI WP (LOE)	10CT91	30SEP92
280165	250	250	0	1148: Cond VCA -	RFI WP (LOE)	10CT91	30SEP92
280175	250	250	0	1148: Manage ADS FY-92	(LOE)	10CT91	30SEP92
280180	250	250	0	1148: Develop NEPA Documentation	RFI WP	10CT91	30SEP92
280705	250	250	0	1148: MDA G Pilot Studies FY-92	(LOE)	10CT91*	30SEP92
280740	63	63	0	1148: Determine Data Needs	RFI WP	10CT91	6JAN92
280745	63	63	0	1148: Develop Sampling Plans	RFI WP	10CT91	6JAN92
280105	18	18	0	1148: Sect11: Comm Relations Plan	RFI WP	9DEC91	6JAN92
280275	18	18	0	1148: Develop Internal Draft	RFI WP	9DEC91*	6JAN92
280750	86	86	0	1148: Write Management Plan	RFI WP	30DEC91	30APR92
280285	19	19	0	1148: DOE/LANL/VE Rev Internal Dft	RFI WP	7JAN92	3FEB92
280295	10	10	0	1148: Inc DOE/LANL Comment Int Dft	RFI WP	4FEB92	18FEB92
280305	10	10	0	1148: Issue DOE Draft	RFI WP	19FEB92	3MAR92
28M010	0	0	0	1148: DOE DRAFT RFI WORK PLAN COMPLETED			3MAR92
280310	22	22	0	1148: DOE Review DOE Draft	RFI WP	4MAR92	2APR92
280315	20	20	0	1148: Inc DOE Comments DOE Draft	RFI WP	3APR92	30APR92
280320	10	10	0	1148: Issue EPA/NMED Draft	RFI WP	1MAY92	14MAY92
28M015	0	0	0	1148: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED			14MAY92
280325	44	44	0	1148: NMED Review	RFI WP	15MAY92	17JUL92
280330	44	44	0	1148: EPA Review	RFI WP	15MAY92	17JUL92
280645	20	20	0	1148: Inc EPA/NMED Comments	RFI WP	20JUL92	14AUG92
280650	28	28	0	1148: Issue Final	RFI WP	17AUG92	24SEP92
28M020	0	0	0	1148: RFI WORK PLAN COMPLETED			24SEP92
280190	249	249	0	1148: Manage ADS FY-93	(LOE)	10CT92	30SEP93
280340	249	249	0	1148: RFI Bench/Pilot Studies	(LOE)	10CT92	30SEP93
280635	249	249	0	1148: Conduct VCA -	(LOE)	10CT92*	30SEP93
280640	60	60	0	1148: Write Contracts and Mobilize	RFI PH1	10CT92*	31DEC92

LANL EM-13 J. KRUEGER  
 REPORT DATE 10AUG92 RUN NO. 101  
 10:30  
 1148 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
ENVIRONMENTAL RESTORATION

ADS 1148: TA-51 54 BELL3/16/92  
 START DATE 10CT91 FIN DATE 30SEP02\*  
 DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
280710	249	249	0	1148: MDA G Pilot Studies FY-93	(LOE)	10CT92	30SEP93
280755	249	249	0	1148: Conduct VCA RFI FY-93	(LOE)	10CT92*	30SEP93
28M025	0	0	0	1148: START RFI			10CT92*
280345	55	55	0	1148: Field Work FY-93	RFI PH1	15JUL93*	30SEP93
280350	55	55	0	1148: Sample Analysis FY-93	RFI PH1	15JUL93	30SEP93
280355	55	55	0	1148: Data Assessment FY-93	RFI PH1	15JUL93	30SEP93
28M035	0	0	0	1148: START DEVELOPING RFI REPORT		15JUL93	
280415	100	100	0	1148: Develop NEPA Documentation	RFI RPT	10AUG93*	6JAN94
280200	249	249	0	1148: Manage ADS FY-94	(LOE)	10CT93	30SEP94
280346	249	249	0	1148: Field Work FY-94	RFI PH1	10CT93*	30SEP94
280351	249	249	0	1148: Sample Analysis FY-94	RFI PH1	10CT93	30SEP94
280356	249	249	0	1148: Data Assessment FY-94	RFI PH1	10CT93	30SEP94
280715	249	249	0	1148: MDA G Pilot Studies FY-94	(LOE)	10CT93	30SEP94
280210	248	248	0	1148: Manage ADS FY-95	(LOE)	30CT94	29SEP95
280347	248	248	0	1148: Field Work FY-95	RFI PH1	30CT94*	29SEP95
280352	248	248	0	1148: Sample Analysis FY-95	RFI PH1	30CT94	29SEP95
280357	248	248	0	1148: Data Assessment FY-95	RFI PH1	30CT94	29SEP95
280720	248	248	0	1148: MDA G Pilot Studies FY-95	(LOE)	30CT94	29SEP95
280760	248	248	0	1148: Conduct VCA RFI FY-95	(LOE)	30CT94*	29SEP95
280230	249	249	0	1148: Manage ADS FY-96	(LOE)	20CT95	30SEP96
280353	100	100	0	1148: Sample Analysis FY-96	RFI PH1	20CT95	29FEB96
280358	125	125	0	1148: Data Assessment FY-96	RFI PH1	20CT95	4APR96
280365	20	20	0	1148: Demobilize Field Work	RFI PH1	20CT95	30OCT95
280725	249	249	0	1148: MDA G Pilot Studies FY-96	(LOE)	20CT95	30SEP96
280765	249	249	0	1148: Conduct VCA RFI FY-96	(LOE)	20CT95	30SEP96
280360	60	60	0	1148: Write Report /WP Modification	RFI PH1	5APR96	28JUN96
280375	22	22	0	1148: DOE Review RPT / WP Mod	RFI PH1	1JUL96	31JUL96
280377	20	20	0	1148: Inc DOE/LANL Comments RPT/WP	RFI PH1	1AUG96	28AUG96
280380	20	20	0	1148: Write Contract and Mobilize	RFI PH2	1AUG96*	28AUG96
28M095	0	0	0	1148: EPA/NMED DRAFT OF PH1 REPORT COMPLETED			28AUG96

-----

LANL EM-13 J. KRUEGER	FINEST HOUR	ADS 1148: TA-51 54	BELL3/16/92
REPORT DATE 10AUG92 RUN NO. 101	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 30SEP02*
10:30			
1148 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91	PAGE NO. 3

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
280370	22	22	0	1148: EPA/NMED Review RPT / WP Mod	RFI PH1	29AUG96	30SEP96
280385	22	22	0	1148: Field Work FY-96	RFI PH2	29AUG96	30SEP96
280390	22	22	0	1148: Sample Analysis FY-96	RFI PH2	29AUG96	30SEP96
280410	22	22	0	1148: Data Assessment FY-96	RFI PH2	29AUG96	30SEP96
280240	249	249	0	1148: Manage ADS FY-97	(LOE)	1OCT96	30SEP97
280372	20	20	0	1148: Inc EPA/NMED Comments RPT/WP	RFI PH1	1OCT96	29OCT96
280386	249	249	0	1148: Field Work FY-97	RFI PH2	1OCT96	30SEP97
280391	249	249	0	1148: Sample Analysis FY-97	RFI PH2	1OCT96	30SEP97
280411	249	249	0	1148: Data Assessment FY-97	RFI PH2	1OCT96	30SEP97
280730	249	249	0	1148: MDA G Pilot Studies FY-97	(LOE)	1OCT96	30SEP97
280770	249	249	0	1148: Conduct VCA RFI FY-97	(LOE)	1OCT96	30SEP97
280374	10	10	0	1148: Issue Final Report/WP Mod	RFI PH1	30OCT96	13NOV96
710000	189	189	0	2114: Conduct VCA - Remediation	(LOE)	2JAN97*	30SEP97
280250	249	249	0	1148: Manage ADS FY-98	(LOE)	1OCT97	30SEP98
280387	200	200	0	1148: Field Work FY-98	RFI PH2	1OCT97	22JUL98
280392	249	249	0	1148: Sample Analysis FY-98	RFI PH2	1OCT97	30SEP98
280412	249	249	0	1148: Data Assessment FY-98	RFI PH2	1OCT97	30SEP98
280735	249	249	0	1148: MDA G Pilot Studies FY-98	(LOE)	1OCT97	30SEP98
280775	249	249	0	1148: Conduct VCA RFI FY-98	(LOE)	1OCT97	30SEP98
710005	249	249	0	2114: Conduct VCA - Remediation	(LOE)	1OCT97	30SEP98
280395	20	20	0	1148: Demobilize Field Work	RFI PH2	23JUL98	19AUG98
28M030	0	0	0	1148: RFI FIELD WORK COMPLETED			19AUG98
280270	249	249	0	1148: Manage ADS FY-99	(LOE)	1OCT98	30SEP99
280393	20	20	0	1148: Sample Analysis FY-99	RFI PH2	1OCT98	29OCT98
280413	30	30	0	1148: Data Assessment FY-99	RFI PH2	1OCT98	13NOV98
280780	249	249	0	1148: Conduct VCA RFI FY-99	(LOE)	1OCT98	30SEP99
280400	100	100	0	1148: Facility Investigation	RFI RPT	16NOV98	13APR99
280405	110	110	0	1148: Investigation Analysis	RFI RPT	16NOV98	27APR99
280425	132	132	0	1148: Prepare Internal Draft	RFI RPT	28APR99	3NOV99
280480	245	245	0	1148: CMS Bench/Pilot Studies	CMS PLN	7MAY99	1MAY00



-----

LANL EM-13 J. KRUEGER	FINEST HOUR	ADS 1148: TA-51 54	BELL3/16/92
REPORT DATE 10AUG92 RUN NO. 101	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 30SEP02*
10:30			
1148 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91	PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
280485	35	35	0	1148: Establish Current Situation CMS PLN	7MAY99	25JUN99
280490	35	35	0	1148: Establish CA Objectives CMS PLN	7MAY99	25JUN99
280495	35	35	0	1148: Develop Screening Technology CMS PLN	7MAY99	25JUN99
280500	245	245	0	1148: Develop NEPA Documentation CMS PLN	7MAY99	1MAY00
28M050	0	0	0	1148: START DEVELOPMENT OF CMS PLAN	7MAY99	
280505	35	35	0	1148: Develop Alternatives CMS PLN	28JUN99	16AUG99
280510	35	35	0	1148: Develop Internal Draft CMS PLN	17AUG99	5OCT99
280271	249	249	0	1148: Manage ADS FY-00 (LOE)	10CT99	29SEP00
280785	249	249	0	1148: Conduct VCA RFI FY-00 (LOE)	10CT99	29SEP00
280515	10	10	0	1148: DOE/LANL/VE Review Int Draft CMS PLN	6OCT99	20OCT99
280520	10	10	0	1148: Inc DOE/LANL Comments Int Dft CMS PLN	21OCT99	3NOV99
280435	20	20	0	1148: DOE/LANL/VE Rev Internal Dft RFI RPT	4NOV99	6DEC99
280525	5	5	0	1148: Issue DOE Draft CMS PLN	4NOV99	10NOV99
280530	22	22	0	1148: DOE Review DOE Draft CMS PLN	11NOV99	15DEC99
280445	40	40	0	1148: Inc DOE/LANL Comments Int Dft RFI RPT	7DEC99	4FEB00
280535	20	20	0	1148: Inc DOE Comments DOE Draft CMS PLN	16DEC99	18JAN00
280540	10	10	0	1148: Issue EPA/NMED Draft CMS PLN	19JAN00	1FEB00
28M055	0	0	0	1148: EPA/NMED DRAFT OF CMS PLAN COMPLETED		1FEB00
280545	44	44	0	1148: EPA Review CMS PLN	2FEB00	4APR00
280550	44	44	0	1148: NMED Review CMS PLN	2FEB00	4APR00
280450	20	20	0	1148: Issue DOE Draft RFI RPT	7FEB00	6MAR00
280455	22	22	0	1148: DOE Review DOE Draft RFI RPT	7MAR00	5APR00
280680	20	20	0	1148: Inc EPA/NMED Comments CMS PLN	5APR00	2MAY00
280460	40	40	0	1148: Inc DOE Comments DOE Draft RFI RPT	6APR00	1JUN00
280685	10	10	0	1148: Issue Final CMS PLN	3MAY00	16MAY00
280690	5	5	0	1148: EPA Approval CMS PLN	17MAY00	23MAY00
28M090	0	0	0	1148: EPA APPROVED CMS PLAN		23MAY00
280555	200	200	0	1148: CMS Bench/Pilot Studies (LOE)	24MAY00	15MAR01
280560	1	1	0	1148: Technical Evaluation CMS RPT	24MAY00	24MAY00
280565	30	30	0	1148: Environmental Evaluaion CMS RPT	24MAY00	6JUL00

LANL EM-13 J. KRUEGER

FINEST HOUR

ADS 1148: TA-51 54

BELL3/16/92

REPORT DATE 10AUG92 RUN NO. 101

ENVIRONMENTAL RESTORATION


START DATE 1OCT91 FIN DATE 30SEP02\*

10:30

1148 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START FINISH	
280570	30	30	0	1148: Human Health Evaluation	CMS RPT	24MAY00	6JUL00
280575	30	30	0	1148: Community Relations Eval	CMS RPT	24MAY00	6JUL00
280580	30	30	0	1148: Cost Evaluation	CMS RPT	24MAY00	6JUL00
280585	30	30	0	1148: Develop NEPA Documentation	CMS RPT	24MAY00	6JUL00
28M060	0	0	0	1148: START CMS WORK		24MAY00	
28M070	0	0	0	1148: START DEVELOPMENT OF CMS REPORT		24MAY00	
280465	20	20	0	1148: Issue EPA/NMED Draft	RFI RPT	2JUN00	29JUN00
28M040	0	0	0	1148: EPA/NMED DRAFT OF RFI REPORT COMPLETED			29JUN00
280470	44	44	0	1148: EPA Review	RFI RPT	30JUN00	31AUG00
280475	44	44	0	1148: NMED Review	RFI RPT	30JUN00	31AUG00
280590	10	10	0	1148: Prepare Internal Draft	CMS RPT	7JUL00	20JUL00
280595	10	10	0	1148: DOE/LANL/VE Rev Internal Drft	CMS RPT	21JUL00	3AUG00
280670	20	20	0	1148: Inc EPA/NMED Comments	RFI RPT	1SEP00	29SEP00
280272	248	248	0	1148: Manage ADS FY-01	(LOE)	2OCT00	28SEP01
280675	20	20	0	1148: Issue Final	RFI RPT	2OCT00	30OCT00
28M045	0	0	0	1148: RFI COMPLETED			30OCT00
28M085	0	0	0	1148: EPA NOTIFICATION OF CMS REQUIREMENTS			30OCT00
280600	35	35	0	1148: Inc DOE/LANL Comments Int Dft	CMS RPT	25JAN01	15MAR01
28M065	0	0	0	1148: CMS WORK COMPLETED			15MAR01
280605	22	22	0	1148: Issue DOE Draft	CMS RPT	16MAR01	16APR01
280610	22	22	0	1148: DOE Review DOE Draft	CMS RPT	17APR01	16MAY01
280615	10	10	0	1148: Inc DOE Comments DOE Draft	CMS RPT	17MAY01	31MAY01
280620	10	10	0	1148: Issue EPA/NMED Draft	CMS RPT	1JUN01	14JUN01
28M075	0	0	0	1148: EPA/NMED DRAFT OF CMS REPORT COMPLETED			14JUN01
280625	44	44	0	1148: EPA Review	CMS RPT	15JUN01	16AUG01
280630	44	44	0	1148: NMED Review	CMS RPT	15JUN01	16AUG01
280695	20	20	0	1148: Inc EPA/NMED Comments	CMS RPT	17AUG01	14SEP01
280700	10	10	0	1148: Issue Final	CMS RPT	17SEP01	28SEP01
28M080	0	0	0	1148: ASSESSMENT COMPLETED			28SEP01

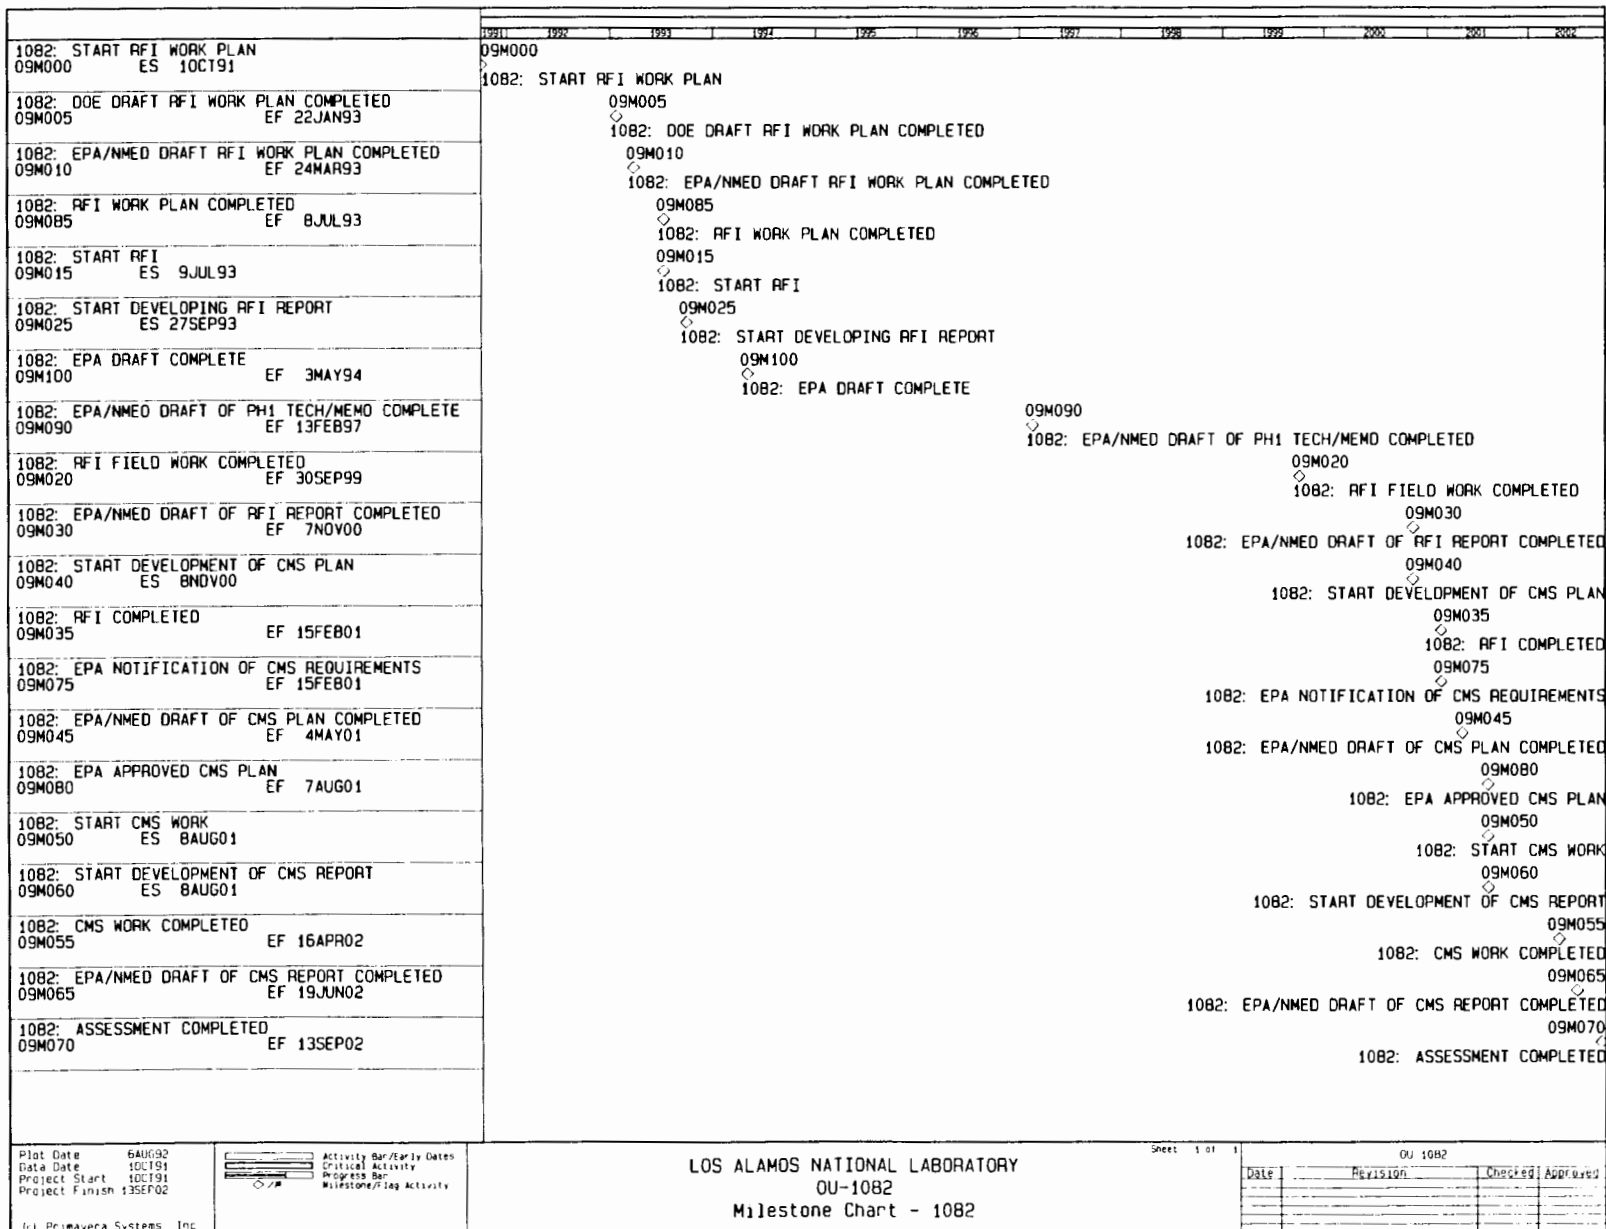

1082:TA-11 13 16 24 25 28 37 BELL

START DATE 10OCT91 FIN DATE 13SEP02

DATA DATE 10OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
090000	250	250	0	1082: Conduct Voluntary C. Actions for RFI WP	10CT91	30SEP92
090005	20	20	0	1082: Develop Scope RFI Work Plan	10CT91	29OCT91
090100	250	250	0	1082: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
090295	250	250	0	1082: Conduct Bench/Pilot Stud. for RFI WP(LOE)	10CT91	30SEP92
095005	250	250	0	CONDUCT VCA - FY92	10CT91	30SEP92
09M000	0	0	0	1082: START RFI WORK PLAN	10CT91	
090010	76	76	0	1082: Locate Existing Data for RFI WP	30OCT91	24FEB92
090020	84	84	0	1082: Analyze Existing Data for RFI WP	2JAN92*	30APR92
090575	190	190	0	1082: Delineate Potential Release Sites	2JAN92*	30SEP92
090015	206	206	0	1082: Develop NEPA Documentation For RFI WP	2MAR92*	23DEC92
090025	42	42	0	1082: Draft Existing Data Report for RFI WP	4MAR92*	30APR92
090040	86	86	0	1082: Write Records Management Plan For RFI WP	1APR92*	31JUL92
090030	40	40	0	1082: Determine Data Needs for RFI WP	1MAY92	26JUN92
090035	64	64	0	1082: Write Community Relations Plan For RFI WP	1MAY92*	31JUL92
090070	180	180	0	1082: Develop LANL Internal Draft of RFI WP	1MAY92*	22JAN93
090045	90	90	0	1082: Develop Data Quality Objectives for RFI WP	26MAY92*	30SEP92
090050	100	100	0	1082: Develop Sampling Plans for RFI WP	24JUL92*	17DEC92
090055	56	56	0	1082: Write Quality Assurance for RFI WP	10CT92*	23DEC92
090060	56	56	0	1082: Write Health & Safety Plan for RFI WP	10CT92*	23DEC92
090065	24	24	0	1082: Write Management Plan for RFI WP	10CT92*	4NOV92
090105	249	249	0	1082: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
090600	45	45	0	1082: Delineate Potential Release Sites	10CT92	8DEC92
090605	66	66	0	1082: Analyze Existing Data for RFI WP	10CT92*	11JAN93
095010	249	249	0	CONDUCT VCA - FY93	10CT92	30SEP93
090075	20	20	0	1082: LANL/VE Review Internal Draft for RFI WP	5NOV92	7DEC92
090080	30	30	0	1082: Incorporate LANL Comments & Dev DOE Draft	8DEC92	22JAN93
090625	77	77	0	1082: Develop Data Quality Objectives for RFI WP	9DEC92	1APR93
090610	23	23	0	1082: Draft Existing Data Report for RFI WP	12JAN93	12FEB93
09M005	0	0	0	1082: DOE DRAFT RFI WORK PLAN COMPLETED		22JAN93
090085	22	22	0	1082: Cond DOE Review of DOE Draft of RFI WP	25JAN93	24FEB93

LANL CLS-DO BRAD MARTIN  
 REPORT DATE 5AUG92 RUN NO. 266  
 15:48  
 1082 SCHEDULE REPORT BY EARLY START

FINEST HOUR

1082:TA-11 13 16 24 25 28 37 BELL  
 START DATE 10CT91 FIN DATE 13SEP02  
 DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
090620	74	74	0	1082: Incorp DOE Comments & Dev EPA/NMED Draft	16FEB93	28MAY93
090090	20	20	0	1082: Incorp DOE Comments & Dev EPA/NMED Draft	25FEB93	24MAR93
09M010	0	0	0	1082: EPA/NMED DRAFT RFI WORK PLAN COMPLETED		24MAR93
090095	44	44	0	1082: Conduct EPA Review of RFI Work Plan	25MAR93	25MAY93
090096	44	44	0	1082: Conduct NMED Review of RFI WP	25MAR93	25MAY93
090615	42	42	0	1082: Determine Data Needs for RFI WP	2APR93	1JUN93
090515	20	20	0	1082: Incorporate EPA/NMED Comments for RFI WP	26MAY93	23JUN93
090630	63	63	0	1082: Develop Sampling Plans for RFI WP	2JUN93	30AUG93
090510	45	45	0	1082: Write PH1 Contracts for RFI	24JUN93	26AUG93
090520	10	10	0	1082: Publish Final RFI Work Plan	24JUN93	8JUL93
09M085	0	0	0	1082: RFI WORK PLAN COMPLETED		8JUL93
090160	245	245	0	1082: Conduct RFI Bench/Pilot Studies (LOE)	9JUL93	1JUL94
09M015	0	0	0	1082: START RFI	9JUL93	
090155	20	20	0	1082: Mobilize for RFI	27AUG93	24SEP93
090635	22	22	0	1082: LANL/VE Review Internal Draft for RFI WP	31AUG93	30SEP93
090165	4	4	0	1082: Conduct RFI PH1 Field Work	27SEP93	30SEP93
090290	4	4	0	1082: Develop NEPA Documentation for RFI Report	27SEP93	30SEP93
09M025	0	0	0	1082: START DEVELOPING RFI REPORT	27SEP93	
090110	249	249	0	1082: Manage ADS During FY-94 (LOE)	10CT93	30SEP94
090166	249	249	0	1082: Conduct RFI PH1 Field Work	10CT93	30SEP94
090170	249	249	0	1082: Conduct RFI PH1 Sample Analysis	10CT93*	30SEP94
090175	249	249	0	1082: Conduct RFI PH1 Data Assessment	10CT93*	30SEP94
090291	100	100	0	1082: Develop NEPA Documentation for RFI Report	10CT93	2MAR94
095015	249	249	0	CONDUCT VCA - FY94	10CT93	30SEP94
090640	22	22	0	1082: Finalize Draft for RFI WP	4APR94*	3MAY94
09M100	0	0	0	1082: EPA DRAFT COMPLETE		3MAY94
090115	248	248	0	1082: Manage ADS During FY-95 (LOE)	30CT94	29SEP95
090167	248	248	0	1082: Conduct RFI PH1 Field Work	30CT94	29SEP95
090171	248	248	0	1082: Conduct RFI PH1 Sample Analysis	30CT94	29SEP95
090176	248	248	0	1082: Conduct RFI PH1 Data Assessment	30CT94	29SEP95



-----

LANL	CLS-DO	BRAD MARTIN	FINEST HOUR	1082:TA-11 13 16 24 25 28 37 BELL
REPORT DATE	5AUG92	RUN NO. 266	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 13SEP02
	15:48			
1082 SCHEDULE REPORT BY	EARLY START			DATA DATE 10CT91 PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
095040	249	249	0	CONDUCT VCA - FY99	10CT98	30SEP99
090215	20	20	0	1082: Demoblize RFI PH2 Field Work	2SEP99	30SEP99
09M020	0	0	0	1082: RFI FIELD WORK COMPLETED		30SEP99
090140	249	249	0	1082: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
090212	15	15	0	1082: Conduct RFI PH2 Sample Analysis	10CT99	22OCT99
090222	25	25	0	1082: Conduct RFI PH2 Data Assessment	10CT99	5NOV99
095045	249	249	0	CONDUCT VCA - FY2000	10CT99	29SEP00
090280	70	70	0	1082: Conduct RFI Report Facility Investigation	8NOV99	23FEB00
090285	70	70	0	1082: Conduct RFI Report Investigation Analysis	8NOV99	23FEB00
090300	90	90	0	1082: Prepare Internal Draft of RFI Report	24FEB00	29JUN00
090305	20	20	0	1082: LANL/VE Review Internal Draft of RFI Rpt	30JUN00	28JUL00
090310	20	20	0	1082:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	31JUL00	25AUG00
090315	10	10	0	1082: Publish DOE Draft of RFI Report	28AUG00	11SEP00
090320	20	20	0	1082: Conduct DOE Review of Draft of RFI Report	12SEP00	10OCT00
090145	248	248	0	1082: Manage ADS During FY-01 (LOE)	20CT00	28SEP01
095050	107	107	0	CONDUCT VCA - FY2001	6OCT00	16MAR01*
090325	15	15	0	1082:Incorp. DOE Rev. Comments DOE Drft RFI Rpt	11OCT00	31OCT00
090330	5	5	0	1082: Publish EPA/NMED Draft of RFI Report	1NOV00	7NOV00
09M030	0	0	0	1082: EPA/NMED DRAFT OF RFI REPORT COMPLETED		7NOV00
090335	40	40	0	1082: Conduct EPA Review of RFI Report	8NOV00	10JAN01
090340	40	40	0	1082: Conduct NMED Review of RFI Report	8NOV00	10JAN01
090345	249	249	0	1082:Conduct Bench/Pilot Studies CMS Plan (LOE)	8NOV00	7NOV01
090350	20	20	0	1082: Establish Current Situation for CMS Plan	8NOV00	8DEC00
090355	30	30	0	1082: Establish CA Objectives for CMS Plan	8NOV00	22DEC00
090360	30	30	0	1082:Develop Screening Technologies for CMS Plan	8NOV00	22DEC00
090365	249	249	0	1082: Develop NEPA Documentation for CMS Plan	8NOV00	7NOV01
09M040	0	0	0	1082: START DEVELOPMENT OF CMS PLAN	8NOV00	
090370	15	15	0	1082: Develop Alternatives for CMS Plan	27DEC00	18JAN01
090540	15	15	0	1082: Incorporate EPA/NMED Comments on RFI Rpt	11JAN01	1FEB01
090375	10	10	0	1082: Develop Internal Draft of CMS Plan	19JAN01	1FEB01






LANL CLS-DO BRAD MARTIN  
 REPORT DATE 5AUG92 RUN NO. 266 ENVIRONMENTAL RESTORATION  
 15:48  
 1082 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 1082:TA-11 13 16 24 25 28 37 BELL  
 START DATE 10CT91 FIN DATE 13SEP02  
 DATA DATE 10CT91 PAGE NO. 6

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
090470	5	5	0	1082: Publish DOE Draft of CMS Report	17APR02	23APR02
090475	20	20	0	1082: Conduct DOE Review of Draft of CMS Report	24APR02	21MAY02
090480	15	15	0	1082: Incorp. DOE Rev Comments DOE Dft CMS Rpt	22MAY02	12JUN02
090490	5	5	0	1082: Publish EPA/NMED Draft of CMS Report	13JUN02	19JUN02
09M065	0	0	0	1082: EPA/NMED DRAFT OF CMS REPORT COMPLETED		19JUN02
090495	40	40	0	1082: Conduct EPA Review of CMS Report	20JUN02	15AUG02
090500	40	40	0	1082: Conduct NMED Review of CMS Report	20JUN02	15AUG02
090565	15	15	0	1082: Incorporate EPA/NMED Comments on CMS Rpt	16AUG02	6SEP02
090570	5	5	0	1082: Publish Final CMS Report	9SEP02	13SEP02
09M070	0	0	0	1082: ASSESSMENT COMPLETED		13SEP02

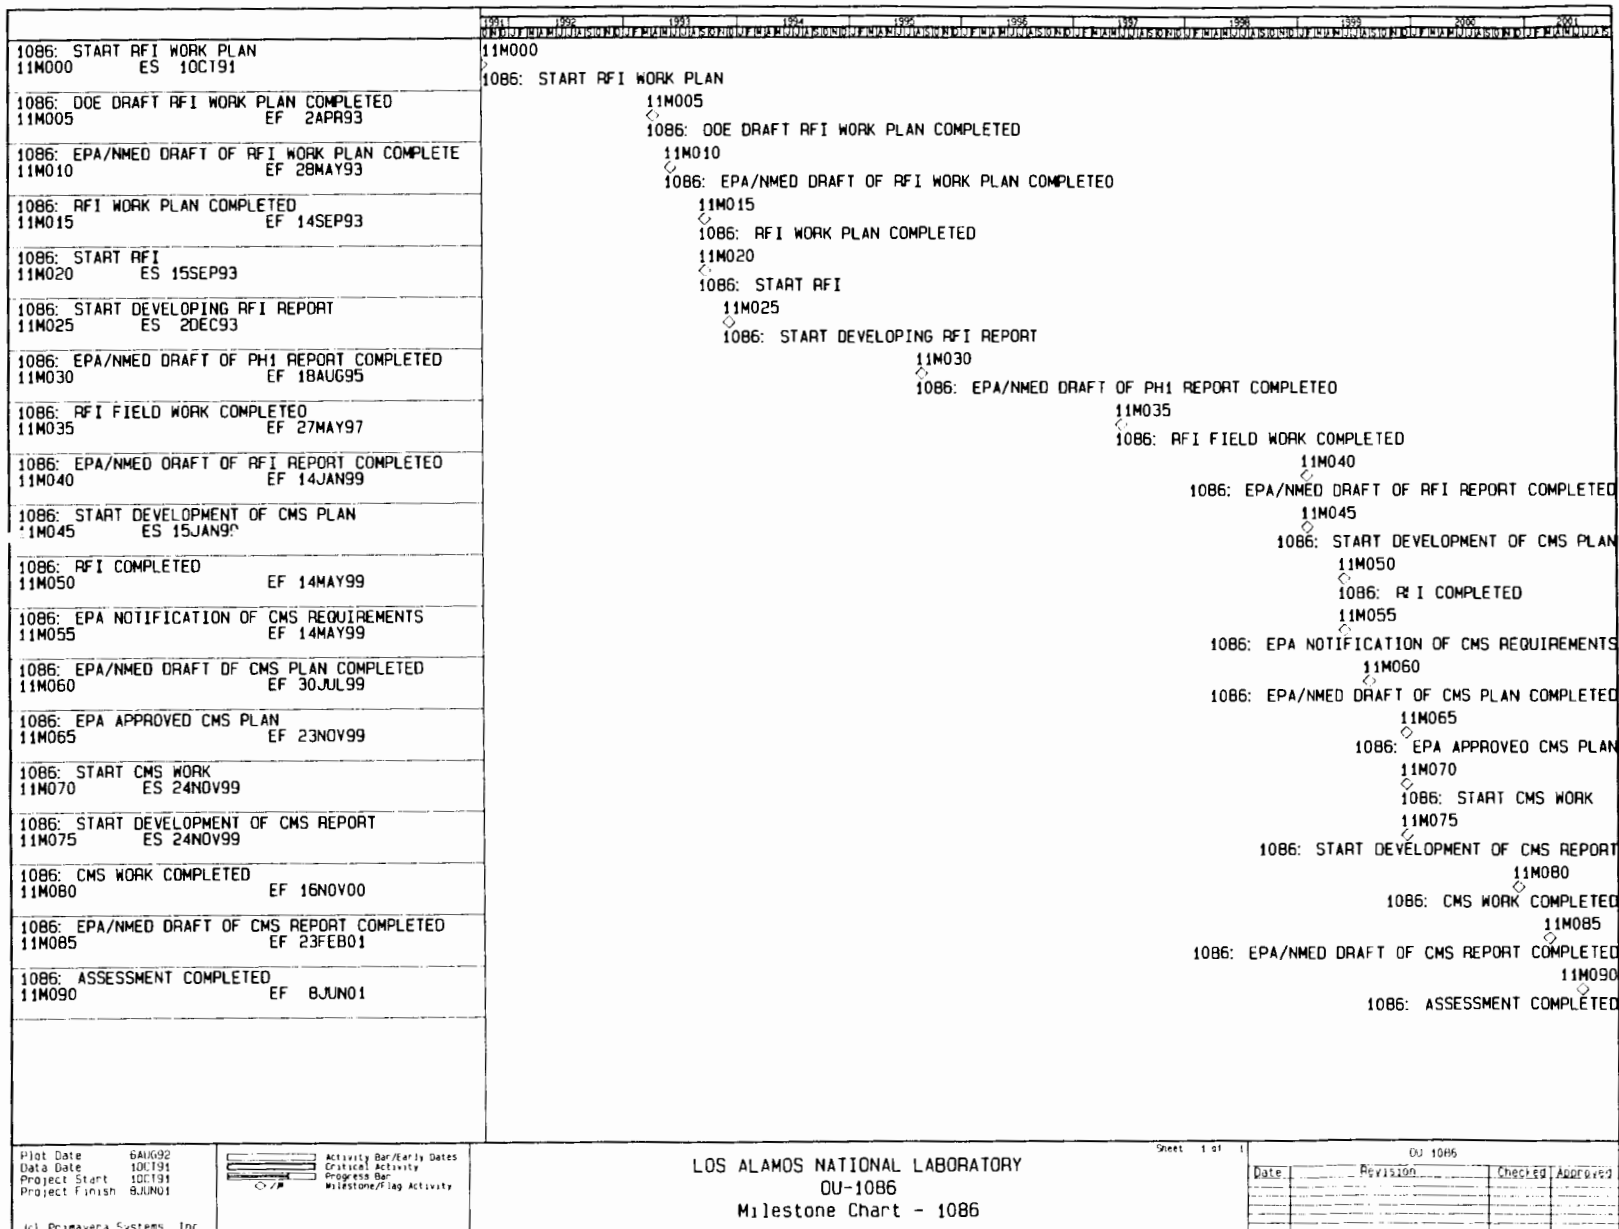

LANL INC-7 AL OGARD  
 REPORT DATE 5AUG92 RUN NO. 137 ENVIRONMENTAL RESTORATION  
 15:49  
 1086 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ADS 1086: TA-15  
 START DATE 10CT91 FIN DATE 8JUN01  
 DATA DATE 10CT91 PAGE NO. 1

TBS 2/17/92

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
110000	250	250	0	1086: Cond Bench/Pilot Studies for RFI WP (LOE)	10CT91	30SEP92
110005	250	250	0	1086: Cond Voluntary C.Actions for RFI WP (LOE)	10CT91	30SEP92
110015	250	250	0	1086: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
110025	250	250	0	1086: Develop NEPA Documentation for RFI WP	10CT91	30SEP92
115005	250	250	0	1086: CONDUCT VCA FY-92	10CT91	30SEP92
11M000	0	0	0	1086: START RFI WORK PLAN	10CT91*	
110010	20	20	0	1086: Develop Scope for RFI WP	13DEC91	15JAN92
110030	40	40	0	1086: Locate Existing Data EPA SWMU'S RFI WP	16JAN92	12MAR92
110035	38	38	0	1086: Analyze Existing Data for RFI WP	13MAR92	5MAY92
110040	20	20	0	1086: Draft Existing Data RPT EPA SWMU'S RFI WP	6MAY92	3JUN92
110045	40	40	0	1086: Determine Data Needs EPA SWMU'S RFI WP	4JUN92	30JUL92
110050	20	20	0	1086: Write Community Relations Plan for RFI WP	31JUL92	27AUG92
110055	20	20	0	1086: Write Records Management Plan for RFI WP	31JUL92	27AUG92
110075	20	20	0	1086: Write Quality Assurance Plan for RFI WP	31JUL92	27AUG92
110080	20	20	0	1086: Write Health & Safety Plan for RFI WP	31JUL92	27AUG92
110085	20	20	0	1086: Write Management Plan for RFI WP	31JUL92	27AUG92
110065	94	94	0	1086: Develop Sampling Plan for RFI WP	28AUG92	19JAN93
110070	249	249	0	1086: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
110600	249	249	0	1098: Cond Bench/Pilot Studies for RFI WP (LOE)	10CT92	30SEP93
110605	249	249	0	1086: Develop NEPA Documentation for RFI WP	10CT92	30SEP93
115010	249	249	0	1086: CONDUCT VCA FY-93	10CT92	30SEP93
110090	20	20	0	1086: Develop LANL Internal Draft of RFI WP	17DEC92	19JAN93
110095	22	22	0	1086: DOE/LANL/VE Review Internal Draft RFI WP	20JAN93	19FEB93
110100	20	20	0	1086: Incorp LANL Rev Comments Intern Dft RFI WP	22FEB93	19MAR93
110105	10	10	0	1086: Issue DOE Draft of RFI WP	22MAR93	2APR93
11M005	0	0	0	1086: DOE DRAFT RFI WORK PLAN COMPLETED		2APR93
110110	10	10	0	1086: DOE Review DOE Draft RFI WP	5APR93	16APR93
110610	40	40	0	1086: Locate Existing Data Balance of SWMU'S PH2	12APR93*	7JUN93
110115	20	20	0	1086: Incorp DOE Comments DOE Draft RFI WP	19APR93	14MAY93
110120	10	10	0	1086: Issue EPA/NMED Draft RFI WP	17MAY93	28MAY93

TBS 2/17/92

START DATE 1OCT91 FIN DATE 8JUN01

DATA DATE 10OCT91 PAGE NO. 2

DATA DATE 10OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
11M010	0	0	0	1086: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		28MAY93
110125	44	44	0	1086: Conduct NMED Review of RFI Work Plan	1JUN93	2AUG93
110130	44	44	0	1086: Conduct EPA Review of RFI Work Plan	1JUN93	2AUG93
110615	38	38	0	1086: Analyze Existing Data Balance SWMU'S PH2	8JUN93	30JUL93
110620	20	20	0	1086: Draft Existing Data RPT Balance SWMU'S PH2	2AUG93	27AUG93
110140	20	20	0	1086: Incorporate EPA/NMED Comments for RFI WP	3AUG93	30AUG93
110625	46	46	0	1086: Determine Data Needs Balance SWMU'S PH2	30AUG93	2NOV93
110135	63	63	0	1086: Write PH1 Contract; Mobilize for RFI	31AUG93	1DEC93
110145	10	10	0	1086: Issue Final RFI Work Plan	31AUG93	14SEP93
11M015	0	0	0	1086: RFI WORK PLAN COMPLETED		14SEP93
11M020	0	0	0	1086: START RFI	15SEP93	
110160	250	250	0	1086: Manage ADS During FY-94 (LOE)	1OCT93	30SEP94
600020	250	250	0	1086: CONDUCT VCA FY-94	1OCT93	30SEP94
110635	98	98	0	1086: Sampling Plan Balance of SWMU'S RFI PH2	3NOV93	30MAR94
110165	327	327	0	1086: Conduct RFI PH1 Field Work	2DEC93	29MAR95
110170	357	357	0	1086: Conduct RFI PH1 Sample Analysis	2DEC93	10MAY95
110175	367	367	0	1086: Conduct RFI PH1 Data Assessment	2DEC93	24MAY95
110180	100	100	0	1086: Prepare NEPA/Environ. Info for RFI Report	2DEC93	27APR94
11M025	0	0	0	1086: START DEVELOPING RFI REPORT	2DEC93	
110185	247	247	0	1086: Manage ADS During FY-95 (LOE)	3OCT94	29SEP95
600025	247	247	0	1086: CONDUCT VCA FY-95	3OCT94	29SEP95
110195	20	20	0	1086: Demobilize RFI PH1 Field Work	30MAR95	26APR95
110190	60	60	0	1086: Write Draft RFI PH1 Report/WP Modification	25MAY95	18AUG95
11M030	0	0	0	1086: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		18AUG95
110131	20	20	0	1086: Incorp. DOE/LANL Rev. Comments PH1 Rpt Mod	21AUG95	18SEP95
110205	22	22	0	1086: DOE/LANL Review PH1 Report/WP Modification	21AUG95	20SEP95
110210	20	20	0	1086: Write PH2 Contract; Mobilize for RFI	21AUG95	18SEP95
110200	22	22	0	1086: EPA/NMED Review PH1 Report/WP Modification	19SEP95	19OCT95
110230	249	249	0	1086: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
115015	249	249	0	1086: CONDUCT VCA FY-96	2OCT95	30SEP96

LANL INC-7 AL OGARD

FINEST HOUR

ADS 1086: TA-15

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 137

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 8JUN01

15:49

1086 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
110132	40	40	0	1086: Incorp. EPA/NMED Rev. Comments PH1 Rpt Mod	20OCT95	19DEC95
110133	10	10	0	1086: Issue Final PH1 Report/Work Plan Mod	20DEC95	5JAN96
110215	327	327	0	1086: Conduct RFI PH2 Field Work	8JAN96	28APR97
110220	357	357	0	1086: Conduct RFI PH2 Sample Analysis	8JAN96	10JUN97
110225	367	367	0	1086: Conduct RFI PH2 Data Assessment	8JAN96	24JUN97
110255	249	249	0	1086: Manage ADS During FY-97 (LOE)	10CT96	30SEP97
115020	249	249	0	1086: CONDUCT VCA FY-97	10CT96	30SEP97
560000	249	249	0	1086: Remed - Conduct VCA FY-97 (LOE)	10CT96	30SEP97
110245	20	20	0	1086: Demoblize RFI PH2 Field Work	29APR97	27MAY97
11M035	0	0	0	1086: RFI FIELD WORK COMPLETED		27MAY97
110235	100	100	0	1086: Conduct RFI Report Facility Investigation	25JUN97	17NOV97
110240	110	110	0	1086: Conduct RFI Report Investigation Analysis	25JUN97	3DEC97
110290	249	249	0	1086: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
115025	249	249	0	1086: CONDUCT VCA FY-98	10CT97	30SEP98
560005	249	249	0	1086: Conduct VCA FY-98 (LOE)	10CT97	30SEP98
110250	132	132	0	1086: Prepare Internal Draft of RFI Report	4DEC97	15JUN98
110260	22	22	0	1086: DOE/LANL/VE Rev Internal Draft of RFI Rpt	16JUN98	16JUL98
110265	40	40	0	1086: Incorp. LANL Rev. Comments Intern Dft RFI Rpt	17JUL98	11SEP98
110270	10	10	0	1086: Issue DOE Draft of RFI Report	14SEP98	25SEP98
110275	22	22	0	1086: Conduct Review of DOE Draft of RFI Report	28SEP98	28OCT98
110410	249	249	0	1086: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
115030	249	249	0	1086: CONDUCT VCA FY-99	10CT98	30SEP99
110280	40	40	0	1086: Incorp. DOE Rev. Comments DOE Dft RFI Rpt	29OCT98	30DEC98
110285	10	10	0	1086: Issue EPA/NMED Draft of RFI Report	31DEC98	14JAN99
11M040	0	0	0	1086: EPA/NMED DRAFT OF RFI REPORT COMPLETED		14JAN99
110295	44	44	0	1086: Conduct EPA Review of RFI Report	15JAN99	19MAR99
110300	44	44	0	1086: Conduct NMED Review of RFI Report	15JAN99	19MAR99
110305	245	245	0	1086: Cond Bench/Pilot Studies for CMS Plan LOE	15JAN99	10JAN00
110310	35	35	0	1086: Establish Current Situation for CMS Plan	15JAN99	8MAR99
110315	35	35	0	1086: Establish CA Objectives for CMS Plan	15JAN99	8MAR99

LANL INC-7 AL OGARD

FINEST HOUR

ADS 1086: TA-15

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 137  
15:49

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 8JUN01

1086 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
110320	35	35	0	1086: Develop Screening Technologies for CMS Pl	15JAN99	8MAR99
110325	245	245	0	1086: Develop NEPA Documentation for CMS Plan	15JAN99	10JAN00
11M045	0	0	0	1086: START DEVELOPMENT OF CMS PLAN	15JAN99	
110330	15	15	0	1086: Develop Alternatives for CMS Plan	9MAR99	29MAR99
110335	20	20	0	1086: Incorp EPA/NMED Comments on RFI Report	22MAR99	16APR99
110340	10	10	0	1086: Develop Internal Draft of CMS Plan	30MAR99	12APR99
110345	10	10	0	1086: DOE/LANL/VE Rev Internal Draft of CMS Pl	13APR99	26APR99
110350	20	20	0	1086: Issue Final RFI Report	19APR99	14MAY99
110355	10	10	0	1086:Incorp. LANL REV Comments Intern Dft CMS Pl	27APR99	10MAY99
110360	5	5	0	1086: Issue DOE Draft of CMS Plan	11MAY99	17MAY99
11M050	0	0	0	1086: RFI COMPLETED		14MAY99
11M055	0	0	0	1086: EPA NOTIFICATION OF CMS REQUIREMENTS		14MAY99
110365	22	22	0	1086: Conduct Review of DOE Draft of CMS Plan	18MAY99	17JUN99
110370	20	20	0	1086: Incorp DOE Rev Comments DOE Dft of CMS Pl	18JUN99	16JUL99
110375	10	10	0	1086: Issue EPA/NMED Draft of CMS Plan	19JUL99	30JUL99
11M060	0	0	0	1086: EPA/NMED DRAFT OF CMS PLAN COMPLETED		30JUL99
110380	44	44	0	1086: Conduct EPA Review of CMS Plan	2AUG99	10CT99
110385	44	44	0	1086: Conduct NMED Review of CMS Plan	2AUG99	10CT99
110445	249	249	0	1086: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
600051	249	249	0	1086: CONDUCT VCA FY-2000	10CT99	29SEP00
110390	20	20	0	1086: Incorp EPA/NMED Comments on CMS Plan	40CT99	1NOV99
110395	10	10	0	1086: Issue Final CMS Plan	2NOV99	16NOV99
110400	5	5	0	1086: EPA Approves CMS Plan	17NOV99	23NOV99
11M065	0	0	0	1086: EPA APPROVED CMS PLAN		23NOV99
110405	245	245	0	1086: Conduct CMS Bench/Pilot Studies (LOE)	24NOV99	16NOV00
110415	30	30	0	1086: Conduct Technical Evaluation for CMS Rpt	24NOV99	11JAN00
110420	30	30	0	1086: Conduct Environmental Eval for CMS Rpt	24NOV99	11JAN00
110425	30	30	0	1086: Cond Human Health Evaluation for CMS Rpt	24NOV99	11JAN00
110430	30	30	0	1086: Cond Community Relations Eval for CMS Rpt	24NOV99	11JAN00
110435	30	30	0	1086: Conduct Cost Evaluation for CMS Report	24NOV99	11JAN00

LANL INC-7 AL OGARD

FINEST HOUR

ADS 1086: TA-15

TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 137  
15:49


ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 8JUN01

1086 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
110440	30	30	0	1086: Develop NEPA Documentation for CMS Report	24NOV99	11JAN00
11M070	0	0	0	1086: START CMS WORK	24NOV99	
11M075	0	0	0	1086: START DEVELOPMENT OF CMS REPORT	24NOV99	
110450	10	10	0	1086: Prepare Internal Draft of CMS Report	12JAN00	26JAN00
110455	10	10	0	1086: DOE/LANL/VE Rev Internal Draft of CMS Rpt	27JAN00	9FEB00
110460	35	35	0	1086:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	27SEP00	16NOV00
600055	100	100	0	1086: CONDUCT VCA FY-2001	20CT00	1MAR01
11M080	0	0	0	1086: CMS WORK COMPLETED		16NOV00
110465	10	10	0	1086: Issue DOE Draft of CMS Report	17NOV00	4DEC00
110470	22	22	0	1086: Conduct Review of DOE Draft of CMS Report	5DEC00	8JAN01
110475	22	22	0	1086: Incorp DOE Rev Comments DOE Dft CMS Rpt	9JAN01	8FEB01
110480	10	10	0	1086: Issue EPA/NMED Draft of CMS Report	9FEB01	23FEB01
11M085	0	0	0	1086: EPA/NMED DRAFT OF CMS REPORT COMPLETED		23FEB01
110485	44	44	0	1086: Conduct EPA Review of CMS Report	26FEB01	26APR01
110490	44	44	0	1086: Conduct NMED Review of CMS Report	26FEB01	26APR01
110495	20	20	0	1086: Incorp EPA/NMED Comments on CMS Report	27APR01	24MAY01
110505	10	10	0	1086: Issue Final CMS Report	25MAY01	8JUN01
11M090	0	0	0	1086: ASSESSMENT COMPLETED		8JUN01

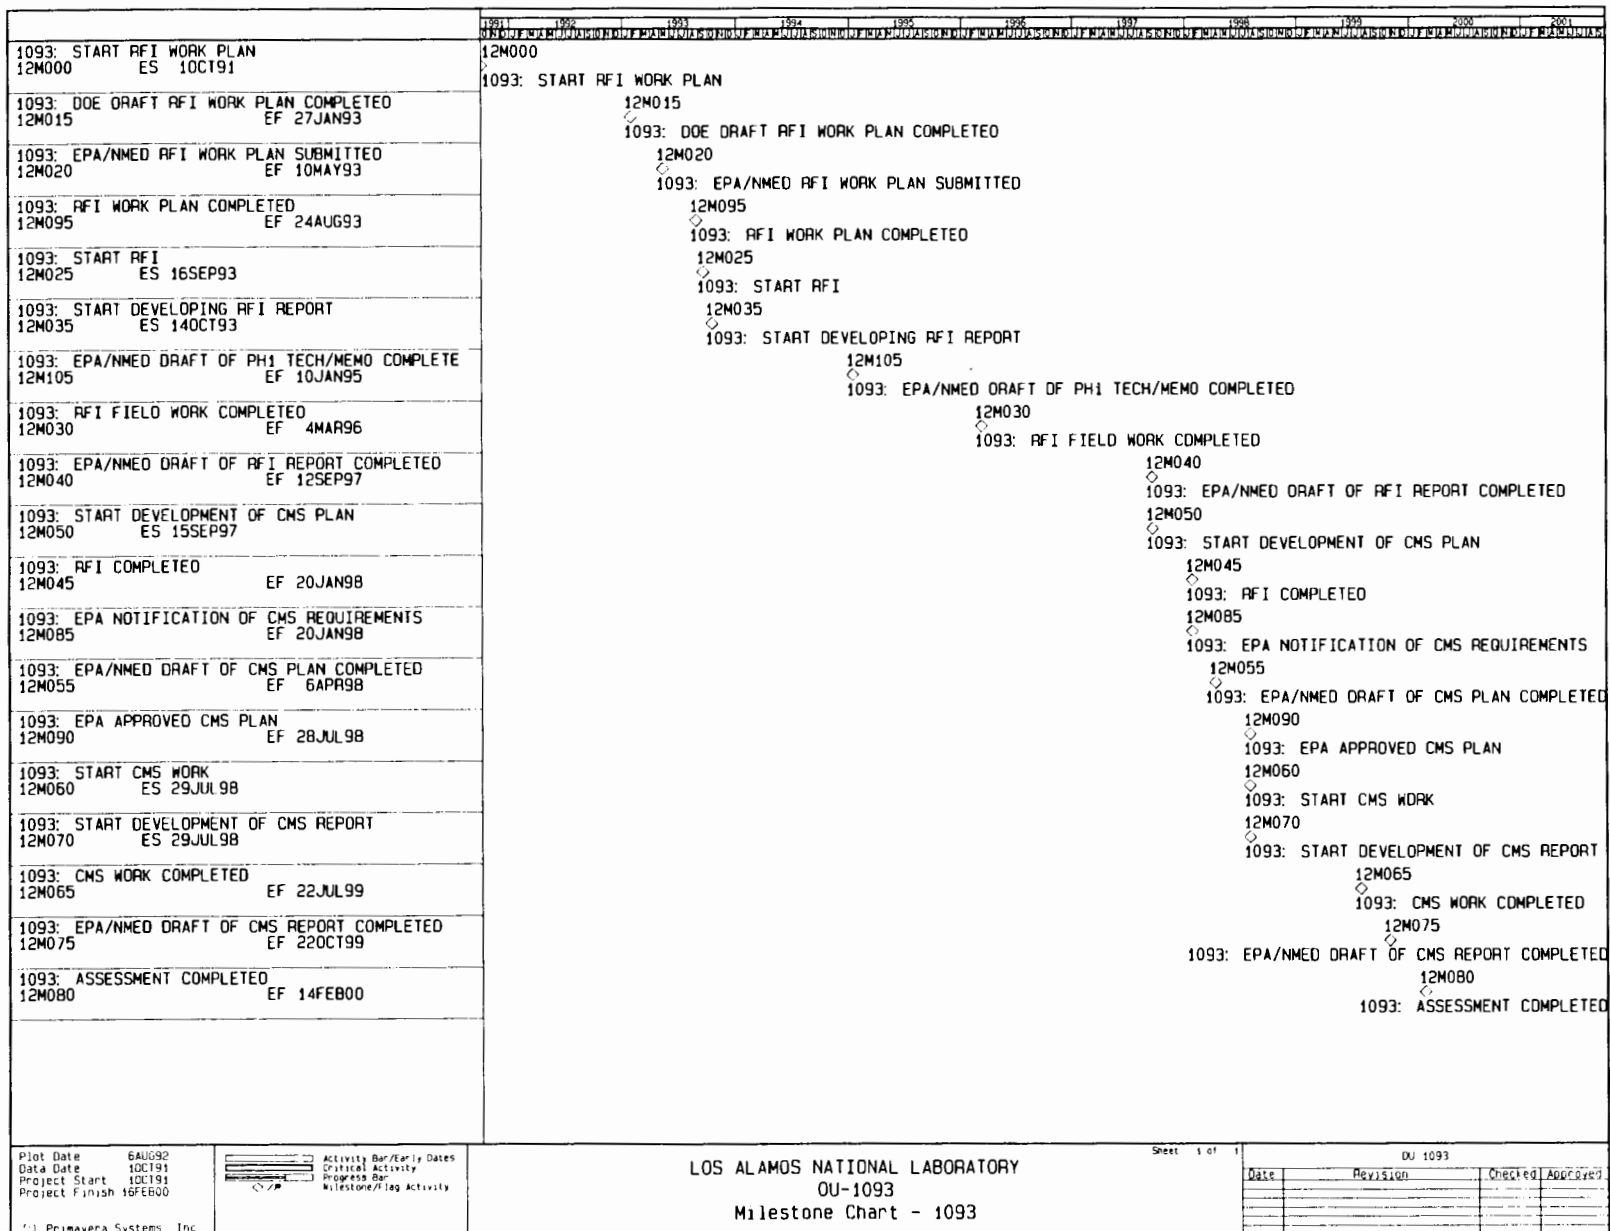



ADS 1093: TA-18 27 65      TBS 2/17/94

START DATE 1OCT91 FIN DATE 16FEB00

DATA DATE 10OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
120035	101	101	0	1093: Prepare Draft Historical Operations for WP	10CT91	2MAR92
120186	60	60	0	1093: Prepare Dft for Records Mgmt Pl for WP	10CT91	31DEC91
120339	246	246	0	1093: Manage ADS During FY-92 (LOE)	10CT91	24SEP92
120805	246	246	0	1093: Conduct Vol Corr Actions for RFI WP (LOE)	10CT91	24SEP92
120810	245	245	0	1093: Cond Bench/Pilot Studies for RFI WP (LOE)	10CT91	23SEP92
125005	246	246	0	CONDUCT VCA FY-92	10CT91	24SEP92
12M000	0	0	0	1093: START RFI WORK PLAN	10CT91	
120055	104	104	0	1093: Prepare NEPA Environmental Settings	1NOV91*	6APR92
120095	82	82	0	1093: Prepare Dft Technical Approach for WP	16DEC91	14APR92
120110	42	42	0	1093: Prepare Draft Nature and Extent for WP	16DEC91	18FEB92
120125	42	42	0	1093: Prepare Draft Data Requirements for WP	17JAN92	17MAR92
120140	42	42	0	1093: Prepare Draft Field Sampling Plan for WP	3MAR92	29APR92
120200	22	22	0	1093: Review Draft Fact Sheets for WP	17MAR92	15APR92
120155	42	42	0	1093: Prepare Dft Quality Assurance Plan for WP	1APR92	29MAY92
120170	42	42	0	1093: Prepare Dft Health and Safety Plan for WP	1APR92	29MAY92
120185	42	42	0	1093: Prepare Dft Community Relations Pl. for WP	1APR92	29MAY92
120210	42	42	0	1093: Prepare Dft Project Management Plan for WP	1APR92	29MAY92
120150	10	10	0	1093: Revise Draft Field Sampling Plan for WP	15APR92	28APR92
120000	40	40	0	1093: Develop LANL Internal Draft RFI Work Plan	24SEP92	20NOV92
120340	245	245	0	1093: Manage ADS During FY-93 (LOE)	25SEP92	20SEP93
120900	57	57	0	1093: Nepa Activity Prior to WP Submittal	10CT92*	24DEC92
120905	57	57	0	1093: Prepare NEPA Draft Environmental Setting	10CT92*	24DEC92
120910	57	57	0	1093: Prepare Draft Field Sampling Plan	10CT92*	24DEC92
125010	245	245	0	CONDUCT VCA - FY-93	10CT92*	24SEP93
120005	20	20	0	1093: Conduct LANL/VE Rev of Int Draft RFI WP	23NOV92	22DEC92
120010	20	20	0	1093:Incorp LANL Comments/Develop DOE Dft RFI WP	29DEC92	27JAN93
12M015	0	0	0	1093: DOE DRAFT RFI WORK PLAN COMPLETED		27JAN93
120015	22	22	0	1093: Conduct DOE Review of DOE Draft RFI WP	28JAN93	1MAR93
120020	40	40	0	1093: Incorp DOE Comments into EPA/NMED RFI WP	2MAR93	26APR93
120025	10	10	0	1093: Publish EPA/NMED Draft RFI Work Plan	27APR93	10MAY93

LANL MEE-4 GENE GOULD

FINEST HOUR

ADS 1093: TA-18 27 65 TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 107  
15:50

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 16FEB00

1093 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
12M020	0	0	0	1093: EPA/NMED RFI WORK PLAN SUBMITTED		10MAY93
120030	44	44	0	1093: Conduct EPA Review of RFI Work Plan	11MAY93	13JUL93
120031	44	44	0	1093: Conduct NMED Review of RFI Work Plan	11MAY93	13JUL93
120740	45	45	0	1093: Write PH1 Contracts for RFI	14JUL93	15SEP93
120745	20	20	0	1093: Incorporate EPA/NMED Comments for RFI WP	14JUL93	10AUG93
120750	10	10	0	1093: Publish Final RFI Work Plan	11AUG93	24AUG93
12M095	0	0	0	1093: RFI WORK PLAN COMPLETED		24AUG93
120390	20	20	0	1093: Mobilize for RFI	16SEP93	13OCT93
120395	245	245	0	1093: Conduct RFI Bench/Pilot Studies (LOE)	16SEP93	8SEP94
120735	245	245	0	1093: Assmt - Conduct VCA (LOE)	16SEP93	8SEP94
12M025	0	0	0	1093: START RFI	16SEP93	
120345	246	246	0	1093: Manage ADS During FY-94 (LOE)	21SEP93	14SEP94
125015	246	246	0	CONDUCT VCA FY-94	27SEP93	20SEP94
120400	245	245	0	1093: Conduct RFI PH1 Field Work	14OCT93	6OCT94
120405	245	245	0	1093: Conduct RFI PH1 Sample Analysis	14OCT93	6OCT94
120410	245	245	0	1093: Conduct RFI PH1 Data Assessment	14OCT93	6OCT94
120525	100	100	0	1093: Develop NEPA Documentation for RFI Report	14OCT93	14MAR94
12M035	0	0	0	1093: START DEVELOPING RFI REPORT	14OCT93	
120350	244	244	0	1093: Manage ADS During FY-95 (LOE)	15SEP94	8SEP95
125020	245	245	0	CONDUCT VCA FY-95	21SEP94	15SEP95
120415	60	60	0	1093: Write RFI PH1 Tech Memo/WP Modification	7OCT94	10JAN95
120420	20	20	0	1093: Demobilize RFI PH1 Field Work	7OCT94	4NOV94
12M105	0	0	0	1093: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		10JAN95
120425	22	22	0	1093: EPA/NMED Rev PH1 Tech Memo/WP Modification	11JAN95	10FEB95
120430	22	22	0	1093: DOE Review PH1 Tech Memo/WP Modification	11JAN95	10FEB95
120435	20	20	0	1093: Write PH2 Contract; Mobilize for RFI	11JAN95	8FEB95
120440	245	245	0	1093: Conduct RFI PH2 Field Work	13FEB95	6FEB96
120445	245	245	0	1093: Conduct RFI PH2 Sample Analysis	13FEB95	6FEB96
120455	245	245	0	1093: Conduct RFI PH2 Data Assessment	13FEB95	6FEB96
120355	246	246	0	1093: Manage ADS During FY-96 (LOE)	11SEP95	4SEP96

LANL MEE-4	GENE GOULD	FINEST HOUR	ADS 1093: TA-18 27 65	TBS 2/17/92
REPORT DATE	5AUG92	RUN NO. 107	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 16FEB00
15:50				
1093 SCHEDULE REPORT BY EARLY START			DATA DATE 10CT91	PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
125025	245	245	0	CONDUCT VCA FY-96	18SEP95	10SEP96
120450	18	18	0	1093: Demoblize RFI PH2 Field Work	7FEB96	4MAR96
120515	100	100	0	1093: Conduct RFI Report Facility Investigation	7FEB96	27JUN96
120520	110	110	0	1093: Conduct RFI Report Investigation Analysis	7FEB96	12JUL96
12M030	0	0	0	1093: RFI FIELD WORK COMPLETED		4MAR96
120535	132	132	0	1093: Prepare Internal Draft of RFI Report	15JUL96	27JAN97
120360	245	245	0	1093: Manage ADS During FY-97 (LOE)	5SEP96	28AUG97
125030	245	245	0	CONDUCT VCA FY-97	11SEP96	4SEP97
570000	189	189	0	1093: Conduct VCA (LOE)	2JAN97*	30SEP97
120540	20	20	0	1093: LANL/VE Review Internal Draft of RFI Rpt	28JAN97	25FEB97
120545	40	40	0	1093:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	26FEB97	22APR97
120550	20	20	0	1093: Publish DOE Draft of RFI Report	23APR97	20MAY97
120555	22	22	0	1093: Conduct Review of DOE Draft of RFI Report	21MAY97	20JUN97
120560	40	40	0	1093:Incorp. DOE Rev. Comments DOE Dft RFI Rpt	23JUN97	18AUG97
120565	18	18	0	1093: Publish EPA/NMED Draft of RFI Report	19AUG97	12SEP97
120365	245	245	0	1093: Manage ADS During FY-98 (LOE)	29AUG97	24AUG98
125035	245	245	0	CONDUCT VCA FY-98	5SEP97	28AUG98
12M040	0	0	0	1093: EPA/NMED DRAFT OF RFI REPORT COMPLETED		12SEP97
120570	44	44	0	1093: Conduct EPA Review of RFI Report	15SEP97	17NOV97
120575	44	44	0	1093: Conduct NMED Review of RFI Rpt	15SEP97	17NOV97
120580	245	245	0	1093: Conduct Bench/Pilot Studies CMS Plan (LOE)	15SEP97	8SEP98
120585	35	35	0	1093: Establish Current Situation for CMS Plan	15SEP97	3NOV97
120590	35	35	0	1093: Establish CA Objectives for CMS Plan	15SEP97	3NOV97
120595	35	35	0	1093: Develop Screening Technologies for CMS Pl	15SEP97	3NOV97
120600	245	245	0	1093: Develop NEPA Documentation for CMS Plan	15SEP97	8SEP98
12M050	0	0	0	1093: START DEVELOPMENT OF CMS PLAN	15SEP97	
570005	245	245	0	1093: Conduct VCA (LOE)	1OCT97	24SEP98
120605	15	15	0	1093: Develop Alternatives for CMS Plan	4NOV97	27NOV97
120770	20	20	0	1093: Incorporate EPA/NMED Comments on RFI Rpt	18NOV97	17DEC97
120610	10	10	0	1093: Develop Internal Draft of CMS Plan	28NOV97	11DEC97

ADS 1093: TA-18 27 65      TBS 2/17/92

START DATE 10OCT91 FIN DATE 16FEB00

DATA DATE 10OCT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
120615	10	10	0	1093: LANL/VE Review Internal Draft of CMS Plan	12DEC97	29DEC97
120775	20	20	0	1093: Publish Final RFI Report	18DEC97	20JAN98
120620	10	10	0	1093:Incorp. LANL REV Comments Intern Dft CMS PL	30DEC97	14JAN98
120625	5	5	0	1093: Publish DOE Draft of CMS Plan	15JAN98	21JAN98
12M045	0	0	0	1093: RFI COMPLETED		20JAN98
12M085	0	0	0	1093: EPA NOTIFICATION OF CMS REQUIREMENTS		20JAN98
120630	22	22	0	1093: Conduct Review of DOE Draft of CMS Plan	22JAN98	23FEB98
120635	20	20	0	1093:Incorp. DOE Rev.Comments DOE Dft.of CMS Pl	24FEB98	23MAR98
120640	10	10	0	1093: Publish EPA/NMED Draft of CMS Plan	24MAR98	6APR98
12M055	0	0	0	1093: EPA/NMED DRAFT OF CMS PLAN COMPLETED		6APR98
120645	44	44	0	1093: Conduct EPA Review of CMS Plan	7APR98	8JUN98
120650	44	44	0	1093: Conduct NMED Review of CMS Plan	7APR98	8JUN98
120780	20	20	0	1093: Incorporate EPA/NMED Comments on CMS Plan	9JUN98	7JUL98
120785	10	10	0	1093: Publish Final CMS Plan	8JUL98	21JUL98
120790	5	5	0	1093: EPA Approves CMS Plan	22JUL98	28JUL98
12M090	0	0	0	1093: EPA APPROVED CMS PLAN		28JUL98
120655	245	245	0	1093: Conduct CMS Bench/Pilot Studies (LOE)	29JUL98	22JUL99
120660	30	30	0	1093: Conduct Technical Evaluation for CMS Rpt	29JUL98	9SEP98
120665	30	30	0	1093: Conduct Environmental Eval for CMS Report	29JUL98	9SEP98
120670	30	30	0	1093: Conduct Human Health Eval for CMS Report	29JUL98	9SEP98
120675	30	30	0	1093: Conduct Community Relations Eval. CMS Rpt	29JUL98	9SEP98
120680	30	30	0	1093: Conduct Cost Evaluation for CMS Report	29JUL98	9SEP98
120685	30	30	0	1093: Develop NEPA Documentation for CMS Report	29JUL98	9SEP98
12M060	0	0	0	1093: START CMS WORK	29JUL98	
12M070	0	0	0	1093: START DEVELOPMENT OF CMS REPORT	29JUL98	
120370	245	245	0	1093: Manage ADS During FY-99 (LOE)	25AUG98	18AUG99
125040	245	245	0	CONDUCT VCA FY-99	31AUG98	24AUG99
120690	10	10	0	1093: Prepare Internal Draft of CMS Report	10SEP98	23SEP98
120695	10	10	0	1093: LANL/VE Review Internal Draft of CMS Rpt	24SEP98	7OCT98
120700	35	35	0	1093: Incorp.LANL Rev Commt Intern Dft CMS Rpt	3JUN99	22JUL99


ADS 1093: TA-18 27 65      TBS 2/17/92

START DATE 1OCT91 FIN DATE 16FEB00

DATA DATE 10OCT91 PAGE NO. 5

DATA DATE 10OCT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
12M065	0	0	0	1093: CMS WORK COMPLETED		22JUL99
120705	10	10	0	1093: Publish DOE Draft of CMS Report	23JUL99	5AUG99
120710	22	22	0	1093: Conduct Review of DOE Draft of CMS Report	6AUG99	7SEP99
120375	115	115	0	1093: Manage ADS During FY-00 (LOE)	19AUG99	8FEB00
125045	117	117	0	CONDUCT VCA FY-00	25AUG99	16FEB00
120715	22	22	0	1093:Incorp. DOE Rev Comments DOE Dft CMS Report	8SEP99	7OCT99
120720	10	10	0	1093: Publish EPA/NMED Draft of CMS Report	8OCT99	22OCT99
12M075	0	0	0	1093: EPA/NMED DRAFT OF CMS REPORT COMPLETED		22OCT99
120725	44	44	0	1093: Conduct EPA Review of CMS Report	25OCT99	30DEC99
120730	44	44	0	1093: Conduct NMED Review of CMS Report	25OCT99	30DEC99
120795	20	20	0	1093: Incorporate EPA/NMED Comments on CMS Rpt	3JAN00	31JAN00
120800	10	10	0	1093: Publish Final CMS Report	1FEB00	14FEB00
12M080	0	0	0	1093: ASSESSMENT COMPLETED		14FEB00

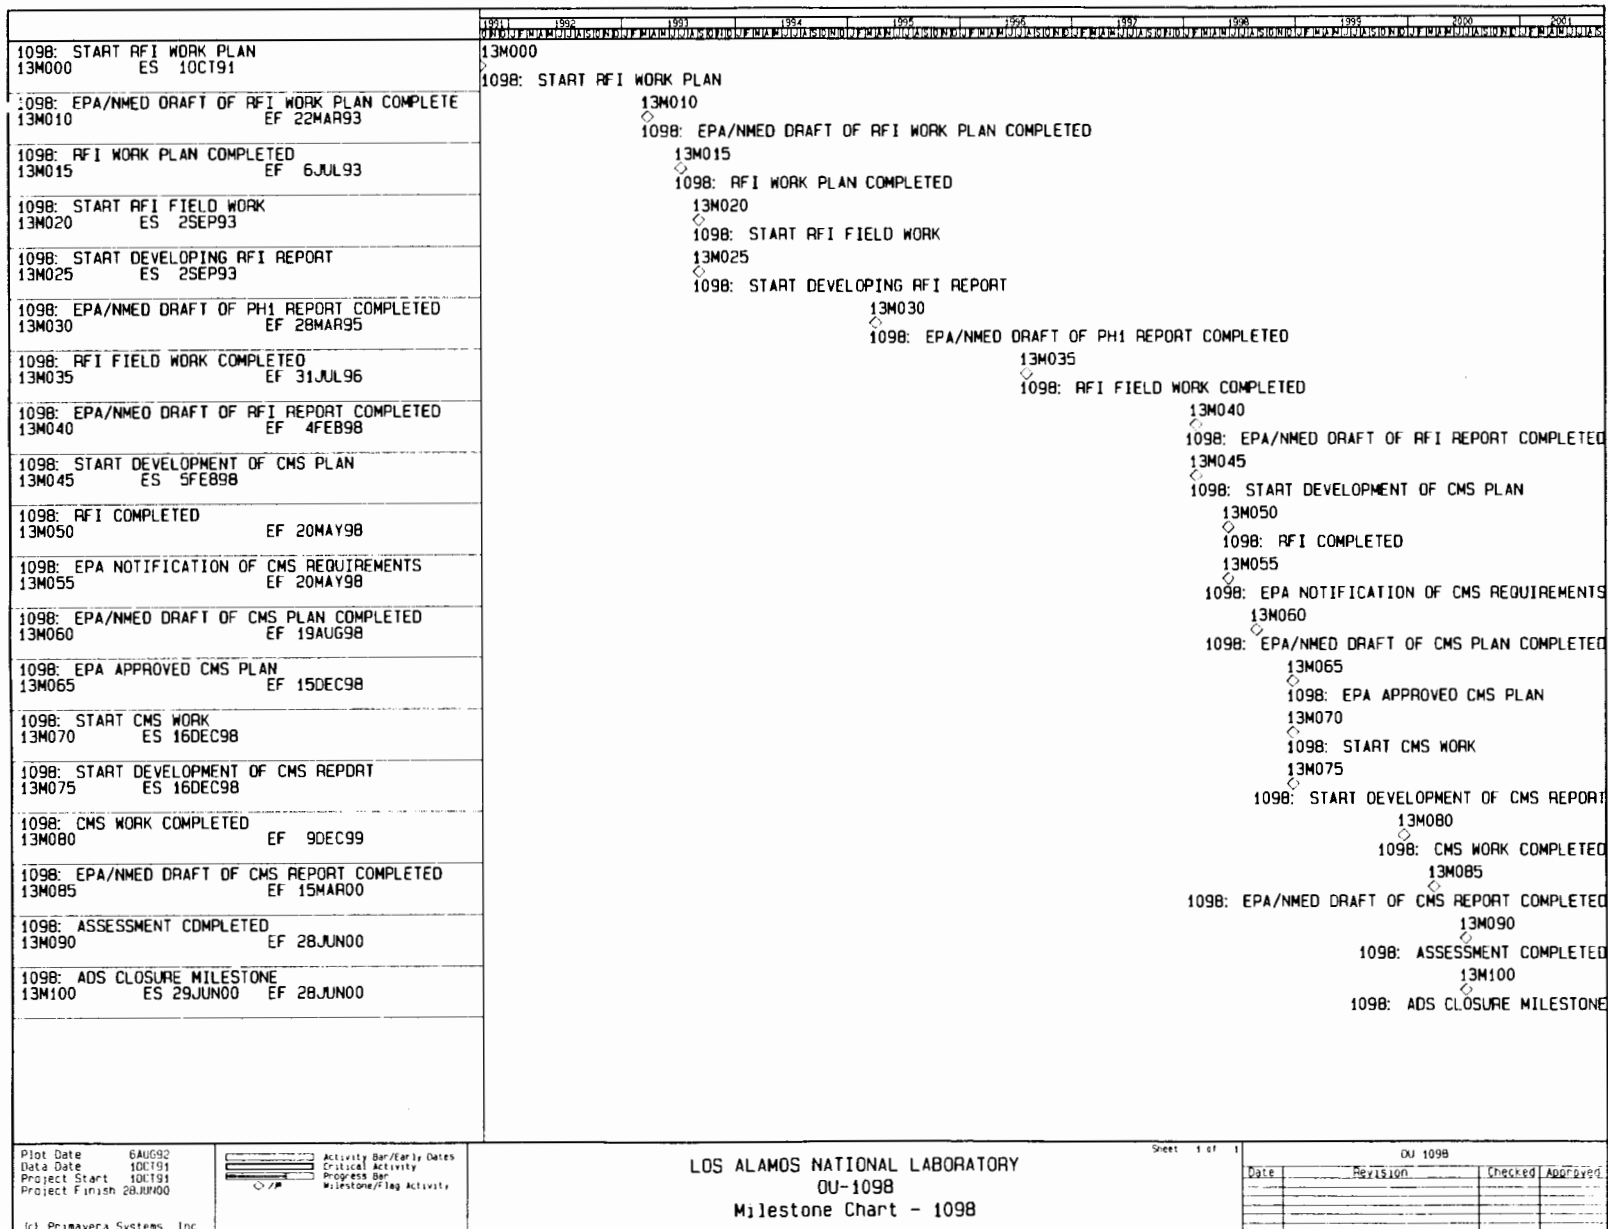

LANL INC-4 P. LONGMIRE	FINEST HOUR	ADS 1098: TA-2 41	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 70	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 28JUN00
15:50			
1098 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91	PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
130000	250	250	0	1098: Cond Bench/Pilot Studies for RFI WP (LOE)	10CT91	30SEP92
130005	250	250	0	1098: Cond Voluntary C.Actions for RFI WP (LOE)	10CT91	30SEP92
130015	250	250	0	1098: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
130025	250	250	0	1098: Develop NEPA Documentation for RFI WP FY92	10CT91	30SEP92
610010	250	250	0	1098: CONDUCT VCA FY-92	10CT91	30SEP92
13M000	0	0	0	1098: START RFI WORK PLAN	10CT91*	
130010	24	24	0	1098: Develop Scope for RFI WP	30CT91*	6NOV91
130030	40	40	0	1098: Locate Existing Data for RFI WP	7NOV91	9JAN92
130035	38	38	0	1098: Analyze Existing Data for RFI WP	10JAN92	5MAR92
130040	20	20	0	1098: Draft Existing Data Report for RFI WP	6MAR92	2APR92
130045	40	40	0	1098: Determine Data Needs for RFI WP	3APR92	29MAY92
130065	60	60	0	1098: Develop Sampling Plan for RFI WP	1JUN92	24AUG92
130080	20	20	0	1098: Write Health & Safety Plan for RFI WP	25AUG92	22SEP92
130055	20	20	0	1098: Write Records Management Plan for RFI WP	27AUG92	24SEP92
130075	20	20	0	1098: Write Quality Assurance Plan for RFI WP	31AUG92	28SEP92
130050	20	20	0	1098: Write Community Relations Plan for RFI WP	2SEP92	30SEP92
130085	20	20	0	1098: Write Management Plan for RFI WP	4SEP92	20CT92
130070	249	249	0	1098: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
130515	249	249	0	1098: FY-93 Conduct Bench/Pilot Studies RFI(LOE)	10CT92	30SEP93
130600	249	249	0	1098: Develop NEPA Documentation for RFI WP FY93	10CT92	30SEP93
130605	38	38	0	1098: Analyze Existing Data for RFI WP-FY93	10CT92*	25NOV92
610015	249	249	0	1098: CONDUCT VCA FY-93	10CT92	30SEP93
130090	20	20	0	1098: Develop LANL Internal Draft of RFI WP	50CT92	2NOV92
130095	22	22	0	1098: DOE/LANL/VE Review Internal Draft RFI WP	3NOV92	7DEC92
130610	20	20	0	1098: Draft Existing Data Report for RFI WP FY93	30NOV92	29DEC92
130100	20	20	0	1098: Incorporate LANL Rev Comments Intern Dft RFI WP	8DEC92	7JAN93
130615	60	60	0	1098: Develop Sampling Plan for RFI WP FY-93	30DEC92*	26MAR93
130105	10	10	0	1098: Issue DOE Draft of RFI WP	8JAN93	22JAN93
130110	10	10	0	1098: DOE Review of DOE Draft of RFI WP	25JAN93	5FEB93
130115	20	20	0	1098: Incorporate DOE Rev.Comments into DOE Dft RFI W	8FEB93	8MAR93

LANL INC-4 P. LONGMIRE  
 REPORT DATE 5AUG92 RUN NO. 70  
 1098 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

ADS 1098: TA-2 41  
 START DATE 10CT91  
 DATA DATE 10CT91

TBS 2/17/92  
 FIN DATE 28JUN00  
 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
130120	10	10	0	1098: Issue EPA/NMED Draft of RFI Work Plan	9MAR93	22MAR93
13M010	0	0	0	1098: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		22MAR93
130125	44	44	0	1098: Conduct NMED Review of RFI Work Plan	23MAR93	21MAY93
130130	44	44	0	1098: Conduct EPA Review of RFI Work Plan	23MAR93	21MAY93
130510	128	128	0	1098: Conduct Tech Support for Gen Charac (LOE)	1APR93*	30SEP93
130140	20	20	0	1098: Incorporate EPA/NMED Comments for RFI WP	24MAY93	21JUN93
130135	65	65	0	1098: Write Ph1 Contracts and Mobilze for RFI	2JUN93	1SEP93
130145	10	10	0	1098: Issue Final RFI Work Plan	22JUN93	6JUL93
13M015	0	0	0	1098: RFI WORK PLAN COMPLETED		6JUL93
130165	245	245	0	1098: Conduct RFI PH1 Field Work	2SEP93	25AUG94
130180	245	245	0	1098: Prep NEPA Environmental Info for RFI Rpt	2SEP93	25AUG94
13M020	0	0	0	1098: START RFI FIELD WORK	2SEP93	
13M025	0	0	0	1098: START DEVELOPING RFI REPORT	2SEP93	
130155	250	250	0	1098: Assmt - Conduct VCA (LOE)	10CT93*	30SEP94
130160	250	250	0	1098: Manage ADS During FY-94 (LOE)	10CT93	30SEP94
130520	250	250	0	1098: FY-94 Conduct Bench/Pilot Studies RFI(LOE)	10CT93	30SEP94
610020	250	250	0	1098: CONDUCT VCA FY-94	10CT93	30SEP94
130170	245	245	0	1098: Conduct RFI PH1 Sample Analysis	15OCT93	7OCT94
130175	245	245	0	1098: Conduct RFI PH1 Data Assessment	29OCT93	24OCT94
130195	20	20	0	1098: Demobilize RFI PH1 Field Work	26AUG94	23SEP94
130185	247	247	0	1098: Manage ADS During FY-95 (LOE)	30CT94	29SEP95
610025	247	247	0	1098: CONDUCT VCA FY-95	30CT94	29SEP95
130190	60	60	0	1098: Write Draft RFI PH1 Report / WP Mod	25OCT94	26JAN95
130205	22	22	0	1098: DOE Review PH1 Report / WP Modification	27JAN95	28FEB95
130207	20	20	0	1098: Inc DOE/LANL/VE Comments Ph1 Rpt/WP Mod	1MAR95	28MAR95
13M030	0	0	0	1098: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		28MAR95
130200	22	22	0	1098: EPA/NMED Rev PH1 Report / WP Modification	29MAR95	27APR95
130208	40	40	0	1098: Inc EPA/NMED Comments Ph1 Rpt /WP Mod	28APR95	23JUN95
130210	20	20	0	1098: Write PH2 Contract; Mobilize for RFI	12JUN95	10JUL95
130209	10	10	0	1098: Issue Final Ph1 Report / WP Modification	26JUN95	10JUL95



TBS 2/17/92

1098 SCHEDULE REPORT BY EARLY START

DATA DATE 10OCT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
130215	245	245	0	1098: Conduct RFI PH2 Field Work	11JUL95	2JUL96
130220	245	245	0	1098: Conduct RFI PH2 Sample Analysis	22AUG95	14AUG96
130225	245	245	0	1098: Conduct RFI PH2 Data Assessment	6SEP95	28AUG96
130230	249	249	0	1098: Manage ADS During FY-96 (LOE)	20CT95	30SEP96
610030	249	249	0	1098: CONDUCT VCA FY-96	20CT95	30SEP96
130245	20	20	0	1098: Demoblize RFI PH2 Field Work	3JUL96	31JUL96
13M035	0	0	0	1098: RFI FIELD WORK COMPLETED		31JUL96
130235	100	100	0	1098: Conduct RFI Report Facility Investigation	29AUG96	28JAN97
130255	249	249	0	1098: Manage ADS During FY-97 (LOE)	10CT96	30SEP97
610035	249	249	0	1098: CONDUCT VCA FY-97	10CT96	30SEP97
580000	189	189	0	1098: Conduct VCA UNDERGROUND TANKS FY-97 (LOE)	2JAN97*	30SEP97
130240	110	110	0	1098: Conduct RFI Report Investigation Analysis	29JAN97	3JUL97
130250	132	132	0	1098: Prepare Internal Draft of RFI Report	29JAN97	5AUG97
130260	22	22	0	1098: DOE/LANL/VE Rev Internal Draft of RFI Rpt	7JUL97	5AUG97
130265	40	40	0	1098: Incorp.LANL Rev Comments Intern Dft RFI WP	6AUG97	10CT97
130290	249	249	0	1098: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
580005	249	249	0	1098: Conduct VCA (LOE) FY-98	10CT97	30SEP98
610040	249	249	0	1098: CONDUCT VCA FY-98	10CT97	30SEP98
130270	10	10	0	1098: Issue DOE Draft of RFI Report	20CT97	16OCT97
130275	22	22	0	1098: Conduct Review of DOE Draft of RFI Report	17OCT97	18NOV97
130280	40	40	0	1098: Incorp DOE Rev Comments DOE Dft RFI Report	19NOV97	21JAN98
130285	10	10	0	1098: Issue EPA/NMFD Draft of RFI Report	22JAN98	4FEB98
13M040	0	0	0	1098: EPA/NMED DRAFT OF RFI REPORT COMPLETED		4FEB98
130295	44	44	0	1098: Conduct EPA Review of RFI Report	5FEB98	8APR98
130300	44	44	0	1098: Conduct NMED Review of RFI Report	5FEB98	8APR98
130305	245	245	0	1098: Cond Bench/Pilot Studies for CMS Plan(LOE)	5FEB98	29JAN99
130310	35	35	0	1098: Establish Current Situation for CMS Plan	5FEB98	26MAR98
130315	35	35	0	1098: Establish CA Objectives for CMS Plan	5FEB98	26MAR98
130320	35	35	0	1098: Develop Screening Technologies CMS Plan	5FEB98	26MAR98
130325	245	245	0	1098: Develop NEPA Documentation for CMS Plan	5FEB98	29JAN99

-----


LANL INC-4 P. LONGMIRE	FINEST HOUR	ADS 1098: TA-2 41	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 70	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 28JUN00
15:50			
1098 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91	PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
13M045	0	0	0	1098: START DEVELOPMENT OF CMS PLAN	5FEB98	
130330	15	15	0	1098: Develop Alternatives for CMS Plan	27MAR98	16APR98
130335	20	20	0	1098: Incorp EPA/NMED Comments on RFI Report	9APR98	6MAY98
130340	10	10	0	1098: Develop Internal Draft of CMS Plan	17APR98	30APR98
130345	10	10	0	1098: DOE/LANL/VE Rev Internal Draft of CMS Plan	1MAY98	14MAY98
130350	10	10	0	1098: Issue Final RFI Report	7MAY98	20MAY98
130355	10	10	0	1098:Incorp LANL REV Comments Intern Dft RFI WP	15MAY98	29MAY98
13M050	0	0	0	1098: RFI COMPLETED		20MAY98
13M055	0	0	0	1098: EPA NOTIFICATION OF CMS REQUIREMENTS		20MAY98
130360	5	5	0	1098: Issue DOE Draft of CMS Plan	1JUN98	5JUN98
130365	22	22	0	1098: Cond Review of DOE Draft of CMS Plan	8JUN98	8JUL98
130370	20	20	0	1098:Incorp DOE Rev.Comments DOE Dft of CMS Plan	9JUL98	5AUG98
130375	10	10	0	1098: Issue EPA/NMED Draft of CMS Plan	6AUG98	19AUG98
13M060	0	0	0	1098: EPA/NMED DRAFT OF CMS PLAN COMPLETED		19AUG98
130380	44	44	0	1098: Conduct EPA Review of CMS Plan	20AUG98	22OCT98
130385	44	44	0	1098: Conduct NMED Review of CMS Plan	20AUG98	22OCT98
130410	245	245	0	1098: Manage ADS During FY-99 (LOE)	1OCT98	24SEP99
610045	249	249	0	1098: CONDUCT VCA FY-99	1OCT98	30SEP99
130390	20	20	0	1098: Incorp EPA/NMED Comments on CMS Plan	23OCT98	20NOV98
130395	10	10	0	1098: Issue Final CMS Plan	23NOV98	8DEC98
130400	5	5	0	1098: EPA Approves CMS Plan	9DEC98	15DEC98
13M065	0	0	0	1098: EPA APPROVED CMS PLAN		15DEC98
130405	245	245	0	1098: Conduct CMS Bench/Pilot Studies (LOE)	16DEC98	9DEC99
130415	30	30	0	1098: Conduct Technical Evaluation for CMS Rpt	16DEC98	1FEB99
130420	30	30	0	1098: Conduct Environmental Eval for CMS Report	16DEC98	1FEB99
130425	30	30	0	1098:Cond Human Health Evaluation for CMS Report	16DEC98	1FEB99
130430	30	30	0	1098: Cond Community Relations Eval for CMS Rpt	16DEC98	1FEB99
130435	30	30	0	1098: Conduct Cost Evaluation for CMS Report	16DEC98	1FEB99
130440	30	30	0	1098: Develop NEPA Documentation for CMS Report	16DEC98	1FEB99
13M070	0	0	0	1098: START CMS WORK	16DEC98	

LANL INC-4 P. LONGMIRE	FINEST HOUR	ADS 1098: TA-2 41	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 70	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 28JUN00
15:50		DATA DATE 1OCT91	PAGE NO. 5
1098 SCHEDULE REPORT BY EARLY START			

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
13M075	0	0	0	1098: START DEVELOPMENT OF CMS REPORT	16DEC98	
130450	10	10	0	1098: Prepare Internal Draft of CMS Report	2FEB99	16FEB99
130455	10	10	0	1098: DOE/LANL/VE Rev Internal Draft of CMS Rpt	17FEB99	2MAR99
130445	87	87	0	1098: Manage ADS During FY-00 (LOE)	27SEP99	4FEB00
610050	88	88	0	CONDUCT VCA FY-2000	1OCT99	11FEB00
130460	35	35	0	1098:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	19OCT99	9DEC99
13M080	0	0	0	1098: CMS WORK COMPLETED		9DEC99
130465	10	10	0	1098: Issue DOE Draft of CMS Report	10DEC99	23DEC99
130470	22	22	0	1098: Conduct Review of DOE Draft of CMS Report	28DEC99	28JAN00
130475	22	22	0	1098:Incorp. DOE Rev Comments DOE Dft CMS Rpt	31JAN00	1MAR00
130480	10	10	0	1098: Issue EPA/NMED Draft of CMS Report	2MAR00	15MAR00
13M085	0	0	0	1098: EPA/NMED DRAFT OF CMS REPORT COMPLETED		15MAR00
130485	44	44	0	1098: Conduct EPA Review of CMS Report	16MAR00	16MAY00
130490	44	44	0	1098: Conduct NMED Review of CMS Report	16MAR00	16MAY00
130495	20	20	0	1098: Incorp EPA/NMED Comments on CMS Report	17MAY00	14JUN00
130505	10	10	0	1098: Issue Final CMS Report	15JUN00	28JUN00
13M090	0	0	0	1098: ASSESSMENT COMPLETED		28JUN00
13M100	0	0	0	1098: ADS CLOSURE MILESTONE	29JUN00	28JUN00

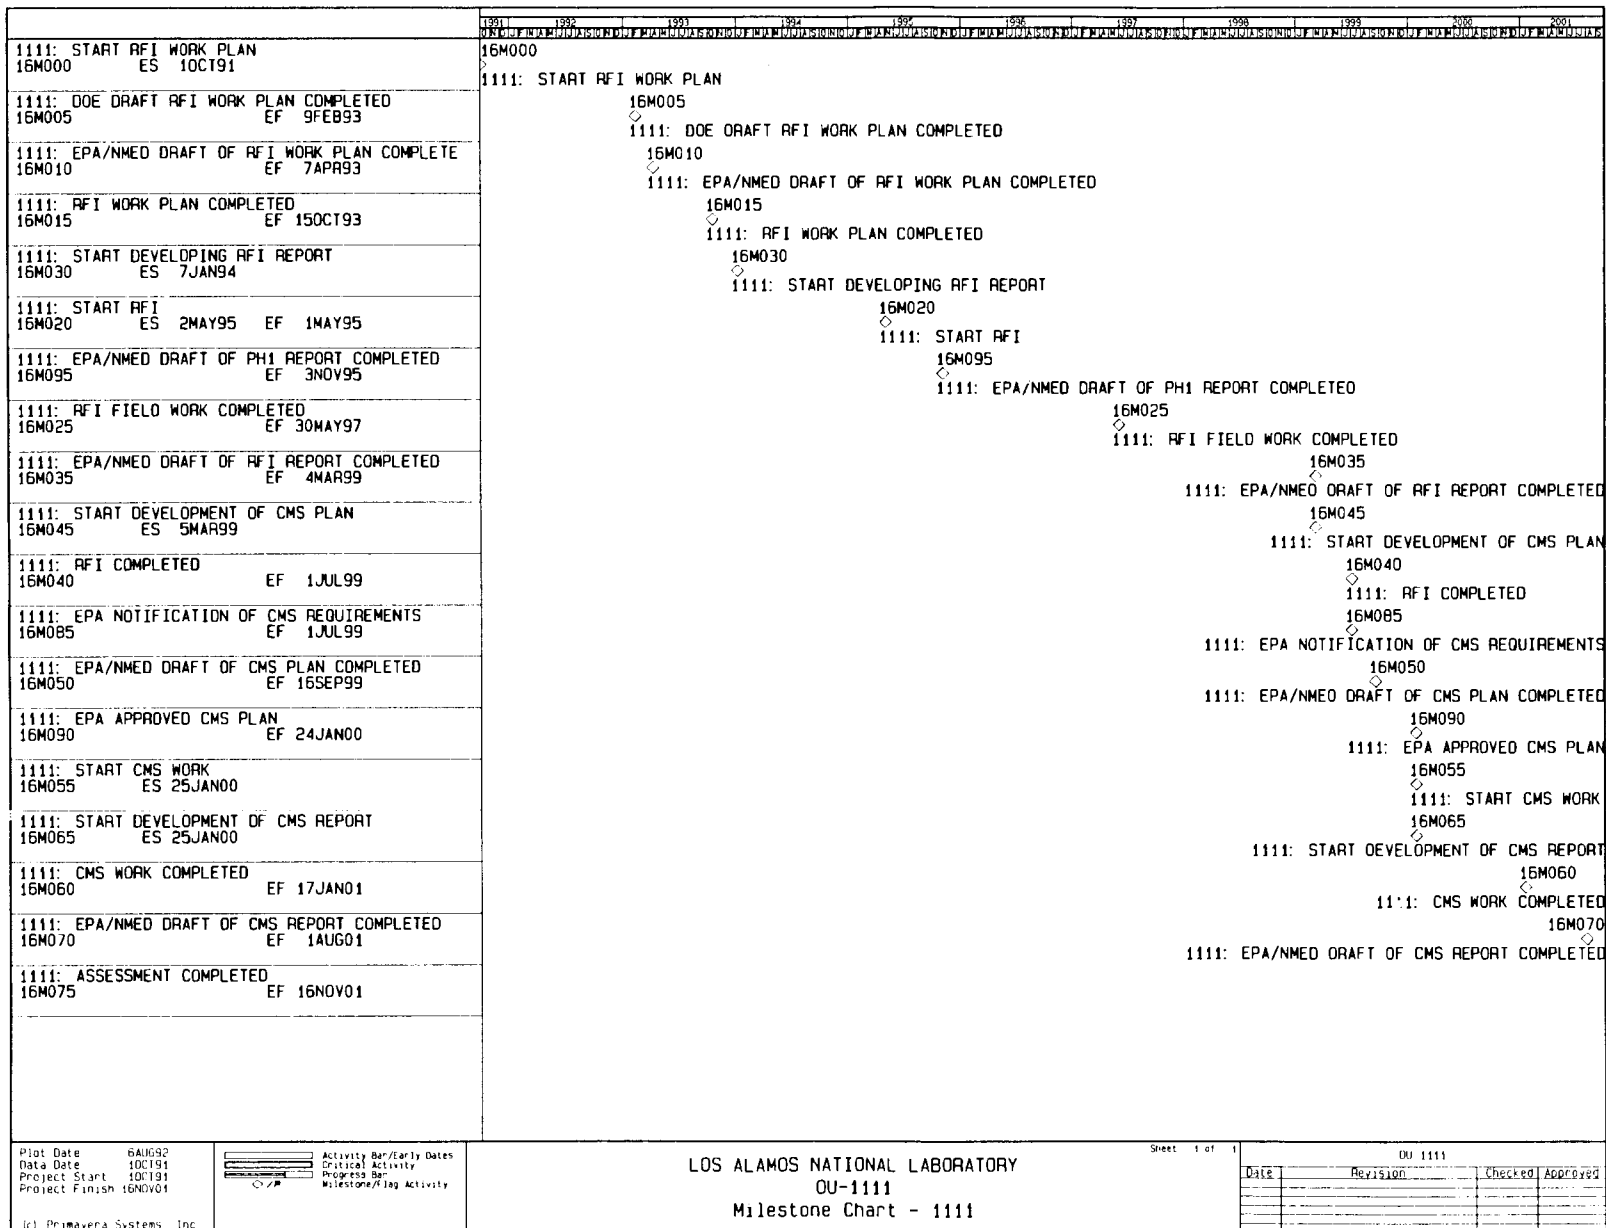

LANL EES-1 C. ROFER  
 REPORT DATE 5AUG92 RUN NO. 204 ENVIRONMENTAL RESTORATION  
 15:53  
 1111 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 1111:TA-6 7 22 40 58 62 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 16NOV01  
 DATA DATE 10CT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
160000	250	250	0	1111:Conduct Bench/Pilot Studies for RFI WP(LOE)	10CT91	30SEP92
160005	250	250	0	1111:Conduct Voluntary C.Actions for RFI WP(LOE)	10CT91	30SEP92
160015	250	250	0	1111: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
160180	250	250	0	1111: Conduct RFI Bench/Pilot Studies (LOE)	10CT91	30SEP92
160640	250	250	0	1111: Conduct MDA F Pilot Studies FY-92 (LOE)	10CT91	30SEP92
616005	250	250	0	CONDUCT VCA FY-92	10CT91	30SEP92
16M000	0	0	0	1111: START RFI WORK PLAN	10CT91*	
160010	20	20	0	1111: Develop Scope for RFI WP	10OCT91*	6NOV91
160020	250	250	0	1111: Develop NEPA Documentation for RFI WP	10OCT91	8OCT92
160025	40	40	0	1111: Locate Existing Data for RFI WP	7NOV91	9JAN92
160035	38	38	0	1111: Analyze Existing Data for RFI WP	10JAN92	5MAR92
160045	20	20	0	1111: Draft Existing Data Report for RFI WP	6MAR92	2APR92
160055	40	40	0	1111: Determine Data Needs for RFI WP	3APR92	29MAY92
160060	20	20	0	1111: Write Community Relations Plan for RFI WP	3APR92	30APR92
160065	20	20	0	1111: Write Records Management Plan for RFI WP	3APR92	30APR92
160095	20	20	0	1111: Write Quality Assurance Plan for RFI WP	3APR92	30APR92
160100	20	20	0	1111: Write Health & Safety Plan for RFI WP	3APR92	30APR92
160105	20	20	0	1111: Write Management Plan for RFI WP	3APR92	30APR92
160845	20	20	0	1111: Write Records Management Plan for RFI WP	3APR92	30APR92
160840	20	20	0	1111: Write Community Relations Plan for RFI WP	10APR92	7MAY92
160075	40	40	0	1111: Develop Data Quality Objectives for RFI WP	1JUN92	27JUL92
160085	60	60	0	1111: Develop Sampling Plan for RFI WP	28JUL92	21OCT92
160030	249	249	0	1111: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
160645	249	249	0	1111: Conduct MDA F Pilot Studies FY-93 (LOE)	10CT92	30SEP93
160830	20	20	0	1111: Develop Scope for RFI WP (NON PERMIT SWMU)	10CT92*	29OCT92
616010	249	249	0	CONDUCT VCA FY-93	10CT92	30SEP93
160115	20	20	0	1111: Develop LANL Internal Draft of RFI WP	22OCT92	19NOV92
160800	40	40	0	1111: Locate Existing Data for non-permit&SWMU's	30OCT92	31DEC92
160125	22	22	0	1111: DOE/LANL/VE Review Internal Draft RFI WP	20NOV92	23DEC92
160135	20	20	0	1111: Incorp.LANL Rev Comments Intern Dft RFI WP	24DEC92	26JAN93

LANL EES-1 C. ROFER  
 REPORT DATE 5AUG92 RUN NO. 204  
 15:53  
 1111 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

1111:TA-6 7 22 40 58 62 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 16NOV01  
 DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
160805	38	38	0	1111: Analyze Existing Data	8JAN93*	4MAR93
160145	10	10	0	1111: Issue DOE Draft of RFI WP	27JAN93	9FEB93
16M005	0	0	0	1111: DOE DRAFT RFI WORK PLAN COMPLETED		9FEB93
160150	10	10	0	1111: DOE Review DOE Draft RFI WP	10FEB93	24FEB93
160155	20	20	0	1111: Incorporate DOE Rev. Comments DOE Dft RFI WP	25FEB93	24MAR93
160810	20	20	0	1111: Draft memo on non-permit & SWMU's	5MAR93	1APR93
160160	10	10	0	1111: Publish EPA/NMED Draft of RFI Work Plan	25MAR93	7APR93
160815	40	40	0	1111: Det Data Needs for eval of potential CM	2APR93	27MAY93
16M010	0	0	0	1111: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		7APR93
160165	44	44	0	1111: Conduct NMED Review of RFI Work Plan	8APR93	9JUN93
160170	44	44	0	1111: Conduct EPA Review of RFI Work Plan	8APR93	9JUN93
160820	40	40	0	1111: Devp Data Qlty Obj for samp of non-permit SW	28MAY93	26JUL93
160595	20	20	0	1111: Incorporate EPA/NMED Comments for RFI WP	10JUN93	8JUL93
160040	250	250	0	1111: Manage ADS During FY-94 (LOE)	10CT93*	30SEP94
160650	250	250	0	1111: Conduct MDA F Pilot Studies FY-94 (LOE)	10CT93	30SEP94
160825	60	60	0	1111: Develop Sampling Plan for non-permit SWMUs	10CT93*	30DEC93
616015	250	250	0	CONDUCT VCA FY-94	10CT93	30SEP94
160590	63	63	0	1111: Write PH1 Contract; Mobilize for RFI	40CT93	6JAN94
160600	10	10	0	1111: Issue Final RFI Work Plan	40CT93	15OCT93
16M015	0	0	0	1111: RFI WORK PLAN COMPLETED		15OCT93
160185	327	327	0	1111: Conduct RFI PH1 Field Work	7JAN94	1MAY95
160190	357	357	0	1111: Conduct RFI PH1 Sample Analysis	7JAN94	13JUN95
160310	100	100	0	1111: Prepare NEPA/Environ. Info for RFI Report	7JAN94	31MAY94
16M030	0	0	0	1111: START DEVELOPING RFI REPORT	7JAN94	
160195	367	367	0	1111: Conduct RFI PH1 Data Assessment	22FEB94	9AUG95
160050	247	247	0	1111: Manage ADS During FY-95 (LOE)	30CT94*	29SEP95
160655	247	247	0	1111: Conduct MDA F Pilot Studies FY-95 (LOE)	30CT94	29SEP95
616020	247	247	0	CONDUCT VCA FY-95	30CT94	29SEP95
160205	20	20	0	1111: Demobilize RFI PH1 Field Work	2MAY95	30MAY95
160520	245	245	0	1111: Assmt - Conduct VCA (LOE)	2MAY95	24APR96

LANL EES-1 C. ROFER

FINEST HOUR

1111:TA-6 7 22 40 58 62 TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 204

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 16NOV01

15:53

1111 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
16M020	0	0	0	1111: START RFI	2MAY95	1MAY95
160200	60	60	0	1111: Write Draft RFI PH1 Report/WP Modification	10AUG95	3NOV95
160070	249	249	0	1111: Manage ADS During FY-96 (LOE)	20CT95	30SEP96
160660	249	249	0	1111: Conduct MDA F Pilot Studies FY-96 (LOE)	20CT95	30SEP96
616025	249	249	0	CONDUCT VCA FY-96	20CT95	30SEP96
16M095	0	0	0	1111: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		3NOV95
160131	20	20	0	1111: Incorp. DOE/LANL Rev. Comments PH1 Rpt Mod	6NOV95	6DEC95
160215	22	22	0	1111: DOE/LANL Review PH1 Report/WP Modification	6NOV95	8DEC95
160220	20	20	0	1111: Write PH2 Contract; Mobilize for RFI	6NOV95	6DEC95
160210	22	22	0	1111: EPA/NMED Review PH1 Report/WP Modification	7DEC95	10JAN96
160132	40	40	0	1111: Incorp. EPA/NMED Rev. Comments PH1 Rpt Mod	11JAN96	8MAR96
160225	327	327	0	1111: Conduct RFI PH2 Field Work	11JAN96	1MAY97
160230	357	357	0	1111: Conduct RFI PH2 Sample Analysis	11JAN96	13JUN97
160240	367	367	0	1111: Conduct RFI PH2 Data Assessment	26FEB96	11AUG97
160133	10	10	0	1111: Issue Final PH1 Report/Work Plan Mod	11MAR96	22MAR96
160080	249	249	0	1111: Manage ADS During FY-97 (LOE)	10CT96	30SEP97
160665	249	249	0	1111: Conduct MDA F Pilot Studies FY-97 (LOE)	10CT96	30SEP97
616030	249	249	0	CONDUCT VCA FY-97	10CT96	30SEP97
160235	20	20	0	1111: Demoblize RFI PH2 Field Work	2MAY97	30MAY97
16M025	0	0	0	1111: RFI FIELD WORK COMPLETED		30MAY97
160300	100	100	0	1111: Conduct RFI Report Facility Investigation	12AUG97	8JAN98
160305	110	110	0	1111: Conduct RFI Report Investigation Analysis	12AUG97	23JAN98
160090	249	249	0	1111: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
160675	249*	249*	0	1111: Conduct MDA F Pilot/Studies FY-98 (LOE)	10CT97	30SEP98
616035	249	249	0	CONDUCT VCA FY-98	10CT97	30SEP98
160320	132	132	0	1111: Prepare Internal Draft of RFI Report	26JAN98	31JUL98
160325	22	22	0	1111: DOE/LANL/VE Rev Internal Draft of RFI Rpt	3AUG98	1SEP98
160330	40	40	0	1111:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	2SEP98	29OCT98
160110	249	249	0	1111: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
616040	249	249	0	CONDUCT VCA FY-99	10CT98	30SEP99

LANL EES-1 C. ROFER

FINEST HOUR

1111:TA-6 7 22 40 58 62 TBS 2/17/92

REPORT DATE 5AUG92 RUN NO. 204  
15:53

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 16NOV01

1111 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
160335	10	10	0	1111: Issue DOE Draft of RFI Report	30OCT98	13NOV98
160340	22	22	0	1111: Conduct Review of DOE Draft of RFI Report	16NOV98	17DEC98
160345	40	40	0	1111:Incorp. DOE Rev. Comments DOE Drft RFI Rpt	18DEC98	18FEB99
160350	10	10	0	1111: Issue EPA/NMED Draft of RFI Report	19FEB99	4MAR99
16M035	0	0	0	1111: EPA/NMED DRAFT OF RFI REPORT COMPLETED		4MAR99
160355	44	44	0	1111: Conduct EPA Review of RFI Report	5MAR99	5MAY99
160360	44	44	0	1111: Conduct NMED Review of RFI Report	5MAR99	5MAY99
160365	245	245	0	1111: Conduct Bench/Pilot Studies CMS Plan (LOE)	5MAR99	28FEB00
160370	35	35	0	1111: Establish Current Situation for CMS Plan	5MAR99	22APR99
160375	35	35	0	1111: Establish CA Objectives for CMS Plan	5MAR99	22APR99
160380	35	35	0	1111: Develop Screening Technologies for CMS Pl	5MAR99	22APR99
160385	245	245	0	1111: Develop NEPA Documentation for CMS Plan	5MAR99	28FEB00
16M045	0	0	0	1111: START DEVELOPMENT OF CMS PLAN	5MAR99	
160390	15	15	0	1111: Develop Alternatives for CMS Plan	23APR99	13MAY99
160605	20	20	0	1111: Incorporate EPA/NMED Comments for RFI Rpt	6MAY99	3JUN99
160395	10	10	0	1111: Develop Internal Draft of CMS Plan	14MAY99	27MAY99
160400	10	10	0	1111: DOE/LANL/VE Rev Internal Draft of CMS PL	28MAY99	11JUN99
160610	20	20	0	1111: Issue Final RFI Report	4JUN99	1JUL99
160405	10	10	0	1111:Incorp. LANL REV Comments Intern Dft CMS PL	14JUN99	25JUN99
160410	5	5	0	1111: Issue DOE Draft of CMS Plan	28JUN99	2JUL99
16M040	0	0	0	1111: RFI COMPLETED		1JUL99
16M085	0	0	0	1111: EPA NOTIFICATION OF CMS REQUIREMENTS		1JUL99
160415	22	22	0	1111: Conduct Review of DOE Draft of CMS Plan	6JUL99	4AUG99
160420	20	20	0	1111: Incorp. DOE Rev.Comments DOE Dft.of CMS PL	5AUG99	1SEP99
160425	10	10	0	1111: Issue EPA/NMED Draft of CMS Plan	2SEP99	16SEP99
16M050	0	0	0	1111: EPA/NMED DRAFT OF CMS PLAN COMPLETED		16SEP99
160430	44	44	0	1111: Conduct EPA Review of CMS Plan	17SEP99	19NOV99
160435	44	44	0	1111: Conduct NMED Review of CMS Plan	17SEP99	19NOV99
160120	249	249	0	1111: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
616045	249	249	0	CONDUCT VCA FY-00	10CT99	29SEP00




LANL EES-1 C. ROFER  
 REPORT DATE 5AUG92 RUN NO. 204  
 15:53  
 1111 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

1111:TA-6 7 22 40 58 62 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 16NOV01  
 DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
160615	20	20	0	1111: Incorporate EPA/NMED Comments on CMS Plan	22NOV99	21DEC99
160620	10	10	0	1111: Publish Final CMS Plan	22DEC99	7JAN00
160625	10	10	0	1111: Issue Final CMS Plan	10JAN00	24JAN00
16M090	0	0	0	1111: EPA APPROVED CMS PLAN		24JAN00
160440	245	245	0	1111: CMS Bench/Pilot Studies	25JAN00	17JAN01
16M055	0	0	0	1111: START CMS WORK	25JAN00	
16M065	0	0	0	1111: START DEVELOPMENT OF CMS REPORT	25JAN00	
160130	248	248	0	1111: Manage ADS During FY-01 (LOE)	20CT00	28SEP01
616050	21	21	0	CONDUCT VCA FY-01	20CT00	31OCT00
16M060	0	0	0	1111: CMS WORK COMPLETED		17JAN01
160445	30	30	0	1111: Cond Technical Evaluation for CMS Report	18JAN01	1MAR01
160450	30	30	0	1111: Conduct Environmental Eval for CMS Report	18JAN01	1MAR01
160455	30	30	0	1111: Conduct Human Health Eval for CMS Report	18JAN01	1MAR01
160460	30	30	0	1111: Cond Community Relations Eval. CMS Rpt	18JAN01	1MAR01
160465	30	30	0	1111: Conduct Cost Evaluation for CMS Report	18JAN01	1MAR01
160470	30	30	0	1111: Develop NEPA Documentation for CMS Report	18JAN01	1MAR01
160475	10	10	0	1111: Prepare Internal Draft of CMS Report	2MAR01	15MAR01
160480	10	10	0	1111: DOE/LANL/VE Rev Internal Draft of CMS Rpt	16MAR01	29MAR01
160485	35	35	0	1111:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	30MAR01	17MAY01
160490	10	10	0	1111: Issue DOE Draft of CMS Report	18MAY01	1JUN01
160495	22	22	0	1111: Conduct Review of DOE Draft of CMS Report	4JUN01	3JUL01
160500	10	10	0	1111:Incorp. DOE Rev Comments DOE Dft CMS Report	5JUL01	18JUL01
160505	10	10	0	1111: Issue EPA/NMED Draft of CMS Report	19JUL01	1AUG01
16M070	0	0	0	1111: EPA/NMED DRAFT OF CMS REPORT COMPLETED		1AUG01
160510	44	44	0	1111: Conduct EPA Review of CMS Report	2AUG01	30CT01
160515	44	44	0	1111: Conduct NMED Review of CMS Report	2AUG01	30CT01
160630	20	20	0	1111: Incorporate EPA/NMED Comments on CMS Rpt	4OCT01	1NOV01
160635	10	10	0	1111: Issue Final CMS Report	2NOV01	16NOV01
16M075	0	0	0	1111: ASSESSMENT COMPLETED		16NOV01

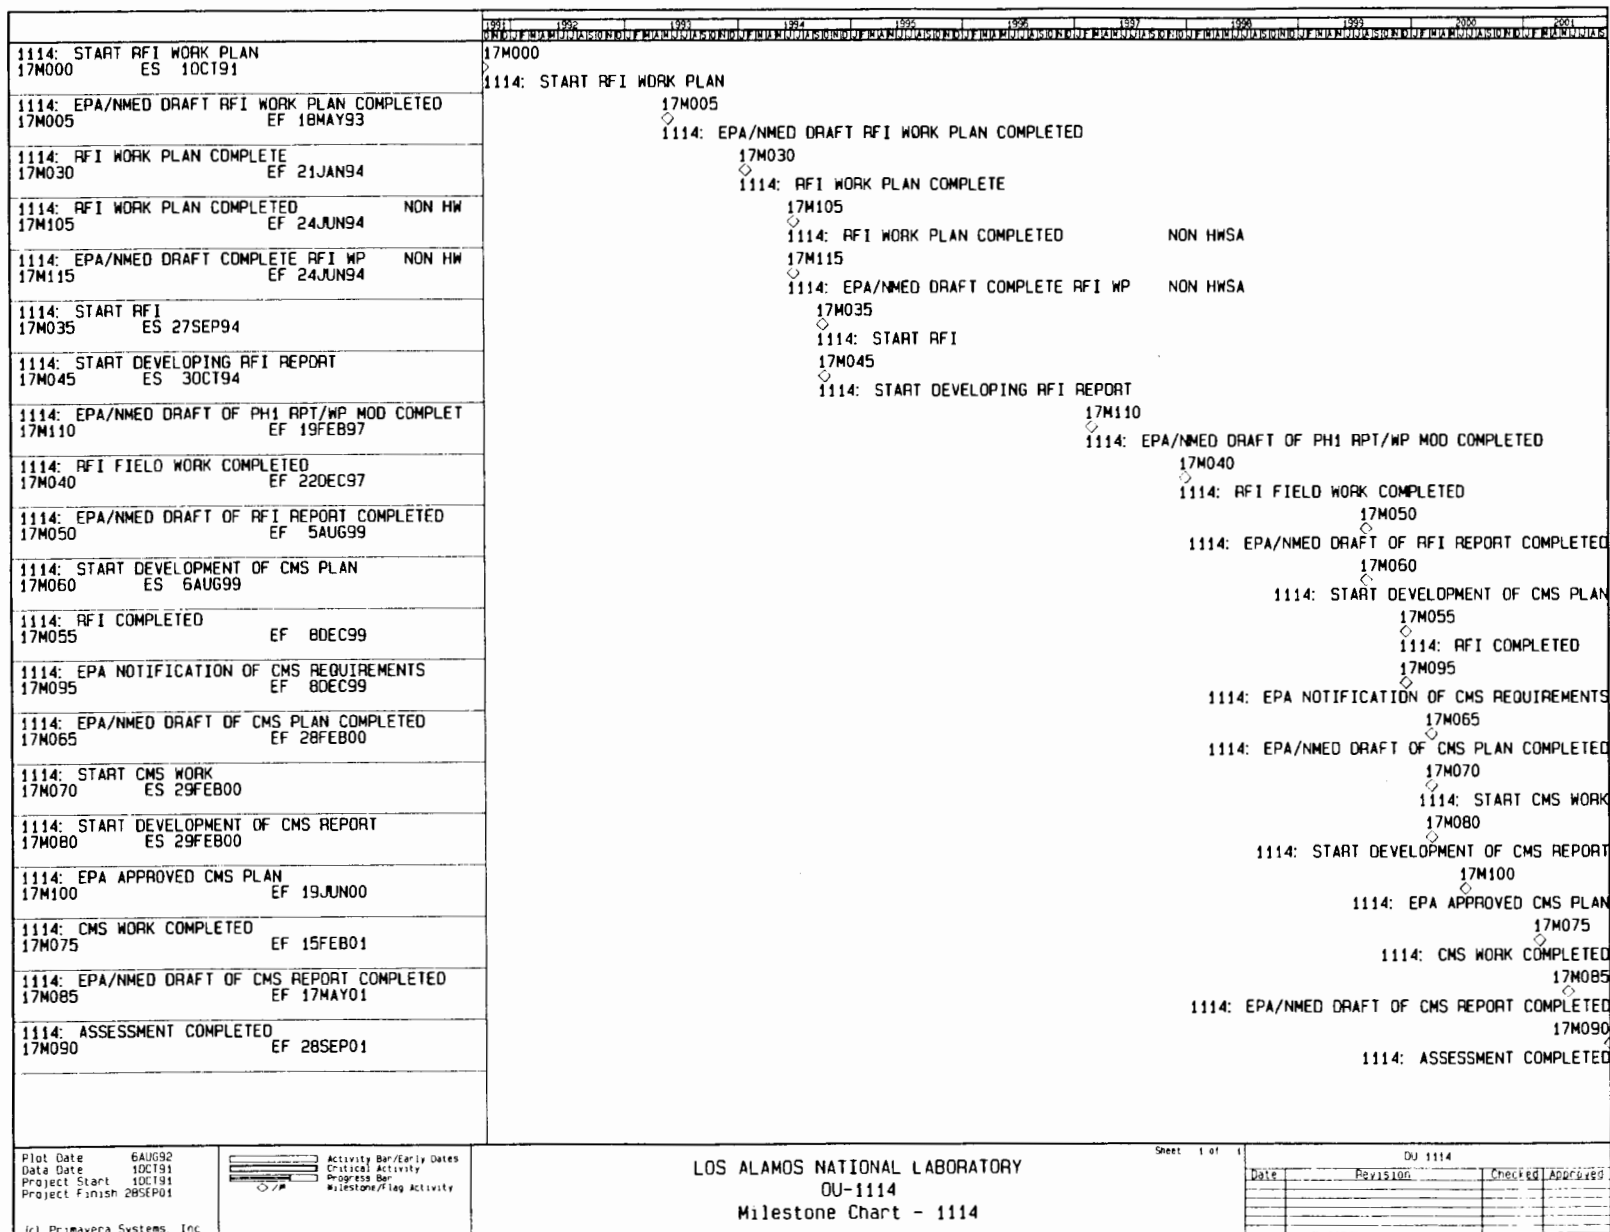

-----

LANL	CLS-DO	ED GRIGGS	FINEST HOUR	1114:TA-3 30 59 60 61 64 BELL3/16/92
REPORT DATE	6AUG92	RUN NO. 109	ENVIRONMENTAL RESTORATION	START DATE 10CT91 FIN DATE 28SEP01
	18:03			
1114 SCHEDULE REPORT BY EARLY START				DATA DATE 10CT91 PAGE NO. 1

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
170320	77	77	0	1114: Develop Scope RFI WP	10CT91	27JAN92
170340	87	87	0	1114: Locate Existing Data RFI WP	10CT91	10FEB92
170445	250	250	0	1114: Manage ADS FY-92 (LOE)	10CT91	30SEP92
170850	250	250	0	1114: Bench/Pilot Studies RFI WP (LOE)	10CT91	30SEP92
170860	250	250	0	1114: Conduct VCA RFI WP (LOE)	10CT91	30SEP92
17M000	0	0	0	1114: START RFI WORK PLAN	10CT91*	
170345	204	204	0	1114: Develop NEPA Documentation RFI WP	30OCT91*	24AUG92
170085	21	21	0	1114: Write Draft Comm Rel Plan RFI WP	2JAN92*	31JAN92
170095	21	21	0	1114: Write Draft Records Mgmt Plan RFI WP	2JAN92*	31JAN92
170380	40	40	0	1114: Analyze Existing Data RFI WP	8JAN92*	5MAR92
170043	90	90	0	1114: DELINEATE SWMU BOUNDARIES	3FEB92*	9JUN92
170090	20	20	0	1114: Write Final Comm Rel Plan RFI WP	3FEB92	2MAR92
170100	20	20	0	1114: Write Final Records Mgmt Plan RFI WP	3FEB92	2MAR92
170400	74	74	0	1114: Draft Existing Data Report RFI WP	5FEB92*	19MAY92
170065	22	22	0	1114: Write Draft QA Plan RFI WP	2MAR92*	31MAR92
170075	22	22	0	1114: Write Draft H & S Plan RFI WP	2MAR92*	31MAR92
170420	71	71	0	1114: Determine Data Needs RFI WP	6MAR92*	15JUN92
170045	114	114	0	1114: Develop Data Quality Object. RFI WP	20MAR92*	28AUG92
170055	116	116	0	1114: Develop Sampling Plan RFI WP	17APR92*	30SEP92
170060	40	40	0	1114: Develop Management Plan RFI WP	15MAY92*	13JUL92
170070	23	23	0	1114: Write Final QA Plan RFI WP	1JUN92*	1JUL92
170080	23	23	0	1114: Write Final H & S Plan RFI WP	1JUN92*	1JUL92
170105	60	60	0	1114: Write Internal Draft RFI WP	10CT92*	31DEC92
170450	249	249	0	1114: Manage ADS FY-93 (LOE)	10CT92	30SEP93
175010	249	249	0	1114: VCA Remove Underground Fuel Storage Tanks	10CT92*	30SEP93
170115	20	20	0	1114: DOE/LANL/VE Rvw Internal Drft RFI WP	4JAN93	1FEB93
170116	15	15	0	1114: Inc DOE/LANL Comment Int Drft RFI WP	2FEB93	23FEB93
170110	20	20	0	1114: Write DOE Draft RFI WP	24FEB93	23MAR93
170130	20	20	0	1114: DOE Review DOE Draft RFI WP	24MAR93	20APR93
170120	10	10	0	1114: Inc DOE Comments DOE Draft RFI WP	21APR93	4MAY93

LANL	CLS-DO	ED GRIGGS	FINEST HOUR	1114:TA-3	30	59	60	61	64	BELL3/16/92
REPORT DATE	6AUG92	RUN NO.	109	ENVIRONMENTAL RESTORATION	START DATE	10CT91	FIN DATE	28SEP01		
	18:03									
1114 SCHEDULE	REPORT BY	EARLY START			DATA DATE	10CT91	PAGE NO.	2		

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED	
						START	FINISH
170125	10	10	0	1114: Issue EPA/NMED Draft	RFI WP	5MAY93	18MAY93
17M005	0	0	0	1114: EPA/NMED DRAFT RFI WORK PLAN COMPLETED			18MAY93
171000	106	106	0	1114: Delineate Potential Releases	RFI WP NON HWSA	1JUN93*	29OCT93
171005	64	64	0	1114: Analyze Existing Data	RFI WP NON HWSA	1JUN93*	30AUG93
171010	42	42	0	1114: Draft Existing Data Report	RFI WP NON HWSA	1JUL93	30AUG93
171015	43	43	0	1114: Determine Data Needs	RFI WP NON HWSA	28SEP93*	1DEC93
170140	44	44	0	1114: EPA Review	RFI WP	30SEP93*	6DEC93
170141	44	44	0	1114: NMED Review	RFI WP	30SEP93*	6DEC93
171020	140	140	0	1114: Write DOE/LANL Int Draft	RFI WP NON HWSA	30SEP93*	26APR94
170455	249	249	0	1114: Manage ADS FY-94	(LOE)	1OCT93	30SEP94
170845	249	249	0	1114: Conduct VCA FY-94	(LOE)	1OCT93	30SEP94
171025	75	75	0	1114: Develop DQO's	RFI WP NON HWSA	2DEC93*	23MAR94
170870	20	20	0	1114: Inc EPA/NMED Comments	RFI WP	7DEC93	6JAN94
171030	62	62	0	1114: Develop Sampling Plan	RFI WP NON HWSA	3JAN94*	31MAR94
170875	10	10	0	1114: Issue Final	RFI WP	7JAN94	21JAN94
17M030	0	0	0	1114: RFI WORK PLAN COMPLETE			21JAN94
171035	22	22	0	1114: DOE/LANL/VE Rvw Int Draft	RFI WP NON HWSA	27APR94	26MAY94
171040	20	20	0	1114: DOE Review DOE Draft	RFI WP NON HWSA	27MAY94	24JUN94
170865	65	65	0	1114: Write Contracts and Mobilize	RFI	24JUN94*	26SEP94
17M105	0	0	0	1114: RFI WORK PLAN COMPLETED	NON HWSA		24JUN94
17M115	0	0	0	1114: EPA/NMED DRAFT COMPLETE	RFI WP NON HWSA		24JUN94
170505	250	250	0	1114: RFI Bench/Pilot Studies	(LOE)	27SEP94	27SEP95
170510	4	4	0	1114: Field Work FY-94	RFI PH1	27SEP94	30SEP94
170515	4	4	0	1114: Sample Analysis FY-94	RFI PH1	27SEP94	30SEP94
170520	4	4	0	1114: Data Assessment FY-94	RFI PH1	27SEP94	30SEP94
17M035	0	0	0	1114: START RFI		27SEP94	
170460	248	248	0	1114: Manage ADS FY-95	(LOE)	30CT94	29SEP95
170511	248	248	0	1114: Field Work FY-95	RFI PH1	30CT94	29SEP95
170516	248	248	0	1114: Sample Analysis FY-95	RFI PH1	30CT94	29SEP95
170521	248	248	0	1114: Data Assessment FY-95	RFI PH1	30CT94	29SEP95

LAWL	CLS-DO	ED GRIGGS	FINEST HOUR	1114:TA-3	30	59	60	61	64	BELL3/16/92
REPORT DATE	6AUG92	RUN NO.	109	ENVIRONMENTAL RESTORATION	START DATE	10CT91	FIN DATE	28SEP01		
	18:03									
1114 SCHEDULE REPORT BY	EARLY START				DATA DATE	10CT91	PAGE NO.	3		

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED	
						START	FINISH
170635	100	100	0	1114: Develop NEPA Documentation	RFI RPT	30OCT94	2MAR95
17M045	0	0	0	1114: START DEVELOPING RFI REPORT		30OCT94*	
170465	249	249	0	1114: Manage ADS FY-96	(LOE)	20OCT95	30SEP96
170512	190	190	0	1114: Field Work FY-96	RFI PH1	20OCT95	8JUL96
170517	210	210	0	1114: Sample Analysis FY-96	RFI PH1	20OCT95	5AUG96
170522	230	230	0	1114: Data Assessment FY-96	RFI PH1	20OCT95	3SEP96
170530	20	20	0	1114: Demobilize	RFI PH1	9JUL96	5AUG96
170545	20	20	0	1114: Write Contracts and Mobilize	RFI PH2	9JUL96	5AUG96
170550	39	39	0	1114: Field Work FY-96	RFI PH2	6AUG96	30SEP96
170555	39	39	0	1114: Sample Analysis FY-96	RFI PH2	6AUG96	30SEP96
170565	39	39	0	1114: Data Assessment FY-96	RFI PH2	6AUG96	30SEP96
170525	60	60	0	1114: Write Report/WP Modification	RFI PH1	4SEP96	2DEC96
170470	249	249	0	1114: Manage ADS FY-97	(LOE)	10OCT96	30SEP97
170551	249	249	0	1114: Field Work FY-97	RFI PH2	10OCT96	30SEP97
170556	249	249	0	1114: Sample Analysis FY-97	RFI PH2	10OCT96	30SEP97
170566	249	249	0	1114: Data Assessment FY-97	RFI PH2	10OCT96	30SEP97
170540	22	22	0	1114: DOE/LANL Review RPT/WP MOD	RFI PH1	3DEC96	6JAN97
620000	189	189	0	1114: Conduct VCA	(LOE)	2JAN97*	30SEP97
170542	20	20	0	1114: Inc DOE/LANL Comments RPT/WP	RFI PH1	7JAN97	4FEB97
170544	10	10	0	1114: Issue EPA/NMED Draft RPT/WP	RFI PH1	5FEB97	19FEB97
17M110	0	0	0	1114: EPA/NMED DRAFT OF PH1 RPT/WP MOD COMPLETED			19FEB97
170535	22	22	0	1114: EPA/NMED Review RPT/WP MOD	RFI PH1	20FEB97	21MAR97
170536	20	20	0	1114: Inc EPA/NMED Comments RPT/WP	RFI PH1	24MAR97	18APR97
170538	10	10	0	1114: Issue Final RPT/WP Mod	RFI PH1	21APR97	2MAY97
170475	249	249	0	1114: Manage ADS FY-98	(LOE)	10OCT97	30SEP98
170552	35	35	0	1114: Field Work FY-98	RFI PH2	10OCT97	20NOV97
170557	45	45	0	1114: Sample Analysis FY-98	RFI PH2	10OCT97	8DEC97
170567	55	55	0	1114: Data Assessment FY-98	RFI PH2	10OCT97	22DEC97
620005	249	249	0	1114: Conduct VCA	(LOE)	10OCT97	30SEP98
170560	20	20	0	1114: Demobilize	RFI PH2	21NOV97	22DEC97

-----

LANL	CLS-DO	ED GRIGGS		FINEST HOUR		1114:TA-3 30 59 60 61 64 BELL3/16/92
REPORT DATE	6AUG92	RUN NO.	109	ENVIRONMENTAL RESTORATION		START DATE 10CT91 FIN DATE 28SEP01
	18:03					
1114 SCHEDULE REPORT BY	EARLY START					DATA DATE 10CT91 PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
17M040	0	0	0	1114: RFI FIELD WORK COMPLETED		22DEC97
170625	100	100	0	1114: Facility Investigation RFI RPT	23DEC97	18MAY98
170630	110	110	0	1114: Investigation Analysis RFI RPT	23DEC97	2JUN98
170645	132	132	0	1114: Prepare Internal Draft RFI RPT	3JUN98	11DEC98
170480	249	249	0	1114: Manage ADS FY-99 (LOE)	10CT98	30SEP99
170650	20	20	0	1114: DOE/LANL/VE Rvw Internal Drft RFI RPT	14DEC98	13JAN99
170655	40	40	0	1114: Inc DOE/LANL Comments Int Dft RFI RPT	14JAN99	12MAR99
170660	20	20	0	1114: Issue DOE Draft RFI RPT	15MAR99	9APR99
170665	22	22	0	1114: DOE Review DOE Draft RFI RPT	12APR99	11MAY99
170670	40	40	0	1114: Inc DOE Comments DOE Draft RFI RPT	12MAY99	8JUL99
170675	20	20	0	1114: Issue EPA/NMED Draft RFI RPT	9JUL99	5AUG99
17M050	0	0	0	1114: EPA/NMED DRAFT OF RFI REPORT COMPLETED		5AUG99
170680	44	44	0	1114: EPA Review RFI RPT	6AUG99	7OCT99
170685	44	44	0	1114: NMED Review RFI RPT	6AUG99	7OCT99
170690	245	245	0	1114: Bench/Pilot Studies CMS PLN(LOE)	6AUG99	31JUL00
170695	35	35	0	1114: Establish Current Situation CMS PLN	6AUG99	24SEP99
170700	35	35	0	1114: Establish CA Objectives CMS PLN	6AUG99	24SEP99
170705	35	35	0	1114: Develop Screening Technology CMS PLN	6AUG99	24SEP99
170710	245	245	0	1114: Develop NEPA Documentation CMS PLN	6AUG99	31JUL00
17M060	0	0	0	1114: START DEVELOPMENT OF CMS PLAN		6AUG99
170715	15	15	0	1114: Develop Alternatives CMS PLN	27SEP99	18OCT99
170485	249	249	0	1114: Manage ADS FY-00 (LOE)	10CT99	29SEP00
170895	20	20	0	1114: Inc EPA/NMED Comments RFI RPT	8OCT99	5NOV99
170720	10	10	0	1114: Develop Internal Draft CMS PLN	19OCT99	1NOV99
170725	10	10	0	1114: DOE/LANL/VE Rvw Internal Drft CMS PLN	2NOV99	16NOV99
170900	20	20	0	1114: Issue Final RFI RPT	8NOV99	8DEC99
170730	10	10	0	1114: Inc DOE/LANL Comments Int Dft CMS PLN	17NOV99	2DEC99
170735	5	5	0	1114: Issue DOE Draft CMS PLN	3DEC99	9DEC99
17M055	0	0	0	1114: RFI COMPLETED		8DEC99
17M095	0	0	0	1114: EPA NOTIFICATION OF CMS REQUIREMENTS		8DEC99

1114:TA-3 30 59 60 61 64 BELL3/16/92

START DATE 10OCT91 FIN DATE 28SEP01

START DATE 1997/1 END DATE 2001/01


DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED	
						START	FINISH
170740	22	22	0	1114: DOE Review DOE Draft	CMS PLN	10DEC99	13JAN00
170745	20	20	0	1114: Inc DOE Comments DOE Draft	CMS PLN	14JAN00	11FEB00
170750	10	10	0	1114: Issue EPA/NMED Draft	CMS PLN	14FEB00	28FEB00
17M065	0	0	0	1114: EPA/NMED DRAFT OF CMS PLAN COMPLETED			28FEB00
170755	44	44	0	1114: EPA Review	CMS PLN	29FEB00	28APR00
170760	44	44	0	1114: NMED Review	CMS PLN	29FEB00	28APR00
170765	242	242	0	1114: Bench/Pilot Studies	CMS (LOE)	29FEB00	15FEB01
170770	30	30	0	1114: Technical Evaluation	CMS RPT	29FEB00	10APR00
170775	30	30	0	1114: Environmental Evaluation	CMS RPT	29FEB00	10APR00
170780	30	30	0	1114: Human Health Evaluation	CMS RPT	29FEB00	10APR00
170785	30	30	0	1114: Community Relations Eval	CMS RPT	29FEB00	10APR00
170790	30	30	0	1114: Cost Evaluation	CMS RPT	29FEB00	10APR00
170795	30	30	0	1114: Develop NEPA Documentation	CMS RPT	29FEB00	10APR00
17M070	0	0	0	1114: START CMS WORK		29FEB00	
17M080	0	0	0	1114: START DEVELOPMENT OF CMS REPORT		29FEB00	
170800	10	10	0	1114: Prepare Internal Draft	CMS RPT	11APR00	24APR00
170805	10	10	0	1114: DOE/LANL/VE Rvw Internal Drft	CMS RPT	25APR00	8MAY00
170905	20	20	0	1114: Inc EPA/NMED Comments	CMS PLN	1MAY00	26MAY00
170910	10	10	0	1114: Issue Final	CMS PLN	30MAY00	12JUN00
170915	5	5	0	1114: EPA Approval CMS Plan		13JUN00	19JUN00
17M100	0	0	0	1114: EPA APPROVED CMS PLAN			19JUN00
170490	248	248	0	1114: Manage ADS FY-01	(LOE)	20CT00	28SEP01
170810	35	35	0	1114: Inc DOE/LANL Comments Int Dft	CMS RPT	27DEC00	15FEB01
17M075	0	0	0	1114: CMS WORK COMPLETED			15FEB01
170815	10	10	0	1114: Issue DOE Draft	CMS RPT	16FEB01	2MAR01
170820	22	22	0	1114: DOE Review DOE Draft	CMS RPT	5MAR01	3APR01
170825	22	22	0	1114: Inc DOE Comments DOE Draft	CMS RPT	4APR01	3MAY01
170830	10	10	0	1114: Issue EPA/NMED Draft	CMS RPT	4MAY01	17MAY01
17M085	0	0	0	1114: EPA/NMED DRAFT OF CMS REPORT COMPLETED			17MAY01
170835	44	44	0	1114: EPA Review	CMS RPT	18MAY01	20JUL01

LANL	CLS-DO	ED GRIGGS	FINEST HOUR	1114:TA-3 30 59 60 61 64 BELL3/16/92
REPORT DATE	6AUG92	RUN NO. 109	ENVIRONMENTAL RESTORATION	START DATE 1OCT91 FIN DATE 28SEP01
	18:03			
1114 SCHEDULE REPORT BY	EARLY START			DATA DATE 1OCT91 PAGE NO. 6

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
170840	44	44	0	1114: NMED Review	CMS RPT	18MAY01	20JUL01
170920	20	20	0	1114: Inc EPA/NMED Comments	CMS RPT	23JUL01	17AUG01
170925	10	10	0	1114: Issue Final	CMS RPT	20AUG01	31AUG01
17M090	0	0	0	1114: ASSESSMENT COMPLETED			28SEP01



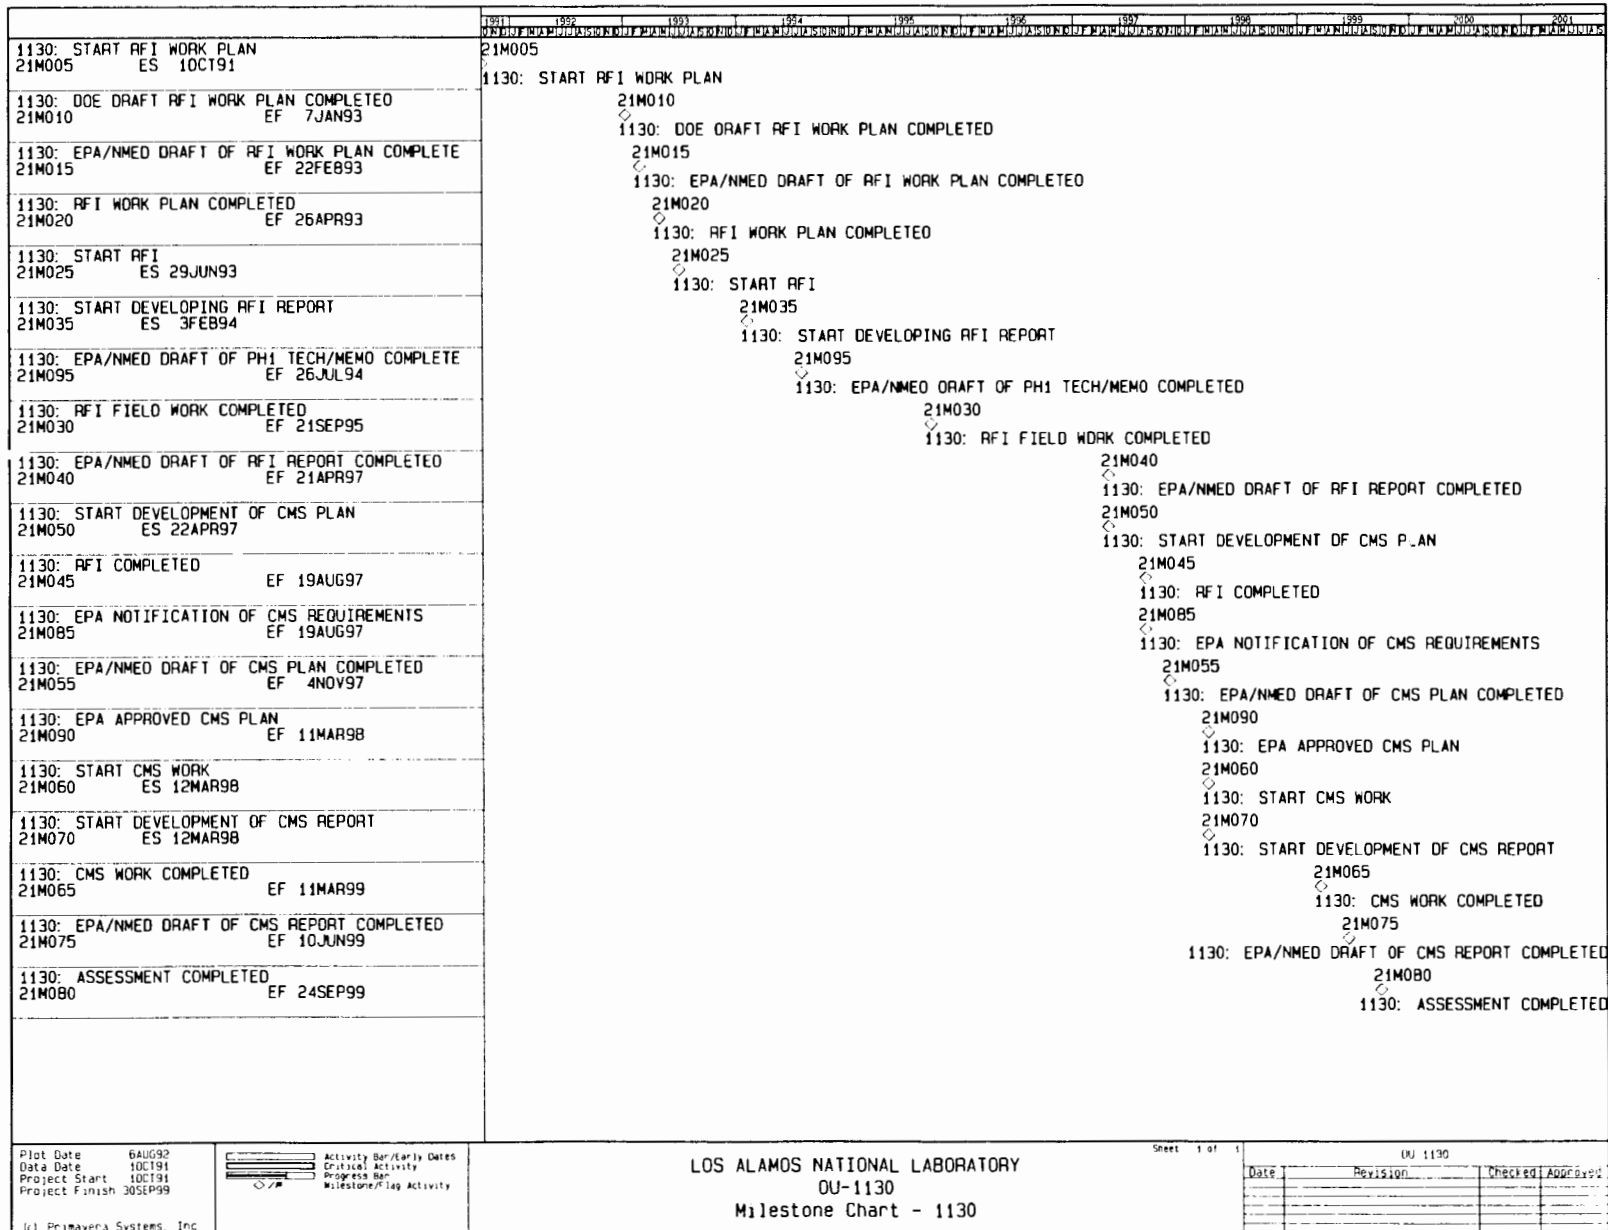

ADS 1130: TA-36 68 71      TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP99

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
210005	249	249	0	1130:Conduct Voluntary C.Actions for RFI WP(LOE)	1OCT91	29SEP92
210010	20	20	0	1130: Develop Scope for RFI WP	1OCT91	29OCT91
210015	250	250	0	1130: Manage ADS During FY-92 (LOE)	1OCT91	30SEP92
21M005	0	0	0	1130: START RFI WORK PLAN	1OCT91*	
210025	81	81	0	1130: Locate Existing Data for RFI WP	16OCT91	14FEB92
210020	230	230	0	1130: Develop NEPA Documentation for RFI WP	30OCT91	30SEP92
210035	105	105	0	1130: Analyze Existing Data for RFI WP	30OCT91	3APR92
210055	105	105	0	1130: Determine Data Needs for RFI WP	2DEC91	1MAY92
210060	24	24	0	1130: Write Community Relations Plan for RFI WP	2DEC91	7JAN92
210065	25	25	0	1130: Write Records Management Plan for RFI WP	2DEC91	8JAN92
210045	27	27	0	1130: Draft Existing Data Report for RFI WP	6DEC91	17JAN92
210085	91	91	0	1130: Develop Sampling Plan for RFI WP	16DEC91	27APR92
210095	22	22	0	1130: Write Quality Assurance Plan for RFI WP	27APR92	27MAY92
210105	22	22	0	1130: Write Management Plan for RFI WP	27APR92	27MAY92
210100	20	20	0	1130: Write Health & Safety Plan for RFI WP	28APR92	26MAY92
210030	249	249	0	1130: Manage ADS During FY-93 (LOE)	1OCT92	30SEP93
210115	20	20	0	1130: Develop LANL Internal Draft of RFI WP	1OCT92*	29OCT92
210173	74	74	0	DEVELOP NEPA DOCUMENT	1OCT92*	22JAN93
210125	20	20	0	1130: LANL/VE Review Internal Draft RFI WP	16OCT92	13NOV92
210135	20	20	0	1130:Incorp.LANL Rev Comments Intern Dft RFI WP	16NOV92	15DEC92
210145	14	14	0	1130: Issue DOE Draft of RFI WP	16DEC92	7JAN93
21M010	0	0	0	1130: DOE DRAFT RFI WORK PLAN COMPLETED		7JAN93
210150	22	22	0	1130:Conduct DOE Review of DOE Draft of RFI WP	8JAN93	9FEB93
210155	20	20	0	1130:Incorporate DOE Rev.Comments DOE Dft RFI WP	25JAN93	22FEB93
210160	10	10	0	1130: Issue EPA/NMED Draft of RFI Work Plan	8FEB93	22FEB93
21M015	0	0	0	1130: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		22FEB93
210165	44	44	0	1130: Conduct NMED Review of RFI WP	23FEB93	23APR93
210170	44	44	0	1130: Conduct EPA Review of RFI Work Plan	23FEB93	23APR93
210530	20	20	0	1130: Incorporate EPA/NMED Comments for RFI WP	30MAR93	26APR93
210535	10	10	0	1130: Issue Final RFI Work Plan	13APR93	26APR93

ADS 1130: TA-36 68 71      TBS 2/17/92

START DATE 1OCT91 FIN DATE 30SEP99

START DATE 100197 FIN DATE 000077

DATA DATE 10OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
210525	65	65	0	1130: Write PH1 Contracts for RFI/Mobilize	26APR93	27JUL93
21M020	0	0	0	1130: RFI WORK PLAN COMPLETED		26APR93
210185	189	189	0	1130: Conduct RFI PH1 Field Work	30APR93	2FEB94
210190	199	199	0	1130: Conduct RFI PH1 Sample Analysis	30APR93	16FEB94
210195	229	229	0	1130: Conduct RFI PH1 Data Assessment	1JUN93*	29APR94
210310	101	101	0	1130: Develop NEPA Documentation for RFI Report	7JUN93	27OCT93
21M025	0	0	0	1130: START RFI	29JUN93	
210040	250	250	0	1130: Manage ADS During FY-94 (LOE)	1OCT93	30SEP94
210180	249	249	0	1130: Conduct RFI Bench/Pilot Studies (LOE)	1OCT93*	29SEP94
210520	250	250	0	1130: Assmt - Conduct VCA (LOE)	1OCT93*	30SEP94
210205	20	20	0	1130: Demobilize RFI PH1 Field Work	3FEB94	3MAR94
21M035	0	0	0	1130: START DEVELOPING RFI REPORT	3FEB94	
210200	60	60	0	1130: Write RFI PH1 Tech Memo/WP Modification	2MAY94	26JUL94
21M095	0	0	0	1130: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		26JUL94
210210	22	22	0	1130: EPA/NMED Rev PH1 Tech Memo/WP Modification	27JUL94	25AUG94
210215	22	22	0	1130: DOE Review PH1 Tech Memo/WP Modification	27JUL94	25AUG94
210220	20	20	0	1130: Write PH2 Contract; Mobilize for RFI	27JUL94	23AUG94
210225	248	248	0	1130: Conduct RFI PH2 Field Work	24AUG94	23AUG95
210230	248	248	0	1130: Conduct RFI PH2 Sample Analysis	24AUG94	23AUG95
210240	248	248	0	1130: Conduct RFI PH2 Data Assessment	24AUG94	23AUG95
210050	247	247	0	1130: Manage ADS During FY-95 (LOE)	3OCT94	29SEP95
210235	20	20	0	1130: Demoblize RFI PH2 Field Work	24AUG95	21SEP95
210300	103	103	0	1130: Conduct RFI Report Facility Investigation	24AUG95	26JAN96
210305	113	113	0	1130: Conduct RFI Report Investigation Analysis	24AUG95	9FEB96
21M030	0	0	0	1130: RFI FIELD WORK COMPLETED		21SEP95
210070	249	249	0	1130: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
210320	132	132	0	1130: Prepare Internal Draft of RFI Report	12FEB96	16AUG96
210325	20	20	0	1130: LANL/VE Review Internal Draft of RFI Rpt	19AUG96	16SEP96
210330	40	40	0	1130:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	17SEP96	13NOV96
210080	249	249	0	1130: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97

LANL EM-8 SHARAD KELKAR  
 REPORT DATE 5AUG92 RUN NO. 154 ENVIRONMENTAL RESTORATION  
 1130 SCHEDULE REPORT BY EARLY START  
 ADS 1130: TA-36 68 71 TBS 2/17/92  
 START DATE 10CT91 FIN DATE 30SEP99  
 DATA DATE 10CT91 PAGE NO. 3


ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
210335	20	20	0	1130: Issue DOE Draft of RFI Report	14NOV96	13DEC96
210340	26	26	0	1130: Conduct Review of DOE Draft of RFI Report	16DEC96	24JAN97
650000	189	189	0	2209: Remed - Conduct VCA (LOE)	2JAN97*	30SEP97
210345	40	40	0	1130:Incorp. DOE Rev. Comments DOE Drft RFI Rpt	27JAN97	24MAR97
210350	20	20	0	1130: Issue EPA/NMED Draft of RFI Report	25MAR97	21APR97
21M040	0	0	0	1130: EPA/NMED DRAFT OF RFI REPORT COMPLETED		21APR97
210355	44	44	0	1130: Conduct EPA Review of RFI Report	22APR97	23JUN97
210360	44	44	0	1130: Conduct NMED Review of RFI Report	22APR97	23JUN97
210365	249	249	0	1130: Conduct Bench/Pilot Studies for CMS Pl(LOE	22APR97	21APR98
210370	35	35	0	1130: Establish Current Situation for CMS Plan	22APR97	10JUN97
210375	35	35	0	1130: Establish CA Objectives for CMS Plan	22APR97	10JUN97
210380	35	35	0	1130: Develop Screening Technologies for CMS Pl	22APR97	10JUN97
210385	249	249	0	1130: Develop NEPA Documentation for CMS Plan	22APR97	21APR98
21M050	0	0	0	1130: START DEVELOPMENT OF CMS PLAN	22APR97	
210390	15	15	0	1130: Develop Alternatives for CMS Plan	11JUN97	1JUL97
210555	20	20	0	1130: Incorporate EPA/NMED Comments on RFI Rpt	24JUN97	22JUL97
210395	10	10	0	1130: Develop Internal Draft of CMS Plan	2JUL97	16JUL97
210400	10	10	0	1130: LANL/VE Review Internal Draft of CMS Plan	17JUL97	30JUL97
210560	20	20	0	1130: Issue Final RFI Report	23JUL97	19AUG97
210405	10	10	0	1130:Incorp. LANL REV Comments Intern Dft CMS Pl	31JUL97	13AUG97
210410	5	5	0	1130: Issue DOE Draft of CMS Plan	14AUG97	20AUG97
21M045	0	0	0	1130: RFI COMPLETED		19AUG97
21M085	0	0	0	1130: EPA NOTIFICATION OF CMS REQUIREMENTS		19AUG97
210415	22	22	0	1130: Conduct Review of DOE Draft of CMS Plan	21AUG97	22SEP97
210420	20	20	0	1130:Incorp. DOE Rev.Comments DOE Dft.of CMS Pl	23SEP97	21OCT97
210090	249	249	0	1130: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
650005	249	249	0	2209: Remed - Conduct VCA (LOE)	10CT97	30SEP98
210425	10	10	0	1130: Issue EPA/NMED Draft of CMS Plan	22OCT97	4NOV97
21M055	0	0	0	1130: EPA/NMED DRAFT OF CMS PLAN COMPLETED		4NOV97
210430	48	48	0	1130: Conduct EPA Review of CMS Plan	5NOV97	20JAN98

-----

LANL EM-8 SHARAD KELKAR	FINEST HOUR	ADS 1130: TA-36 68 71	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 154	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 30SEP99
15:56			
1130 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91	PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
210435	48	48	0	1130: Conduct NMED Review of CMS Plan	5NOV97	20JAN98
210565	20	20	0	1130: Incorporate EPA/NMED Comments on CMS Plan	21JAN98	18FEB98
210570	10	10	0	1130: Issue Final CMS Plan	19FEB98	4MAR98
210575	5	5	0	1130: EPA Approves Plan	5MAR98	11MAR98
21M090	0	0	0	1130: EPA APPROVED CMS PLAN		11MAR98
210440	249	249	0	1130: Conduct CMS Bench/Pilot Studies (LOE)	12MAR98	11MAR99
210445	30	30	0	1130: Conduct Technical Evaluation for CMS Rpt	12MAR98	22APR98
210450	30	30	0	1130: Conduct Environmental Eval for CMS Report	12MAR98	22APR98
210455	30	30	0	1130: Conduct Human Health Eval for CMS Report	12MAR98	22APR98
210460	30	30	0	1130: Conduct Community Relations Eval CMS Rpt	12MAR98	22APR98
210465	30	30	0	1130: Conduct Cost Evaluation for CMS Report	12MAR98	22APR98
210470	30	30	0	1130: Develop NEPA Documentation for CMS Report	12MAR98	22APR98
21M060	0	0	0	1130: START CMS WORK	12MAR98	
21M070	0	0	0	1130: START DEVELOPMENT OF CMS REPORT	12MAR98	
210475	10	10	0	1130: Prepare Internal Draft of CMS Report	23APR98	6MAY98
210480	10	10	0	1130: LANL/VE Review Internal Draft of CMS Rpt	7MAY98	20MAY98
210110	249	249	0	1130: Manage ADS During FY-99 (LOE)	1OCT98	30SEP99
210485	35	35	0	1130:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	21JAN99	11MAR99
21M065	0	0	0	1130: CMS WORK COMPLETED		11MAR99
210490	10	10	0	1130: Issue DOE Draft of CMS Report	12MAR99	25MAR99
210495	22	22	0	1130: Conduct Review of DOE Draft of CMS Report	26MAR99	26APR99
210500	22	22	0	1130:Incorp. DOE Rev Comments DOE Dft CMS Report	27APR99	26MAY99
210505	10	10	0	1130: Issue EPA/NMED Draft of CMS Report	27MAY99	10JUN99
21M075	0	0	0	1130: EPA/NMED DRAFT OF CMS REPORT COMPLETED		10JUN99
210510	44	44	0	1130: Conduct EPA Review of CMS Report	11JUN99	12AUG99
210515	44	44	0	1130: Conduct NMED Review of CMS Rpt	11JUN99	12AUG99
210580	20	20	0	1130: Incorporate EPA/NMED Comments on CMS Rpt	13AUG99	10SEP99
210585	10	10	0	1130: Issue Final CMS Report	13SEP99	24SEP99
21M080	0	0	0	1130: ASSESSMENT COMPLETED		24SEP99

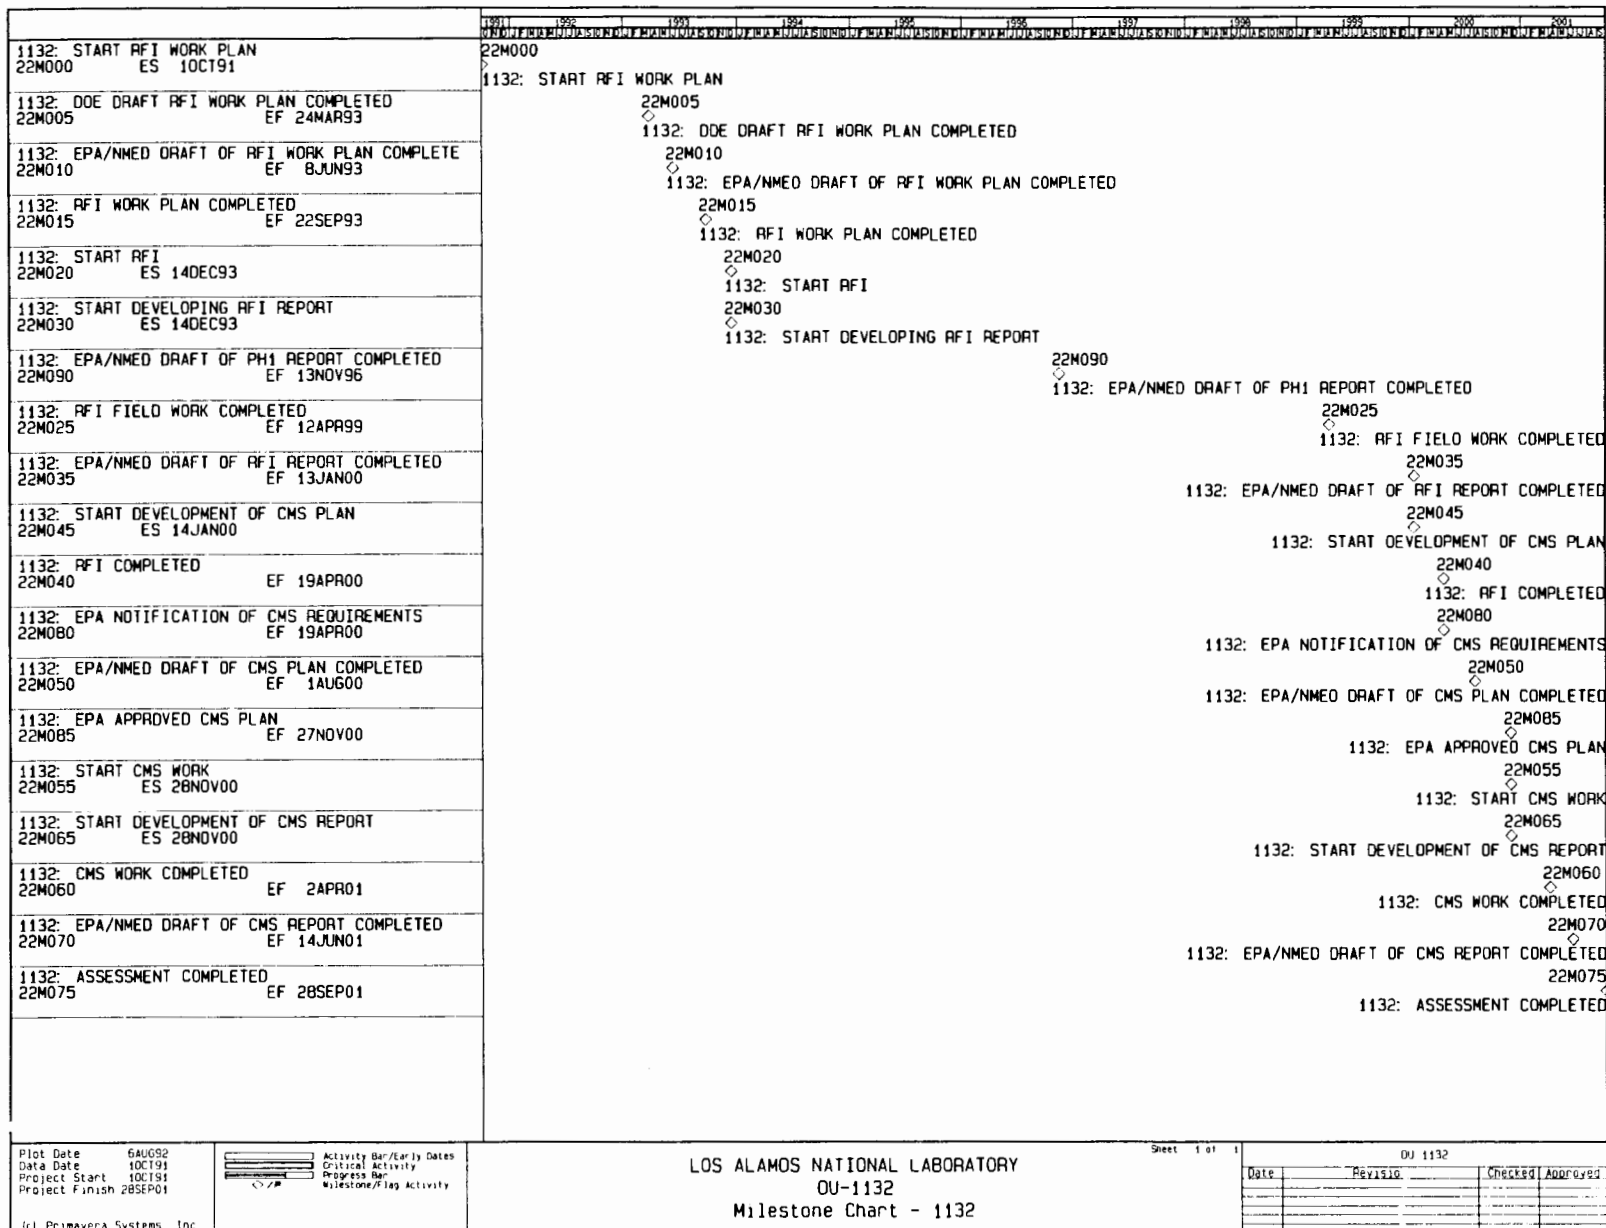

BASELINE

START DATE 10OCT91 FIN DATE 28SEP01

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
220010	65	65	0	1132: Develop Scope for RFI WP	1OCT91	8JAN92
220015	250*	250*	0	1132: Manage ADS During FY-92 (LOE)	1OCT91*	30SEP92
22M000	0	0	0	1132: START RFI WORK PLAN	1OCT91	
220025	40	40	0	1132: Locate Existing Data for RFI WP	24DEC91	24FEB92
220035	38	38	0	1132: Analyze Existing Data for RFI WP	25FEB92	16APR92
220045	20	20	0	1132: Draft Existing Data Report for RFI WP	17APR92	14MAY92
220055	40	40	0	1132: Determine Data Needs for RFI WP	15MAY92	13JUL92
220075	37	37	0	1132: Develop Data Quality Objectives for RFI WP	14JUL92	2SEP92
220085	65	65	0	1132: Develop Sampling Plan for RFI WP	3SEP92	9DEC92
220000	249	249	0	1132:FY93 Conduct Bench/Pilot Studies (LOE)	1OCT92*	30SEP93
220030	249	249	0	1132: Manage ADS During FY-93 (LOE)	1OCT92	30SEP93
220060	20	20	0	1132: Write Community Relations Plan for RFI WP	10NOV92	9DEC92
220065	20	20	0	1132: Write Records Management Plan for RFI WP	10NOV92	9DEC92
220095	20	20	0	1132: Write Quality Assurance Plan for RFI WP	10NOV92	9DEC92
220100	20	20	0	1132: Write Health & Safety Plan for RFI WP	10NOV92	9DEC92
220105	20	20	0	1132: Write Management Plan for RFI WP	10NOV92	9DEC92
220115	20	20	0	1132: Develop LANL Internal Draft of RFI WP	10DEC92	11JAN93
220125	20	20	0	1132: LANL/VE Review Internal Draft RFI WP	12JAN93	9FEB93
220135	20	20	0	1132:Incorp LANL Rev Comments into Int Dft RFIWP	10FEB93	10MAR93
220145	10	10	0	1132: Issue DOE Draft of RFI WP	11MAR93	24MAR93
22M005	0	0	0	1132: DOE DRAFT RFI WORK PLAN COMPLETED		24MAR93
220150	22	22	0	1132: Cond DOE Review of DOE Draft of RFI WP	25MAR93	23APR93
220155	20	20	0	1132:Incorp DOE Rev.Comments into DOE Dft RFI WP	26APR93	21MAY93
220020	106	106	0	1132: FY93 Develop NEPA Doc for RFI WP	3MAY93*	30SEP93
220160	11	11	0	1132: Issue EPA/NMED Draft of RFI Work Plan	24MAY93	8JUN93
22M010	0	0	0	1132: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		8JUN93
220165	44	44	0	1132: Conduct NMED Review of RFI WP	9JUN93	10AUG93
220170	44	44	0	1132: Conduct EPA Review of RFI Work Plan	9JUN93	10AUG93
220530	20	20	0	1132: Incorporate EPA/NMED Comments for RFI WP	11AUG93	8SEP93
220525	16	16	0	1132: FY93 Write Ph1 Contracts for RFI/Mobilize	9SEP93	30SEP93

LANL MEE-4 G. GOULD

FINEST HOUR

ADS 1132:TA-39

BASELINE

REPORT DATE 6AUG92 RUN NO. 114  
17:39

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 28SEP01

1132 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
220535	10	10	0	1132: Issue Final RFI Work Plan	9SEP93	22SEP93
22M015	0	0	0	1132: RFI WORK PLAN COMPLETED		22SEP93
220021	20	20	0	1132: FY94 Develop NEPA Doc for RFI WP	1OCT93	28OCT93
220040	250	250	0	1132: Manage ADS During FY-94 (LOE)	1OCT93	30SEP94
220180	250	250	0	1132: FY94 Conduct RFI Bench/Pilot Studies	1OCT93*	30SEP94
220526	49	49	0	1132: FY94 Write Ph1 Contracts for RFI/Mobilize	1OCT93	13DEC93
220185	201	201	0	1132: FY94 Conduct RFI PH1 Field Work	14DEC93	30SEP94
220190	201	201	0	1132: FY94 Conduct RFI PH1 Sample Analysis	14DEC93	30SEP94
220195	201	201	0	1132: FY94 Conduct RFI PH1 Data Assessment	14DEC93	30SEP94
220310	100	100	0	1132: Develop NEPA Documentation for RFI Report	14DEC93	9MAY94
660000	201	201	0	1132: Conduct VCA (LOE)	14DEC93	30SEP94
22M020	0	0	0	1132: START RFI	14DEC93	
22M030	0	0	0	1132: START DEVELOPING RFI REPORT	14DEC93	
220050	247	247	0	1132: Manage ADS During FY-95 (LOE)	3OCT94	29SEP95
220186	126	126	0	1132: FY95 Conduct RFI PH1 Field Work	3OCT94	10APR95
220191	247	247	0	1132: FY95 Conduct RFI PH1 Sample Analysis	3OCT94	29SEP95
220196	247	247	0	1132: FY95 Conduct RFI PH1 Data Assessment	3OCT94	29SEP95
220595	247	247	0	1132: FY95 Conduct Bench/Pilot Studies (LOE)	3OCT94*	29SEP95
660001	126	126	0	1132: Conduct VCA (LOE)	3OCT94	10APR95
220205	20	20	0	1132: Demobilize RFI PH1 Field Work	11APR95	8MAY95
220070	249	249	0	1132: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
220192	156	156	0	1132: FY96 Conduct RFI PH1 Sample Analysis	2OCT95	17MAY96
220197	166	166	0	1132: FY96 Conduct RFI PH1 Data Assessment	2OCT95	3JUN96
220200	60	60	0	1132: Write RFI PH1 Report/WP Modification	4JUN96	27AUG96
220215	23	23	0	1132: DOE/LANL Review PH1 Report/WP Modification	28AUG96	30SEP96
220080	249	249	0	1132: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
220216	20	20	0	1132:Inc DOE/LANL Comments PHI RPT/WP Mod	1OCT96	29OCT96
220217	10	10	0	1132:EPA/NMED Draft PHI Rpt Compl	30OCT96	13NOV96
22M090	0	0	0	1132: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		13NOV96
220210	22	22	0	1132: EPA/NMED Rev PH1 Report/WP Modification	14NOV96	17DEC96



LANL MEE-4 G. GOULD

FINEST HOUR

ADS 1132:TA-39

BASELINE

REPORT DATE 6AUG92 RUN NO. 114

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 28SEP01

17:39

1132 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
220211	11	11	0	1132:Inc EPA/NMED Comments PHI Rpt/WP	18DEC96	6JAN97
220212	10	10	0	1132:Issue Final RFI PHI Rpt	7JAN97	21JAN97
220220	20	20	0	1132: Write PH2 Contract; Mobilize for RFI	22JAN97	19FEB97
220225	156	156	0	1132: FY97 Conduct RFI PH2 Field Work	20FEB97	30SEP97
220230	156	156	0	1132: FY97 Conduct RFI PH2 Sample Analysis	20FEB97	30SEP97
220240	156	156	0	1132: FY97 Conduct RFI PH2 Data Assessment	20FEB97	30SEP97
220090	249	249	0	1132: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
220226	180	180	0	1132: FY98 Conduct RFI PH2 Field Work	10CT97	23JUN98
220231	249	249	0	1132: FY98 Conduct RFI PH2 Sample Analysis	10CT97	30SEP98
220241	249	249	0	1132: FY98 Conduct RFI PH2 Data Assessment	10CT97	30SEP98
220227	178	178	0	1132: FY99 Conduct RFI PH2 Field Work	24JUN98	15MAR99
220110	249	249	0	1132: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
220232	87	87	0	1132: FY99 Conduct RFI PH2 Sample Analysis	10CT98	10FEB99
220242	87	87	0	1132: FY99 Conduct RFI PH2 Data Assessment	10CT98	10FEB99
220300	45	45	0	1132: Conduct RFI Report Facility Investigation	11FEB99	15APR99
220305	50	50	0	1132: Conduct RFI Report Investigation Analysis	11FEB99	22APR99
220235	20	20	0	1132: Demobilize RFI PH2 Field Work	16MAR99	12APR99
22M025	0	0	0	1132: RFI FIELD WORK COMPLETED		12APR99
220320	40	40	0	1132: Prepare Internal Draft of RFI Report	23APR99	18JUN99
220325	30	30	0	1132: LANL/VE Review Internal Draft of RFI Rpt	21JUN99	2AUG99
220330	30	30	0	1132: Incorporate LANL Rev. Comments Int Dft RFI Rpt	3AUG99	14SEP99
220335	25	25	0	1132: Issue DOE Draft of RFI Report	15SEP99	20OCT99
220120	249	249	0	1132: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
220340	15	15	0	1132: Conduct Review of DOE Draft of RFI Report	21OCT99	10NOV99
220345	20	20	0	1132: Incorporate DOE Rev. Comments DOE Drft RFI Rpt	11NOV99	13DEC99
220350	20	20	0	1132: Issue EPA/NMED Draft of RFI Report	14DEC99	13JAN00
22M035	0	0	0	1132: EPA/NMED DRAFT OF RFI REPORT COMPLETED		13JAN00
220355	33	33	0	1132: Conduct EPA Review of RFI Report	14JAN00	2MAR00
220360	33	33	0	1132: Conduct NMED Review of RFI Rpt	14JAN00	2MAR00
220370	33	33	0	1132: Establish Current Situation for CMS Plan	14JAN00	2MAR00

LANL MEE-4 G. GOULD

FINEST HOUR

ADS 1132:TA-39

BASELINE

REPORT DATE 6AUG92 RUN NO. 114

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 28SEP01

17:39

1132 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 4


ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
220375	33	33	0	1132: Establish CA Objectives for CMS Plan	14JAN00	2MAR00
220380	33	33	0	1132: Dev Screening Technologies for CMS Plan	14JAN00	2MAR00
220385	33	33	0	1132: Develop NEPA Documentation for CMS Plan	14JAN00	2MAR00
22M045	0	0	0	1132: START DEVELOPMENT OF CMS PLAN	14JAN00	
220390	19	19	0	1132: Develop Alternatives for CMS Plan	3MAR00	29MAR00
220555	14	14	0	1132: Incorporate EPA/NMED Comments on RFI Rpt	3MAR00	22MAR00
220560	20	20	0	1132: Issue Final RFI Report	23MAR00	19APR00
220395	10	10	0	1132: Develop Internal Draft of CMS Plan	30MAR00	12APR00
220400	10	10	0	1132: LANL/VE Review Internal Draft of CMS Plan	13APR00	26APR00
22M040	0	0	0	1132: RFI COMPLETED		19APR00
22M080	0	0	0	1132: EPA NOTIFICATION OF CMS REQUIREMENTS		19APR00
220405	10	10	0	1132: Incorp. LANL REV Comments Intern Dft CMS P	27APR00	10MAY00
220410	5	5	0	1132: Issue DOE Draft of CMS Plan	11MAY00	17MAY00
220415	22	22	0	1132: Conduct Review of DOE Draft of CMS Plan	18MAY00	19JUN00
220420	20	20	0	1132: Incorp. DOE Rev.Comments DOE Dft.of CMS PL	20JUN00	18JUL00
220425	10	10	0	1132: Issue EPA/NMED Draft of CMS Plan	19JUL00	1AUG00
22M050	0	0	0	1132: EPA/NMED DRAFT OF CMS PLAN COMPLETED		1AUG00
220430	44	44	0	1132: Conduct EPA Review of CMS Plan	2AUG00	3OCT00
220435	44	44	0	1132: Conduct NMED Review of CMS Plan	2AUG00	3OCT00
220221	248	248	0	1132: Manage ADS During FY-01 (LOE)	2OCT00	28SEP01
220565	20	20	0	1132: Incorporate EPA/NMED Comments on CMS Plan	4OCT00	1NOV00
220570	10	10	0	1132: Issue Final CMS Plan	2NOV00	16NOV00
220575	5	5	0	1132: EPA Approves CMS Plan	17NOV00	27NOV00
22M085	0	0	0	1132: EPA APPROVED CMS PLAN		27NOV00
220440	85	85	0	1132: Conduct CMS Bench/Pilot Studies (LOE)	28NOV00	2APR01
220445	30	30	0	1132: Conduct Technical Evaluation for CMS Rpt	28NOV00	11JAN01
220450	30	30	0	1132: Cond Envir Evaluation for CMS Report	28NOV00	11JAN01
220455	30	30	0	1132: Conduct Human Health Eval for CMS Report	28NOV00	11JAN01
220460	30	30	0	1132: Cond Comm Relations Eval.for CMS Report	28NOV00	11JAN01
220465	30	30	0	1132: Conduct Cost Evaluation for CMS Report	28NOV00	11JAN01

BASELINE

START DATE 1OCT91 FIN DATE 28SEP01

DATA DATE 10OCT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
220470	30	30	0	1132: Develop NEPA Documentation for CMS Report	28NOV00	11JAN01
22M055	0	0	0	1132: START CMS WORK	28NOV00	
22M065	0	0	0	1132: START DEVELOPMENT OF CMS REPORT	28NOV00	
220475	10	10	0	1132: Prepare Internal Draft of CMS Report	12JAN01	26JAN01
220480	10	10	0	1132: LANL/VE Review Internal Draft of CMS Rpt	29JAN01	9FEB01
220485	35	35	0	1132:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	12FEB01	2APR01
22M060	0	0	0	1132: CMS WORK COMPLETED		2APR01
220490	10	10	0	1132: Issue DOE Draft of CMS Report	3APR01	16APR01
220495	22	22	0	1132: Conduct Review of DOE Draft of CMS Report	17APR01	16MAY01
220500	10	10	0	1132:Incorp. DOE Rev Comments DOE Dft CMS Report	17MAY01	31MAY01
220505	10	10	0	1132: Issue EPA/NMED Draft of CMS Report	1JUN01	14JUN01
22M070	0	0	0	1132: EPA/NMED DRAFT OF CMS REPORT COMPLETED		14JUN01
220510	44	44	0	1132: Conduct EPA Review of CMS Report	15JUN01	16AUG01
220515	44	44	0	1132: Conduct NMED Review of CMS Report	15JUN01	16AUG01
220580	20	20	0	1132: Incorporate EPA/NMED Comments on CMS Rpt	17AUG01	14SEP01
220585	10	10	0	1132: Issue Final CMS Report	17SEP01	28SEP01
22M075	0	0	0	1132: ASSESSMENT COMPLETED		28SEP01

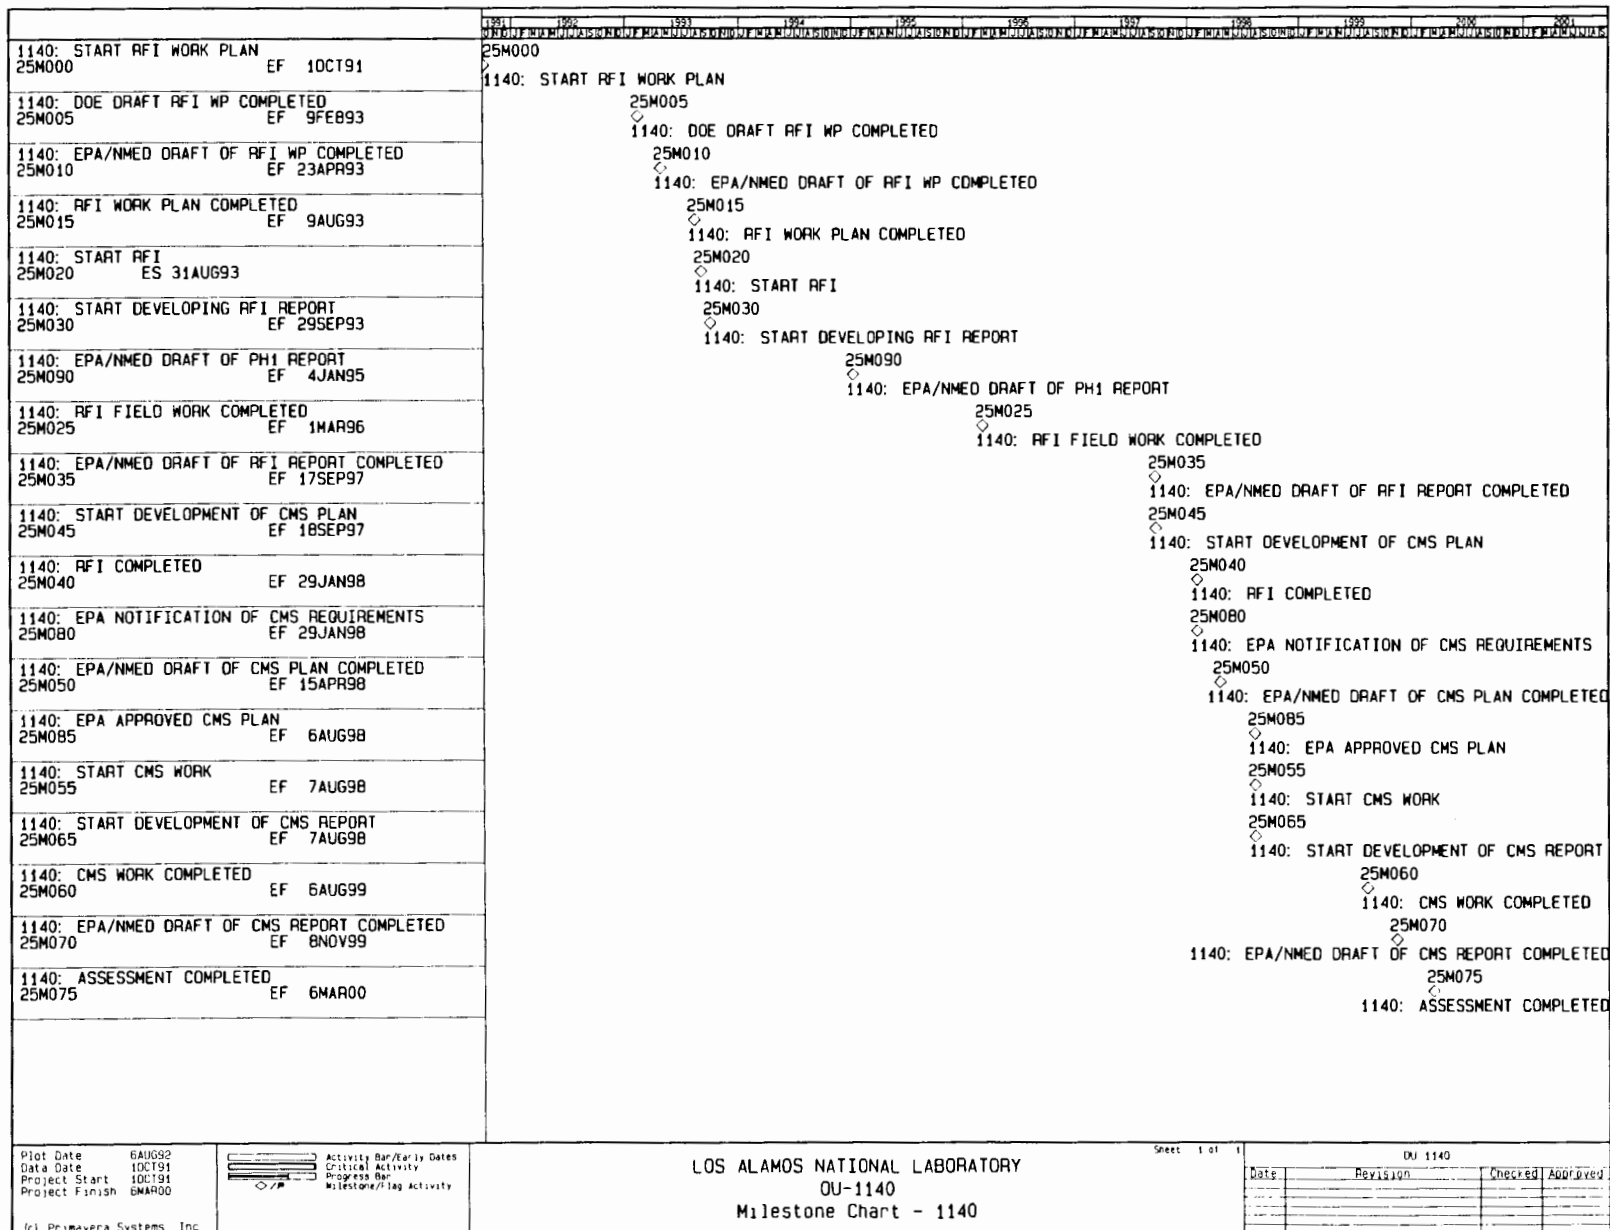

LANL	CLS-6	ROY MICHELOTTI	FINEST HOUR	ADS 1140:TA-46	BASELINE
REPORT DATE	6AUG92	RUN NO. 143	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 6MAR00
	18:08				
1140 SCHEDULE	REPORT BY	EARLY START		DATA DATE 10CT91	PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
250100	250	250	0	1140: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
25M000	0	0	0	1140: START RFI WORK PLAN		10CT91*
250005	32	32	0	1140: Develop Scope RFI Work Plan	20CT91*	18NOV91
250006	246	246	0	1140:Conduct Voluntary C.Actions for RFI WP(LOE)	20CT91*	25SEP92
250030	139	139	0	1140: Determine Data Needs for RFI WP	1NOV91*	26MAY92
250010	74	74	0	1140: Locate Existing Data for RFI WP	4NOV91*	25FEB92
250015	224	224	0	1140: Develop NEPA Documentation for RFI WP	4NOV91*	25SEP92
250020	64	64	0	1140: Analyze Existing Data for RFI WP	2MAR92*	29MAY92
250045	106	106	0	1140: Develop Data Quality Objectives for RFI WP	1MAY92*	30SEP92
250025	22	22	0	1140: Draft Existing Data Report for RFI WP	8SEP92*	70CT92
250035	22	22	0	1140: Write Community Relations Plan for RFI WP	10CT92*	2NOV92
250040	22	22	0	1140: Write Records Management Plan for RFI WP	10CT92*	2NOV92
250050	90	90	0	1140: Develop Sampling Plans for RFI WP	10CT92*	16FEB93
250105	249	249	0	1140: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
25M005	0	0	0	1140: DOE DRAFT RFI WP COMPLETED		9FEB93*
250055	20	20	0	1140: Write QA Plan for RFI WP	23FEB93*	22MAR93
250060	20	20	0	1140: Write Health & Safety Plan for RFI WP	23FEB93*	22MAR93
250065	20	20	0	1140: Write Management Plan for RFI WP	23FEB93*	22MAR93
250066	246	246	0	1140: Cond Bench/Pilot Studies for RFI WP (LOE)	23FEB93*	15FEB94
250070	20	20	0	1140: Develop LANL Internal Draft of RFI WP	23MAR93*	19APR93
250075	20	20	0	1140: LANL/VE Review Internal Draft for RFI WP	23APR93*	20MAY93
25M010	0	0	0	1140: EPA/NMED DRAFT OF RFI WP COMPLETED		23APR93*
250080	20	20	0	1140: Incorp. LANL Comments & Dev DOE Draft WP	21MAY93*	18JUN93
250085	22	22	0	1140: Conduct DOE Review DOE Draft RFI WP	21JUN93*	21JUL93
250090	20	20	0	1140: Incorp DOE Comments & Dev EPA/NMED Dft WP	22JUL93*	18AUG93
250091	10	10	0	1140: Publish EPA/NMED Draft of RFI Work Plan	5AUG93*	18AUG93
25M015	0	0	0	1140: RFI WORK PLAN COMPLETED		9AUG93*
250095	44	44	0	1140: Conduct EPA Review Draft RFI WP	19AUG93*	20OCT93
250096	44	44	0	1140: Conduct NMED Review Draft RFI WP	19AUG93*	20OCT93
250505	45	45	0	1140: Write PH1 Contracts for RFI	19AUG93*	21OCT93

LANL	CLS-6	ROY MICHELOTTI	FINEST HOUR	ADS 1140:TA-46	BASELINE
REPORT DATE	6AUG92	RUN NO. 143	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 6MAR00
1140 SCHEDULE REPORT BY	18:08	EARLY START		DATA DATE 10CT91	PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
250155	20	20	0	1140: Mobilize for RFI	31AUG93*	28SEP93
250160	245	245	0	1140: Conduct RFI Bench/Pilot Studies (LOE)	31AUG93*	23AUG94
250500	245	245	0	1140: Assmt - Conduct VCA (LOE)	31AUG93*	23AUG94
25M020	0	0	0	1140: START RFI	31AUG93*	
250165	245	245	0	1140: Conduct RFI PH1 Field Work	29SEP93*	21SEP94
250170	245	245	0	1140: Conduct RFI PH1 Sample Analysis	29SEP93*	21SEP94
250175	245	245	0	1140: Conduct RFI PH1 Data Assessment	29SEP93*	21SEP94
25M030	0	0	0	1140: START DEVELOPING RFI REPORT		29SEP93*
250290	100	100	0	1140: Develop NEPA Documentation for RFI Report	30SEP93*	28FEB94
250110	250	250	0	1140: Manage ADS During FY-94 (LOE)	1OCT93	30SEP94
250510	20	20	0	1140: Incorporate EPA/NMED Comments for RFI WP	21OCT93*	18NOV93
250515	10	10	0	1140: Publish Final RFI Work Plan	19NOV93*	6DEC93
250180	60	60	0	1140: Write RFI PH1 Report Modification	28SEP94*	29DEC94
250185	20	20	0	1140: Demobilize RFI PH1 Field Work	28SEP94*	26OCT94
250115	247	247	0	1140: Manage ADS During FY-95 (LOE)	3OCT94	29SEP95
25M090	0	0	0	1140: EPA/NMED DRAFT OF PH1 REPORT		4JAN95*
250190	22	22	0	1140: EPA/NMED Rev PH1 Tech Memo/WP Modification	5JAN95*	6FEB95
250195	22	22	0	1140: DOE Review PH1 Tech Memo/WP Modification	5JAN95*	6FEB95
250200	20	20	0	1140: Write PH2 Contract; Mobilize for RFI	5JAN95*	2FEB95
250205	245	245	0	1140: Conduct RFI PH2 Field Work	3FEB95*	29JAN96
250210	245	245	0	1140: Conduct RFI PH2 Sample Analysis	3FEB95*	29JAN96
250220	245	245	0	1140: Conduct RFI PH2 Data Assessment	3FEB95*	29JAN96
250120	249	249	0	1140: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
250215	20	20	0	1140: Demoblize RFI PH2 Field Work	2FEB96*	1MAR96
250280	100	100	0	1140: Conduct RFI Report Facility Investigation	2FEB96*	24JUN96
250285	110	110	0	1140: Conduct RFI Report Investigation Analysis	2FEB96*	9JUL96
25M025	0	0	0	1140: RFI FIELD WORK COMPLETED		1MAR96*
250300	132	132	0	1140: Prepare Internal Draft of RFI Report	10JUL96*	22JAN97
250125	249	249	0	1140: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
680000	189	189	0	1140: Conduct VCA (LOE)	2JAN97*	30SEP97

-----

LANL	CLS-6	ROY MICHELOTTI	FINEST HOUR	ADS 1140:TA-46	BASELINE
REPORT DATE	6AUG92	RUN NO. 143	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 6MAR00
	18:08				
1140 SCHEDULE REPORT BY	EARLY START			DATA DATE 10CT91	PAGE NO. 3

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
250305	20	20	0	1140: LANL/VE Review Internal Draft of RFI Rpt	29JAN97*	26FEB97
250310	40	40	0	1140:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	27FEB97*	23APR97
250315	20	20	0	1140: Publish DOE Draft of RFI Report	24APR97*	21MAY97
250320	22	22	0	1140: Conduct Review of DOE Draft of RFI Report	22MAY97*	23JUN97
250325	40	40	0	1140:Incorp. DOE Rev. Comments DOE Drft RFI Rpt	24JUN97*	19AUG97
250330	20	20	0	1140: Publish EPA/NMED Draft of RFI Report	20AUG97*	17SEP97
25M035	0	0	0	1140: EPA/NMED DRAFT OF RFI REPORT COMPLETED		17SEP97*
250335	44	44	0	1140: Conduct EPA Review of RFI Report	18SEP97*	24NOV97
250340	44	44	0	1140: Conduct NMED Review of RFI Rpt	18SEP97*	24NOV97
25M045	0	0	0	1140: START DEVELOPMENT OF CMS PLAN		18SEP97*
250345	245	245	0	1140: Conduct Bench/Pilot Studies CMS Pl (LOE)	19SEP97*	14SEP98
250350	35	35	0	1140: Establish Current Situation for CMS Plan	19SEP97*	7NOV97
250355	35	35	0	1140: Establish CA Objectives for CMS Plan	19SEP97*	7NOV97
250360	35	35	0	1140: Develop Screening Technologies for CMS Pl	19SEP97*	7NOV97
250365	245	245	0	1140: Develop NEPA Documentation for CMS Plan	19SEP97*	14SEP98
250130	249	249	0	1140: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
680005	245	245	0	1140: Conduct VCA (LOE)	10CT97*	24SEP98
250370	15	15	0	1140: Develop Alternatives for CMS Plan	11NOV97*	3DEC97
250535	20	20	0	1140: Incorporate EPA/NMED Comments on RFI Rpt	25NOV97*	22DEC97
250375	10	10	0	1140: Develop Internal Draft of CMS Plan	4DEC97*	17DEC97
250380	10	10	0	1140: LANL/VE Review Internal Draft of CMS Plan	18DEC97*	5JAN98
250540	20	20	0	1140: Publish Final RFI Report	23DEC97*	23JAN98
250385	10	10	0	1140:Incorp. LANL REV Comments Intern Dft CMS Pl	9JAN98*	23JAN98
250390	5	5	0	1140: Publish DOE Draft of CMS Plan	26JAN98*	30JAN98
25M040	0	0	0	1140: RFI COMPLETED		29JAN98*
25M080	0	0	0	1140: EPA NOTIFICATION OF CMS REQUIREMENTS		29JAN98*
250395	22	22	0	1140: Conduct Review of DOE Draft of CMS Plan	2FEB98*	4MAR98
250400	20	20	0	1140:Incorp. DOE Rev.Comments DOE Dft.of CMS Pl	5MAR98*	1APR98
250405	10	10	0	1140: Publish EPA/NMED Draft of CMS Plan	2APR98*	15APR98
25M050	0	0	0	1140: EPA/NMED DRAFT OF CMS PLAN COMPLETED		15APR98*


LANL	CLS-6	ROY MICHELOTTI	FINEST HOUR	ADS 1140:TA-46	BASELINE
REPORT DATE	6AUG92	RUN NO. 143	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 6MAR00
	18:08				
1140 SCHEDULE REPORT BY	EARLY START			DATA DATE 10CT91	PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
250410	44	44	0	1140: Conduct EPA Review of CMS Plan	16APR98*	17JUN98
250415	44	44	0	1140: Conduct NMED Review of CMS Plan	16APR98*	17JUN98
250545	20	20	0	1140: Incorporate EPA/NMED Comments on CMS Plan	18JUN98*	16JUL98
250550	10	10	0	1140: Publish Final CMS Plan	17JUL98*	30JUL98
250555	5	5	0	1140: EPA Approves CMS Plan	31JUL98*	6AUG98
25M085	0	0	0	1140: EPA APPROVED CMS PLAN		6AUG98*
25M055	0	0	0	1140: START CMS WORK		7AUG98*
25M065	0	0	0	1140: START DEVELOPMENT OF CMS REPORT		7AUG98*
250420	245	245	0	1140: Conduct CMS Bench/Pilot Studies (LOE)	10AUG98*	3AUG99
250425	30	30	0	1140: Conduct Technical Evaluation for CMS Rpt	10AUG98*	21SEP98
250430	30	30	0	1140: Conduct Environmental Eval for CMS Report	10AUG98*	21SEP98
250435	30	30	0	1140: Conduct Human Health Eval for CMS Report	10AUG98*	21SEP98
250440	30	30	0	1140: Conduct Community Relations Eval. CMS Rpt	10AUG98*	21SEP98
250445	30	30	0	1140: Conduct Cost Evaluation for CMS Report	10AUG98*	21SEP98
250450	30	30	0	1140: Develop NEPA Documentation for CMS Report	10AUG98*	21SEP98
250455	10	10	0	1140: Prepare Internal Draft of CMS Report	22SEP98*	5OCT98
250135	249	249	0	1140: Manage ADS During FY-99 (LOE)	1OCT98	30SEP99
250460	10	10	0	1140: LANL/VE Review Internal Draft of CMS Rpt	6OCT98*	20OCT98
250465	35	35	0	1140:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	18JUN99*	6AUG99
25M060	0	0	0	1140: CMS WORK COMPLETED		6AUG99*
250470	10	10	0	1140: Publish DOE Draft of CMS Report	9AUG99*	20AUG99
250475	22	22	0	1140: Conduct DOE Review of Draft of CMS Report	23AUG99*	22SEP99
250480	22	22	0	1140:Incorp. DOE Rev Commt into DOE Dft CMS Rpt	23SEP99*	25OCT99
250140	100	100	0	1140: Manage ADS During FY-00 (LOE)	1OCT99	1MAR00
250485	10	10	0	1140: Publish EPA/NMED Draft of CMS Report	26OCT99*	8NOV99
25M070	0	0	0	1140: EPA/NMED DRAFT OF CMS REPORT COMPLETED		8NOV99*
250490	44	44	0	1140: Conduct EPA Review of CMS Report	9NOV99*	18JAN00
250495	44	44	0	1140: Conduct NMED Rev of CMS Report	9NOV99*	18JAN00
250560	20	20	0	1140: Incorporate EPA/NMED Comments on CMS Rpt	24JAN00*	18FEB00
250565	10	10	0	1140: Publish Final CMS Report	22FEB00*	6MAR00



LANL	CLS-6	ROY MICHELOTTI	FINEST HOUR	ADS 1140:TA-46	BASELINE
REPORT DATE	6AUG92	RUN NO. 143	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 6MAR00
	18:08			DATA DATE 1OCT91	PAGE NO. 5
1140 SCHEDULE REPORT BY EARLY START					

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
25M075	0	0	0	1140: ASSESSMENT COMPLETED		6MAR00*

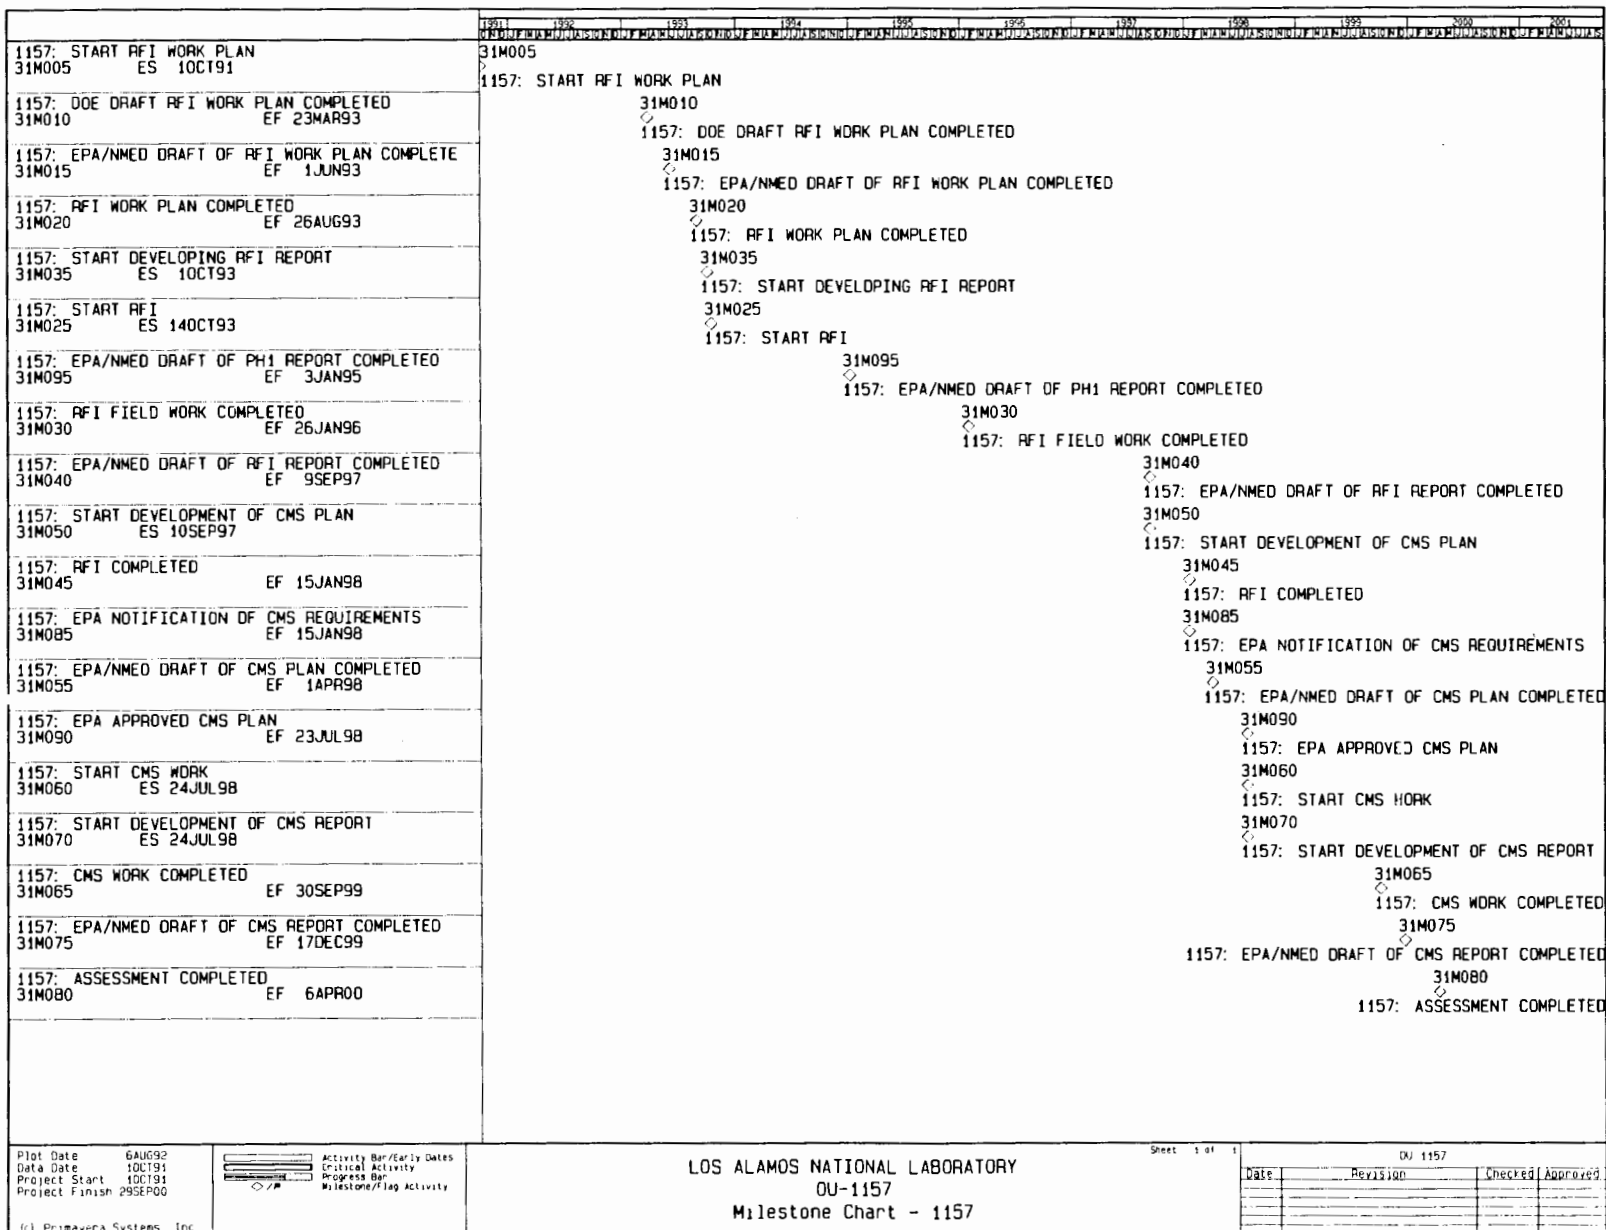

LANL EES-5 T. GLATZMAIER	FINEST HOUR	ADS 1157 TA-8 9 23 69	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 1OCT91	FIN DATE 29SEP00
16:00			
1157 SCHEDULE REPORT BY EARLY START		DATA DATE 1OCT91	PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
310180	250	250	0	1157: Conduct RFI Bench/Pilot Studies (LOE)	10CT91	30SEP92
31M005	0	0	0	1157: START RFI WORK PLAN	10CT91*	
310000	210	210	0	1157:Conduct Bench/Pilot Studies for RFI WP(LOE)	2DEC91*	30SEP92
310005	210	210	0	1157:Conduct Voluntary C.Actions for RFI WP(LOE)	2DEC91*	30SEP92
310010	20	20	0	1157: Develop Scope for RFI WP	2DEC91*	31DEC91
310015	210	210	0	1157: Manage ADS During FY-92 (LOE)	2DEC91*	30SEP92
310020	250	250	0	1157: Develop NEPA Documentation for RFI WP	2DEC91	1DEC92
310025	40	40	0	1157: Locate Existing Data for RFI WP	2DEC91	30JAN92
310035	38	38	0	1157: Analyze Existing Data for RFI WP	31JAN92	25MAR92
310045	20	20	0	1157: Draft Existing Data Report for RFI WP	26MAR92	22APR92
310055	37	37	0	1157: Determine Data Needs for RFI WP	23APR92	15JUN92
310060	20	20	0	1157: Write Community Relations Plan for RFI WP	23APR92	20MAY92
310065	20	20	0	1157: Write Records Management Plan for RFI WP	23APR92	20MAY92
310075	37	37	0	1157: Develop Data Quality Objectives for RFI WP	16JUN92	6AUG92
310085	60	60	0	1157: Develop Sampling Plan for RFI WP	21AUG92*	17NOV92
310030	249	249	0	1157: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
310095	20	20	0	1157: Write Quality Assurance Plan for RFI WP	18NOV92	17DEC92
310100	20	20	0	1157: Write Health & Safety Plan for RFI WP	18NOV92	17DEC92
310105	20	20	0	1157: Write Management Plan for RFI WP	18NOV92	17DEC92
310115	20	20	0	1157: Develop LANL Internal Draft of RFI WP	18DEC92	20JAN93
310125	22	22	0	1157: DOE/LANL/VE Review Internal Draft RFI WP	21JAN93	22FEB93
310135	20	20	0	1157:Incorp.LANL Rev Comments Intern Dft Reportr	23FEB93	22MAR93
310145	10	10	0	1157: Publish DOE Draft of RFI WP	23MAR93	5APR93
31M010	0	0	0	1157: DOE DRAFT RFI WORK PLAN COMPLETED		23MAR93*
310150	10	10	0	1157: DOE Review DOE Draft RFI WP	6APR93	19APR93
310155	20	20	0	1157:Incorporate DOE Rev.Comments DOE Dft Report	20APR93	17MAY93
310160	10	10	0	1157: Publish EPA/NMED Draft of RFI Work Plan	18MAY93	1JUN93
31M015	0	0	0	1157: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		1JUN93
310165	31	31	0	1157: Conduct NMED Review of RFI Work Plan	2JUN93	15JUL93
310170	31	31	0	1157: Conduct EPA Review of RFI Work Plan	2JUN93	15JUL93

LANL	EES-5	T. GLATZMAIER	FINEST HOUR	ADS 1157 TA-8 9 23 69	TBS 2/17/92
REPORT DATE	5AUG92	RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 29SEP00
	16:00				
1157 SCHEDULE REPORT BY EARLY START				DATA DATE 10CT91	PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
310525	63	63	0	1157: Write PH1 Contract; Mobilize for RFI	16JUL93	13OCT93
310530	20	20	0	1157: Incorporate EPA/NMED Comments for RFI WP	16JUL93	12AUG93
310535	10	10	0	1157: Issue Final RFI Work Plan	13AUG93	26AUG93
31M020	0	0	0	1157: RFI WORK PLAN COMPLETED		26AUG93
310040	250	250	0	1157: Manage ADS During FY-94 (LOE)	1OCT93	30SEP94
310185	249	249	0	1157: Conduct RFI PH1 Field Work	1OCT93	29SEP94
310190	249	249	0	1157: Conduct RFI PH1 Sample Analysis	1OCT93	29SEP94
310195	249	249	0	1157: Conduct RFI PH1 Data Assessment	1OCT93	29SEP94
310310	100	100	0	1157: Prepare NEPA/Environ. Info for RFI Report	1OCT93	1MAR94
31M035	0	0	0	1157: START DEVELOPING RFI REPORT	1OCT93	
310520	249	249	0	1157: Assmt - Conduct VCA (LOE)	14OCT93	13OCT94
31M025	0	0	0	1157: START RFI	14OCT93	
310200	60	60	0	1157: Write Draft RFI PH1 Report/WP Modification	30SEP94	3JAN95
310205	20	20	0	1157: Demobilize RFI PH1 Field Work	30SEP94	28OCT94
310050	247	247	0	1157: Manage ADS During FY-95 (LOE)	3OCT94	29SEP95
31M095	0	0	0	1157: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		3JAN95
310131	20	20	0	1157: Incorp. DOE/LANL Rev. Comments PH1 Rpt Mod	4JAN95	1FEB95
310215	22	22	0	1157: DOE/LANL Review PH1 Report/WP Modification	4JAN95	3FEB95
310210	22	22	0	1157: EPA/NMED Review PH1 Report/WP Modification	2FEB95	6MAR95
310220	20	20	0	1157: Write PH2 Contract; Mobilize for RFI	2FEB95	2MAR95
310225	205	205	0	1157: Conduct RFI PH2 Field Work	3MAR95	27DEC95
310230	235	235	0	1157: Conduct RFI PH2 Sample Analysis	3MAR95	9FEB96
310240	245	245	0	1157: Conduct RFI PH2 Data Assessment	3MAR95	26FEB96
310132	40	40	0	1157: Incorp. EPA/NMED Rev. Comments PH1 Rpt Mod	7MAR95	1MAY95
310133	10	10	0	1157: Issue Final PH1 Report/Work Plan Mod	2MAY95	15MAY95
310070	249	249	0	1157: Manage ADS During FY-96 (LOE)	2OCT95	30SEP96
310235	20	20	0	1157: Demoblize RFI PH2 Field Work	28DEC95	26JAN96
31M030	0	0	0	1157: RFI FIELD WORK COMPLETED		26JAN96
310300	100	100	0	1157: Conduct RFI Report Facility Investigation	27FEB96	17JUL96
310305	110	110	0	1157: Conduct RFI Report Investigation Analysis	27FEB96	31JUL96

LANL EES-5 T. GLATZMAIER	FINEST HOUR	ADS 1157 TA-8 9 23 69	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 29SEP00
16:00			
1157 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91	PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
310320	132	132	0	1157: Prepare Internal Draft of RFI Report	1AUG96	13FEB97
310080	249	249	0	1157: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
730000	189	189	0	1157: Conduct VCA (LOE)	2JAN97*	30SEP97
310325	22	22	0	1157: DOE/LANL/VE Rev Internal Draft of RFI Rpt	14FEB97	18MAR97
310330	40	40	0	1157:Incorp.LANL Rev.Comments Intern Dft RFI Rpt	19MAR97	13MAY97
310335	10	10	0	1157: Issue DOE Draft of RFI Report	14MAY97	28MAY97
310340	22	22	0	1157: Conduct Review of DOE Draft of RFI Report	29MAY97	27JUN97
310345	40	40	0	1157:Incorp. DOE Rev. Comments DOE Drft RFI Rpt	30JUN97	25AUG97
310350	10	10	0	1157: Issue EPA/NMED Draft of RFI Report	26AUG97	9SEP97
31M040	0	0	0	1157: EPA/NMED DRAFT OF RFI REPORT COMPLETED		9SEP97
310355	44	44	0	1157: Conduct EPA Review of RFI Report	10SEP97	12NOV97
310360	44	44	0	1157:Conduct NMED Review of RFI Report	10SEP97	12NOV97
310365	35	35	0	1157:Conduct Bench/Pilot Studies for CMS Pl(LOE)	10SEP97	29OCT97
310370	35	35	0	1157: Establish Current Situation for CMS Plan	10SEP97	29OCT97
310375	35	35	0	1157: Establish CA Objectives for CMS Plan	10SEP97	29OCT97
310380	35	35	0	1157:Develop Screening Technologies for CMS Plan	10SEP97	29OCT97
31M050	0	0	0	1157: START DEVELOPMENT OF CMS PLAN	10SEP97	
310090	249	249	0	1157: Manage ADS During FY-98 (LOE)	1OCT97	30SEP98
310385	249	249	0	1157: Develop NEPA Documentation for CMS Plan	1OCT97*	30SEP98
730005	249	249	0	1157: Conduct VCA (LOE)	1OCT97	30SEP98
310390	15	15	0	1157: Develop Alternatives for CMS Plan	30OCT97	24NOV97
310555	20	20	0	1157: Incorporate EPA/NMED Comments on RFI Rpt	13NOV97	12DEC97
310395	10	10	0	1157: Develop Internal Draft of CMS Plan	25NOV97	8DEC97
310400	10	10	0	1157: DOE/LANL/VE Rev Internal Draft of CMS Pl	9DEC97	22DEC97
310560	20	20	0	1157: Issue Final RFI Report	15DEC97	15JAN98
310405	10	10	0	1157:Incorp. LANL REV Comments Intern Dft CMS Pl	23DEC97	8JAN98
310410	5	5	0	1157: Issue DOE Draft of CMS Plan	9JAN98	16JAN98
31M045	0	0	0	1157: RFI COMPLETED		15JAN98
31M085	0	0	0	1157: EPA NOTIFICATION OF CMS REQUIREMENTS		15JAN98
310415	22	22	0	1157: Conduct Review of DOE Draft of CMS Plan	19JAN98	18FEB98

-----


LANL	EES-5	T. GLATZMAIER	FINEST HOUR	ADS 1157 TA-8 9 23 69	TBS 2/17/92
REPORT DATE	5AUG92	RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 29SEP00
	16:00				
1157 SCHEDULE	REPORT BY	EARLY START		DATA DATE 10CT91	PAGE NO. 4

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
310420	20	20	0	1157:Incorp. DOE Rev.Comments DOE Dft of CMS Pl	19FEB98	18MAR98
310425	10	10	0	1157: Issue EPA/NMED Draft of CMS Plan	19MAR98	1APR98
31M055	0	0	0	1157: EPA/NMED DRAFT OF CMS PLAN COMPLETED		1APR98
310430	44	44	0	1157: Conduct EPA Review of CMS Plan	2APR98	3JUN98
310435	44	44	0	1157: Conduct NMED Review of CMS Plan	2APR98	3JUN98
310565	20	20	0	1157: Incorporate EPA/NMED Comments on CMS Plan	4JUN98	1JUL98
310570	10	10	0	1157: Issue Final CMS Plan	2JUL98	16JUL98
310575	5	5	0	1157: EPA Approves CMS Plan	17JUL98	23JUL98
31M090	0	0	0	1157: EPA APPROVED CMS PLAN		23JUL98
310445	30	30	0	1157:Conduct Technical Evaluation for CMS Report	24JUL98	3SEP98
310450	30	30	0	1157: Conduct Environmental Eval for CMS Report	24JUL98	3SEP98
310455	30	30	0	1157: Conduct Human Health Eval for CMS Report	24JUL98	3SEP98
310460	30	30	0	1157:Conduct Community Relations Eval for CMSRpt	24JUL98	3SEP98
310465	30	30	0	1157: Conduct Cost Evaluation for CMS Report	24JUL98	3SEP98
310470	30	30	0	1157: Develop NEPA Documentation for CMS Report	24JUL98	3SEP98
31M060	0	0	0	1157: START CMS WORK	24JUL98	
31M070	0	0	0	1157: START DEVELOPMENT OF CMS REPORT	24JUL98	
310475	10	10	0	1157: Prepare Internal Draft of CMS Report	4SEP98	18SEP98
310480	10	10	0	1157: DOE/LANL/VE Rev Internal Draft of CMS Rpt	21SEP98	20CT98
310110	249	249	0	1157: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
310440	249	249	0	1157: Conduct CMS Bench/Pilot Studies (LOE)	10CT98*	30SEP99
310485	35	35	0	1157:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	12AUG99	30SEP99
31M065	0	0	0	1157: CMS WORK COMPLETED		30SEP99
310120	249	249	0	1157: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
310490	10	10	0	1157: Issue DOE Draft of CMS Report	10CT99	15OCT99
310495	22	22	0	1157: Conduct Review of DOE Draft of CMS Report	18OCT99	17NOV99
310500	10	10	0	1157:Incorp. DOE Rev Comments DOE Dft CMS Report	18NOV99	3DEC99
310505	10	10	0	1157: Issue EPA/NMED Draft of CMS Report	6DEC99	17DEC99
31M075	0	0	0	1157: EPA/NMED DRAFT OF CMS REPORT COMPLETED		17DEC99
310510	44	44	0	1157: Conduct EPA Review of CMS Report	20DEC99	24FEB00

LANL EES-5 T. GLATZMAIER	FINEST HOUR	ADS 1157 TA-8 9 23 69	TBS 2/17/92
REPORT DATE 5AUG92 RUN NO. 157	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 29SEP00
16:00			
1157 SCHEDULE REPORT BY EARLY START		DATA DATE 10CT91	PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
310515	44	44	0	1157: Conduct NMED Review of CMS Report	20DEC99	24FEB00
310580	20	20	0	1157: Incorporate EPA/NMED Comments on CMS Plan	25FEB00	23MAR00
310585	10	10	0	1157: Issue Final CMS Report	24MAR00	6APR00
31M080	0	0	0	1157: ASSESSMENT COMPLETED		6APR00

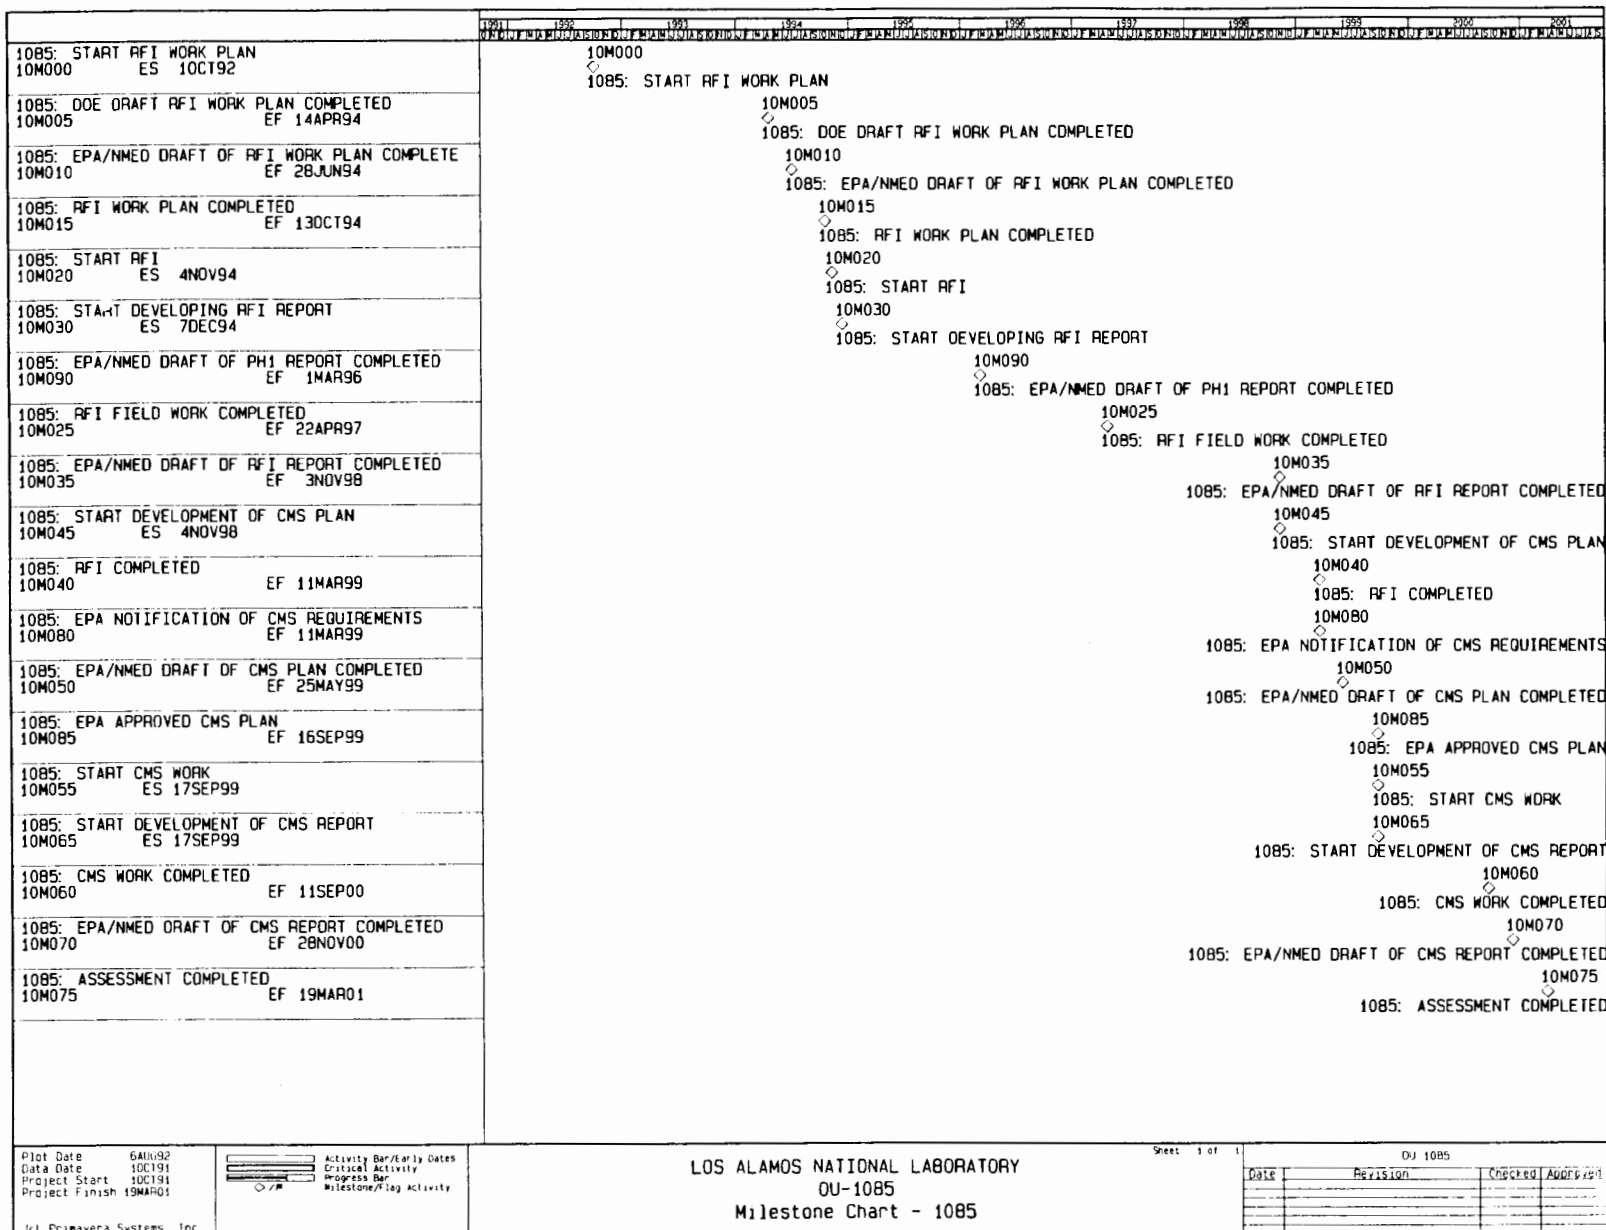



ADS 1085: TA-12 14 67      TBS 2/17/92

START DATE 1OCT91 FIN DATE 19MAR01

DATA DATE 10CT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
100000	249	249	0	1085: Bench/Pilot Studies	RFI WP (LOE)	10CT92	30SEP93
100005	249	249	0	1085: Conduct VCA	RFI WP (LOE)	10CT92	30SEP93
100470	249	249	0	1085: Manage ADS FY-93	(LOE)	10CT92	30SEP93
10M000	0	0	0	1085: START RFI WORK PLAN		10CT92*	
100010	20	20	0	1085: Develop Scope	RFI WP	4FEB93*	4MAR93
100015	245	245	0	1085: Develop NEPA Documentation	RFI WP	5MAR93	25FEB94
100020	40	40	0	1085: Locate Existing Data	RFI WP	5MAR93	29APR93
100050	40	40	0	1085: Data Quality Objectives	RFI WP	5MAR93	29APR93
100025	38	38	0	1085: Analyze Existing Data	RFI WP	9MAR93	29APR93
100030	20	20	0	1085: Draft Existing Data Report	RFI WP	30APR93	27MAY93
100035	40	40	0	1085: Determine Data Needs	RFI WP	26AUG93*	21OCT93
100055	60	60	0	1085: Develop Sampling Plan	RFI WP	7SEP93*	2DEC93
100475	250	250	0	1085: Manage ADS FY-94	(LOE)	10CT93	30SEP94
100040	20	20	0	1085: Community Relations Plan	RFI WP	21OCT93*	18NOV93
100045	20	20	0	1085: Write Records Management Plan	RFI WP	21OCT93*	18NOV93
100060	20	20	0	1085: Write Quality Assurance Plan	RFI WP	3DEC93*	4JAN94
100065	20	20	0	1085: Write Health & Safety Plan	RFI WP	3DEC93*	4JAN94
100070	20	20	0	1085: Write Management Plan	RFI WP	3DEC93*	4JAN94
100075	20	20	0	1085: Develop LANL Internal Draft	RFI WP	5JAN94	2FEB94
100080	20	20	0	1085: DOE/LANL/VE Rev Internal Draft	RFI WP	3FEB94	3MAR94
100085	20	20	0	1085: Inc DOE/LANL Comments Int Dft	RFI WP	4MAR94	31MAR94
100090	10	10	0	1085: Issue DOE Draft	RFI WP	1APR94	14APR94
10M005	0	0	0	1085: DOE DRAFT RFI WORK PLAN COMPLETED			14APR94
100095	22	22	0	1085: DOE Review DOE Draft	RFI WP	15APR94	16MAY94
100100	20	20	0	1085: Inc DOE Comments DOE Draft	RFI WP	17MAY94	14JUN94
100105	10	10	0	1085: Issue EPA/NMED Draft	RFI WP	15JUN94	28JUN94
10M010	0	0	0	1085: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED			28JUN94
100110	44	44	0	1085: NMED Review	RFI WP	29JUN94	30AUG94
100115	44	44	0	1085: EPA Review	RFI WP	29JUN94	30AUG94
100520	45	45	0	1085: Write Contracts	RFI PH1	31AUG94	3NOV94

LANL CLS-1 C. MARTELL

FINEST HOUR

ADS 1085: TA-12 14 67 TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 101

ENVIRONMENTAL RESTORATION

START DATE 1OCT91 FIN DATE 19MAR01

18:23

1085 SCHEDULE REPORT BY EARLY START

DATA DATE 1OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
100525	20	20	0	1085: Inc EPA/NMED Comments RFI WP	31AUG94	28SEP94
100530	10	10	0	1085: Issue Final RFI WP	29SEP94	13OCT94
100480	247	247	0	1085: Manage ADS FY-95 (LOE)	30CT94	29SEP95
10M015	0	0	0	1085: RFI WORK PLAN COMPLETED		13OCT94
100120	20	20	0	1085: Mobilize for RFI	4NOV94	6DEC94
100125	245	245	0	1085: RFI Bench/Pilot Studies (LOE)	4NOV94	31OCT95
100515	245	245	0	1085: Conduct VCA - Assessment (LOE)	4NOV94	31OCT95
10M020	0	0	0	1085: START RFI	4NOV94	
100130	245	245	0	1085: Field Work RFI PH1	7DEC94	1DEC95
100135	245	245	0	1085: Sample Analysis RFI PH1	7DEC94	1DEC95
100140	245	245	0	1085: Data Assessment RFI PH1	7DEC94	1DEC95
100450	100	100	0	1085: Develop NEPA Documentation RFI RPT	7DEC94	3MAY95
10M030	0	0	0	1085: START DEVELOPING RFI REPORT	7DEC94	
100485	249	249	0	1085: Manage ADS FY-96 (LOE)	20CT95	30SEP96
100145	60	60	0	1085: Write Report/WP Modification RFI PH1	4DEC95	1MAR96
100355	20	20	0	1085: Demobilize Field Work RFI PH1	4DEC95	3JAN96
10M090	0	0	0	1085: EPA/NMED DRAFT OF PH1 REPORT COMPLETED		1MAR96
100360	22	22	0	1085: EPA/NMED Review RPT / WP Mod RFI PH1	4MAR96	2APR96
100365	22	22	0	1085: DOE Review Report /WP Mod RFI PH1	4MAR96	2APR96
100370	20	20	0	1085: Write Contract and Mobilize RFI PH2	4MAR96	29MAR96
100375	245	245	0	1085: Field Work RFI PH2	1APR96	25MAR97
100380	245	245	0	1085: Sample Analysis RFI PH2	1APR96	25MAR97
100385	245	245	0	1085: Data Assessment RFI PH2	1APR96	25MAR97
100490	249	249	0	1085: Manage ADS FY-97 (LOE)	10CT96	30SEP97
550000	189	189	0	1085: Conduct VCA (LOE)	2JAN97*	30SEP97
100150	100	100	0	1085: Facility Investigation RFI RPT	26MAR97	14AUG97
100155	110	110	0	1085: Investigation Analysis RFI RPT	26MAR97	28AUG97
100390	20	20	0	1085: Demoblize Field Work RFI PH2	26MAR97	22APR97
10M025	0	0	0	1085: RFI FIELD WORK COMPLETED		22APR97
100160	132	132	0	1085: Prepare Internal Draft RFI RPT	29AUG97	16MAR98

ADS 1085: TA-12 14 67      TBS 2/17/92

START DATE 1OCT91 FIN DATE 19MAR01

DATA DATE 1OCT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
100495	249	249	0	1085: Manage ADS FY-98 (LOE)	10CT97	30SEP98
550005	249	249	0	1085: Conduct VCA (LOE)	10CT97	30SEP98
100165	20	20	0	1085: DOE/LANL/VE Rev Internal Drft RFI RPT	17MAR98	13APR98
100170	40	40	0	1085: Inc DOE/LANL Comments Int Dft RFI RPT	14APR98	9JUN98
100175	20	20	0	1085: Issue DOE Draft RFI RPT	10JUN98	8JUL98
100180	22	22	0	1085: DOE Review DOE Draft RFI RPT	9JUL98	7AUG98
100185	40	40	0	1085: Inc DOE Comments DOE Draft RFI RPT	10AUG98	5OCT98
100500	249	249	0	1085: Manage ADS FY-99 (LOE)	10CT98	30SEP99
100190	20	20	0	1085: Issue EPA/NMED Draft RFI RPT	6OCT98	3NOV98
10M035	0	0	0	1085: EPA/NMED DRAFT OF RFI REPORT COMPLETED		3NOV98
100195	44	44	0	1085: EPA Review RFI RPT	4NOV98	12JAN99
100200	44	44	0	1085: NMED Review RFI RPT	4NOV98	12JAN99
100205	10	10	0	1085: Cond Bench/Pilot Studies CMS PLN(LOE)	4NOV98	18NOV98
100210	35	35	0	1085: Establish Current Situation CMS PLN	4NOV98	29DEC98
100215	35	35	0	1085: Establish CA Objectives CMS PLN	4NOV98	29DEC98
100220	35	35	0	1085: Develop Screening Technology CMS PLN	4NOV98	29DEC98
100460	245	245	0	1085: Develop NEPA Documentation CMS PLN	4NOV98	28OCT99
10M045	0	0	0	1085: START DEVELOPMENT OF CMS PLAN	4NOV98	
100225	15	15	0	1085: Develop Alternatives CMS PLN	30DEC98	21JAN99
100550	20	20	0	1085: Inc EPA/NMED Comments RFI RPT	13JAN99	10FEB99
100230	10	10	0	1085: Develop Internal Draft CMS PLN	22JAN99	4FEB99
100235	10	10	0	1085: DOE/LANL/VE Rev Internal Drft CMS PLN	5FEB99	19FEB99
100555	20	20	0	1085: Issue Final RFI RPT	11FEB99	11MAR99
100240	10	10	0	1085: Inc DOE/LANL Comments Int Dft CMS PLN	22FEB99	5MAR99
100245	5	5	0	1085: Issue DOE Draft CMS PLN	8MAR99	12MAR99
10M040	0	0	0	1085: RFI COMPLETED		11MAR99
10M080	0	0	0	1085: EPA NOTIFICATION OF CMS REQUIREMENTS		11MAR99
100250	22	22	0	1085: DOE Review DOE Draft CMS PLN	15MAR99	13APR99
100255	20	20	0	1085: Inc DOE Comments DOE Draft CMS PLN	14APR99	11MAY99
100260	10	10	0	1085: Issue EPA/NMED Draft CMS PLN	12MAY99	25MAY99

ADS 1085: TA-12 14 67      TBS 2/17/92

START DATE 1OCT91 FIN DATE 19MAR01

DATA DATE 1OCT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
10M050	0	0	0	1085: EPA/NMED DRAFT OF CMS PLAN COMPLETED		25MAY99
100265	44	44	0	1085: EPA Review	CMS PLN	26MAY99 28JUL99
100270	44	44	0	1085: NMED Review	CMS PLN	26MAY99 28JUL99
100560	20	20	0	1085: Inc EPA/NMED Comments	CMS PLN	29JUL99 25AUG99
100565	10	10	0	1085: Issue Final	CMS PLN	26AUG99 9SEP99
100570	5	5	0	1085: EPA Approval	CMS PLN	10SEP99 16SEP99
10M085	0	0	0	1085: EPA APPROVED CMS PLAN		16SEP99
100275	245	245	0	1085: CMS Bench/Pilot Studies	(LOE)	17SEP99 11SEP00
100280	30	30	0	1085: Technical Evaluation	CMS RPT	17SEP99 29OCT99
100285	30	30	0	1085: Environmental Evaluation	CMS RPT	17SEP99 29OCT99
100290	30	30	0	1085: Human Health Evaluation	CMS RPT	17SEP99 29OCT99
100295	30	30	0	1085: Community Relations Eval	CMS RPT	17SEP99 29OCT99
100300	30	30	0	1085: Conduct Cost Evaluation	CMS RPT	17SEP99 29OCT99
100465	30	30	0	1085: Develop NEPA Documentation	CMS RPT	17SEP99 29OCT99
10M055	0	0	0	1085: START CMS WORK		17SEP99
10M065	0	0	0	1085: START DEVELOPMENT OF CMS REPORT		17SEP99
100505	249	249	0	1085: Manage ADS FY-00	(LOE)	1OCT99 29SEP00
100305	10	10	0	1085: Prepare Internal Draft	CMS RPT	1NOV99 15NOV99
100310	22	22	0	1085: DOE/LANL/VE Rev Internal Drft	CMS RPT	16NOV99 17DEC99
100315	35	35	0	1085: Inc DOE/LANL Comments Int Dft	CMS RPT	24JUL00 11SEP00
10M060	0	0	0	1085: CMS WORK COMPLETED		11SEP00
100320	10	10	0	1085: Issue DOE Draft	CMS RPT	12SEP00 25SEP00
100325	22	22	0	1085: DOE Review DOE Draft	CMS RPT	26SEP00 26OCT00
100510	108	108	0	1085: Manage ADS FY-01	(LOE)	20CT00 13MAR01
100330	10	10	0	1085: Inc DOE Comments DOE Draft	CMS RPT	27OCT00 9NOV00
100336	10	10	0	1085: Issue EPA/NMED Draft	CMS RPT	13NOV00 28NOV00
10M070	0	0	0	1085: EPA/NMED DRAFT OF CMS REPORT COMPLETED		28NOV00
100340	44	44	0	1085: EPA Review	CMS RPT	29NOV00 2FEB01
100345	44	44	0	1085: NMED Review	CMS RPT	29NOV00 2FEB01
100575	20	20	0	1085: Inc EPA/NMED Comments	CMS RPT	5FEB01 5MAR01

-----

LANL	CLS-1	C. MARTELL	FINEST HOUR	ADS 1085: TA-12 14 67	TBS 2/17/92
REPORT DATE	6AUG92	RUN NO. 101	ENVIRONMENTAL RESTORATION	START DATE 10CT91	FIN DATE 19MAR01
	18:23				
1085 SCHEDULE REPORT BY	EARLY START			DATA DATE 10CT91	PAGE NO. 5

-----

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
100580	10	10	0	1085: Issue Final CMS RPT	6MAR01	19MAR01
10M075	0	0	0	1085: ASSESSMENT COMPLETED		19MAR01

ADS 1100: TA-20 53 72      TBS 2/17/92

START DATE 1OCT91 FIN DATE 6AUG01

DATA DATE 1OCT91 PAGE NO. 1

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
140005	245	245	0	1 512 812	1100:Conduct Voluntary C.Actions for RFI WP(LOE)	10CT92	24SEP93
140010	20	20	0	1 512 1 1	1100: Develop Scope for RFI WP	10CT92	29OCT92
140035	246	246	0	1 512 7	1100: Manage ADS During FY-93 (LOE)	10CT92	27SEP93
14M000	0	0	0	1 512 1	1100: START RFI WORK PLAN	10CT92*	
140025	245	245	0	1 512 113	1100: Develop NEPA Documentation for RFI WP	27OCT92	19OCT93*
140030	40	40	0	1 512 1 2	1100: Locate Existing Data for RFI WP	30OCT92	31DEC92
140040	38	38	0	1 512 1 2	1100: Analyze Existing Data for RFI WP	4JAN93	26FEB93
140050	20	20	0	1 512 1 2	1100: Draft Existing Data Report for RFI WP	1MAR93	26MAR93
140060	40	40	0	1 512 1 3	1100: Determine Data Needs for RFI WP	29MAR93	21MAY93
140065	20	20	0	1 512 1 5	1100: Write Community Relations Plan for RFI WP	29MAR93	23APR93
140070	20	20	0	1 512 1 5	1100: Write Records Management Plan for RFI WP	29MAR93	23APR93
360010	25	25	0	5 12 1	PREPARE DOE DRAFT FOR CLOSURE PLAN	13MAY93*	17JUN93
360015	30	30	0	5 12 1	REVIEW DOE DRAFT FOR CLOSURE PLAN	18JUN93*	30JUL93
360020	22	22	0	5 12 1	PREPARE NMED DRAFT FOR CLOSURE PLAN	2AUG93*	31AUG93
360025	22	22	0	5 12 1	TRANSMIT NMED DRAFT FOR CLOSURE PLAN	1SEP93*	1OCT93
140090	60	60	0	1 512 1 4	1100: Develop Sampling Plan for RFI WP	10SEP93*	7DEC93
140045	244	244	0	1 512 7	1100: Manage ADS During FY-94 (LOE)	10CT93*	22SEP94
140100	20	20	0	1 512 1 5	1100: Write Quality Assurance Plan for RFI WP	8DEC93	7JAN94
140105	20	20	0	1 512 1 5	1100: Write Health & Safety Plan for RFI WP	8DEC93	7JAN94
140110	20	20	0	1 512 1 6	1100: Write Management Plan for RFI WP	8DEC93	7JAN94
140120	20	20	0	1 512 1 7	1100: Develop LANL Internal Draft of RFI WP	10JAN94	7FEB94
140130	20	20	0	1 512 1 7	1100: LANL/VE Rev Internal Draft RFI Work Plan	8FEB94	8MAR94
140140	20	20	0	1 512 1 7	1100:Incorp LANL Rev Comments into Int Dft RFIWP	9MAR94	5APR94
140150	10	10	0	1 512 1 9	1100: Publish DOE Draft of RFI WP	6APR94	19APR94
14M005	0	0	0	1 512 1 9	1100: DOE DRAFT RFI WORK PLAN COMPLETED		19APR94
140155	22	22	0	1 512 1 9	1100: DOE Reviews DOE Draft of RFI WP	20APR94	19MAY94
140160	20	20	0	1 512 1 9	1100:Incorp DOE Rev.Comments into DOE Dft RFI WP	20MAY94	17JUN94
140165	10	10	0	1 512 110	1100: Publish EPA/NMED Draft of RFI Work Plan	20JUN94	1JUL94
14M010	0	0	0	1 512 110	1100: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		1JUL94
140170	44	44	0	1 512 110	1100: NMED Reviews RFI Work Plan	5JUL94	2SEP94

LANL MEE-4 G. GOULD

FINEST HOUR

ADS 1100: TA-20 53 72 TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 112

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 6AUG01

18:27

1100 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
140175	44	44	0	1 512 110	1100: EPA Reviews RFI Work Plan	5JUL94	2SEP94
140530	45	45	0	1 512 210	1100: Write Ph1 Contracts for RFI	6SEP94	8NOV94
140535	20	20	0	1 512 110	1100: Incorporate EPA/NMED Comments for RFI WP	6SEP94	30CT94
140055	246	246	0	1 512 7	1100: Manage ADS During FY-95 (LOE)	30CT94*	28SEP95
140540	10	10	0	1 512 110	1100: Publish Final RFI Work Plan	4OCT94	18OCT94
14M015	0	0	0	1 512 1	1100: RFI WORK PLAN COMPLETED		18OCT94
140180	20	20	0	1 512 2 1	1100: Mobilize for RFI	9NOV94	9DEC94
140525	245	245	0	1 512 825	1100: Assmt - Conduct VCA (LOE)	9NOV94	3NOV95
14M020	0	0	0	1 512 2	1100: START RFI	9NOV94	
140190	245	245	0	1 512 2 2	1100: Conduct RFI PH1 Field Work	12DEC94	6DEC95
140195	245	245	0	1 512 2 4	1100: Conduct RFI PH1 Sample Analysis	12DEC94	6DEC95
140315	100	100	0	1 512 313	1100: Develop NEPA Documentation for RFI Report	12DEC94	8MAY95
140200	245	245	0	1 512 2 5	1100: Conduct RFI PH1 Data Assessment	13FEB95	6FEB96
14M030	0	0	0	1 512 3	1100: START DEVELOPING RFI REPORT	6MAR95	
140075	245	245	0	1 512 7	1100: Manage ADS During FY-96 (LOE)	20CT95*	24SEP96
140210	20	20	0	1 512 2 1	1100: Demobilize RFI PH1 Field Work	7DEC95	8JAN96
140205	60	60	0	1 512 2 6	1100: Write RFI PH1 Tech Memo/WP Modification	7FEB96	1MAY96
14M090	0	0	0	1 512 2	1100: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		1MAY96
140215	22	22	0	1 512 2 6	1100: EPA/NMED Rev PH1 Tech Memo/WP Modification	2MAY96	3JUN96
140220	22	22	0	1 512 2 6	1100: DOE Reviews PH1 Tech Memo/WP Modification	2MAY96	3JUN96
140225	20	20	0	1 512 2 7	1100: Write PH2 Contract; Mobilize for RFI	2MAY96	30MAY96
140230	245	245	0	1 512 2 8	1100: Conduct RFI PH2 Field Work	31MAY96	23MAY97
140235	245	245	0	1 512 210	1100: Conduct RFI PH2 Sample Analysis	1AUG96	25JUL97
140245	245	245	0	1 512 211	1100: Conduct RFI PH2 Data Assessment	1AUG96	25JUL97
140085	245	245	0	1 512 7	1100: Manage ADS During FY-97 (LOE)	1OCT96*	24SEP97
590000	189	189	0	1 619 8	2206: Remed - Conduct VCA (LOE)	2JAN97*	30SEP97
140240	20	20	0	1 512 2 7	1100: Demoblize RFI PH2 Field Work	27MAY97	23JUN97
14M025	0	0	0	1 512 2	1100: RFI FIELD WORK COMPLETED		23JUN97
140305	100	100	0	1 512 3 1	1100: Prepare RFI Report Facility Investigation	28JUL97	19DEC97
140310	110	110	0	1 512 3 2	1100: Prepare RFI Report Investigation Analysis	28JUL97	7JAN98

ADS 1100: TA-20 53 72      TBS 2/17/92

START DATE 10OCT91 FIN DATE 6AUG01

DATA DATE 10OCT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
140095	245	245	0	1 512 7	1100: Manage ADS During FY-98 (LOE)	10CT97*	24SEP98
590005	245	245	0	1 619 8	2206: Remed - Conduct VCA (LOE)	10CT97	24SEP98
140325	132	132	0	1 512 3 8	1100: Prepare Internal Draft of RFI Report	8JAN98	16JUL98
140330	20	20	0	1 512 3 4	1100: LANL/VE Review Internal Draft of RFI Rpt	17JUL98	13AUG98
140335	40	40	0	1 512 3 4	1100: Incorporate LANL Rev. Comments Internal Draft of RFI Rpt	14AUG98	9OCT98
140115	246	246	0	1 512 7	1100: Manage ADS During FY-99 (LOE)	10CT98*	27SEP99
140340	20	20	0	1 512 3 5	1100: Publish DOE Draft of RFI Report	13OCT98	10NOV98
140345	22	22	0	1 512 3 6	1100: Prepare Review of DOE Draft of RFI Report	11NOV98	14DEC98
140350	40	40	0	1 512 3 6	1100: Incorporate DOE Rev. Comments DOE Draft of RFI Rpt	15DEC98	12FEB99
140355	20	20	0	1 512 3 7	1100: Publish EPA/NMED Draft of RFI Report	16FEB99	15MAR99
14M035	0	0	0	1 512 3 7	1100: EPA/NMED DRAFT OF RFI REPORT COMPLETED		15MAR99
140360	44	44	0	1 512 3 7	1100: EPA Reviews of RFI Report	16MAR99	14MAY99
140365	44	44	0	1 512 3 7	1100: NMED Reviews of RFI Report	16MAR99	14MAY99
140370	245	245	0	1 512 4 5	1100: Conduct Bench/Pilot Studies for CMS Plan (LOE)	16MAR99	8MAR00
140375	35	35	0	1 512 4 1	1100: Establish Current Situation for CMS Plan	16MAR99	3MAY99
140380	35	35	0	1 512 4 2	1100: Establish CA Objectives for CMS Plan	16MAR99	3MAY99
140385	35	35	0	1 512 4 3	1100: Screen Technologies for CMS Plan	16MAR99	3MAY99
140390	245	245	0	1 512 413	1100: Develop NEPA Documentation for CMS Plan	16MAR99	8MAR00
14M045	0	0	0	1 512 4	1100: START DEVELOPMENT OF CMS PLAN	16MAR99	
140395	15	15	0	1 512 4 4	1100: Develop Alternatives for CMS Plan	4MAY99	24MAY99
140560	20	20	0	1 512 3 7	1100: Incorporate EPA/NMED Comments on RFI Rpt	17MAY99	14JUN99
140400	10	10	0	1 512 4 6	1100: Develop Internal Draft of CMS Plan	25MAY99	8JUN99
140405	10	10	0	1 512 4 6	1100: LANL/VE Review Internal Draft of CMS Plan	9JUN99	22JUN99
140565	20	20	0	1 512 3 9	1100: Publish Final RFI Report	15JUN99	13JUL99
140410	10	10	0	1 512 4 6	1100: Incorporate LANL REV Comments Internal Draft of CMS Plan	23JUN99	7JUL99
140415	5	5	0	1 512 4 8	1100: Publish DOE Draft of CMS Plan	8JUL99	14JUL99
14M040	0	0	0	1 512 2	1100: RFI COMPLETED		13JUL99
14M080	0	0	0	1 512 6	1100: EPA NOTIFICATION OF CMS REQUIREMENTS		13JUL99
140420	22	22	0	1 512 4 8	1100: Review Draft of CMS Plan	15JUL99	13AUG99
140425	20	20	0	1 512 4 8	1100: Incorporate DOE Rev. Comments DOE Draft of CMS Plan	16AUG99	13SEP99



ADS 1100: TA-20 53 72      TBS 2/17/92

START DATE 1OCT91 FIN DATE 6AUG01

DATA DATE 1OCT91 PAGE NO. 4


ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
140430	10	10	0	1 512 4 9	1100: Publish EPA/NMED Draft of CMS Plan	14SEP99	27SEP99
14M050	0	0	0	1 512 4 9	1100: EPA/NMED DRAFT OF CMS PLAN COMPLETED		27SEP99
140435	44	44	0	1 512 4 9	1100: EPA Review of CMS Plan	28SEP99	2DEC99
140440	44	44	0	1 512 4 9	1100: NMED Review of CMS Plan	28SEP99	2DEC99
140125	245	245	0	1 512 7	1100: Manage ADS During FY-00 (LOE)	10CT99*	25SEP00
140570	20	20	0	1 512 4 9	1100: Incorporate EPA/NMED Comments on CMS Plan	30DEC99	4JAN00
140575	10	10	0	1 512 4 9	1100: Publish Final CMS Plan	5JAN00	19JAN00
140580	5	5	0	1 512 4 9	1100: EPA Approves CMS Plan	20JAN00	26JAN00
14M085	0	0	0	1 512 4	1100: EPA APPROVED CMS PLAN		26JAN00
140445	245	245	0	1 512 5 1	1100: Conduct CMS Bench/Pilot Studies (LOE)	27JAN00	19JAN01
140450	30	30	0	1 512 6 1	1100: Conduct Technical Evaluation for CMS Report	27JAN00	9MAR00
140455	30	30	0	1 512 6 2	1100: Cond Envir Evaluation for CMS Report	27JAN00	9MAR00
140460	30	30	0	1 512 6 3	1100: Conduct Human Health Eval for CMS Report	27JAN00	9MAR00
140465	30	30	0	1 512 6 4	1100: Cond Comm Relations Eval. for CMS Report	27JAN00	9MAR00
140470	30	30	0	1 512 6 5	1100: Conduct Cost Evaluation for CMS Report	27JAN00	9MAR00
140475	30	30	0	1 512 613	1100: Develop NEPA Documentation for CMS Report	27JAN00	9MAR00
14M055	0	0	0	1 512 5	1100: START CMS WORK	27JAN00	
14M065	0	0	0	1 512 6	1100: START DEVELOPMENT OF CMS REPORT	27JAN00	
140480	10	10	0	1 512 610	1100: Prepare Internal Draft of CMS Report	10MAR00	23MAR00
140485	10	10	0	1 512 6 6	1100: LANL/VE Review Internal Draft of CMS Rpt	24MAR00	6APR00
140135	120	120	0	1 512 7	1100: Manage ADS During FY-01 (LOE)	20CT00*	29MAR01
140490	35	35	0	1 512 6 6	1100: Incorp. LANL Rev Comments Intern. Dft CMS Rpt	28NOV00	19JAN01
14M060	0	0	0	1 512 5	1100: CMS WORK COMPLETED		19JAN01
140495	10	10	0	1 512 6 8	1100: Publish DOE Draft of CMS Report	22JAN01	2FEB01
140500	22	22	0	1 512 6 8	1100: Conduct Review of DOE Draft of CMS Report	5FEB01	7MAR01
140505	22	22	0	1 512 6 8	1100: Incorp. DOE Rev Comments DOE Dft CMS Report	8MAR01	6APR01
140510	10	10	0	1 512 6 9	1100: Publish EPA/NMED Draft of CMS Report	9APR01	20APR01
14M070	0	0	0	1 512 6	1100: EPA/NMED DRAFT OF CMS REPORT COMPLETED		20APR01
140515	44	44	0	1 512 6 9	1100: EPA Reviews CMS Report	23APR01	22JUN01
140520	44	44	0	1 512 6 9	1100: NMED Reviews CMS Report	23APR01	22JUN01

ADS 1100: TA-20 53 72      TBS 2/17/92

START DATE 1OCT91 FIN DATE 6AUG01

DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	SCHEDULED	
						START	FINISH
140585	20	20	0	1 512 6 9	1100: Incorporate EPA/NMED Comments on CMS Rpt	25JUN01	23JUL01
140590	10	10	0	1 512 6 9	1100: Publish Final CMS Report	24JUL01	6AUG01
14M075	0	0	0	1 512 8	1100: ASSESSMENT COMPLETED		6AUG01

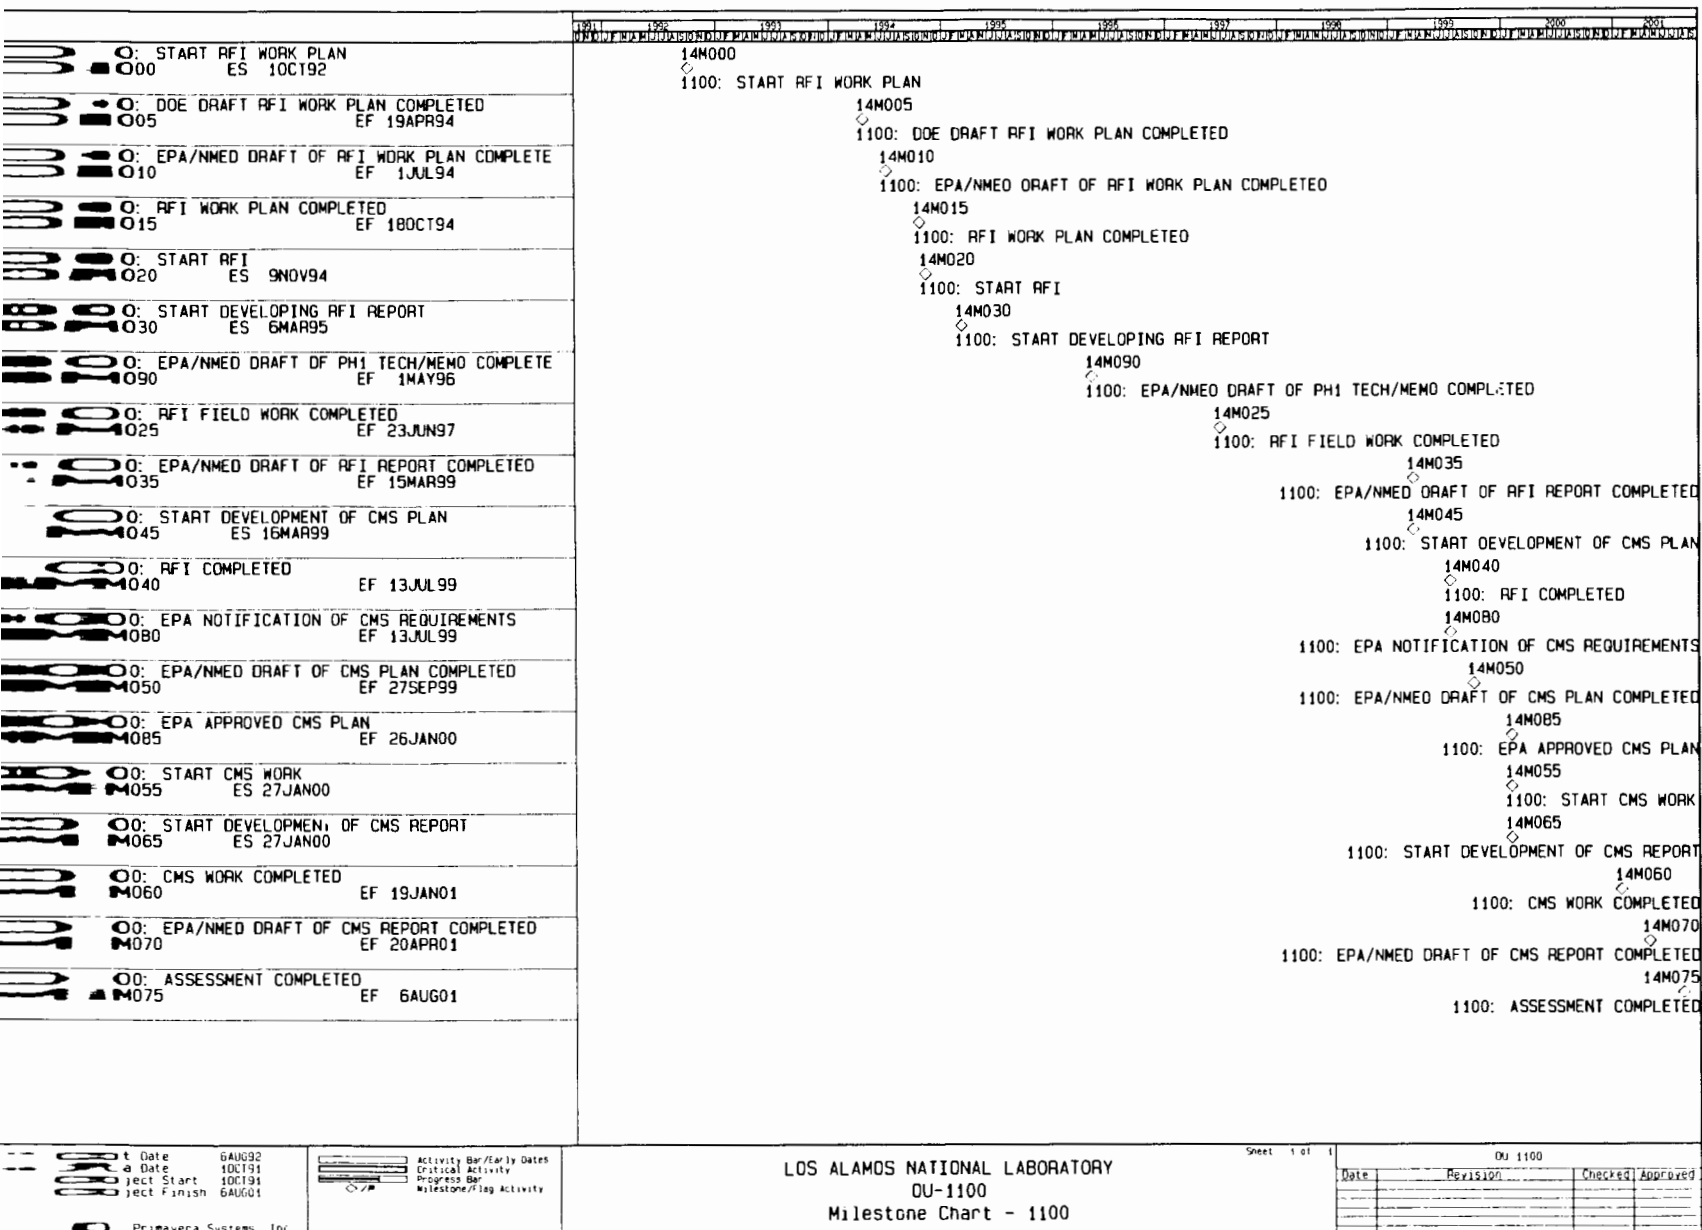

TBS 2/17/92

START DATE 1OCT91 FIN DATE 27AUG01

DATA DATE 10OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
240000	249	249	0	1136:Conduct Bench/Pilot Studies for RFI WP(LOE)	10CT92	30SEP93
240005	249	249	0	1136:Conduct Voluntary C.Actions for RFI WP(LOE)	10CT92	30SEP93
240010	20	20	0	1136: Develop Scope for RFI WP	10CT92	29OCT92
240020	249	249	0	1136: Develop NEPA Documentation for RFI WP	10CT92	30SEP93
240025	44	44	0	1136: Locate Existing Data for RFI WP	10CT92	7DEC92
240030	249	249	0	1136: Manage ADS During FY-93 (LOE)	10CT92	30SEP93
24M000	0	0	0	1136: START RFI WORK PLAN	10CT92*	
240035	38	38	0	1136: Analyze Existing Data for RFI WP	8DEC92	3FEB93
240045	20	20	0	1136: Draft Existing Data Report for RFI WP	4FEB93	4MAR93
240055	40	40	0	1136: Determine Data Needs for RFI WP	5MAR93	29APR93
240075	40	40	0	1136: Develop Data Quality Objectives for RFI WP	30APR93	25JUN93
240085	80	80	0	1136: Develop Sampling Plan for RFI WP	18AUG93	13DEC93
240040	250	250	0	1136: Manage ADS During FY-94 (LOE)	10CT93	30SEP94
240180	250	250	0	1136: Conduct RFI Bench/Pilot Studies (LOE)	10CT93	30SEP94
240060	20	20	0	1136: Write Community Relations Plan for RFI WP	18NOV93	17DEC93
240065	20	20	0	1136: Write Records Management Plan for RFI WP	18NOV93	17DEC93
240095	20	20	0	1136: Write Quality Assurance Plan for RFI WP	18NOV93	17DEC93
240100	20	20	0	1136: Write Health & Safety Plan for RFI WP	18NOV93	17DEC93
240105	20	20	0	1136: Write Management Plan for RFI WP	18NOV93	17DEC93
240115	20	20	0	1136: Develop LANL Internal Draft of RFI WP	6DEC93	5JAN94
240125	20	20	0	1136: LANL/VE Review Internal Draft RFI Work Pl	6JAN94	3FEB94
240135	20	20	0	1136:Incorp LANL Rev Comments into Int Dft RFIWP	4FEB94	4MAR94
240145	10	10	0	1136: Publish DOE Draft of RFI WP	7MAR94	18MAR94
24M005	0	0	0	1136: DOE DRAFT RFI WORK PLAN COMPLETED		18MAR94
240150	22	22	0	1136: Cond DOE Review of DOE Draft of RFI WP	21MAR94	19APR94
240155	20	20	0	1136:Incorp DOE Rev.Comments into DOE Dft RFI WP	20APR94	17MAY94
240160	10	10	0	1136: Publish EPA/NMED Draft of RFI Work Plan	16MAY94	27MAY94
24M010	0	0	0	1136: EPA/NMED DRAFT OF RFI WORK PLAN COMPLETED		27MAY94
240165	44	44	0	1136: Conduct NMED Review of RFI WP	31MAY94	1AUG94
240170	44	44	0	1136: Conduct EPA Review of RFI Work Plan	31MAY94	1AUG94

TBS 2/17/92

START DATE 1OCT91 FIN DATE 27AUG01

DATA DATE 1OCT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
240520	45	45	0	1136: Write PH1 Contracts for RFI	2AUG94	4OCT94
240525	20	20	0	1136: Incorporate EPA/NMED Comments for RFI WP	2AUG94	29AUG94
240530	10	10	0	1136: Publish Final RFI WP	30AUG94	13SEP94
24M015	0	0	0	1136: RFI WORK PLAN COMPLETED		13SEP94
240050	247	247	0	1136: Manage ADS During FY-95 (LOE)	30CT94	29SEP95
240175	20	20	0	1136: Mobilize for RFI	5OCT94	2NOV94
24M020	0	0	0	1136: START RFI	5OCT94	
240185	245	245	0	1136: Conduct RFI PH1 Field Work	3NOV94	30OCT95
240190	245	245	0	1136: Conduct RFI PH1 Sample Analysis	3NOV94	30OCT95
240195	245	245	0	1136: Conduct RFI PH1 Data Assessment	3NOV94	30OCT95
240310	100	100	0	1136: Develop NEPA Documentation for RFI Report	3NOV94	4APR95
24M030	0	0	0	1136: START DEVELOPING RFI REPORT	3NOV94	
240070	249	249	0	1136: Manage ADS During FY-96 (LOE)	20CT95	30SEP96
240585	249	249	0	1136: Assmt - Conduct VCA (LOE)	20CT95*	30SEP96
240200	60	60	0	1136: Write RFI PH1 Tech Memo/WP Modification	31OCT95	31JAN96
240205	20	20	0	1136: Demobilize RFI PH1 Field Work	31OCT95	30NOV95
24M095	0	0	0	1136: EPA/NMED DRAFT OF PH1 TECH/MEMO COMPLETED		31JAN96
240210	22	22	0	1136: EPA/NMED Rev PH1 Tech Memo/WP Modification	1FEB96	4MAR96
240215	22	22	0	1136: DOE Review PH1 Tech Memo/WP Modification	1FEB96	4MAR96
240220	20	20	0	1136: Write PH2 Contract & Mobilize for RFI	5MAR96	1APR96
240225	245	245	0	1136: Conduct RFI PH2 Field Work	2APR96	26MAR97
240230	245	245	0	1136: Conduct RFI PH2 Sample Analysis	2APR96	26MAR97
240240	245	245	0	1136: Conduct RFI PH2 Data Assessment	2APR96	26MAR97
240080	249	249	0	1136: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
670000	189	189	0	2211: Remed - Conduct VCA (LOE)	2JAN97*	30SEP97
240235	20	20	0	1136: Demoblize RFI PH2 Field Work	27MAR97	23APR97
240300	100	100	0	1136: Conduct RFI Report Facility Investigation	27MAR97	15AUG97
240305	110	110	0	1136: Conduct RFI Report Investigation Analysis	27MAR97	29AUG97
24M025	0	0	0	1136: RFI FIELD WORK COMPLETED		23APR97
240320	132	132	0	1136: Prepare Internal Draft of RFI Report	2SEP97	17MAR98

LANL CLS-7 G. ALLEN

FINEST HOUR

ADS 1136: TA-46

TBS 2/17/92

REPORT DATE 6AUG92 RUN NO. 19

ENVIRONMENTAL RESTORATION

START DATE 10CT91 FIN DATE 27AUG01

18:33

1136 SCHEDULE REPORT BY EARLY START

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
240090	249	249	0	1136: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
670005	249	249	0	2211: Remed - Conduct VCA (LOE)	10CT97	30SEP98
240325	20	20	0	1136: LANL/VE Rev Internal Draft of RFI Report	18MAR98	14APR98
240330	40	40	0	1136: Incorp.LANL Rev.Comments Int Dft RFI Rpt	15APR98	10JUN98
240335	20	20	0	1136: Publish DOE Draft of RFI Report	11JUN98	9JUL98
240340	22	22	0	1136: Conduct Review of DOE Draft of RFI Report	10JUL98	10AUG98
240345	40	40	0	1136: Incorp. DOE Rev. Comments DOE Drft RFI Rpt	11AUG98	6OCT98
240110	249	249	0	1136: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
240350	20	20	0	1136: Publish EPA/NMED Draft of RFI Report	7OCT98	4NOV98
24M035	0	0	0	1136: EPA/NMED DRAFT OF RFI REPORT COMPLETED		4NOV98
240355	44	44	0	1136: Conduct EPA Review of RFI Report	5NOV98	13JAN99
240360	44	44	0	1136: Conduct NMED Review of RFI Report	5NOV98	13JAN99
240370	35	35	0	1136: Establish Current Situation for CMS Plan	5NOV98	30DEC98
240375	35	35	0	1136: Establish CA Objectives for CMS Plan	5NOV98	30DEC98
240380	35	35	0	1136: Dev Screening Technologies for CMS Plan	5NOV98	30DEC98
240385	245	245	0	1136: Develop NEPA Documentation for CMS Plan	5NOV98	29OCT99
24M045	0	0	0	1136: START DEVELOPMENT OF CMS PLAN	5NOV98	
240390	15	15	0	1136: Develop Alternatives for CMS Plan	31DEC98	22JAN99
240550	20	20	0	1136: Incorporate EPA/NMED Comments for RFI Rpt	14JAN99	11FEB99
240395	10	10	0	1136: Develop Internal Draft of CMS Plan	25JAN99	5FEB99
240400	10	10	0	1136: LANL/VE Review Internal Draft of CMS Plan	8FEB99	22FEB99
240555	20	20	0	1136: Publish Final RFI Report	12FEB99	12MAR99
240405	10	10	0	1136:Incorp. LANL REV Comments Intern Dft CMS PL	23FEB99	8MAR99
240410	5	5	0	1136: Publish DOE Draft of CMS Plan	9MAR99	15MAR99
24M040	0	0	0	1136: RFI COMPLETED		12MAR99
24M085	0	0	0	1136: EPA NOTIFICATION OF CMS REQUIREMENT		12MAR99
240415	22	22	0	1136: Conduct Review of DOE Draft of CMS Plan	16MAR99	14APR99
240420	20	20	0	1136:Incorp. DOE Rev.Comments DOE Dft.of CMS PL	15APR99	12MAY99
240425	10	10	0	1136: Publish EPA/NMED Draft of CMS Plan	13MAY99	26MAY99
24M050	0	0	0	1136: EPA/NMED DRAFT OF CMS PLAN COMPLETED		26MAY99

LANL CLS-7 G. ALLEN  
 REPORT DATE 6AUG92 RUN NO. 19  
 18:33  
 1136 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

ADS 1136: TA-46  
 START DATE 1OCT91  
 DATA DATE 1OCT91

TBS 2/17/92  
 FIN DATE 27AUG01  
 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
240430	44	44	0	1136: Conduct EPA Review of CMS Plan	27MAY99	29JUL99
240435	44	44	0	1136: Conduct NMED Review of CMS Plan	27MAY99	29JUL99
240560	20	20	0	1136: Incorporate EPA/NMED Comments on CMS Plan	30JUL99	26AUG99
240565	10	10	0	1136: Publish Final CMS Plan	27AUG99	10SEP99
240570	5	5	0	1136: EPA Approves CMS Plan	13SEP99	17SEP99
24M090	0	0	0	1136: EPA APPROVED CMS PLAN		17SEP99
240440	245	245	0	1136: Conduct CMS Bench/Pilot Studies (LOE)	20SEP99	12SEP00
24M055	0	0	0	1136: START CMS WORK	20SEP99	
24M065	0	0	0	1136: START DEVELOPMENT OF CMS REPORT	20SEP99	
240120	248	248	0	1136: Manage ADS During FY-00 (LOE)	1OCT99	28SEP00
240365	248	248	0	1136:Cond Bench/Pilot Studies for CMS Plan (LOE)	1OCT99*	28SEP00
240445	30	30	0	1136:Conduct Technical Evaluation for CMS Report	13SEP00	25OCT00
240450	30	30	0	1136: Cond Envir Evaluation for CMS Report	13SEP00	25OCT00
240455	30	30	0	1136: Conduct Human Health Eval for CMS Report	13SEP00	25OCT00
240460	30	30	0	1136: Cond Comm Relations Eval.for CMS Report	13SEP00	25OCT00
240465	30	30	0	1136: Conduct Cost Evaluation for CMS Report	13SEP00	25OCT00
240470	30	30	0	1136: Develop NEPA Documentation for CMS Report	13SEP00	25OCT00
24M060	0	0	0	1136: CMS WORK COMPLETED		28SEP00
240130	226	226	0	1136: Manage ADS During FY-01 (LOE)	29SEP00	27AUG01
240475	10	10	0	1136: Prepare Internal Draft of CMS Report	26OCT00	8NOV00
240480	22	22	0	1136: LANL/VE Review Internal Draft of CMS Rpt	9NOV00	13DEC00
240485	35	35	0	1136:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	14DEC00	6FEB01
240490	10	10	0	1136: Publish DOE Draft of CMS Report	7FEB01	21FEB01
240495	22	22	0	1136: Conduct Review of DOE Draft of CMS Report	22FEB01	23MAR01
240500	10	10	0	1136:Incorp. DOE Rev Comments DOE Dft CMS Report	26MAR01	6APR01
240505	10	10	0	1136: Publish EPA/NMED Draft of CMS Report	9APR01	20APR01
24M070	0	0	0	1136: EPA/NMED DRAFT OF CMS REPORT COMPLETED		20APR01
240510	44	44	0	1136: Conduct EPA Review of CMS Report	23APR01	22JUN01
240515	44	44	0	1136: Conduct NMED Review of CMS Report	23APR01	22JUN01
240575	20	20	0	1136: Incorporate EPA/NMED Comments on CMS Rpt	25JUN01	23JUL01


TBS 2/17/92

START DATE 1OCT91 FIN DATE 27AUG01

DATA DATE 10OCT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
240580	10	10	0	1136: Publish Final CMS Report	24JUL01	6AUG01
24M075	0	0	0	1136: ASSESSMENT COMPLETED		6AUG01



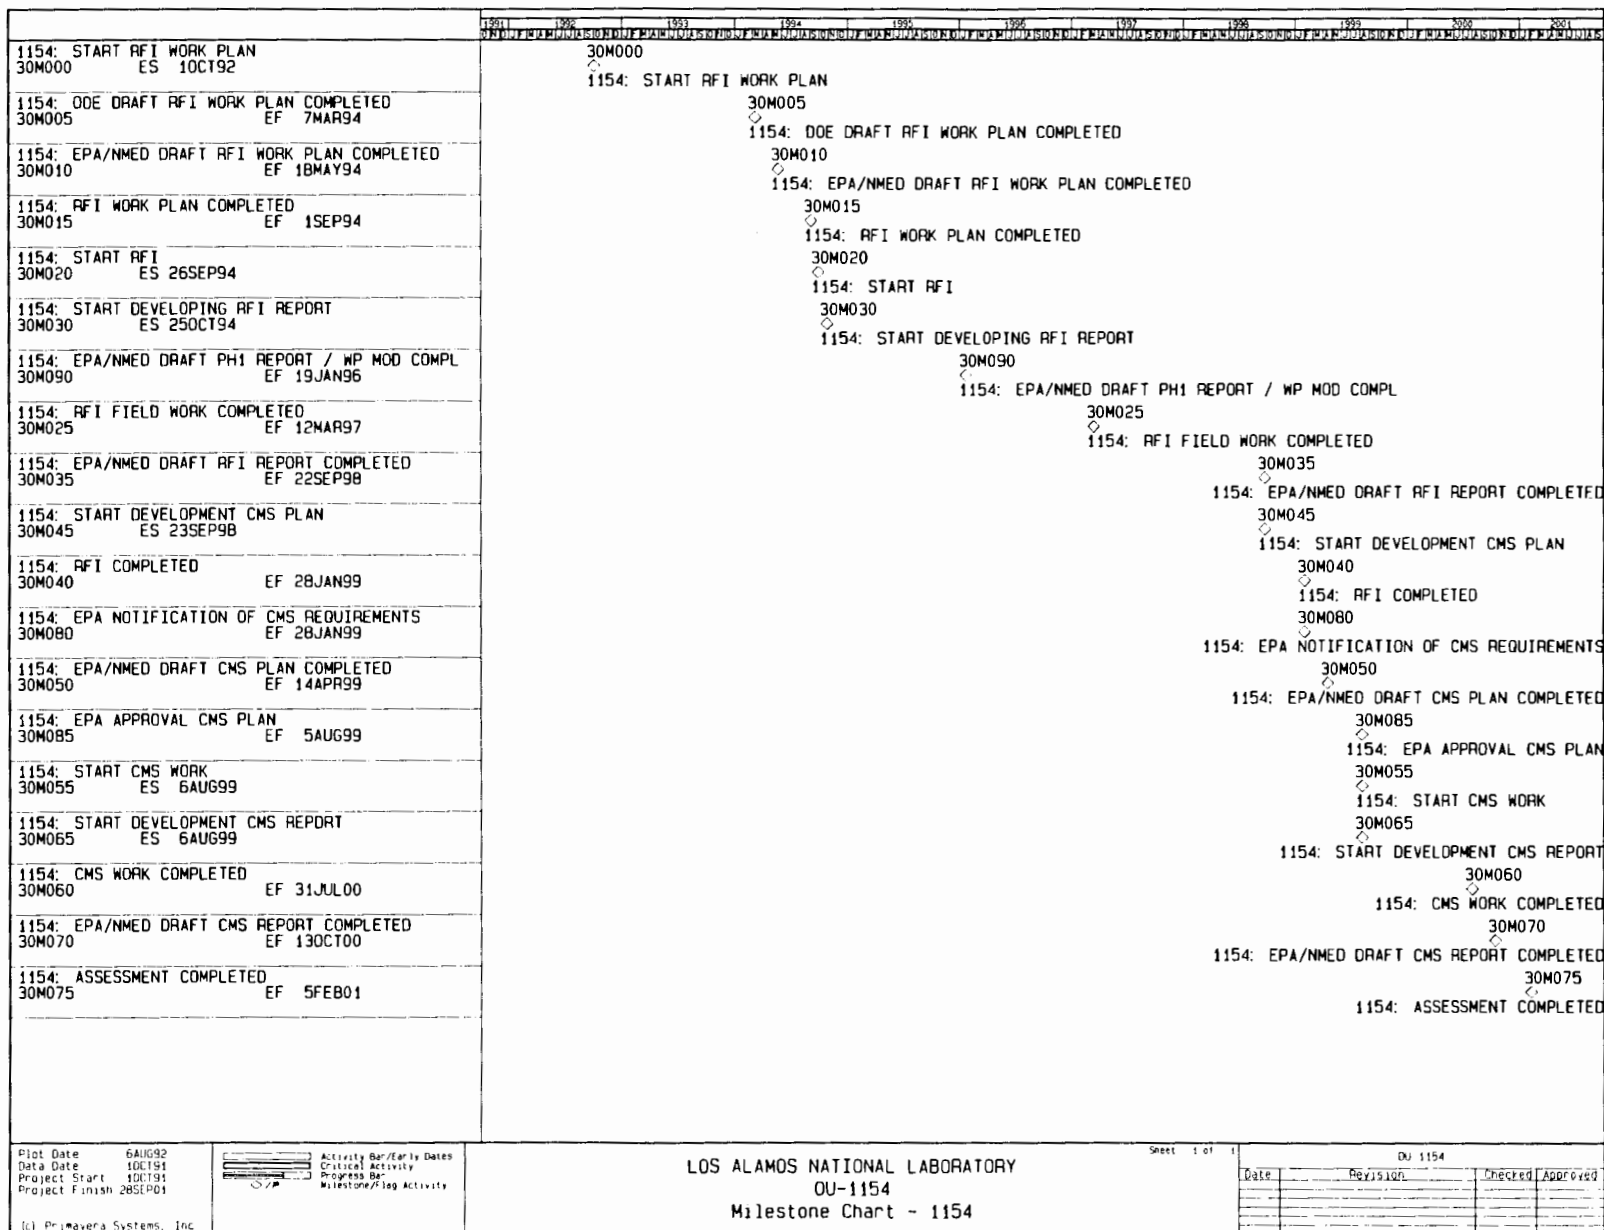

TBS 2/17/92

START DATE 1OCT91 FIN DATE 28SEP01

DATA DATE 10OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
300000	249	249	0	1154: Bench/Pilot Studies RFI WP(LOE)	10CT92	30SEP93
300005	249	249	0	1154: Voluntary Corrective Actions RFI WP(LOE)	10CT92	30SEP93
300030	249	249	0	1154: Manage ADS FY-93 (LOE)	10CT92	30SEP93
600884	249	249	0	1154: Conduct VCA - Assessment FY-93	10CT92*	30SEP93
600886	249	249	0	1154: Conduct VCA - Remediation FY-93	10CT92	30SEP93
30M000	0	0	0	1154: START RFI WORK PLAN	10CT92*	
300010	20	20	0	1154: Develop Scope RFI WP	70CT92*	4NOV92
300020	249	249	0	1154: Develop NEPA Documentation RFI WP	5NOV92	4NOV93
300025	40	40	0	1154: Locate Existing Data RFI WP	5NOV92	7JAN93
300035	38	38	0	1154: Analyze Existing Data RFI WP	8JAN93	4MAR93
300045	20	20	0	1154: Draft Existing Data Report RFI WP	5MAR93	1APR93
300055	40	40	0	1154: Determine Data Needs RFI WP	2APR93	27MAY93
300060	20	20	0	1154: Write Commun Relations Plan RFI WP	2APR93	29APR93
300065	20	20	0	1154: Write Records Mngt Plan RFI WP	2APR93	29APR93
300085	60	60	0	1154: Develop Sampling Plan RFI WP	27JUL93	20OCT93
300040	250	250	0	1154: Manage ADS FY-94 (LOE)	10CT93	30CT94
600888	250	250	0	1154: Conduct VCA - Assessment FY-94	10CT93	30CT94
600890	250	250	0	1154: Conduct VCA - Remediation FY-94	10CT93	30CT94
300095	20	20	0	1154: Write Quality Assurance Plan RFI WP	21OCT93	18NOV93
300100	20	20	0	1154: Write Health & Safety Plan RFI WP	21OCT93	18NOV93
300105	20	20	0	1154: Write Management Plan RFI WP	21OCT93	18NOV93
300115	20	20	0	1154: Develop LANL Internal Draft RFI WP	19NOV93	20DEC93
300125	20	20	0	1154: DOE/LANL/VE Rev Internal Drft RFI WP	21DEC93	21JAN94
300135	20	20	0	1154: Inc DOE/LANL Comment Intn Dft RFI WP	24JAN94	18FEB94
300145	10	10	0	1154: Issue DOE Draft RFI WP	22FEB94	7MAR94
30M005	0	0	0	1154: DOE DRAFT RFI WORK PLAN COMPLETED		7MAR94
300150	22	22	0	1154: DOE Review DOE Draft RFI WP	8MAR94	6APR94
300155	20	20	0	1154: Inc DOE Comments DOE Draft RFI WP	7APR94	4MAY94
300160	10	10	0	1154: Issue EPA/NMED Draft RFI WP	5MAY94	18MAY94
30M010	0	0	0	1154: EPA/NMED DRAFT RFI WORK PLAN COMPLETED		18MAY94

TBS 2/17/92

START DATE 1OCT91 FIN DATE 28SEP01

DATA DATE 10CT91 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
300165	44	44	0	1154: NMED Review	RFI WP	19MAY94	21JUL94
300170	44	44	0	1154: EPA Review	RFI WP	19MAY94	21JUL94
300525	45	45	0	1154: Write Contracts and Mobilize	RFI PH1	22JUL94	23SEP94
300530	20	20	0	1154: Inc EPA/NMED Comments	RFI WP	22JUL94	18AUG94
300535	10	10	0	1154: Issue Final	RFI WP	19AUG94	1SEP94
30M015	0	0	0	1154: RFI WORK PLAN COMPLETED			1SEP94
300175	20	20	0	1154: Mobilize for RFI		26SEP94	24OCT94
30M020	0	0	0	1154: START RFI		26SEP94	
300180	247	247	0	1154: RFI Bench/Pilot Studies	(LOE)	30CT94*	28SEP95
300050	247	247	0	1154: Manage ADS FY-95	(LOE)	40CT94	29SEP95
600892	247	247	0	1154: Conduct VCA - Assessment FY-95		40CT94	29SEP95
600894	247	247	0	1154: Conduct VCA - Remediation FY-95		40CT94	29SEP95
300185	245	245	0	1154: Field Work	RFI PH1	25OCT94	18OCT95
300190	245	245	0	1154: Sample Analysis	RFI PH1	25OCT94	18OCT95
300195	245	245	0	1154: Data Assessment	RFI PH1	25OCT94	18OCT95
300310	100	100	0	1154: Develop NEPA Documentation	RFI RPT	25OCT94	23MAR95
30M030	0	0	0	1154: START DEVELOPING RFI REPORT		25OCT94	
300070	249	249	0	1154: Manage ADS FY-96	(LOE)	20CT95	30SEP96
600896	249	249	0	1154: Conduct VCA - Assessment FY-96		20CT95	30SEP96
600898	249	249	0	1154: Conduct VCA - Remediation FY-96		20CT95	30SEP96
300200	60	60	0	1154: Write Report / WP Mod	RFI PH1	19OCT95	19JAN96
300205	20	20	0	1154: Demobilize Field Work	RFI PH1	19OCT95	16NOV95
30M090	0	0	0	1154: EPA/NMED DRAFT PH1 REPORT / WP MOD COMPL			19JAN96
300210	22	22	0	1154: EPA/NMED Review RPT / WP Mod	RFI PH1	22JAN96	21FEB96
300215	22	22	0	1154: DOE Review Report / WP Mod	RFI PH1	22JAN96	21FEB96
300220	20	20	0	1154: Write Contracts and Mobilize	RFI PH2	22JAN96	16FEB96
300225	245	245	0	1154: Field Work	RFI PH2	20FEB96	11FEB97
300230	245	245	0	1154: Sample Analysis	RFI PH2	20FEB96	11FEB97
300240	245	245	0	1154: Data Assessment	RFI PH2	20FEB96	11FEB97
300080	249	249	0	1154: Manage ADS FY-97	(LOE)	10CT96	30SEP97

TBS 2/17/92

START DATE 1OCT91 FIN DATE 28SEP01

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
600900	249	249	0	1154: Conduct VCA - Assessment FY-97	10CT96	30SEP97
600902	249	249	0	1154: Conduct VCA - Remediation FY-97	10CT96	30SEP97
720000	189	189	0	2213: Conduct VCA - Remediation (LOE)	2JAN97*	30SEP97
300235	20	20	0	1154: Demoblize Field Work RFI PH2	12FEB97	12MAR97
300300	100	100	0	1154: Facility Investigation RFI RPT	12FEB97	3JUL97
300305	110	110	0	1154: Investigation Analysis RFI RPT	12FEB97	18JUL97
30M025	0	0	0	1154: RFI FIELD WORK COMPLETED		12MAR97
300320	132	132	0	1154: Prepare Internal Draft RFI RPT	21JUL97	2FEB98
300090	249	249	0	1154: Manage ADS FY-98 (LOE)	10CT97	30SEP98
600904	249	249	0	1154: Conduct VCA - Assessment FY-98	10CT97	30SEP98
600906	249	249	0	1154: Conduct VCA - Remediation FY-98	10CT97	30SEP98
720005	245	245	0	2213: Conduct VCA - Remediation (LOE)	10CT97	24SEP98
300325	20	20	0	1154: DOE/LANL/VE Rev Internal Dft RFI RPT	3FEB98	3MAR98
300330	40	40	0	1154: Inc DOE/LANL Comment Int Dft RFI RPT	4MAR98	28APR98
300335	20	20	0	1154: Issue DOE Draft RFI RPT	29APR98	27MAY98
300340	22	22	0	1154: DOE Review DOE Draft RFI RPT	28MAY98	26JUN98
300345	40	40	0	1154: Inc DOE Comments DOE Drft RFI RPT	29JUN98	24AUG98
300350	20	20	0	1154: Issue EPA/NMED Draft RFI RPT	25AUG98	22SEP98
30M035	0	0	0	1154: EPA/NMED DRAFT RFI REPORT COMPLETED		22SEP98
300355	44	44	0	1154: EPA Review RFI RPT	23SEP98	25NOV98
300360	44	44	0	1154: NMED Review RFI RPT	23SEP98	25NOV98
300365	245	245	0	1154: Cond Bench/Pilot Studies CMS PLN(LOF)	23SEP98	16SEP99
300370	35	35	0	1154: Establish Current Situation CMS PLN	23SEP98	12NOV98
300375	35	35	0	1154: Establish CA Objectives CMS PLN	23SEP98	12NOV98
300380	35	35	0	1154: Dev Screening Technologies CMS PLN	23SEP98	12NOV98
300385	245	245	0	1154: Develop NEPA Documentation CMS PLN	23SEP98	16SEP99
30M045	0	0	0	1154: START DEVELOPMENT CMS PLAN	23SEP98	
300110	249	249	0	1154: Manage ADS FY-99 (LOE)	10CT98	30SEP99
600908	249	249	0	1154: Conduct VCA - Assessment FY-99	10CT98	30SEP99
600910	249	249	0	1154: Conduct VCA - Remediation FY-99	10CT98	30SEP99

TBS 2/17/92

START DATE 1OCT91 FIN DATE 28SEP01


DATA DATE 1OCT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION		SCHEDULED START	FINISH
300390	15	15	0	1154: Develop Alternatives	CMS PLN	13NOV98	7DEC98
300555	20	20	0	1154: Inc EPA/NMED Comments	RFI RPT	30NOV98	29DEC98
300395	10	10	0	1154: Develop Internal Draft	CMS PLN	8DEC98	21DEC98
300400	10	10	0	1154: DOE/LANL/VE Rev Internal Dft	CMS PLN	22DEC98	7JAN99
300560	20	20	0	1154: Issue Final	RFI RPT	30DEC98	28JAN99
300405	10	10	0	1154: Inc DOE/LANL Comment Int Dft	CMS PLN	8JAN99	22JAN99
300410	5	5	0	1154: Issue DOE Draft	CMS PLN	25JAN99	29JAN99
30M040	0	0	0	1154: RFI COMPLETED			28JAN99
30M080	0	0	0	1154: EPA NOTIFICATION OF CMS REQUIREMENTS			28JAN99
300415	22	22	0	1154: DOE Review DOE Draft	CMS PLN	1FEB99	3MAR99
300420	20	20	0	1154: Inc DOE Comments DOE Draft	CMS PLN	4MAR99	31MAR99
300425	10	10	0	1154: Issue EPA/NMED Draft	CMS PLN	1APR99	14APR99
30M050	0	0	0	1154: EPA/NMED DRAFT CMS PLAN COMPLETED			14APR99
300430	44	44	0	1154: EPA Review	CMS PLN	15APR99	16JUN99
300435	44	44	0	1154: NMED Review	CMS PLN	15APR99	16JUN99
300565	20	20	0	1154: Inc EPA/NMED Comments	CMS PLN	17JUN99	15JUL99
300570	10	10	0	1154: Issue Final	CMS PLN	16JUL99	29JUL99
300575	5	5	0	1154: EPA Approve	CMS PLN	30JUL99	5AUG99
30M085	0	0	0	1154: EPA APPROVAL CMS PLAN			5AUG99
300440	245	245	0	1154: CMS Bench/Pilot Studies	(LOE)	6AUG99	31JUL00
300445	30	30	0	1154: Technical Evaluation	CMS RPT	6AUG99	17SEP99
300450	30	30	0	1154: Environmental Evaluation	CMS RPT	6AUG99	17SEP99
300455	30	30	0	1154: Human Health Evaluation	CMS RPT	6AUG99	17SEP99
300460	30	30	0	1154: Community Relations Eval	CMS RPT	6AUG99	17SEP99
300465	30	30	0	1154: Cost Evaluation	CMS RPT	6AUG99	17SEP99
300470	30	30	0	1154: Develop NEPA Documentation	CMS RPT	6AUG99	17SEP99
30M055	0	0	0	1154: START CMS WORK		6AUG99	
30M065	0	0	0	1154: START DEVELOPMENT CMS REPORT		6AUG99	
300475	10	10	0	1154: Prepare Internal Draft	CMS RPT	20SEP99	10CT99
300120	249	249	0	1154: Manage ADS FY-00	(LOE)	10CT99	29SEP00

TBS 2/17/92

DATA DATE 10CT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
600912	249	249	0	1154: Conduct VCA - Assessment FY-00	10CT99	29SEP00
600914	249	249	0	1154: Conduct VCA - Remediation FY-00	10CT99	29SEP00
300480	22	22	0	1154: DOE/LANL/VE Rev Internal Dft CMS RPT	40CT99	3NOV99
300485	35	35	0	1154: Inc DOE/LANL Comment Int Dft CMS RPT	12JUN00	31JUL00
30M060	0	0	0	1154: CMS WORK COMPLETED		31JUL00
300490	10	10	0	1154: Issue DOE Draft CMS RPT	1AUG00	14AUG00
300495	22	22	0	1154: DOE Review DOE Draft CMS RPT	15AUG00	14SEP00
300500	10	10	0	1154: Inc DOE Comments DOE Draft CMS RPT	15SEP00	28SEP00
300505	10	10	0	1154: Issue EPA/NMED Draft CMS RPT	29SEP00	13OCT00
300130	248	248	0	1154: Manage ADS FY-01 (LOE)	20CT00	28SEP01
600916	248	248	0	1154: Conduct VCA - Assessment FY-01	20CT00	28SEP01
600918	248	248	0	1154: Conduct VCA - Remediation FY-01	20CT00	28SEP01
30M070	0	0	0	1154: EPA/NMED DRAFT CMS REPORT COMPLETED		13OCT00
300510	44	44	0	1154: EPA Review CMS RPT	16OCT00	19DEC00
300515	44	44	0	1154: NMED Review CMS RPT	16OCT00	19DEC00
300580	20	20	0	1154: Inc EPA/NMED Comments CMS RPT	20DEC00	22JAN01
300585	10	10	0	1154: Issue Final CMS RPT	23JAN01	5FEB01
30M075	0	0	0	1154: ASSESSMENT COMPLETED		5FEB01

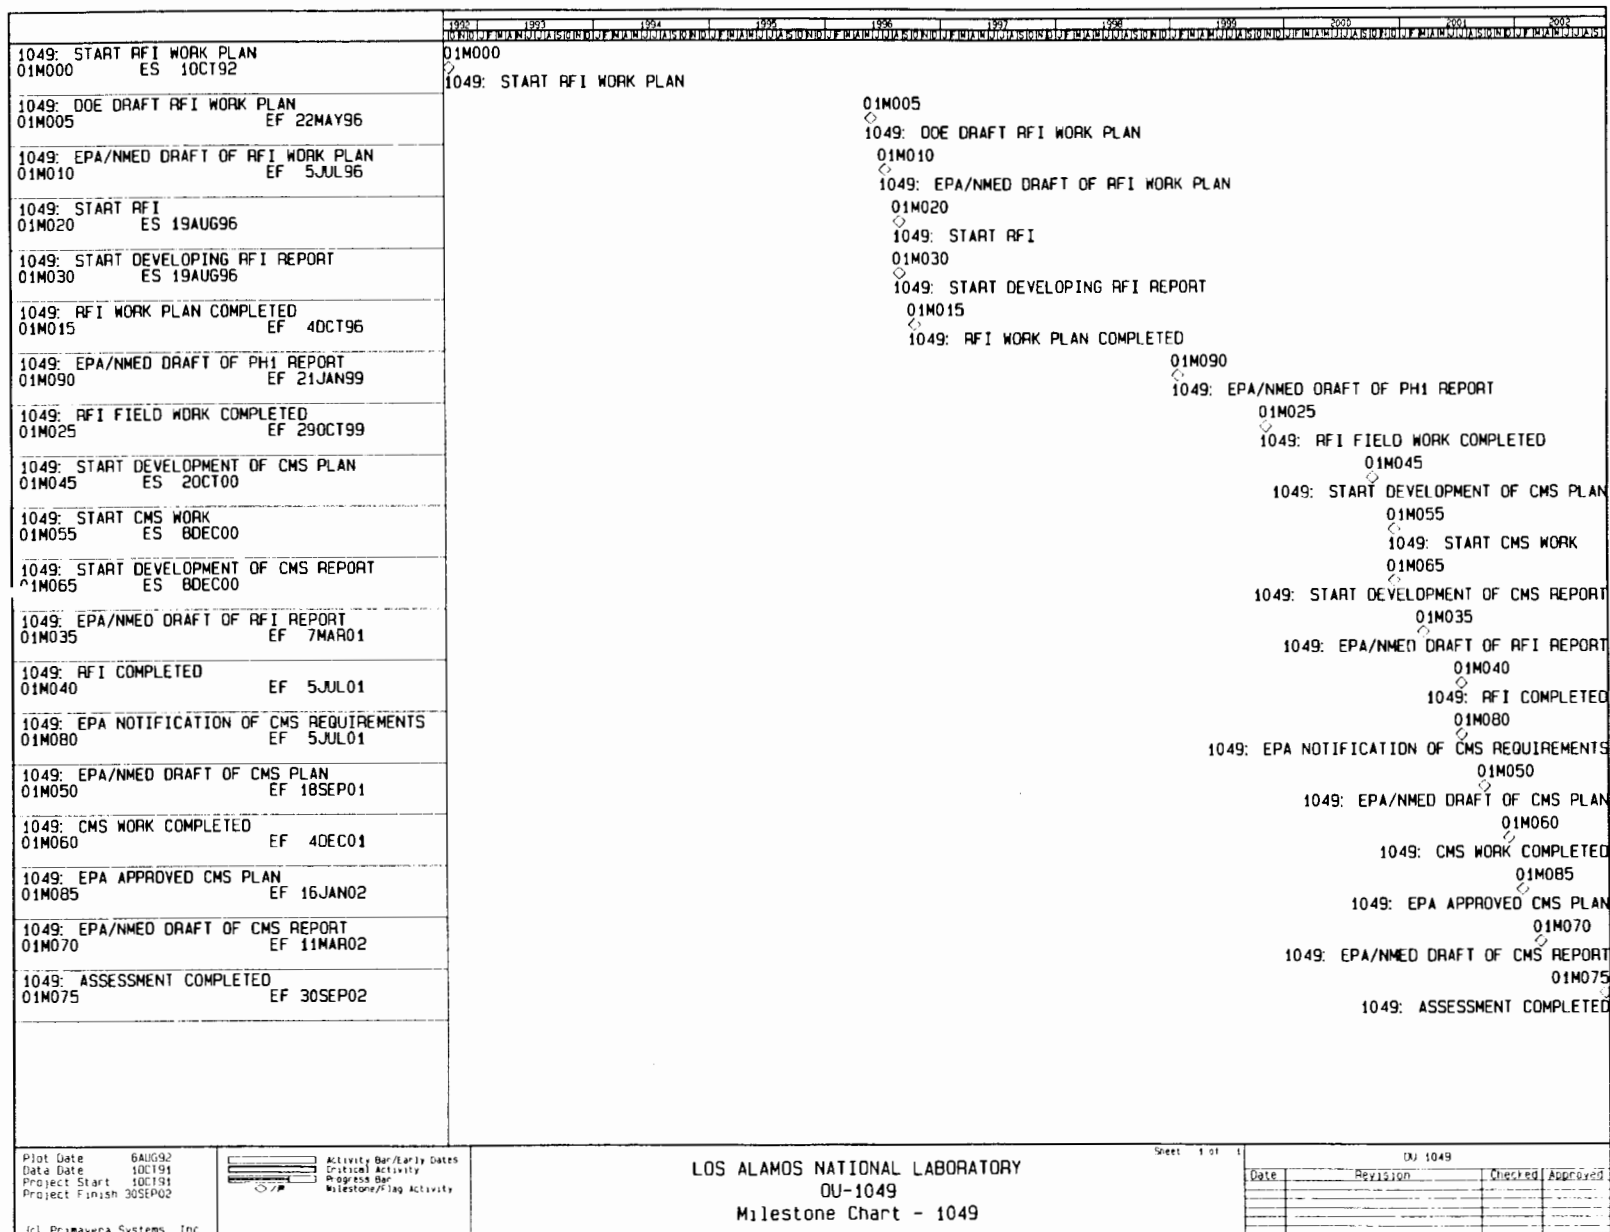

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 1OCT91 PAGE NO. 1

DATA DATE 1OCT91 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
010020	250	250	0	1049: Develop NEPA Documentation for RFI WP	10CT91	30SEP92
010030	250	250	0	1049: Manage ADS During FY-92 (LOE)	10CT91	30SEP92
600002	250	250	0	1049: VCA FY-92	10CT91	30SEP92
010000	249	249	0	1049:Conduct Bench/Pilot Studies for RFI WP(LOE)	10CT92	30SEP93
010005	249	249	0	1049:Conduct Voluntary C.Actions for RFI WP(LOE)	10CT92	30SEP93
010010	63	63	0	1049: Develop Scope for RFI WP	10CT92	6JAN93
010040	249	249	0	1049: Manage ADS FY93 (LOE)	10CT92	30SEP93
600005	249	249	0	1049: VCA FY-93	10CT92	30SEP93
01M000	0	0	0	1049: START RFI WORK PLAN	10CT92*	
010025	90	90	0	1049: Locate Existing Data for RFI WP	30OCT92	16MAR93
010075	40	40	0	1049: Develop Data Quality Objectives for RFI WP	7JAN93	5MAR93
010600	39	39	0	1049: Develop Data Quality Objectives PSS	21JAN93*	17MAR93
010605	21	21	0	1049: Prep Assessment Sampling Plans PSS FY-93	1SEP93*	30SEP93
010050	249	249	0	1049: Manage ADS During FY-94 (LOE)	10CT93	30SEP94
010606	249	249	0	1049: Prep Assessment Sampling Plans PSS FY-94	10CT93	30SEP94
600010	249	249	0	1049: VCA FY-94	10CT93	30SEP94
010070	248	248	0	1049: Manage ADS During FY-95 (LOE)	30CT94	29SEP95
010607	40	40	0	1049: Prep Assessment Sampling Plans PSS FY-95	30CT94	1DEC94
600015	248	248	0	1049: VCA FY-95	30CT94	29SEP95
010610	22	22	0	1049: Conduct Assessment Sampling PSS	2DEC94	5JAN95
010615	64	64	0	1049: Conduct Assessment Sampling Analysis PSS	6JAN95	7APR95
010620	56	56	0	1049: Perform Prelim. Risk Assessment PSS	10APR95	27JUN95
010035	55	55	0	1049: Analyze Existing Data for RFI WP FY-95	12JUN95*	28AUG95
010625	61	61	0	1049: Perform Prelim. Risk Assessment PSS	28JUN95	22SEP95
010036	20	20	0	1049: Analyze Existing Data for RFI WP FY-96	29AUG95	26SEP95
010630	22	22	0	1049: Review Draft RFI Scoping Report PSS	25SEP95	25OCT95
010045	20	20	0	1049: Draft Existing Data Report for RFI WP	27SEP95	25OCT95
010080	249	249	0	1049: Manage ADS During FY-96 (LOE)	20CT95	30SEP96
010618	100	100	0	1049: Develop NEPA Documentation for RFI WP	20CT95*	29FEB96
600018	249	249	0	1049: VCA FY-96	20CT95	30SEP96



LANL EM-13 S. WAGNER  
 REPORT DATE 5AUG92 RUN NO. 438  
 15:44  
 1049 SCHEDULE REPORT BY EARLY START

FINEST HOUR  
 ENVIRONMENTAL RESTORATION

ADS 1049: CANYONS  
 START DATE 10CT91  
 DATA DATE 10CT91

BELL3/16/92  
 FIN DATE 30SEP02  
 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	FINISH
010055	20	20	0	1049: Determine Data Needs for RFI WP	26OCT95	27NOV95
010635	20	20	0	1049: Issue RFI Scoping Report PSS	26OCT95	27NOV95
010085	40	40	0	1049: Develop Sampling Plan for RFI WP	28NOV95	26JAN96
010060	20	20	0	1049: Write Community Relations Plan for RFI WP	29JAN96	26FEB96
010065	20	20	0	1049: Write Records Management Plan for RFI WP	29JAN96	26FEB96
010095	20	20	0	1049: Write Quality Assurance Plan for RFI WP	29JAN96	26FEB96
010100	20	20	0	1049: Write Health & Safety Plan for RFI WP	29JAN96	26FEB96
010105	20	20	0	1049: Write Management Plan for RFI WP	29JAN96	26FEB96
010115	20	20	0	1049: Develop LANL Internal Draft of RFI WP	27FEB96	25MAR96
010125	22	22	0	1049: DOE/LANL/VE Review Internal Draft RFI WP	26MAR96	24APR96
010135	10	10	0	1049: Inc DOE/LANL Comments Internal Draft RFI WP	25APR96	8MAY96
010145	10	10	0	1049: Issue DOE Draft of RFI WP	9MAY96	22MAY96
01M005	0	0	0	1049: DOE DRAFT RFI WORK PLAN		22MAY96
010150	10	10	0	1049: DOE Review DOE Draft RFI WP	23MAY96	6JUN96
010525	60	60	0	1049: Write PH1 Contract; Mobilize for RFI	23MAY96	16AUG96
010155	10	10	0	1049: Inc DOE Comments DOE Draft RFI WP	7JUN96	20JUN96
010160	10	10	0	1049: Issue EPA/NMED Draft RFI WP	21JUN96	5JUL96
01M010	0	0	0	1049: EPA/NMED DRAFT OF RFI WORK PLAN		5JUL96
010165	44	44	0	1049: NMED Review RFI WP	8JUL96	6SEP96
010170	44	44	0	1049: EPA Review RFI WP	8JUL96	6SEP96
010185	279	279	0	1049: Conduct RFI PH1 Field Work	19AUG96	30SEP97
010190	30	30	0	1049: Conduct RFI PH1 Sample Analysis FY-96	19AUG96	30SEP96
010310	50	50	0	1049: Prep NEPA Info for RFI Report	19AUG96	29OCT96
01M020	0	0	0	1049: START RFI	19AUG96	
01M030	0	0	0	1049: START DEVELOPING RFI REPORT	19AUG96	
010530	10	10	0	1049: Incorporate EPA/NMED Comments for RFI WP	9SEP96	20SEP96
010535	10	10	0	1049: Issue Final RFI Work Plan	23SEP96	4OCT96
010090	249	249	0	1049: Manage ADS During FY-97 (LOE)	1OCT96	30SEP97
010191	249	249	0	1049: Conduct RFI PH1 Sample Analysis FY-97	1OCT96	30SEP97
010195	249	249	0	1049: Conduct RFI PH1 Data Assessment FY-97	1OCT96	30SEP97

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10OCT91 PAGE NO. 3

DATA DATE 10CT91 PAGE NO. 3

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
600022	249	249	0	1049: VCA FY-97	10CT96	30SEP97
01M015	0	0	0	1049: RFI WORK PLAN COMPLETED		40CT96
010110	249	249	0	1049: Manage ADS During FY-98 (LOE)	10CT97	30SEP98
010192	200	200	0	1049: Conduct RFI PH1 Sample Analysis FY-98	10CT97	22JUL98
010196	220	220	0	1049: Conduct RFI PH1 Data Assessment FY-98	10CT97	19AUG98
010205	20	20	0	1049: Demobilize RFI PH1 Field Work	10CT97	29OCT97
600030	249	249	0	1049: VCA FY-98	10CT97	30SEP98
010220	20	20	0	1049: Write PH2 Contract; Mobilize for RFI	28JUL98*	24AUG98
010200	60	60	0	1049: Write Draft RFI PH1 Report/WP Modification	20AUG98	16NOV98
010225	26	26	0	1049: Conduct RFI PH2 Field Work FY-98	25AUG98	30SEP98
010230	26	26	0	1049: Conduct RFI PH2 Sample Analysis FY-98	25AUG98	30SEP98
010240	26	26	0	1049: Conduct RFI PH2 Data Assessment FY-98	25AUG98	30SEP98
010120	249	249	0	1049: Manage ADS During FY-99 (LOE)	10CT98	30SEP99
010226	249	249	0	1049: Conduct RFI PH2 Field Work FY-99	10CT98	30SEP99
010231	249	249	0	1049: Conduct RFI PH2 Sample Analysis FY-99	10CT98	30SEP99
010241	249	249	0	1049: Conduct RFI PH2 Data Assessment FY-99	10CT98	30SEP99
600035	249	249	0	1049: VCA FY-99	10CT98	30SEP99
010215	22	22	0	1049: DOE/LANL Review PH1 Report/WP Modification	17NOV98	18DEC98
010131	20	20	0	1049: Incorp. DOE/LANL Rev. Comments PH1 Rpt Mod	21DEC98	21JAN99
01M090	0	0	0	1049: EPA/NMED DRAFT OF PH1 REPORT		21JAN99
010210	22	22	0	1049: EPA/NMED Review PH1 Report/WP Modification	22JAN99	23FEB99
010132	40	40	0	1049: Incorp. EPA/NMED Rev. Comments PH1 Rpt Mod	24FEB99	20APR99
010133	10	10	0	1049: Issue Final PH1 Report/Work Plan Mod	21APR99	4MAY99
010130	249	249	0	1049: Manage ADS During FY-00 (LOE)	10CT99	29SEP00
010232	105	105	0	1049: Conduct RFI PH2 Sample Analysis FY-00	10CT99	8MAR00
010235	20	20	0	1049: Demobilize RFI PH2 Field Work	10CT99	29OCT99
010242	125	125	0	1049: Conduct RFI PH2 Data Assessment FY-00	10CT99	5APR00
600040	249	249	0	1049: VCA FY-00	10CT99	29SEP00
01M025	0	0	0	1049: RFI FIELD WORK COMPLETED		29OCT99
010300	60	60	0	1049: Conduct RFI Report Facility Investigation	6APR00	29JUN00

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10CT91 PAGE NO. 4

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
010305	90	90	0	1049: Conduct RFI Report Investigation Analysis	6APR00	11AUG00
010320	124	124	0	1049: Prepare Internal Draft of RFI Report	6APR00	29SEP00
010140	248	248	0	Manage ADS During FY-01 (LOE)	20CT00	28SEP01
010325	22	22	0	1049: DOE/LANL/VE Rev Internal Draft of RFI Rpt	20CT00	1NOV00
010365	245	245	0	1049:Cond Bench/Pilot Studies for CMS Plan (LOE)	20CT00	25SEP01
010370	20	20	0	1049: Establish Current Situation for CMS Plan	20CT00	30OCT00
010375	20	20	0	1049: Establish CA Objectives for CMS Plan	20CT00	30OCT00
010380	20	20	0	1049: Dev Screening Technologies for CMS Plan	20CT00	30OCT00
010385	245	245	0	1049: Develop NEPA Documentation for CMS Plan	20CT00	25SEP01
600045	248	248	0	1049: VCA FY-01	20CT00	28SEP01
01M045	0	0	0	1049: START DEVELOPMENT OF CMS PLAN	20CT00	
010390	15	15	0	1049: Develop Alternatives for CMS Plan	31OCT00	21NOV00
010330	20	20	0	1049: Inc DOE/LANL Rev.Comments Int Dft RFI Rpt	2NOV00	4DEC00
010395	10	10	0	1049: Develop Internal Draft of CMS Plan	22NOV00	7DEC00
010335	10	10	0	1049: Issue DOE Draft of RFI Report	5DEC00	18DEC00
010400	10	10	0	1049: DOE/LANL/VE Rev Internal Draft of CMS Pl	8DEC00	21DEC00
010440	246	246	0	1049: Conduct CMS Bench/Pilot Studies (LOE)	8DEC00	4DEC01
010445	20	20	0	1049: Conduct Technical Evaluation for CMS Rpt	8DEC00	9JAN01
010450	20	20	0	1049: Cond Envir Evaluation for CMS Report	8DEC00	9JAN01
010455	20	20	0	1049: Conduct Human Health Eval for CMS Report	8DEC00	9JAN01
010460	20	20	0	1049: Cond Comm Relations Eval.for CMS Report	8DEC00	9JAN01
010465	20	20	0	1049: Conduct Cost Evaluation for CMS Report	8DEC00	9JAN01
010470	20	20	0	1049: Develop NEPA Documentation for CMS Report	8DEC00	9JAN01
01M055	0	0	0	1049: START CMS WORK	8DEC00	
01M065	0	0	0	1049: START DEVELOPMENT OF CMS REPORT	8DEC00	
010340	22	22	0	1049: Conduct Review of DOE Draft of RFI Report	19DEC00	23JAN01
010405	10	10	0	1049:Incorp. LANL REV Comments Intern Dft CMS PL	22DEC00	9JAN01
010410	5	5	0	1049: Issue DOE Draft of CMS Plan	10JAN01	17JAN01
010475	10	10	0	1049: Prepare Internal Draft of CMS Report	10JAN01	24JAN01
010345	20	20	0	1049: Incorp. DOE Rev. Comments DOE Drft RFI Rpt	24JAN01	21FEB01

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10OCT91 PAGE NO. 5

DATA DATE 10OCT91 PAGE NO. 5

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED	
					START	FINISH
010480	10	10	0	1049: DOE/LANL/VE Rev Internal Draft of CMS Rpt	25JAN01	7FEB01
010350	10	10	0	1049: Issue EPA/NMED Draft of RFI Report	22FEB01	7MAR01
01M035	0	0	0	1049: EPA/NMED DRAFT OF RFI REPORT		7MAR01
010355	44	44	0	1049: Conduct EPA Review of RFI Report	8MAR01	8MAY01
010360	44	44	0	1049: Conduct NMED Review of RFI Report	8MAR01	8MAY01
010555	20	20	0	1049: Incorporate EPA/NMED Comments on RFI Rpt	9MAY01	6JUN01
010560	20	20	0	1049: Issue Final RFI Report	7JUN01	5JUL01
01M040	0	0	0	1049: RFI COMPLETED		5JUL01
01M080	0	0	0	1049: EPA NOTIFICATION OF CMS REQUIREMENTS		5JUL01
010415	22	22	0	1049: Conduct Review of DOE Draft of CMS Plan	6JUL01	6AUG01
010420	20	20	0	1049:Incorp. DOE Rev.Comments DOE Dft.of CMS Pl.	7AUG01	4SEP01
010425	10	10	0	1049: Issue EPA/NMED Draft of CMS Plan	5SEP01	18SEP01
01M050	0	0	0	1049: EPA/NMED DRAFT OF CMS PLAN		18SEP01
010430	44	44	0	1049: Conduct EPA Review of CMS Plan	19SEP01	21NOV01
010435	44	44	0	1049: Conduct NMED Review of CMS Plan	19SEP01	21NOV01
010142	249	249	0	Manage ADS During FY-02 (LOE)	1OCT01	30SEP02
600050	249	249	0	1049: VCA FY-02	1OCT01	30SEP02
010485	35	35	0	1049:Incorp.LANL Rev Comments Intern.Dft CMS Rpt	12OCT01	4DEC01
010565	20	20	0	1049: Incorporate EPA/NMED Comments on CMS Plan	26NOV01	21DEC01
01M060	0	0	0	1049: CMS WORK COMPLETED		4DEC01
010490	10	10	0	1049: Issue DOE Draft of CMS Report	5DEC01	18DEC01
010495	22	22	0	1049: Conduct Review of DOE Draft of CMS Report	19DEC01	23JAN02
010570	10	10	0	1049: Issue Final CMS Plan	24DEC01	9JAN02
010575	5	5	0	1049: EPA Approves CMS Plan	10JAN02	16JAN02
01M085	0	0	0	1049: EPA APPROVED CMS PLAN		16JAN02
010500	22	22	0	1049:Incorp. DOE Rev Comments DOE Dft CMS Report	24JAN02	25FEB02
010505	10	10	0	1049: Issue EPA/NMED Draft of CMS Report	26FEB02	11MAR02
01M070	0	0	0	1049: EPA/NMED DRAFT OF CMS REPORT		11MAR02
010510	44	44	0	1049: Conduct EPA Review of CMS Report	12MAR02	10MAY02
010515	44	44	0	1049: Conduct NMED Rev of CMS Report	12MAR02	10MAY02

BELL3/16/92

START DATE 1OCT91 FIN DATE 30SEP02

DATA DATE 10OCT91 PAGE NO. 6

ACTIVITY ID	ORIG DUR	REM DUR	%	ACTIVITY DESCRIPTION	SCHEDULED START	SCHEDULED FINISH
010580	20	20	0	1049: Incorporate EPA/NMED Comments on CMS Rpt	13MAY02	10JUN02
010585	10	10	0	1049: Issue Final CMS Report	11JUN02	24JUN02
01M075	0	0	0	1049: ASSESSMENT COMPLETED		30SEP02
