

 ENTERED



National Nuclear Security Administration
Sandia Site Office
P.O. Box 5400
Albuquerque, New Mexico 87185-5400



DEC 21 2009

CERTIFIED MAIL-RETURN RECEIPT REQUESTED

James Bearzi, Chief
Hazardous Waste Bureau
New Mexico Environment Department
2905 Rodeo Park Road East, Bldg. 1
Santa Fe, NM 87505




Dear Mr. Bearzi:

On behalf of the U. S. Department of Energy/National Nuclear Security Administration (DOE/NNSA), and Sandia Corporation (Sandia), DOE/NNSA is submitting the December 2009 Consolidated Quarterly Report for the Environmental Restoration Project that addresses all quarterly reporting (from August through October 2009) required under the Hazardous and Solid Waste Amendments (HSWA) Module of the Resource Conservation and Recovery Act (RCRA) Permit, the Compliance Order on Consent and the Chemical Waste Landfill (CWL) Closure Plan for Sandia National Laboratories/New Mexico (SNL/NM), EPA No. 5890110518.

Should you have any questions regarding this project quarterly report please contact me at (505) 845-6036, or Joe Estrada of my staff at (505) 845-5326. For perchlorate or CWL groundwater related items, please contact John Gould, also of my staff, at (505) 854-6089.

Sincerely,


Patty Wagner
Manager

Enclosure (1)

cc w/enclosure:

W. Moats, NMED-HWB (via Certified Mail)
L. King, EPA, Region 6 (via Certified Mail)
T. Skibitski, NMED-OB, MS-1396
B. Birch, NMED-OB, MS-1396
J. Estrada, SSO, MS-0184
J. Gould, SSO, MS-0184
Zimmerman Library, UNM
SNL ES&H Records Center, SNL/NM, Org. 6765, MS-0718

James Bearzi

-2-

DEC 21 2009

cc w/o enclosure:

J. Lehr, NA-56, HQ/FORS

T. Longo, NA-56, HQ/GTN

A. Blumberg, SNL/NM, Org. 11100, MS-0141

M. Walck, SNL/NM, Org. 6700, MS-0701

D. Miller, SNL/NM, Org. 6765, MS-0718

T. Cooper, SNL/NM, Org. 4133, MS-0729

J. Cochran, SNL/NM, Org. 6765, MS-0719

M. Skelly, SNL/NM, Org. 6765, MS-0718

C. Daniel, SNL/NM, Org. 10667, MS-0718



**Sandia
National
Laboratories**

Sandia National Laboratories, New Mexico (SNL/NM)

Environmental Restoration Project

A Department of Energy Environmental Cleanup Program

**CONSOLIDATED
Quarterly Report**

August-September-October

December 2009



United States Department of Energy
Sandia Site Office

Sandia is a multiprogram laboratory operated by Sandia Corporation, a Lockheed Martin Company, for the United States Department of Energy's National Nuclear Security Administration under contract DE-AC04-94AL85000.

CONSOLIDATED QUARTERLY REPORT

December 2009

SANDIA NATIONAL LABORATORIES/NEW MEXICO (SNL/NM)

ENVIRONMENTAL RESTORATION PROJECT

DEPARTMENT OF ENERGY (DOE):	Sandia Site Office
CONTRACTOR:	Sandia Corporation
PROJECT MANAGER:	John Cochran

NUMBER OF POTENTIAL RELEASE SITES SUBJECT TO THIS PERMIT: 36
SUSPECT WASTE: radionuclides, metals, organics, and explosives.

OVERVIEW

This Consolidated Quarterly Report for the Sandia National Laboratories Environmental Project addresses all quarterly reporting requirements pertaining to the Hazardous and Solid Waste Amendments (HSWA) Module of the Resource Conservation and Recovery Act (RCRA) Permit, the Compliance Order on Consent (Consent Order), and the Chemical Waste Landfill (CWL) Closure Plan. The following entities and reporting periods are addressed in these Sections:

SECTION I

Environmental Restoration Project Quarterly Report, reporting period: August-October 2009

SECTION II

Chemical Waste Landfill Quarterly Report, reporting period: August-October 2009

SECTION III

Perchlorate Screening Quarterly Report, reporting period: July-September 2009



Environmental Restoration Project Consolidated Quarterly Report

Section I

Environmental Restoration Project Quarterly Report

December 2009



United States Department of Energy
Sandia Site Office

Sandia is a multiprogram laboratory managed and operated by Sandia Corporation, a wholly-owned subsidiary of Lockheed Martin Corporation, for the United States Department of Energy's National Nuclear Security Administration under contract DE-AC04-94AL85000

TABLE OF CONTENTS

Abbreviations and Acronyms	i
1.0 Introduction.....	1
2.0 ER Work Completed this Quarter.....	1
2.1 Mixed Waste Landfill (MWL).....	1
2.1.1 MWL Documents submitted to NMED pending regulatory review and approval.....	1
2.2 Project Management Site Closure.....	2
2.2.1 Permit Modification Request submitted in March 2006.....	2
2.2.2 Permit Modification Request submitted in January 2008.....	2
2.3 Site-Wide Hydrogeologic Characterization.....	3
2.3.1 TA-3/5 Groundwater.....	3
2.3.2 Burn Site Groundwater (BSG).....	3
2.3.3 Tijeras Arroyo Groundwater (TAG).....	3
2.3.4 Mixed Waste Landfill Groundwater (MWL).....	4
2.3.5 Chemical Waste Landfill Groundwater (CWL).....	4
2.4 Corrective Action Management Unit (CAMU).....	4
2.4.1 CAMU Waste Management Activities	5
2.5 Suspected Solid Waste Management Unit: Long Term Environmental Stewardship (LTES) Site 501, Cable Debris Site	6
2.5.1 LTES Documents submitted to NMED pending regulatory review and approval.....	6

ABBREVIATIONS AND ACRONYMS

BSG	Burn Site Groundwater
BW	background well
CAC	Corrective Action Complete
CFR	Code of Federal Regulations
CME	Corrective Measures Evaluation
COC	Contaminants of Concern
CWL	Chemical Waste Landfill
EB	equipment blank
EPA	U.S. Environmental Protection Agency
ER	Environmental Restoration Project
ET	evapotranspirative
FB	field blank
FOP	Field Operating Procedure
FY09	Fiscal Year 2009
LTES	Long Term Environmental Stewardship
MCL	maximum contaminant level
MDL	method detection limit
NOD	Notice of Deficiency
µg/L	microgram per liter
mg/L	milligram per liter
MW	monitoring well
MWL	Mixed Waste Landfill
NMED	New Mexico Environment Department
pH	potential of hydrogen
QC	quality control
RCRA	Resource Conservation and Recovery Act
RPD	relative percent difference
Sandia	Sandia Corporation
SC	specific conductance
SNL/NM	Sandia National Laboratories/New Mexico
SWMU	Solid Waste Management Unit
TAG	Tijeras Arroyo Groundwater
TB	trip blank
TCE	trichloroethene
VCM	Voluntary Corrective Measure
VE	Vapor Extraction
VOC	volatile organic compound

1.0 Introduction

This Environmental Restoration Consolidated Quarterly Report (ER Quarterly Report) discusses ongoing corrective actions being implemented by the Sandia National Laboratories (SNL) Environmental Restoration (ER) Project. The status of regulatory closure activities is outlined below. In this Section, the Quarter refers to the August through October 2009 quarterly reporting period.

2.0 ER Work Completed this Quarter

2.1 Mixed Waste Landfill (MWL)

- The MWL Evapotranspirative (ET) Cover Construction was completed on September 3, 2009. Activities completed during this reporting period included installation of the Topsoil Layer, revegetation, and supplemental watering.
- A second quarterly progress report on the MWL ET Cover Construction Project is provided concurrent with this ER Project Quarterly Report. The construction progress report will summarize ET Cover construction activities from August through October 2009 as required by the NMED Final Order.
- Preparation of the MWL Corrective Measures Implementation Report is ongoing and will be completed in February 2010
- On October 29, 2009, DOE/Sandia received a Notice of Disapproval for the "MWL Groundwater Monitoring Report Calendar Year 2008" submitted to NMED in May 2009. DOE/Sandia anticipate submitting a response to NMED in November 2009.
- Mixed Waste Landfill Groundwater monitoring results for 2009, including sampling conducted during this reporting period, will be compiled in the next annual MWL Groundwater Monitoring Report (anticipated delivery to NMED in the spring of 2010).

2.1.1 MWL Documents submitted to NMED pending regulatory review and approval

- There are no MWL Documents currently pending that require regulatory review and approval.

2.2 Project Management and Site Closure

ER Sites undergoing regulatory and administrative closure activities are presently addressed under project management. Two permit modification requests are currently in progress with the New Mexico Environment Department (NMED) and are outlined below. The sites, summarized below, were discussed with NMED and public stakeholders in June 2009 as part of comment resolution process for the renewal of the SNL Resource Conservation and Recovery Amendment (RCRA Permit). NMED indicated verbally at the meeting that some of the sites included in the March 2006 and January 2008 permit modification requests would require groundwater characterization and additional soil characterization; official written communication regarding these requirements is anticipated.

2.2.1 Permit Modification Request submitted in March 2006

- Twenty-six sites were submitted to NMED for the final determination of Corrective Action Complete (CAC) in March 2006. The sites included nineteen SWMUs, and seven AOCs. The NMED issued a Notice of Public Comment Period and Intent to Approve a Class 3 Permit Modification of the RCRA Permit for Sandia National Laboratories for these 26 sites on December 10, 2007. The NMED public review and comment period ended on February 8, 2008. The SWMUs and AOCs included in this permit modification request are listed below.

SWMUs – 4, 5, 46, 49, 52, 68, 91, 101, 116, 138, 140, 147, 149, 150, 154, 161, 196, 233, 234

AOCs – 1090, 1094, 1095, 1114, 1115, 1116, and 1117.

2.2.2 Permit Modification Request submitted in January 2008

- Five sites were submitted for the final regulatory determination of CAC in a permit modification request in January 2008. This permit modification included all remaining SNL ER sites with the exception of the three active sites (SWMUs 83, 84, and 240), three Groundwater Investigation sites (Tijeras Arroyo, Technical Area V, and Burn Site), and the MWL (SWMU 76). Final reporting of the Corrective Measure Implementation for the MWL is pending. The MWL is addressed separately in section 2.1 of this Section of this ER Quarterly Report. The four SWMUs and one AOC included in the January 2008 permit modification request are listed below.

SWMUs – 8, 28-2, 58, and 105

AOC – 1101

2.3 Site-Wide Hydrogeologic Characterization

2.3.1 TA-3/5 Groundwater

- Groundwater sampling was completed in August and September 2009. Results of perchlorate analysis are discussed in Section III of this ER Quarterly Report, and other analytical results will be discussed in the Calendar Year 2009 Groundwater Protection Program (GWPP) Annual Groundwater Monitoring Report (anticipated delivery to NMED in the summer of 2010).
- On August 12, 2009, DOE/Sandia received a second Notice of Deficiency (NOD) from the NMED on the Technical Area V Corrective Measures Evaluation (CME) Report (submitted July 2005). A response to the NOD will be submitted in November 2009.

2.3.2 Burn Site Groundwater (BSG)

- Groundwater sampling was completed in September 2009. Results of perchlorate analysis are discussed in Section III of this ER Quarterly Report, and other analytical results will be discussed in the Calendar Year 2009 GWPP Annual Groundwater Monitoring Report (anticipated delivery to NMED in the summer of 2010).
- On April 30, 2009, DOE/Sandia received a letter from NMED entitled “Perchlorate Contamination in Groundwater,” requiring, among other items, characterization of the nature and extent of perchlorate contamination at or near the Burn Site. A work plan to fulfill NMED’s requirements will be submitted by DOE/Sandia in November 2009.

2.3.3 Tijeras Arroyo Groundwater (TAG)

- Groundwater sampling began in July 2009 and was completed in August of 2009. Results of perchlorate analysis are discussed in Section III of this ER Quarterly Report, and other analytical results will be discussed in the Calendar Year 2009 GWPP Annual Groundwater Monitoring Report (anticipated delivery to NMED in the summer of 2010).

- On August 12, 2009, DOE/Sandia received a second NOD from the NMED on the TAG Continuing Investigation Report (submitted in November 2005). A response from DOE/Sandia is expected to be delivered in January 2010.

2.3.4 Mixed Waste Landfill Groundwater (MWL)

- Groundwater sampling was performed in October 2009. Results from these MWL sampling events will be discussed in the upcoming MWL Annual Groundwater Monitoring Report (anticipated delivery to NMED in the spring of 2010).

2.3.5 Chemical Waste Landfill Groundwater (CWL)

- CWL semi-annual groundwater monitoring activities were performed in October 2009. Analytical results associated with the October 2009 sampling event have not been received and will be summarized in Section II of the next ER Quarterly Report to be submitted in March 2010.

2.3.5.1 Groundwater Documents submitted to the NMED pending regulatory review and approval

- CME Report for Tijeras Arroyo Groundwater, submitted August 2005.
- BSG Interim Measures Work Plan, submitted May 2005.
- BSG Current Conceptual Model of Groundwater Flow and Contaminant Transport, submitted April 2008.
- BSG CME Work Plan, submitted April 2008.

2.4 Corrective Action Management Unit (CAMU)

CAMU Post-closure Care operations consist of vadose-zone monitoring, leachate removal, and post-closure inspections, as required in the permit. Activities for this reporting period include the following:

- Weekly pumping of leachate from the leachate collection and removal system.
- Weekly inspection of the less-than-90-day area.

- Quarterly inspection of the site (September 2009), including containment cell cover, storm water diversion structures, security fences, gates, signs, and benchmarks:
 - Approximately 40 four-wing saltbush plants were identified growing on the cover. These plants can develop extensive root systems that could damage the high-density polyethylene cover. They were removed on October 23, 2009.
- Quarterly monitoring of the Vadose Zone Monitoring System (VZMS) was conducted in September 2009. Results will be posted in the annual CAMU report.
- Waste management associated with the leachate collection was conducted (see below).
- Composite leachate sampling for waste characterization was conducted on September 15, 2009.

2.4.1 CAMU Waste Management Activities

- Waste stored on site at the beginning of this period:
 - 30 gallons of leachate.
 - 2 lbs PPE.
- Waste generated on-site during the period:
 - 137 gallons of leachate.
 - 2 gallons of rinsate.
 - 5 lbs PPE, paper wipes, plastic drum pump.
- Waste removed from site by the Hazardous Waste Management Facility:
 - 107 gallons of leachate on September 29, 2009.
 - 2 gallons of rinsate on September 29, 2009.
 - 5 lbs PPE, paper wipes, plastic drum pump on September 29, 2009.
- Waste remaining on site at the end of this period:
 - 60 gallons of leachate.
 - 2 lbs PPE.

2.4.1.1 CAMU Regulatory Activities

- On October 30, 2009, SNL/DOE delivered a “Notification of Class 1 Modification to Hazardous Waste Operating Permits for SNL/NM, Environmental Protection Agency ID NM5890110518 effective on October 26, 2009” to NMED.
 - Pager contact information for emergency coordinators has been updated due to a recent change in vendors for pager services.

2.5 Suspected Solid Waste Management Unit: Long Term Environmental Stewardship (LTES) Site 501, Cable Debris Site

- In August 17, 2009 a temporary irrigation system was installed at the Cable Debris Site, the site was seeded and 1/2" gravel applied.
- On September 21, 2009, DOE/Sandia received NMED's "Notice of Disapproval: Investigation Report and Proposal for Corrective Action Complete for LTES Site 1/Cable Debris Site" delivered to NMED in March 2009.
- On October 5, 2009, after successful re-vegetation, the irrigation system was removed from the Cable Debris Site.
- In October, a memorandum was drafted that standardized LTES and other RCRA site names. This resulted in a name change for the Cable Debris Site from LTES Site 1 to LTES Site 501.

2.5.1 LTES Documents submitted to NMED pending regulatory review and approval

- There are no LTES Documents currently pending that require regulatory review and approval.



Environmental Restoration Project Consolidated Quarterly Report

Section II

**Chemical Waste Landfill
Quarterly Closure Progress Report**

December 2009



United States Department of Energy
Sandia Site Office

Sandia is a multiprogram laboratory managed and operated by Sandia Corporation, a wholly-owned subsidiary of Lockheed Martin Corporation, for the United States Department of Energy's National Nuclear Security Administration under contract DE-AC04-94AL85000

SECTION II. CHEMICAL WASTE LANDFILL QUARTERLY PROGRESS REPORT

This Sandia National Laboratories/New Mexico (SNL/NM) Chemical Waste Landfill (CWL) Quarterly Closure Progress Report has been prepared pursuant to the CWL Final Closure Plan and Post-closure Permit Application (Closure Plan) (SNL/NM December 1992). This section documents activities at the CWL for the reporting period of August through October 2009. CWL semi-annual groundwater monitoring activities were performed in October 2009. Analytical results associated with the October 2009 sampling event have not been received and will be summarized in Section II of the next Environmental Restoration (ER) Consolidated Quarterly Report to be submitted in March 2010.

1.0 Introduction

All voluntary corrective measures (VCMs) activities for the CWL have been completed. The CWL Landfill Excavation (LE) VCM Final Report was submitted to the NMED in April 2003 (SNL/NM April 2003) and approved by the NMED in December 2003 (Moats December 2003). The Site Operational Boundary Closure Addendum to the LE VCM Final Report was submitted to the NMED in August 2005 (SNL/NM August 2005) and approved by the NMED on October 25, 2005 (Bearzi October 2005). With the submittal of the Waste Management Addendum to the LE VCM Final Report in the February 22, 2006 CWL Quarterly Closure Progress Report (SNL/NM February 2006), as Appendix B, all LE VCM regulatory deliverables have been submitted. With the completion of the VCMs, technical meetings will be held on an as-needed basis. The public will continue to be informed of significant events through the Environmental Restoration (ER) Project public meeting process.

Installation of the cover as an interim measure was requested in April 2004 (Wagner April 2004) and approved with conditions in September 2004 (Kieling September 2004); the cover was completed in September 2005 in accordance with the conditions of approval. All field activities, with the exception of long-term monitoring, have been completed at the CWL.

2.0 Status of Closure

The Final Toxic Substances Control Act (TSCA) Closure Report documents the completion of all closure activities specified in the "Risk-Based Approval Request, 40 CFR 761.61(c) Risk-Based Method for Management of PCB [Polychlorinated Biphenyl] Materials" (SNL/NM October 2001), approved by the U.S. Environmental Protection Agency (EPA) in June 2002 (Cooke June 2002). The Final TSCA Closure Report was submitted to the EPA and NMED on November 2, 2006 (SNL/NM November 2006).

Upcoming CWL Closure Plan reporting activities include revising and submitting the Final Resource Conservation and Recovery Act (RCRA) Closure Report, to be submitted after NMED approval of the Corrective Measures Study (CMS) Report has been received. The Final RCRA Closure Report will document both the backfilling of the former CWL and installation of the cover.

On May 21, 2007, the NMED issued, for public comment, the draft post-closure care permit for the CWL. Also included in the public notices were the CMS Report and the Closure Plan amendment (changes to Chapter 12 revising the closure process). On July 19, 2007, DOE and Sandia responded in opposition to the issuance of the CWL post-closure care permit as drafted and offered a number of

comments, the most important of which were related to groundwater and vadose zone monitoring. In addition, DOE and Sandia requested that a public hearing be scheduled to address these outstanding issues.

For this reporting period the post-closure care permit negotiations that included a CWL Closure Plan amendment addressing the replacement of four groundwater monitoring wells, were completed and approved by NMED. Sandia and DOE signatures for the final settlement agreement were provided in October and the settlement agreement and Final Order In the Matter of Application for a Post-Closure Care Hazardous Waste Permit for the Chemical Waste Landfill, Sandia National Laboratories No. NM5890110518 (Final Order) were signed by NMED on October 15, 2009. NMED issued a "Notice of Approval Final Remedy and Closure Plan Amendment Chemical Waste Landfill" on October 16, 2009. Sandia will now proceed with the replacement of four groundwater monitoring wells at the CWL according to the approved Closure Plan Amendment.

3.0 Water Monitoring Assessment

CWL semi-annual groundwater monitoring activities were performed in October 2009. Analytical results associated with this groundwater sampling event have not been received. The October 2009 activities associated with the groundwater monitoring task will be summarized in the next ER Quarterly Progress Report to be submitted in March 2010.

No soil-gas sampling was performed at the CWL during this reporting period. Soil-gas sampling is not required under the Closure Plan but is expected to be a requirement for post-closure care (Kieling, December 2003).

4.0 Projected Activities for the Upcoming Quarter

Planning and contracting associated with the replacement of four groundwater monitoring wells at the CWL according to the approved Closure Plan Amendment will proceed during the next quarter. After installation of the four groundwater monitoring wells, Sandia and DOE will prepare and submit the CWL Final RCRA Closure Report.

5.0 References

Bearzi, J.P. (New Mexico Environment Department), October 2005. Letter to P. Wagner (U.S. Department of Energy) and P.B. Davies (Sandia Corporation), "Notice of Approval: Chemical Waste Landfill Site Operational Boundary Closure Addendum to the Landfill Excavation Corrective Measure Final Report; August 2005, Sandia National Laboratories, NM5890110518, HWB-SNL-05-021." October 25, 2005.

Cooke, G. (U.S. Environmental Protection Agency Region 6), June 2002. Letter to M.J. Zamorski (U.S. Department of Energy), "Approval of the TSCA Risk-Based Approach Request for the CWL." June 26, 2002.

Kieling, J.E. (New Mexico Environment Department), December 2003. Letter to

K.L. Boardman (U.S. Department of Energy) and P.B. Davies (Sandia Corporation), "Chemical Waste Landfill Corrective Measures Study, May 2003, Sandia National Laboratories, NM5890110518, HWB-SNL-03-013 " December 12, 2003.

Kieling, J.E. (New Mexico Environment Department), September 2004. Letter to P. Wagner (U.S. Department of Energy) and P.B. Davies (Sandia Corporation), "Approval With Conditions of the Landfill Cover Interim Measure at the Chemical Waste Landfill, Sandia National Laboratories, NM5890110518, HWB-SNL-03-013." September 22, 2004.

Moats, W.P. (New Mexico Environment Department), December 2003. Letter to K.L. Boardman (U.S. Department of Energy) and P.B. Davies (Sandia Corporation), "Final Approval, Landfill Excavation Voluntary Corrective Measures, Final Report, April 2003, Sandia National Laboratories, NM5890110518 HWB-SNL-03-012." December 16, 2003.

Sandia National Laboratories/New Mexico (SNL/NM), December 1992. "The Chemical Waste Landfill Final Closure Plan and Postclosure Permit Application," Sandia National Laboratories, Albuquerque, New Mexico.

Sandia National Laboratories/New Mexico (SNL/NM), October 2001. "Risk-Based Approval Request, 40 CFR 761.61 (c) Risk-Based Method For Management of PCB Materials," Chemical Waste Landfill Remediation and Corrective Action Management Unit, Sandia National Laboratories, Albuquerque, New Mexico. October 24, 2001.

Sandia National Laboratories/New Mexico (SNL/NM), April 2004. "Request for Approval to Install the Vegetative Soil Cover Presented in the RAP as an Interim Measure," Sandia National Laboratories, Albuquerque, New Mexico. April 19, 2004.

Sandia National Laboratories/New Mexico (SNL/NM), August 2005. "Chemical Waste Landfill Site Operational Boundary Closure Addendum to the Landfill Excavation Voluntary Corrective Measure Final Report," Sandia National Laboratories, Albuquerque, New Mexico.

Sandia National Laboratories/New Mexico (SNL/NM), February 2006. "Chemical Waste Landfill Quarterly Closure Progress Report," Sandia National Laboratories, Albuquerque, New Mexico.

Sandia National Laboratories/New Mexico (SNL/NM), November 2006. "Chemical Waste Landfill Toxic Substances Control Act Final Report." Sandia National Laboratories, Albuquerque, New Mexico. November 2, 2006.

Wagner, P. (U.S. Department of Energy), April 2004. Letter to J. Kieling (New Mexico Environment Department) requesting approval of "an interim measure (cover) at the Chemical Waste Landfill." April 19, 2004.



Environmental Restoration Project Consolidated Quarterly Report

Section III

**Perchlorate Screening Quarterly Monitoring Report
Third Quarter of Calendar Year 2009
(July, August, and September 2009)**

December 2009



United States Department of Energy
Sandia Site Office

Sandia is a multiprogram laboratory managed and operated by Sandia Corporation, a wholly-owned subsidiary of Lockheed Martin Corporation, for the United States Department of Energy's National Nuclear Security Administration under contract DE-AC04-94AL85000

**Section III:
Perchlorate Screening Quarterly Monitoring Report Third Quarter of
Calendar Year 2009 (July, August, and September 2009)**

Executive Summary

Section IV.B of the Compliance Order on Consent (the Order), between the New Mexico Environment Department (NMED), the U.S. Department of Energy (DOE), and Sandia Corporation (Sandia) for Sandia National Laboratories/New Mexico (SNL/NM), effective on April 29, 2004, stipulates that a select group of groundwater monitoring wells be sampled for perchlorate at SNL/NM (NMED April 2004). This report summarizes the perchlorate monitoring completed during the third quarter of Calendar Year 2009 (CY2009) (July, August, and September 2009) in response to the requirements of the Order. During the third quarter of CY2009, groundwater samples were collected from CYN-MW6, LWDS-MW1, TA1-W-06, TA1-W-08, TA2-W-01, and TA2-W-27.

CYN-MW6 is one of the seven wells in the Burn Site Groundwater monitoring well network. LWDS-MW1 is in the Technical Area V Groundwater Investigation study area and was sampled for the second time for perchlorate based on requirements stipulated in an April 2009 letter from the NMED (NMED April 2009). TA1-W-06, TA1-W-08, TA2-W-01, and TA2-W-27 are in the Tijeras Arroyo Groundwater Investigation study area and were sampled for the first time for perchlorate based on NMED requirements (NMED April 2009). All samples were submitted to General Engineering Laboratories (GEL) for perchlorate analysis using U.S. Environmental Protection Agency (EPA) Method 314.0 (EPA November 1999).

No perchlorate was detected in the environmental samples from LWDS-MW1, TA1-W-06, TA1-W-08, TA2-W-01, or TA2-W-27 at a method detection limit of 4 micrograms per liter ($\mu\text{g/L}$). In September of 2009 the environmental samples from CYN-MW6 revealed perchlorate at concentrations of 4.12 and 4.71 $\mu\text{g/L}$. The source for the perchlorate in the groundwater at CYN-MW6 is unknown although a natural source may be present. Because perchlorate concentrations in monitoring well CYN-MW6 have exceeded the screening level, DOE/Sandia initiated a negotiation process with the NMED (SNL/NM March 2007) to determine the frequency of continued monitoring. In November 2008, DOE/Sandia received approval from NMED to discontinue quarterly monitoring and proceed with semiannual sampling for perchlorate at CYN-MW6 (NMED November 2008).

TABLE OF CONTENTS

1.0	Introduction.....	1
2.0	Scope of Activities.....	3
3.0	Regulatory Criteria.....	5
4.0	Monitoring Results.....	6
5.0	Summary and Conclusions	7
6.0	References.....	11

List of Figures

<u>Figure</u>	<u>Title</u>	
1	Sandia National Laboratories New Mexico Current Perchlorate-Screening Monitoring-Well Network (July, August, September 2009).....	2
2	Perchlorate-Concentrations ($\mu\text{g/L}$) over Time in CYN-MW6.....	12

List of Tables

<u>Table</u>	<u>Title</u>	
1	Current Perchlorate-Screening Monitoring-Well Network Third Quarter of CY2009 (July, August, and September 2009).....	3
2	Sample Details for Third Quarter of CY2009 Perchlorate Sampling	5
3	Summary of Perchlorate Screening Analytical Results for the Current Monitoring-Well Network, as of Third Quarter CY2009	8
4	Perchlorate Screening Groundwater Monitoring Field Water Quality Measurements, Third Quarter of CY2009	13

Appendices

Appendix A. Analytical Laboratory Certificates of Analysis for the Perchlorate Data

Appendix B. Data Validation Sample Findings Summary Sheets for the Perchlorate Data

Acronyms

AOP	Administrative Operating Procedures
ARCOC	analysis request and chain of custody
CME	Corrective Measures Evaluation
COA	certificates of analyses
CY	Calendar Year
CYN	Canyons (Burn Site)
DO	dissolved oxygen
DOE	Department of Energy
EPA	U.S. Environmental Protection Agency
FOP	Field Operating Procedure
GEL	General Engineering Laboratories
HQ	hazard quotient
LTES	Long Term Environmental Stewardship
LWDS	Liquid Waste Disposal System
MDL	method detection limit
MW	monitoring well
ND	non-detect
NMED	New Mexico Environment Department
NTU	Nephelometric Turbidity Units
ORP	oxidation-reduction potential
pH	potential of hydrogen
PQL	practical quantitation limits
QC	quality control
SAP	Standard Operating Procedures
SC	specific conductance
SNL/NM	Sandia National Laboratories, New Mexico
TA	Technical Area
µg/L	microgram per liter
W	well

1.0 Introduction


Section IV.B of the Compliance Order on Consent (the Order), between the New Mexico Environment Department (NMED), the U.S. Department of Energy (DOE), and Sandia Corporation (Sandia) for Sandia National Laboratories/New Mexico (SNL/NM), effective on April 29, 2004, stipulates that a select group of groundwater monitoring wells be sampled for perchlorate at SNL/NM (NMED April 2004). This report summarizes the perchlorate screening monitoring completed during the third quarter of Calendar Year 2009 (CY2009) (July, August, and September 2009) in response to the requirements of the Order. The outline of this report is based on the required elements of a "Periodic Monitoring Report" described in Section X.D. of the Order (NMED April 2004).

In November 2005, DOE/Sandia submitted a letter report on the status of perchlorate screening in groundwater at SNL/NM monitoring wells (SNL/NM November 2005). The purpose of that letter report was to summarize previous correspondence and sampling results, and to outline proposed future work to comply with NMED requirements for perchlorate screening in groundwater. Per the letter report, quarterly reports will be submitted for wells actively in the perchlorate-screening monitoring-well network. Based on NMED response (NMED January 2006), DOE/Sandia will submit each quarterly report within 90 days following the quarter that the data represent. In November 2008, DOE/Sandia received approval from NMED to proceed to semiannual reporting (NMED November 2008), and then upon further consideration NMED once more required quarterly reporting (NMED April 2009). This did not alter the previously negotiated frequency for CYN-MW6, an existing well that has been under the sampling and reporting requirements of the Order since the well was installed, which will remain at semiannual sampling and reporting.

This report is the fifteenth to be submitted since the November 2005 letter report; the previous reports were submitted Fourth Quarter of Calendar Year 2005 through the Second Quarter of Calendar Year 2009 (SNL/NM February 2006, SNL/NM June 2006, SNL/NM September 2006, SNL/NM December 2006, SNL/NM March 2007, SNL/NM June 2007, SNL/NM September 2007, SNL/NM December 2007, SNL/NM March 2008, SNL/NM June 2008, SNL/NM September 2008, SNL/NM December 2008, SNL/NM June 2009a, and SNL/NM September 2009).

Groundwater monitoring well CYN-MW6 (Figure 1) has now been sampled 13 times, LWDS-MW1 has been sampled two consecutive quarters; and TA1-W-06, TA1-W-08, TA2-W-01, and TA2-W-27 (Figure 1) have been sampled one quarter. The Order requires that new wells be sampled for perchlorate for a minimum of four quarters (NMED April 2004). Reporting will continue as long as a groundwater monitoring well remains in the perchlorate-screening monitoring well network unless negotiated otherwise with NMED. The April 30, 2009 NMED letter, required that monitoring well TA1-W-03 be sampled for perchlorate. However, a groundwater sample could not be collected from monitoring well TA1-W-03 due to unstable turbidity measurements. Two attempts were made to sample this well on July 16th and 24th, 2009. A total of 88 gallons was purged and turbidity measurements ranged from 5.30 Nephelometric Turbidity Units (NTU) to >1000 NTU. SNL/NM personnel have scheduled a borehole camera survey of this monitoring well to examine the physical condition of the well casing. If the well casing is still intact, TA1-W-03 will be redeveloped to remove the silt and clay material that produce the turbid water.

Figure 1. Sandia National Laboratories, New Mexico Current Perchlorate-Screening Monitoring-Well Network (July, August, and September 2009)

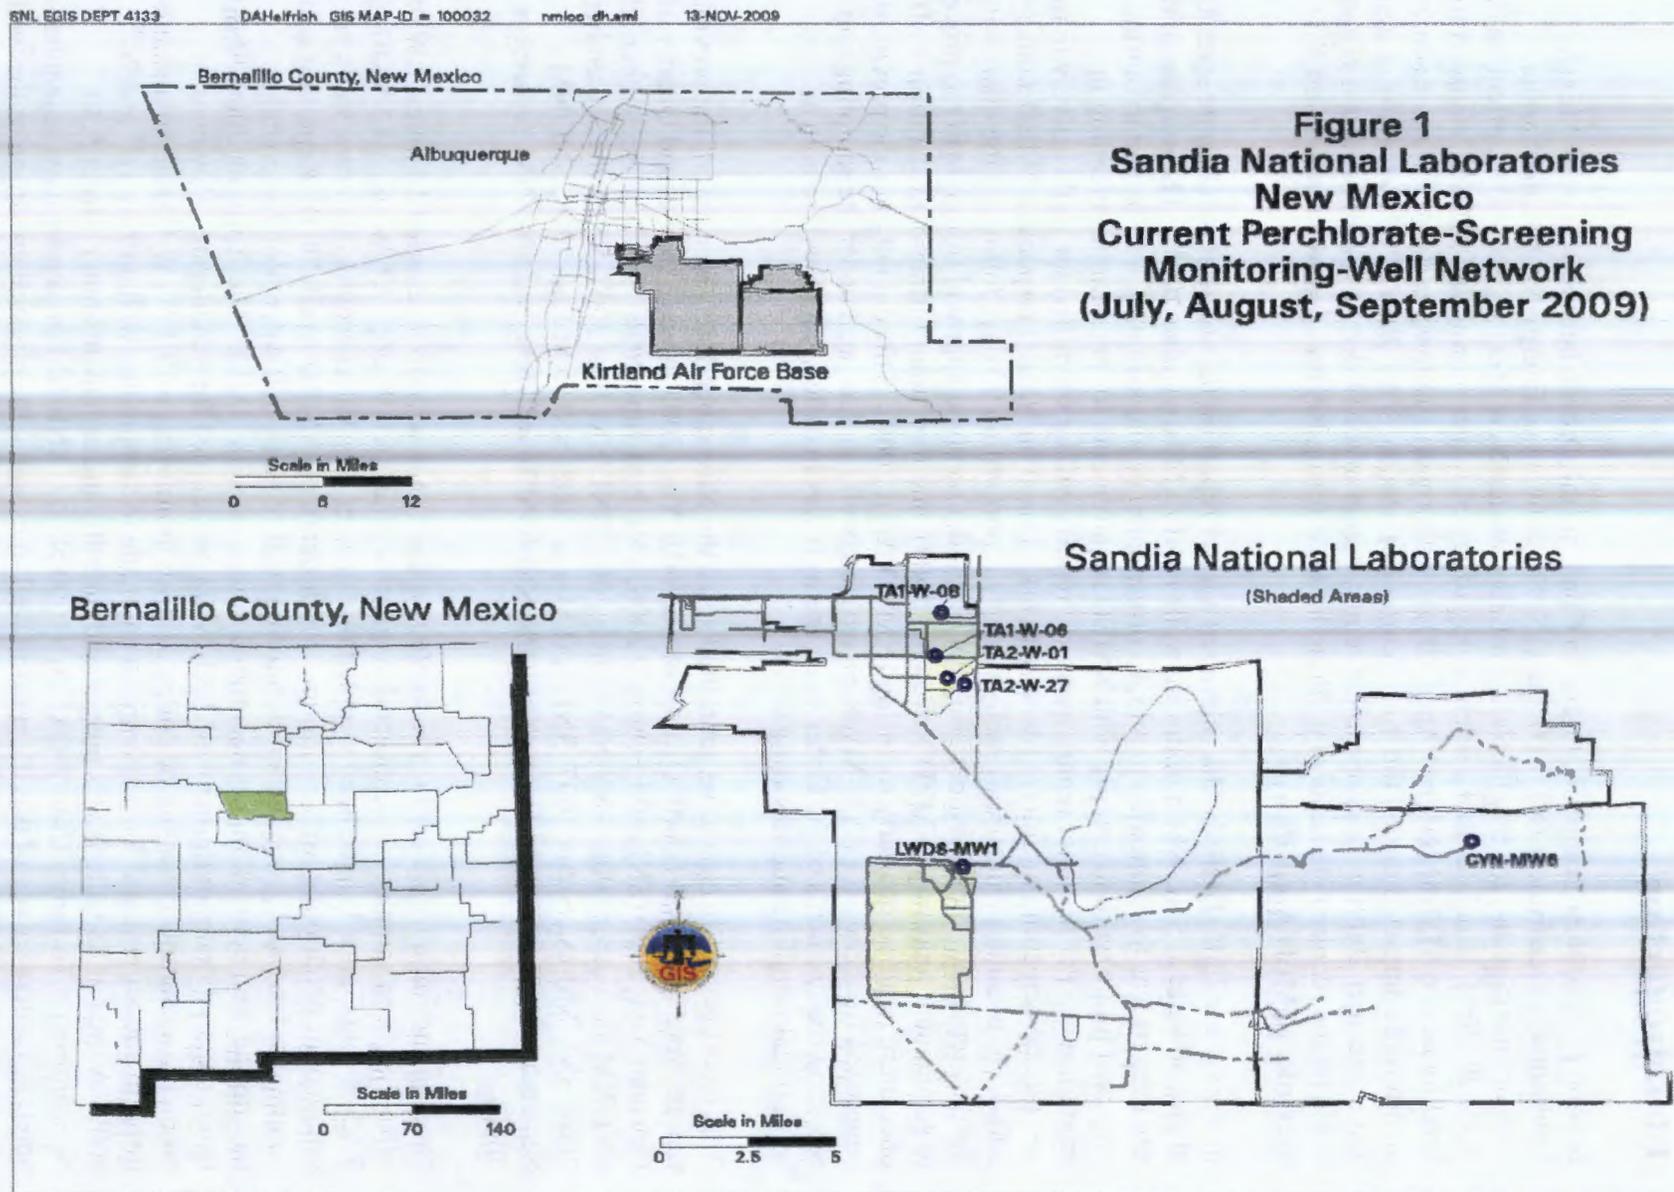

2.0 Scope of Activities

This report provides perchlorate screening results from the third quarter of CY2009 (July, August, and September 2009) for the wells currently active in the perchlorate screening program as shown on Figure 1 and listed in Table 1. It should be noted that CYN-MW6 is currently being sampled on a semi-annual basis and all other wells are being sampled quarterly. Per the requirements of Table XI-1 of the Order, a well with four consecutive quarters of non-detect results at the screening level/method detection limit (MDL) of 4 micrograms per liter ($\mu\text{g/L}$) is removed from the requirement of continued monitoring for perchlorate. Data from numerous wells identified in the Order have satisfied this requirement and, therefore, these wells have been removed from the perchlorate screening program. Data for these wells were provided in previous reports, and are not discussed in this current report. Wells discussed in previous perchlorate screening reports include: CYN-MW1D, CYN-MW5, CYN-MW7, CYN-MW8, MRN-2, MRN-3D, MWL-BW1, MWL-BW2, MWL-MW1, MWL-MW7, MWL-MW8, MWL-MW9, NWT3-MW2, and SWTA3-MW4.

Table 1
Current Perchlorate-Screening Monitoring-Well Network
Third Quarter of CY2009
(July, August, and September 2009)

Well	Date Sampled	Number of Consecutive Sampling Events ^a	Remaining Number of Sampling Events ^b	Sampling Method
CYN-MW6	30-SEP-2009	13	TBD ^c	Bennett™ Pump
LWDS-MW1	15-SEP-2009	2	2	Bennett™ Pump
TA1-W-06	21-JUL-2009	1	3	Bennett™ Pump
TA1-W-08	22-JUL-2009	1	3	Bennett™ Pump
TA2-W-01	30-JUL-2009	1	3	Bennett™ Pump
TA2-W-27	3-AUG-2009	1	3	Bennett™ Pump

Notes

^a Includes this sampling event.

^b Per the requirements of Table XI-1 of the Order (NMED April 2004) a well will be removed from the perchlorate-screening monitoring-well network after four quarters unless perchlorate is detected above the screening level/MDL of 4 $\mu\text{g/L}$. If perchlorate is detected above the screening level/MDL in a specific well, monitoring will continue at that well at a frequency negotiated with the NMED.

^c TBD = To be determined. This well has been sampled for the required initial four quarters. Because perchlorate concentrations in this well have exceeded the screening level, DOE/Sandia initiated the negotiation process with the NMED to determine further characterization requirements.

DOE/Sandia performed groundwater sampling at six wells on the dates listed in Table 1. CYN-MW6 was installed after the Order was finalized and was therefore required to be sampled for perchlorate as a "new" well; the other five wells were specifically required by NMED's April 2009 letter (NMED April 2009). Groundwater sampling activities were conducted in conformance with procedures outlined in the investigation-specific sampling and analysis plans (SAP) entitled:

- "Tijeras Arroyo Groundwater Investigation, Mini-SAP for FY09, 4th Quarter Sampling, July/August 2009" (SNL/NM June 2009b).
- "Burn Site Groundwater Monitoring, Mini-SAP for Fourth Quarter Fiscal Year 2009" (SNL/NM August 2009a); and
- "TA-V Groundwater Monitoring Mini-SAP for Fourth Quarter, Fiscal Year 2009" (SNL/NM August 2009b).

As described in the Mini-SAPs, groundwater sampling was performed in conformance with current Sandia Environmental Management, Long Term Environmental Stewardship (LTES) Project field operating procedures (FOPs). A portable BennettTM groundwater sampling system was used to collect the groundwater samples. The sampling pump and tubing bundle were decontaminated prior to installation into monitoring wells in accordance with procedures described in FOP 05-03, "LTES Groundwater Sampling Equipment Decontamination" (SNL/NM August 2007a). Wells TA1-W-06, TA1-W-08, TA2-W-01, and TA2-W-27 were purged a minimum of one saturated screen volume before sampling in conformance with FOP 05-01, "LTES Groundwater Monitoring Well Sampling and Field Analytical Measurements" (SNL/NM August 2007b). Wells CYN-MW6 and LWDS-MW1 are low-yield monitoring wells, and these wells were purged dry and allowed to recover before sampling to ensure the most representative groundwater sample possible.

Field water-quality measurements for turbidity, potential of hydrogen (pH), temperature, specific conductance (SC), oxidation-reduction potential (ORP), and dissolved oxygen (DO) were obtained from the well prior to collecting groundwater samples. Groundwater temperature, SC, ORP, DO, and pH were measured with a YSITM Model 620 Water Quality Meter. Turbidity was measured with a HACHTM Model 2100P turbidity meter. Purging continued until four stable measurements for turbidity, pH, temperature, and SC were obtained. Groundwater stability was considered acceptable when measurements were within 10 percent or less than 5 nephelometric turbidity units for turbidity, 0.1 pH units, 1.0 degree Celsius, and SC within 5 percent. Field Measurement Logs documenting details of well purging and water quality measurements were submitted to the Sandia Customer-Funded Records Center.

The groundwater samples were submitted to General Engineering Laboratories (GEL) for chemical analysis for perchlorate using U.S. Environmental Protection Agency (EPA) Method 314.0 (EPA November 1999). The sample identification, Analysis Request/Chain-of-Custody (ARCO) form number, and the sample shipment date are provided in Table 2. The analytical report from GEL, including certificates of analyses (COA) (Appendix A), analytical methods, MDLs, practical quantitation limits (PQLs), dates of analyses, results of quality control (QC) analyses, and data validation findings (Appendix B) have been submitted to the Sandia Customer-Funded Records Center.

Table 2
Sample Details for the Third Quarter of CY2009 Perchlorate Sampling

Well	Sample Identification	ARCOG Number	Date Shipped
CYN-MW6	087734-020 087735-020	612392	30-SEP-09
LWDS-MW1	087662-020 087663-020	612368	15-SEP-09
TA1-W-06	087550-020 087551-020	612301	21-JUL-09
TA1-W-08	087553-020	612302	22-JUL-09
TA2-W-01	087562-020	612306	30-JUL-09
TA2-W-27	087566-020 087567-020	612308	03-AUG-09

Notes

ARCOG = Analysis request and chain of custody.

3.0 Regulatory Criteria

In a given monitoring well, four consecutive non-detects (NDs) using the screening level/MDL of 4 µg/L are considered by the NMED to be evidence of the absence of perchlorate, such that additional monitoring for perchlorate in that well is not required. If perchlorate is detected using the screening level/MDL of 4 µg/L in a specific well, monitoring will continue at that well at a frequency negotiated with the NMED. The Order (NMED April 2004) also requires that for detections equal to or greater than 4 µg/L, the DOE/Sandia will evaluate the nature and extent of perchlorate contamination, based on a screening level/MDL of 4 µg/L, and requires that the results of this evaluation be incorporated into a Corrective Measures Evaluation (CME). Section VII.C of the Order clarifies that the CME process will be initiated where there was a release to the environment and where corrective measures are necessary to protect human health or the environment.

In March 2007, DOE/Sandia received a letter from the NMED stating the requirement that DOE/Sandia “determine the nature and extent of the contamination and complete a Corrective Measures Evaluation for the perchlorate-impacted groundwater in the vicinity of CYN-MW6” (NMED March 2007). As this was based solely on the four quarters of monitoring results, DOE/Sandia submitted a letter to the NMED in April 2007 (SNL/NM April 2007) which recommended further characterization through continued quarterly monitoring of CYN-MW6 for four additional quarters, ending in December 2007, to assure appropriate characterization of this

well. In January 2008, DOE/Sandia requested a meeting with NMED to discuss the need for continued monitoring or additional characterization work, and potentially, a CME.

In preparation of discussing the perchlorate-impacted groundwater in the vicinity of CYN-MW6 and to show that the requirement "to determine the nature and extent of contamination" (NMED March 2007) has been met, DOE/Sandia provided supporting information to the NMED (SNL/NM March 2008). Perchlorate in surface soils has been characterized at Solid Waste Management Units (SWMUs) in the study area (SNL/NM June 2006; SNL/NM March 2008--Appendix C). Based upon these data, DOE/Sandia believe the nature and extent of perchlorate in groundwater at the Burn Site has been sufficiently characterized. Since 2004, four other monitoring wells in the vicinity of the Burn Site have been sampled and analyzed for perchlorate, including CYN-MW1D, CYN-MW5, CYN-MW7, and CYN-MW8. All of these wells were sampled for four quarters and all results were non-detect for perchlorate (SNL/NM March 2008--Appendix D).

Per the requirements of Section VI.K.1.b of the Order (NMED April 2004), a human health risk assessment has been performed to evaluate the potential for adverse health effects from the concentrations of perchlorate detected in CYN-MW6 groundwater. The maximum concentration of perchlorate in CYN-MW6 to date (8.93 $\mu\text{g/L}$) was used in the assessment. The calculated hazard quotient (HQ) of 0.35 is less than the NMED target level of a Hazard Index (the sum of all HQs) of 1.0 (NMED June 2006) (SNL/NM March 2008--Appendix E).

Because perchlorate concentrations in monitoring well CYN-MW6 have exceeded the screening level, DOE/Sandia initiated a negotiation process with the NMED (SNL/NM March 2007) to determine the frequency of continued monitoring. In November 2008, DOE/Sandia received approval from NMED to proceed with semi-annual monitoring of perchlorate in CYN-MW6 and proceed with semiannual reporting of all perchlorate results (NMED November 2008). Upon further consideration, NMED once more required that DOE/Sandia resume quarterly reporting of perchlorate results with the exception of CYN-MW6 (NMED April 2009).

In April 2009, DOE/Sandia received a letter from the NMED requiring DOE/Sandia to characterize the nature and extent of the perchlorate contamination in soils and groundwater in the Burn Site Groundwater study area (NMED April 2009). A characterization work plan is currently being prepared for submittal to the NMED. The NMED has also requested that DOE/Sandia monitor perchlorate concentrations for a minimum of four quarters at several Tijeras Arroyo Groundwater and Technical Area-V monitoring wells, including TA1-W-03, TA1-W-06, TA1-W-08, TA2-W-01, TA2-W-27, and LWDS-MW1 (NMED April 2009).

4.0 Monitoring Results

Table 3 summarizes current and historical perchlorate results for wells currently in the perchlorate monitoring network. The analytical laboratory COA for the third quarter of CY2009 perchlorate data is included as Appendix A. Perchlorate was not detected above the screening level in LWDS-MW1, TA1-W-06, TA1-W-08, TA2-W-01, or TA2-W-27. Consistent with historical analytical results, perchlorate was detected above the screening level/MDL in the third quarter of CY2009 in CYN-MW6. As shown in Figure 2, the concentrations of perchlorate found in CYN-MW6 in September 2009 (4.12 and 4.71 $\mu\text{g/L}$) is significantly less than concentrations from previous quarters (for example,

SNL/NM June 2009a). These low concentrations for the CYN-MW6 environmental and duplicate sample values were qualified as an estimated quantity with a suspected negative bias (“J-“) because the matrix spike recovered beyond established acceptance criteria, due to matrix interference. The hydrograph of CYN-MW6 is provided at the end of this Section.

Table 4 summarizes field water quality measurements collected immediately before the analytical sample was collected. Field water quality measurements include turbidity, pH, temperature, SC, ORP, and DO.

The analytical data were reviewed and qualified in accordance with AOP 00-03 Revision 2, “Data Validation Procedure for Chemical and Radiochemical Data” (SNL/NM July 2007). Although validation qualifiers were assigned to several of the analytical results, no problems were identified with the analytical data that resulted in the qualification of the data as unusable. The data are acceptable and reported quality control measures are adequate. The data validation sample findings summary sheets for the perchlorate data are included as Appendix B.

There was one variance from requirements set forth in the Tijeras Arroyo Groundwater Investigation Mini-SAP (SNL/NM June 2009b): no groundwater sample was collected from monitoring well TA1-W-03 due to unstable turbidity measurements during pre-sampling purging. No other variances or nonconformances in field activities or field conditions from requirements in the groundwater monitoring mini-SAPs (SNL/NM June 2009b, August 2009a, and August 2009b) were identified during the third quarter of CY2009 sampling activities.

5.0 Summary and Conclusions

Based on the analytical data presented in Table 3 and in previous reports, the following statements can be made:

- No perchlorate was detected in the environmental sample from groundwater monitoring wells LWDS-MW1, TA1-W-06, TA1-W-08, TA2-W-01, or TA2-W-27 at a screening level/MDL of 4 µg/L.
- Since June 2004 (the start of sampling required by the Order), perchlorate has only been detected above the screening level/MDL (4 µg/L) in one of the wells (CYN-MW6) in the perchlorate-screening monitoring-well network.
- The analytical results from CYN-MW6 for the third quarter of CY2009 sampling event (4.12 and 4.71 µg/L) is significantly less than concentrations reported since the inception of sampling for perchlorate at CYN-MW6 in March 2006 (Figure 2). These lower concentrations are attributed to matrix interference.
- A human health risk assessment has been performed to evaluate the potential for adverse health effects from the concentrations of perchlorate detected in CYN-MW6 groundwater. The maximum concentration of perchlorate in CYN-MW6 to date (8.93 µg/L) was used in the assessment. The calculated HQ of 0.35 is less than the NMED target level of a Hazard Index (the sum of all HQs) of 1.0 (NMED June 2006 and SNL/NM March 2008).

Table 3
Summary of Perchlorate Screening Analytical Results for the
Current Monitoring-Well Network, as of Third Quarter CY2009.

Well ID	Sample Date	ARCOC No.	Sample No.	Perchlorate Result ^a (µg/L)	MDL ^b (µg/L)	PQL ^c (µg/L)	MCL ^d (µg/L)	Laboratory Qualifier ^e	Validation Qualifier ^f	Analytical Method ^g	Comments
CYN-MW6	23-Mar-06	609578	075985-020	6.92	4.0	12	NE	J		EPA 314.0	
			075986-020	7.44	4.0	12	NE	J		EPA 314.0	Duplicate sample
			075985-R20	6.39	0.50	2.0	NE	Hh	HT, J	EPA 6850M	Verification/Re-analysis
			075986-R20	6.48	0.50	2.0	NE	Hh	HT, J	EPA 6850M	Verification/Re-analysis
	22-Jun-06	609929	078687-020	6.63	4.0	12	NE	J		EPA 314.0	
			078688-020	6.45	4.0	12	NE	J		EPA 314.0	Duplicate sample
			078687-021	6.99	1.0	4.0	NE			EPA 6850M	Verification
			078688-021	6.92	1.0	4.0	NE			EPA 6850M	Verification/Duplicate Sample
	20-Sep-06	610652	081626-020	7.52	4.0	12	NE	J		EPA 314.0	
			081626-R20	6.96	1.0	4.0	NE		P2	EPA 6850M	Verification/Re-analysis
	15-Dec-06	611057	083858-020	8.46	4.0	12	NE	J		EPA 314.0	
			083859-020	8.93	4.0	12	NE	J		EPA 314.0	Duplicate sample
	14-Mar-07	611200	084237-020	8.12	4.0	12	NE	J		EPA 314.0	
	27-Jun-07	611399	084833-020	6.57	4.0	12	NE	J	J-, X1	EPA 314.0	
			084833-R20	5.94	0.5	2.0	NE			EPA 6850M	Verification/Re-analysis
	12-Sep-07	611581	085249-020	7.74	4.0	12	NE	J		EPA 314.0	
			085249-R20	6.46	0.5	2.0	NE	Hh	J	EPA 6850M	Verification/Re-analysis
	18-Dec-07	611668	085446-020	6.20	4.0	12	NE	J		EPA 314.0	
			085447-020	6.56	4.0	12	NE	J		EPA 314.0	Duplicate sample
	10-Mar-08	611749	085661-020	7.25	4.0	12	NE	J		EPA 314.0	
23-Jun-08	611912	086280-020	6.67	4.0	12	NE	J		EPA 314.0		
17-Sep-08	612004	086782-020	6.85	4.0	12	NE	J		EPA 314.0		
02-Mar-09	612120	087047-020	7.24	4.0	12	NE	J		EPA 314.0		
30-Sep-09	612392	087734-020	4.12	4.0	12	NE	J	J-	EPA 314.0		
		087735-020	4.71	4.0	12	NE	J	J-	EPA 314.0	Duplicate sample	

Refer to notes at the bottom of table.

Table 3 (continued)
Summary of Perchlorate Screening Analytical Results for the
Current Monitoring-Well Network, as of Third Quarter CY2009.

Well ID	Sample Date	ARCO No.	Sample No.	Perchlorate Result ^a (µg/L)	MDL ^b (µg/L)	PQL ^c (µg/L)	MCL ^d (µg/L)	Laboratory Qualifier ^e	Validation Qualifier ^f	Analytical Method ^g	Comments
LWDS-MW1	10-Jun-09	612210	087464-020	ND	4.0	12	NE	U		EPA 314.0	
	15-Sep-09	612368	087662-020	ND	4.0	12	NE	HU	UJ	EPA 314.0	
			087663-020	ND	4.0	12	NE	HU	UJ	EPA 314.0	Duplicate sample
TA1-W-06	21-Jul-09	612301	087550-020	ND	4.0	12	NE	U		EPA 314.0	
			087551-020	ND	4.0	12	NE	U		EPA 314.0	Duplicate sample
TA1-W-08	22-Jul-09	612302	087553-020	ND	4.0	12	NE	U		EPA 314.0	
TA2-W-01	30-Jul-09	612306	087562-020	ND	4.0	12	NE	U		EPA 314.0	
TA2-W-27	03-Aug-09	612308	087566-020	ND	4.0	12	NE	U		EPA 314.0	
			087567-020	ND	4.0	12	NE	U		EPA 314.0	Duplicate sample

Notes

^aResult

Values in **bold** exceed the screening level/MDL.

ND not detected (at method detection limit).

µg/L micrograms per liter.

^bMDL

Method detection limit. The minimum concentration that can be measured and reported with 99% confidence that the analyte is greater than zero, analyte is matrix specific.

^cPQL

Practical quantitation limit. The lowest concentration of analytes in a sample that can be reliably determined within specified limits of precision and accuracy by that indicated method under routine laboratory operating conditions.

^dMCL

Maximum contaminant level. Established by the U.S. Environmental Protection Agency Primary Water Regulations [40 CFR 141.11(b)], and subsequent amendments or the New Mexico Environmental Improvement Board in Title 20, Chapter 7, Part 1 of the New Mexico Administrative Code (20MAC 7.1).

NE = Not established.

^eLab Qualifier

H = Analytical holding time was exceeded.

h = Prep holding time was exceeded.

J = Amount detected is below the practical quantitation limit.

U = Analyte is absent or below the method detection limit.

Table 3 (concluded)
Summary of Perchlorate Screening Analytical Results for the
Current Monitoring-Well Network, as of Third Quarter CY2009.

Notes (continued)

⁶Validation Qualifier

If cell is blank, then all quality control samples meet acceptance criteria with respect to submitted samples and no qualifier was assigned.

HT = The holding time was exceeded for the associated sample analysis.

J = The associated value is an estimated quantity.

J- = The associated value is an estimated quantity with a suspected negative bias.

P2 = Insufficient quality control data to determine laboratory precision.

UJ = Analyte is absent or below the method detection limit and the associated quantitation limits (MDL and PQL) may be inaccurate or imprecise because the analysis was performed outside method specific hold time requirements.

X1 = General data quality is suspect.

⁹Analytical Method

EPA 314.0: U.S. Environmental Protection Agency, November 1999, "Perchlorate in Drinking Water Using Ion Chromatography," EPA 815/R-00-014 (EPA November 1999).

EPA 6850M: U.S. Environmental Protection Agency, April 2005, "Perchlorate in Water, Soils, and Solids Using High Performance Liquid Chromatography/Electrospray Ionization/Mass Spectrometry (HPLC/ESI/MS)," draft, Method 6850 (EPA April 2005).

DOE/Sandia will continue semiannual monitoring of perchlorate in CYN-MW6 and quarterly monitoring of perchlorate in LWDS-MW1, TA1-W-06, TA1-W-08, TA2-W-01, and TA2-W-27. If the borehole camera survey of TA1-W-03 shows that there is no problem with the physical condition of the well casing, the well will be redeveloped to remove the silt and clay material causing the high turbidity. After redevelopment TA1-W-03 will be added to the perchlorate screening well network and will be sampled a minimum of four consecutive quarters.

Based on recent requirements (NMED April 2009), DOE/Sandia will prepare a work plan for submittal to the NMED that describes efforts to characterize the nature and extent of the perchlorate contamination in soils and groundwater in the Burn Site Groundwater study area.

6.0 References

EPA (see US Environmental Protection Agency).

New Mexico Environment Department (NMED) April 2004. "Compliance Order on Consent Pursuant to the New Mexico Hazardous Waste Act 74-4-10: Sandia National Laboratories Consent Order," New Mexico Environment Department, April 24, 2004.

New Mexico Environment Department (NMED) January 2006. "RE: Monitoring Groundwater for Perchlorate, Report of November 22, 2005. Sandia National Laboratories EPA ID# NM5890110518." Letter to Patty Wagner (SSO/NNSA) and Peter Davies (SNL/NM) from James Bearzi. January 27, 2006.

New Mexico Environment Department (NMED) June 2006. "Technical Background Document for Development of Soil Screening Levels, Revision 4.0," New Mexico Environment Department, Hazardous Waste Bureau and Ground Water Quality Bureau Voluntary Remediation Program, Santa Fe, New Mexico. (NMED 2006, 092513). June 2006.

New Mexico Environment Department (NMED) March 2007. "RE: Notice of Approval: Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2006 (April, May, and June) September 20, 2006. Sandia National Laboratories, EPA ID# NM5890110518. HWB-SNL-06-011" Letter to Patty Wagner (SSO/NNSA) and Peter Davies (SNL/NM) from James Bearzi. March 23, 2007.

New Mexico Environment Department (NMED) November 2008. "RE: Perchlorate Issues" Personal Communication (electronic mail) to John Cochran (SNL/NM) from Sid Brandwein (NMED/HWB). November 07, 2008.

Figure 2
Perchlorate Concentrations ($\mu\text{g/L}$) over Time in CYN-MW6

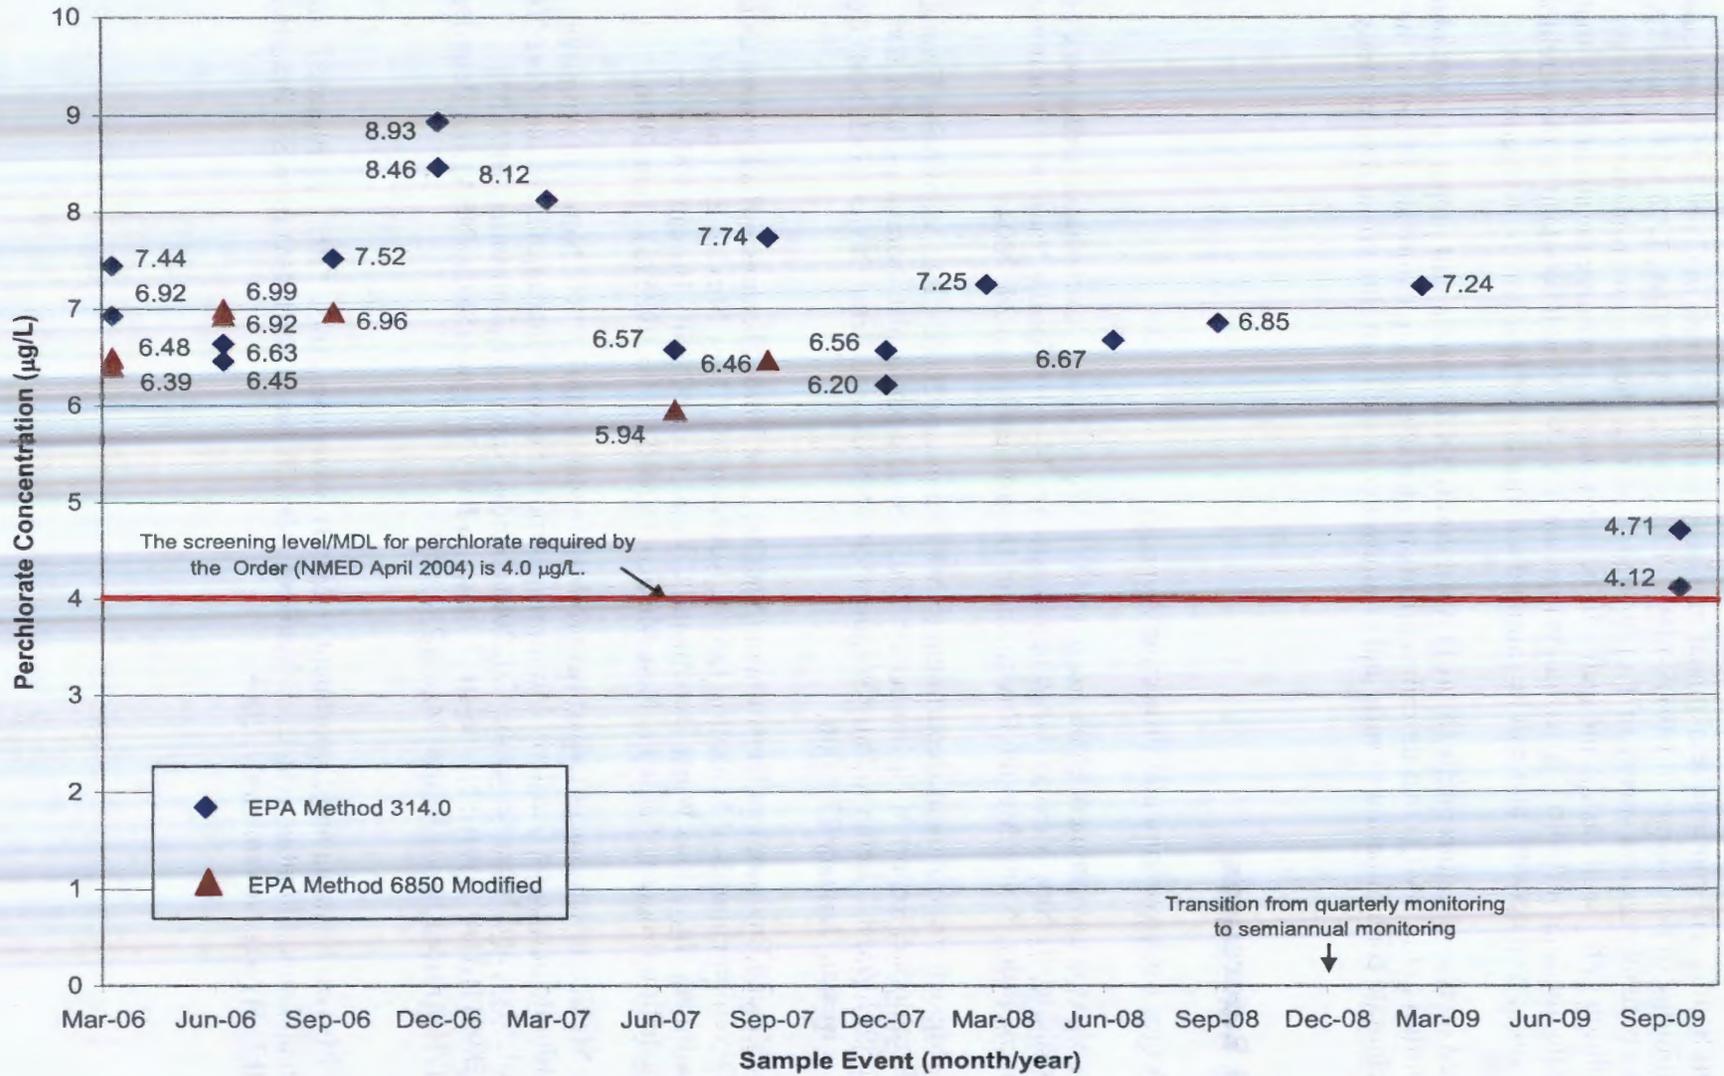


Table 4
Perchlorate Screening Groundwater Monitoring
Field Water Quality Measurements^a, Third Quarter of CY2009

Well ID	Sample Date	Temperature (°C)	Specific Conductivity (µmho/cm)	Oxidation Reduction Potential (mV)	pH	Turbidity (NTU)	Dissolved Oxygen (% Sat)	Dissolved Oxygen (mg/L)
CYN-MW6	30-Sep-09	16.37	1236	151.0	6.99	1.24	24.0	2.34
LWDS-MW1	15-Sep-09	20.23	799	380.0	7.55	0.36	80.7	7.28
TA1-W-06	21-Jul-09	21.98	937	202.8	7.56	0.36	82.7	7.20
TA1-W-08	22-Jul-09	20.54	2072	203.8	7.39	0.78	82.8	7.41
TA2-W-01	30-Jul-09	20.97	687	223.7	7.65	0.40	79.2	7.04
TA2-W-27	03-Aug-09	23.24	909	199.5	7.53	0.36	89.6	7.61

Notes

^a Field measurements made immediately before the groundwater sample was collected.
°C degrees Celsius.
% Sat percent saturation.
µmho/cm micromhos per centimeter.
mg/L milligrams per liter.
mV millivolts.
NTU nephelometric turbidity units.
pH potential of hydrogen (negative logarithm of the hydrogen ion concentration).

New Mexico Environment Department (NMED) April 2009. RE: Perchlorate Contamination in Groundwater, Sandia National Laboratories, EPA ID# NM5890110518." Letter to Kimberly Davis (SSO/NNSA) and Francis Nimick (SNL/NM) from James Bearzi. April 30, 2009.

Sandia National Laboratories, New Mexico (SNL/NM) November 2005. To James Bearzi (NMED), "Letter Report on the Status of Perchlorate Screening in Groundwater at Sandia Monitoring Wells" Sandia National Laboratories, New Mexico Environmental Restoration Project. November 22, 2005.

Sandia National Laboratories, New Mexico (SNL/NM) February 2006. "Perchlorate Screening Quarterly Monitoring Report, Fourth Quarter of Calendar Year 2005 (October, November, and December 2005)". Sandia National Laboratories, New Mexico Environmental Restoration Project. February 24, 2006.

Sandia National Laboratories, New Mexico (SNL/NM) June 2006. "Perchlorate Screening Quarterly Monitoring Report, First Quarter of Calendar Year 2006 (January, February, and March 2006)". Sandia National Laboratories, New Mexico Environmental Restoration Project. June 7, 2006.

Sandia National Laboratories, New Mexico (SNL/NM) September 2006. "Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2006 (April, May, and June 2006)". Sandia National Laboratories, New Mexico Environmental Restoration Project. September 20, 2006.

Sandia National Laboratories, New Mexico (SNL/NM) December 2006. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Third Quarter of Calendar Year 2006 (July, August, and September 2006)". Sandia National Laboratories, New Mexico Environmental Restoration Project. December 2006.

Sandia National Laboratories, New Mexico (SNL/NM) March 2007. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Fourth Quarter of Calendar Year 2006 (October, November, and December 2006)". Sandia National Laboratories, New Mexico Environmental Restoration Project. March 27, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) April 2007. Response to March 23, 2007 NMED letter entitled "RE: Notice of Approval: Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2006 (April, May, and June) September 20, 2006. Sandia National Laboratories, EPA ID# NM5890110518. HWB-SNL-06-011". Letter to James Bearzi (NMED HWB) from Patty Wagner (SSO/NNSA). Sandia National Laboratories, New Mexico Environmental Restoration Project. April 19, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) June 2007. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, First Quarter of Calendar Year 2007 (January, February, and March 2007)". Sandia National Laboratories, New Mexico Environmental Restoration Project. June 27, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) July 2007. Sandia Administrative Operating Procedure 00-03, Revision 2, "Data Validation Procedure for Chemical and Radiochemical Data." Sandia National Laboratories, New Mexico Sample Management Office. July 16, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) August 2007a. Sandia Field Operating Procedure 05-03, Revision 02 "LTES Groundwater Sampling Equipment Decontamination," Sandia National Laboratories, New Mexico Long Term Environmental Stewardship, Environmental Management Department. August 16, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) August 2007b. Sandia Field Operating Procedure 05-01, Revision 02 "LTES Groundwater Monitoring Well Sampling and Field Analytical Measurements," Sandia National Laboratories, New Mexico Long Term Environmental Stewardship, Environmental Management Department. August 16, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) September 2007. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2007 (April, May, and June 2007)". Sandia National Laboratories, New Mexico Environmental Restoration Project. September 26, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) December 2007. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Third Quarter of Calendar Year 2007 (July, August, and September 2007)". Sandia National Laboratories, New Mexico Environmental Restoration Project. December 27, 2007.

Sandia National Laboratories, New Mexico (SNL/NM) March 2008. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Fourth Quarter of Calendar Year 2007 (October, November, and December 2007)". Sandia National Laboratories, New Mexico Environmental Restoration Project. March 26, 2008.

Sandia National Laboratories, New Mexico (SNL/NM) June 2008. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, First Quarter of Calendar Year 2008 (January, February, and March 2008)". Sandia National Laboratories, New Mexico Environmental Restoration Project. June 27, 2008.

Sandia National Laboratories, New Mexico (SNL/NM) September 2008. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2008 (April, May, and June 2008)". Sandia National Laboratories, New Mexico Environmental Restoration Project. September 23, 2008.

Sandia National Laboratories, New Mexico (SNL/NM) December 2008. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Third Quarter of Calendar Year 2008 (July, August, and September 2008)". Sandia National Laboratories, New Mexico Environmental Restoration Project. December 22, 2008.

Sandia National Laboratories, New Mexico (SNL/NM) June 2009a. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Fourth Quarter of Calendar Year 2008 and First Quarter of Calendar Year 2009 (October 2008 through March

2009)". Sandia National Laboratories, New Mexico Environmental Restoration Project. June 18, 2009.

Sandia National Laboratories, New Mexico (SNL/NM) June 2009b. "Tijeras Arroyo Groundwater Investigation, Mini-Sampling and Analysis Plan (SAP) for FY09, 4th Quarter Sampling, July/August 2009". Sandia National Laboratories, New Mexico Environmental Restoration Project. June 24, 2009.

Sandia National Laboratories, New Mexico (SNL/NM) August 2009a. "Burn Site Groundwater Monitoring, Mini-Sampling and Analysis Plan (SAP) for Fourth Quarter Fiscal Year 2009". Sandia National Laboratories, New Mexico Environmental Restoration Project. August 25, 2009.


Sandia National Laboratories, New Mexico (SNL/NM) August 2009b. "TA-V Groundwater Monitoring, Mini-Sampling and Analysis Plan (SAP) for Fourth Quarter, Fiscal Year 2009". Sandia National Laboratories, New Mexico Environmental Restoration Project. August 3, 2009.

Sandia National Laboratories, New Mexico (SNL/NM) September 2009. "Consolidated Quarterly Report, Section III: Perchlorate Screening Quarterly Monitoring Report, Second Quarter of Calendar Year 2009 (April 2009 through June 2009)". Sandia National Laboratories, New Mexico Environmental Restoration Project. September 30, 2009.

U.S. Environmental Protection Agency (EPA) November 1999, "Perchlorate in Drinking Water Using Ion Chromatography," EPA 815/R-00-014. November 1999.

U.S. Environmental Protection Agency (EPA) April 2005, "Perchlorate in Water, Soils, and Solids Using High Performance Liquid Chromatography/Electrospray Ionization/Mass Spectrometry (HPLC/ESI/MS)," Draft, Method 6850. April 2005.

Groundwater Elevations Over Time at CYN-MW6

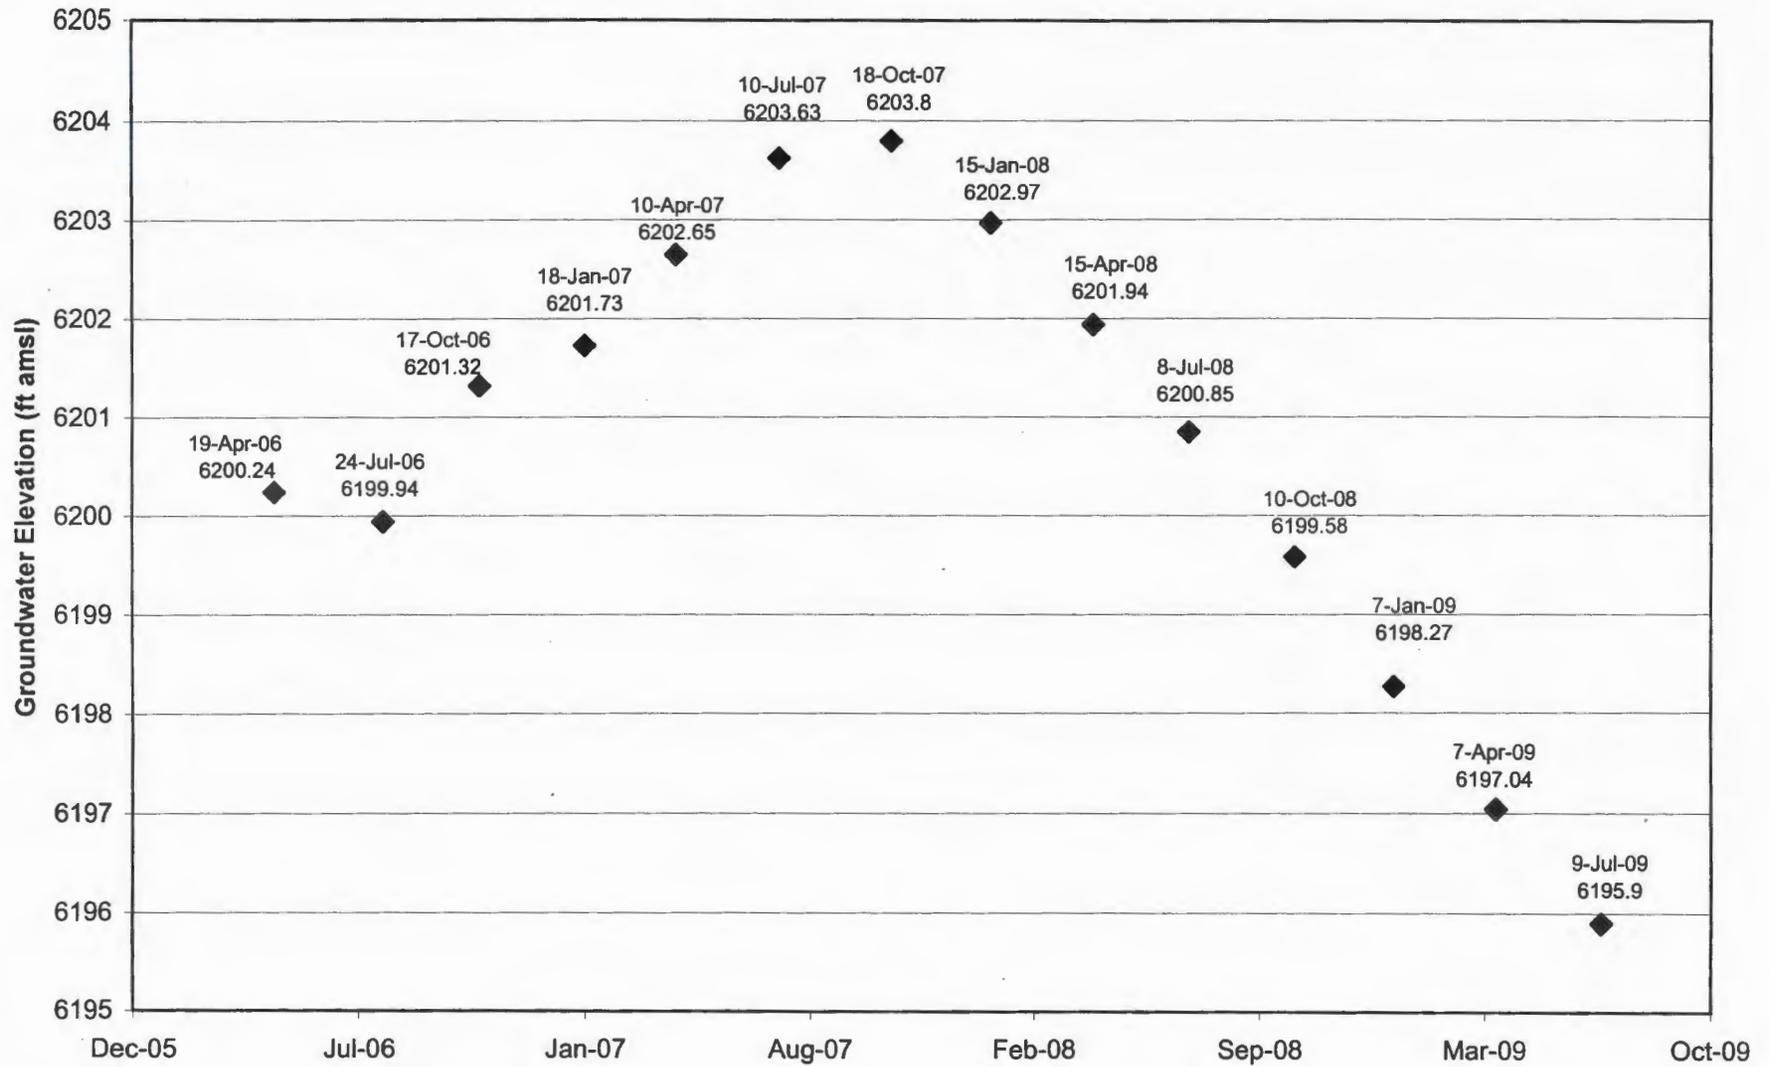

Appendix A

Analytical Laboratory Certificates of Analysis for the Perchlorate Data

CONTRACT LABORATORY ANALYSIS REQUEST AND CHAIN OF CUSTODY

Internal Lab

Batch No. <i>N/A</i>		SMO Use		AR/COC		612301	
Dept. No./Mail Stop: 4133/1089	Date Samples Shipped: <i>7/21/09</i>	Project/Task No. 125778.10.11.01		<input type="checkbox"/> Waste Characterization -Send preliminary/copy report to:			
Project/Task Manager: Don Schofield	Carrier/Waybill No. <i>103651</i>	SMO Authorization: <i>Pat G. SMO</i>		<input type="checkbox"/> Released by COC No.:			
Project Name: TAG-GWM	Lab Contact: Edie Ken/803-556-8171	Contract #: 691436		<input checked="" type="checkbox"/> Validation Required			
Record Center Code: ER/1306/DAT	Lab Destination: GEL	<i>SUB BOTTLE ORDER</i>		Bill To: Sandia National Labs (Accounts Payable)			
Logbook Ref. No.: NA	SMO Contact/Phone: Pam Puissant/505-844-3185			P.O. Box 5800 MS 0154 Albuquerque, NM 87185-0154 <i>2337466</i>			
Service Order No. CFO# 010-09	Send Report to SMO: Lorraine Herrera /505-844-3199			Parameter & Method Requested			

Location	Tech Area	Reference LOV (available at SMO)									
Building	Room										

Sample No.-Fraction	ER Sample ID or Sample Location Detail	Depth (ft)	ER Site No.	Date/Time (hr) Collected	Sample Matrix	Container		Preservative	Collection Method	Sample Type	Parameter & Method Requested	Lab Sample ID
						Type	Volume					
087550-001	TA1-W-06	319	NA	072109/0931	GW	G	3x40 ml	HCL	G	SA	VOC (SW846-8260B)	026 .15
087550-009	TA1-W-06	319	NA	072109/0933	GW	P	500 ml	HNO3	G	SA	TAL Metals+total Ur(SW846-6020/7470)	027 .16
087550-016	TA1-W-06	319	NA	072109/0935	GW	P	250 ml	4C	G	SA	Major Anions (SW846-9056)	028 .17
087550-018	TA1-W-06	319	NA	072109/0934	GW	P	250 ml	H2SO4	G	SA	NPN (353.2)	029 .18
087550-020	TA1-W-06	319	NA	072109/0936	GW	P	250 ml	4C	G	SA	Perchlorate (314.0)	030 .19
087550-033	TA1-W-06	319	NA	072109/0937	GW	P	1 L	HNO3	G	SA	Gamma Spec (short list)(901.0)	031 .20
087550-034	TA1-W-06	319	NA	072109/0938	GW	P	1 L	HNO3	G	SA	Gross Alpha/Beta (900.0)	032 .21
087550-036	TA1-W-06	319	NA	072109/0939	GW	AG	250 ml	4C	G	SA	Tritium (906.0)	033 .22
087551-001	TA1-W-06	319	NA	072109/0931	GW	G	3x40 ml	HCL	G	DU	VOC (SW846-8260B) <i>DOC</i>	034 .15
087551-018	TA1-W-06	319	NA	072109/0934	GW	P	250 ml	H2SO4	G	DU	NPN (353.2) <i>DOC</i>	035 .18
087551-020	TA1-W-06	319	NA	072109/0936	GW	P	250 ml	4C	G	DU	Perchlorate (314.0) <i>DOC</i>	036 .19

RMMA <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No		Ref. No.	Sample Tracking		Smo Use	Special Instructions/QC Requirements		Abnormal Conditions on Receipt Lab Use
Sample Disposal <input type="checkbox"/> Return to Client <input checked="" type="checkbox"/> Disposal by lab			Date Entered (mm/dd/yy)			EDD <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No		
Turnaround Time <input type="checkbox"/> 7 Day <input type="checkbox"/> 15 Day <input checked="" type="checkbox"/> 30 Day			Entered by:			Level D Package <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No		
Return Samples By: <input type="checkbox"/> Negotiated TAT <input type="checkbox"/> QC inits.						*Send report to: Tim Jackson/ORG. 4133/MS. 1089/ 284-2547		
Sample Team Members	Name	Signature	Init	Company/Organization/Phone/Cellular				
	Robert Lynch	<i>[Signature]</i>	RL	Weston/4133/844-4013/250-7090				
	William J. Gibson	<i>[Signature]</i>	WJG	Weston/4133/844-4013/239-7367		Major Anions/Br, Cl, F, I, SO4		
						*Please list as separate report.		

1. Relinquished by <i>[Signature]</i> Org. 4133 Date <i>7/21/09</i> Time <i>1000</i>	4. Relinquished by	Org.	Date	Time
1. Received by <i>[Signature]</i> Org. 4133 Date <i>7/21/09</i> Time <i>1000</i>	4. Received by	Org.	Date	Time
2. Relinquished by <i>[Signature]</i> Org. 4133 Date <i>7/21/09</i> Time <i>1215</i>	5. Relinquished by	Org.	Date	Time
2. Received by <i>[Signature]</i> Org. GEL Date <i>7-21-09</i> Time <i>0740</i>	5. Received by	Org.	Date	Time
3. Relinquished by	6. Relinquished by	Org.	Date	Time
3. Received by	6. Received by	Org.	Date	Time

10

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
1515 Eubank SE
Albuquerque, New Mexico 87123
Contact: Ms. Pamela M. Puissant
Project: **Level C, Groundwater Monitoring**

Report Date: August 14, 2009

Client Sample ID: 087550-020
Sample ID: 233746030
Matrix: AQUEOUS
Collect Date: 21-JUL-09 09:36
Receive Date: 22-JUL-09
Collector: Client

Project: SNLSGWater
Client ID: SNLS003
Client Desc.: TA1-W-06
Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108/04/09	2232	888074	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

CONTRACT LABORATORY ANALYSIS REQUEST AND CHAIN OF CUSTODY

Internal Lab

Batch No. <u>N/A</u>		SMO Use		AR/COC		612302						
Dept. No./Mail Stop: 4133/1089		Date Samples Shipped: <u>7-22-09</u>		Project/Task No. <u>125778.10.11.01</u>		<input type="checkbox"/> Waste Characterization						
Project/Task Manager: Don Schofield		Carrier/Waybill No. <u>103697</u>		SMO Authorization: <u>[Signature]</u>		-Send preliminary/copy report to:						
Project Name: TAG-GWM		Lab Contact: Edie Kent/803-556-8171		Contract #: 691436		<input type="checkbox"/> Released by COC No.:						
Record Center Code: ER/1306/DAT		Lab Destination: GEL		<u>SUB BOTTLE ORDER</u>		<input checked="" type="checkbox"/> Validation Required						
Logbook Ref. No.: NA		SMO Contact/Phone: Pam Puissant/505-844-3185				Bill To: Sandia National Labs (Accounts Payable)						
Service Order No. CFO# 010-09		Send Report to SMO: Lorraine Herrera /505-844-3199				P.O. Box 5800 MS 0154 Albuquerque, NM 87185-0154						
Location		Tech Area		Reference LOV (available at SMO)								
Building		Room										
Sample No.-Fraction	ER Sample ID or Sample Location Detail	Depth (ft)	ER Site No.	Date/Time (hr) Collected	Sample Matrix	Container Type	Volume	Preservative	Collection Method	Sample Type	Parameter & Method Requested	Lab Sample ID
087553-001	TA1-W-08	320	NA	07/22/09 0951	GW	G	3x40 ml	HCL	G	SA	VOC (SW846-8260B)	038
087553-009	TA1-W-08	320	NA	07/22/09 0952	GW	P	500 ml	HNO3	G	SA	TAL Metals+total Ur(SW846-6020/7470)	039
087553-016	TA1-W-08	320	NA	07/22/09 0953	GW	P	250 ml	4C	G	SA	Major Anions (SW846-9056)	040
087553-018	TA1-W-08	320	NA	07/22/09 0954	GW	P	250 ml	H2SO4	G	SA	NPN (353.2)	041
087553-020	TA1-W-08	320	NA	07/22/09 0955	GW	P	250 ml	4C	G	SA	Perchlorate (314.0)	042
087553-033	TA1-W-08	320	NA	07/22/09 0957	GW	P	1 L	HNO3	G	SA	Gamma Spec (short list)(901.0)	043
087553-034	TA1-W-08	320	NA	07/22/09 0958	GW	P	1 L	HNO3	G	SA	Gross Alpha/Beta (900.0)	044
087553-036	TA1-W-08	320	NA	07/22/09 0959	GW	AG	250 ml	4C	G	SA	Tritium (906.0)	045
087554-001	TAG-TB8	NA	NA	07/22/09 0951	DIW	G	3x40 ml	HCL	G	TB	VOC (SW846-8260B) <u>boc</u>	046
RMMA <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Ref. No.		Sample Tracking		Smo Use		Special Instructions/QC Requirements				Abnormal Conditions on Receipt Lab Use		
Sample Disposal <input type="checkbox"/> Return to Client <input checked="" type="checkbox"/> Disposal by lab		Date Entered (mm/dd/yy)		Entered by:		EDD <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No						
Turnaround Time <input type="checkbox"/> 7 Day <input type="checkbox"/> 15 Day <input checked="" type="checkbox"/> 30 Day		Negotiated TAT		QC inits.		Level D Package <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No						
Return Samples By:		Name		Signature		Init		Company/Organization/Phone/Cellular		*Send report to:		
Sample Team Members		Robert Lynch		<u>[Signature]</u>		RL		Weston/4133/844-4013/250-7090		Tim Jackson/ORG. 4133/MS. 1089/ 284-2547		
		Alfred Santillanes		<u>[Signature]</u>		AS		Weston/4133/844-5130/228-0710				
		William J. Gibson		<u>[Signature]</u>		WJG		Weston/4133/844-4013/239-7367				
										Major Anions/Br, Cl, F, SO4		
										*Please list as separate report.		
1. Relinquished by <u>Alfred Santillanes</u> Org. 4133 Date <u>7/22/09</u> Time <u>1009</u>		4. Relinquished by		Org.		Date		Time				
1. Received by <u>Don Schofield</u> Org. 4133 Date <u>7/22/09</u> Time <u>1009</u>		4. Received by		Org.		Date		Time				
2. Relinquished by <u>Edie Kent</u> Org. 4133 Date <u>7/22/09</u> Time <u>1215</u>		5. Relinquished by		Org.		Date		Time				
2. Received by <u>Edie Kent</u> Org. GEL Date <u>7-23-09</u> Time <u>0735</u>		5. Received by		Org.		Date		Time				
3. Relinquished by		Org.		Date		Time		6. Relinquished by		Org. Date Time		
3. Received by		Org.		Date		Time		6. Received by		Org. Date Time		

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
 Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
 1515 Eubank SE
 Albuquerque, New Mexico 87123
 Contact: Ms. Pamela M. Puissant
 Project: Level C, Groundwater Monitoring

Report Date: August 14, 2009

Client Sample ID: 087551-020
 Sample ID: 233746036
 Matrix: AQUEOUS
 Collect Date: 21-JUL-09 09:36
 Receive Date: 22-JUL-09
 Collector: Client

Project: SNLSGWater
 Client ID: SNLS003
 Client Desc.: TA I-W-06
 Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108/04/09	2252	888074	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
1515 Eubank SE
Albuquerque, New Mexico 87123
Contact: Ms. Pamela M. Puissant
Project: Level C, Groundwater Monitoring

Report Date: August 14, 2009

Client Sample ID: 087553-020
Sample ID: 233746042
Matrix: AQUEOUS
Collect Date: 22-JUL-09 09:55
Receive Date: 23-JUL-09
Collector: Client

Project: SNLSGWater
Client ID: SNLS003
Client Desc.: TA1-W-08
Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	Analyst	Date	Time	Batch	Method
Ion Chromatography Federal											
<i>EPA 314.0 Perchlorate by IC "As Received"</i>											
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108/04/09	2312	888074	1	

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
1515 Eubank SE
Albuquerque, New Mexico 87123
Contact: Ms. Pamela M. Puissant
Project: Level C, Groundwater Monitoring

Report Date: August 19, 2009

Client Sample ID: 087562-020
Sample ID: 234180027
Matrix: AQUEOUS
Collect Date: 30-JUL-09 09:17
Receive Date: 31-JUL-09
Collector: Client

Project: SNLSGWater
Client ID: SNLS003

Client Desc.: TA2-W-01
Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108/05/09	0011	888074	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
1515 Eubank SE
Albuquerque, New Mexico 87123
Contact: Ms. Pamela M. Puissant
Project: **Level C, Groundwater Monitoring**

Report Date: September 2, 2009

Client Sample ID: 087566-020
Sample ID: 234517005
Matrix: AQUEOUS
Collect Date: 03-AUG-09 10:27
Receive Date: 04-AUG-09
Collector: Client

Project: SNLSGWater
Client ID: SNLS003
Client Desc.: TA2-W-27
Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108/05/09	1321	891119	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

Certificate of Analysis

Company : Sandia National Laboratories
 Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
 1515 Eubank SE
 Albuquerque, New Mexico 87123
 Contact: Ms. Pamela M. Puissant
 Project: **Level C, Groundwater Monitoring**

Report Date: September 2, 2009

Client Sample ID: 087567-020
 Sample ID: 234517011
 Matrix: AQUEOUS
 Collect Date: 03-AUG-09 10:27
 Receive Date: 04-AUG-09
 Collector: Client

Project: SNLSGWater
 Client ID: SNLS003

Client Desc.: TA2-W-27
 Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	Analyst	Date	Time	Batch	Method
Ion Chromatography Federal											
<i>EPA 314.0 Perchlorate by IC "As Received"</i>											
Perchlorate	U	ND	0.004	0.012	mg/L	1	MAR108	05/09	1419	891119	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

CONTRACT LABORATORY ANALYSIS REQUEST AND CHAIN OF CUSTODY

Internal Lab

Batch No. *NA*

SMO Use

AR/COC

612392

Dept. No./Mail Stop: 4133/1126	Date Samples Shipped: <i>9/30/09</i>	Project/Task No. 125778.10.11.01
Project/Task Manager: Don Schofield	Carrier/Voybill No.: <i>106970</i>	SMO Authorization: <i>Edie Ken GMM</i>
Project Name: Burn Site GWM	Lab Contact: Edie Ken/803-556-8171	Contract #: PO 691436
Record Center Code: ER/1333/DAT	Lab Destination: GEL	<i>585 BOTTLE ORDER</i>
Logbook Ref. No.: ER 058	SMO Contact/Phone: Pam Puissant/505-844-3185	
Service Order No. CF#058-10	Send Report to SMO: Lorraine Herrera/505-844-3199	

<input type="checkbox"/> Waste Characterization -Send preliminary/copy report to:
<input type="checkbox"/> Released by COC No.: _____
<input checked="" type="checkbox"/> Validation Required
Bill To: Sandia National Labs (Accounts Payable) P.O. Box 5800 MS 0154 Albuquerque, NM 87185-0154

Location	Tech Area	Reference LOV (available at SMO)							
Building	Room								

Sample No.-Fraction	ER Sample ID or Sample Location Detail	Pump Depth (ft)	ER Site No.	Date/Time (hr) Collected	Sample Matrix	Container		Preservative	Collection Method	Sample Type	Parameter & Method Requested	Lab Sample ID
						Type	Volume					
087734-001	CYN-MW6	163	NA	093009/0814	GW	G	3x40 ml	HCL	G	SA	VOC (SW846-8260)	024 11
087734-005	CYN-MW6	163	NA	093009/0816	GW	AG	4x1 L	4C	G	SA	TPH Diesel (SW846-8015A/B) SVOC	025 12
087734-006	CYN-MW6	163	NA	093009/0817	GW	G	3x40 ml	HCL	G	SA	TPH Gasoline (SW846-8015A/B) VOC	026 13
087734-009	CYN-MW6	163	NA	093009/0818	GW	P	500 ml	HNO3	G	SA	Total TAL Metals+Total-U (SW846-6020/7470)	027 14
087734-016	CYN-MW6	163	NA	093009/0819	GW	P	500 ml	4C	G	SA	Major Anions (SW846-9056)	028 15
087734-018	CYN-MW6	163	NA	093009/0820	GW	P	250 ml	H2SO4	G	SA	NPN (353.2)	029 16
087734-020	CYN-MW6	163	NA	093009/0821	GW	P	250 ml	4C	G	SA	Perchlorate (314.0)	030 17
087734-033	CYN-MW6	163	NA	093009/0822	GW	P	1 L	HNO3	G	SA	Gamma Spec (short list)(901.1)	031 18
087734-034	CYN-MW6	163	NA	093009/0823	GW	P	1 L	HNO3	G	SA	Gross Alpha/Beta (900.0)	032 19
087734-036	CYN-MW6	163	NA	093009/0824	GW	AG	250 ml	4C	G	SA	Tritium (906.0)	033 20

RMMA <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Ref. No. _____ Sample Disposal <input type="checkbox"/> Return to Client <input checked="" type="checkbox"/> Disposal by lab Turnaround Time <input type="checkbox"/> 7 Day <input type="checkbox"/> 15 Day <input checked="" type="checkbox"/> 30 Day Return Samples By: <input type="checkbox"/> Negotiated TAT <input type="checkbox"/> QC Inits.	Sample Tracking SMO Use _____ Date Entered (mm/dd/yy) _____ Entered by: _____	Special Instructions/QC Requirements EDD <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No Level D Package <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No *Send report to: Tim Jackson/Org. 4133/MS 0756/505-284-2547 Sampling complete for Burn Site 4th Quarter 2009. * Major Anions/Br, Cl, F, SO4 *Please list as separate report.	Abnormal Conditions on Receipt <div style="text-align: center;">Lab Use</div>
--	--	---	---

1. Relinquished by <i>William J Gibson</i> Org. <i>4133</i> Date <i>9/30/09</i> Time <i>0950</i> 1. Received by <i>Edie Ken GMM</i> Org. <i>4133</i> Date <i>9/30/09</i> Time <i>0950</i> 2. Relinquished by <i>Edie Ken GMM</i> Org. <i>4133</i> Date <i>9/30/09</i> Time <i>1300</i> 2. Received by <i>Edie Ken GMM</i> Org. <i>GEL</i> Date <i>10-1-09</i> Time <i>0745</i> 3. Relinquished by _____ Org. _____ Date _____ Time _____ 3. Received by _____ Org. _____ Date _____ Time _____	4. Relinquished by _____ Org. _____ Date _____ Time _____ 4. Received by _____ Org. _____ Date _____ Time _____ 5. Relinquished by _____ Org. _____ Date _____ Time _____ 5. Received by _____ Org. _____ Date _____ Time _____ 6. Relinquished by _____ Org. _____ Date _____ Time _____ 6. Received by _____ Org. _____ Date _____ Time _____
---	--

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
1515 Eubank SE
Albuquerque, New Mexico 87123
Contact: Ms. Pamela M. Puissant
Project: **Level C, Groundwater Monitoring**

Report Date: October 24, 2009

Client Sample ID: 087734-020
Sample ID: 237978030
Matrix: AQUEOUS
Collect Date: 30-SEP-09 08:21
Receive Date: 01-OCT-09
Collector: Client

Project: SNLSGWater
Client ID: SNLS003

Client Desc.: CYN-MW6
Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	J	0.00412	0.004	0.012	mg/L	1	MARI	10/21/09	1949	909715 1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

Certificate of Analysis

Company : Sandia National Laboratories
 Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
 1515 Eubank SE
 Albuquerque, New Mexico 87123
 Contact: Ms. Pamela M. Puissant
 Project: **Level C, Groundwater Monitoring**

Report Date: October 24, 2009

Client Sample ID: 087735-020
 Sample ID: 237978037
 Matrix: AQUEOUS
 Collect Date: 30-SEP-09 08:21
 Receive Date: 01-OCT-09
 Collector: Client

Project: SNLSGWater
 Client ID: SNLS003

Client Desc.: CYN-MW6
 Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	Analyst	Date	Time	Batch	Method
Ion Chromatography Federal											
<i>EPA 314.0 Perchlorate by IC "As Received"</i>											
Perchlorate	J	0.00471	0.004	0.012	mg/L	1	MAR110	21/09	2047	909715	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

CONTRACT LABORATORY ANALYSIS REQUEST AND CHAIN OF CUSTODY

Internal Lab

Batch No. *N/A*

SMO Use

AR/COC

612368

Dept. No./Mail Stop: 4133/1126	Date Samples Shipped: <i>9/15/09</i>	Project/Task No. 125778.10.11.01	<input type="checkbox"/> Waste Characterization
Project/Task Manager: Don Schofield	Carrier/Waybill No. <i>05512</i>	SMO Authorization: <i>[Signature]</i>	-Send preliminary/copy report to:
Project Name: TA-V GWM	Lab Contact: Edie Ken/803-556-8171	Contract #: 691436	<input type="checkbox"/> Released by COC No.:
Record Center Code: ER/1306/DAT	Lab Destination: GEL	<i>SEE BOTTLE ORDER</i>	<input checked="" type="checkbox"/> Validation Required
Logbook Ref. No.: NA	SMO Contact/Phone: Pam Puissant/505-844-3185		Bill To: Sandia National Labs (Accounts Payable)
Service Order No. CFO# 012-10	Send Report to SMO: Lorraine Herrera /505-844-3199		P.O. Box 5800 MS 0154 Albuquerque, NM 87185-0154

Location	Tech Area	Reference LOV(available at SMO)
Building	Room	

Sample No.-Fraction	ER Sample ID or Sample Location Detail	Depth (ft)	ER Site No.	Date/Time(hr) Collected	Sample Matrix	Container		Preservative	Collection Method	Sample Type	Parameter & Method Requested	Lab Sample ID
						Type	Volume					
087662-001	LWDS-MW1	514	NA	091509/0843	GW	G	3x40 ml	HCL	G	SA	VOC (SW846-8260B)	017 .1
087662-009	LWDS-MW1	514	NA	091509/0845	GW	P	500 ml	HNO3	G	SA	TAL Metals+total Ur(SW846-6020/7470)	018 .2
087662-016	LWDS-MW1	514	NA	091509/0846	GW	P	500 ml	4C	G	SA	Major Anions (SW846-9056)	019 .3
087662-018	LWDS-MW1	514	NA	091509/0847	GW	P	250 ml	H2SO4	G	SA	NPN (353.2)	020 .4
087662-020	LWDS-MW1	514	NA	091509/0848	GW	P	250 ml	4C	G	SA	Perchlorate (314.0)	021 .7
087662-033	LWDS-MW1	514	NA	091509/0849	GW	P	1 L	HNO3	G	SA	Gamma Spec (short list)(901.0)	022 .1
087662-034	LWDS-MW1	514	NA	091509/0851	GW	P	1 L	HNO3	G	SA	Gross Alpha/Beta (900.0)	023 .6
087662-036	LWDS-MW1	514	NA	091509/0853	GW	AG	250 ml	4C	G	SA	Tritium (906.0)	024 .7
087663-001	LWDS-MW1	514	NA	091509/0843	GW	G	3x40 ml	HCL	G	DU	VOC (SW846-8260B)	025 .1
087663-009	LWDS-MW1	514	NA	091509/0845	GW	P	500 ml	HNO3	G	DU	TAL Metals+total Ur(SW846-6020/7470)	026 .2
087663-016	LWDS-MW1	514	NA	091509/0846	GW	P	500 ml	4C	G	DU	Major Anions (SW846-9056)	027 .3

RMMA <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Ref. No.	Sample Tracking SMO Use	Special Instructions/QC Requirements	Abnormal Conditions on Receipt																
Sample Disposal <input type="checkbox"/> Return to Client <input checked="" type="checkbox"/> Disposal by lab	Date Entered(mm/dd/yyyy)	EDD <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	Lab Use																
Turnaround Time <input type="checkbox"/> 7 Day <input type="checkbox"/> 15 Day <input checked="" type="checkbox"/> 30 Day	Entered by:	Level D Package <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No																	
Return Samples By: <input type="checkbox"/> Negotiated TAT <input type="checkbox"/> QC inits	*Send report to:																		
<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th>Name</th> <th>Signature</th> <th>Init</th> <th>Company/Organization/Phone/Cellular</th> </tr> </thead> <tbody> <tr> <td>Robert Lynch</td> <td><i>[Signature]</i></td> <td>RL</td> <td>Weston/4133/844-4013/250-7090</td> </tr> <tr> <td>Alfred Santillanes</td> <td><i>[Signature]</i></td> <td>AS</td> <td>Weston/4133/844-5130/228-0710</td> </tr> <tr> <td>William J. Gibson</td> <td><i>[Signature]</i></td> <td>WG</td> <td>Weston/4133/844-4013/239-7367</td> </tr> </tbody> </table>		Name	Signature	Init	Company/Organization/Phone/Cellular	Robert Lynch	<i>[Signature]</i>	RL	Weston/4133/844-4013/250-7090	Alfred Santillanes	<i>[Signature]</i>	AS	Weston/4133/844-5130/228-0710	William J. Gibson	<i>[Signature]</i>	WG	Weston/4133/844-4013/239-7367	Tim Jackson/ORG. 4133/MS 0756/ 284-2547 <i>TA-V GWM "COMPOSITE" with GWINNER</i>	
Name	Signature	Init	Company/Organization/Phone/Cellular																
Robert Lynch	<i>[Signature]</i>	RL	Weston/4133/844-4013/250-7090																
Alfred Santillanes	<i>[Signature]</i>	AS	Weston/4133/844-5130/228-0710																
William J. Gibson	<i>[Signature]</i>	WG	Weston/4133/844-4013/239-7367																
*Please list as separate report.																			

1. Relinquished by <i>[Signature]</i> Org. <i>9/33</i> Date <i>9/15/09</i> Time <i>0930</i>	4. Relinquished by Org. Date Time
1. Received by <i>[Signature]</i> Org. <i>9/33</i> Date <i>9/15/09</i> Time <i>0930</i>	4. Received by Org. Date Time
2. Relinquished by <i>[Signature]</i> Org. <i>9/33</i> Date <i>9/15/09</i> Time <i>1140</i>	5. Relinquished by Org. Date Time
2. Received by <i>[Signature]</i> Org. <i>GEL</i> Date <i>9-16-09</i> Time <i>0745</i>	5. Received by Org. Date Time
3. Relinquished by Org. Date Time	6. Relinquished by Org. Date Time
3. Received by Org. Date Time	6. Received by Org. Date Time

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
 Address : MS-0756, Org. 06765, Bldg. 823/Rm. 4276
 1515 Eubank SE
 Albuquerque, New Mexico 87123
 Contact: Ms. Pamela M. Puissant
 Project: **Level C, Groundwater Monitoring**

Report Date: October 19, 2009

Client Sample ID: 087662-020
 Sample ID: 237241021
 Matrix: AQUEOUS
 Collect Date: 15-SEP-09 08:48
 Receive Date: 16-SEP-09
 Collector: Client

Project: SNLSGWater
 Client ID: SNLS003

Client Desc.: LWDS-MW1
 Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	AnalystDate	Time	Batch	Method
Ion Chromatography Federal										
<i>EPA 314.0 Perchlorate by IC "As Received"</i>										
Perchlorate	HU	ND	0.004	0.012	mg/L	1	MAR110/18/09	2116	905757	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

GEL LABORATORIES LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Sandia National Laboratories
 Address : MS-0716, Org. 06765, Bldg. 823/Rm. 4276
 1515 Eubank SE
 Albuquerque, New Mexico 87123
 Contact: Ms. Pamela M. Puissant
 Project: **Level C, Groundwater Monitoring**

Report Date: October 19, 2009

Client Sample ID: 087663-020
 Sample ID: 237241029
 Matrix: AQUEOUS
 Collect Date: 15-SEP-09 08:48
 Receive Date: 16-SEP-09
 Collector: Client

Project: SNL\$GWater
 Client ID: SNLS003

Client Desc.: LWDS-MWI
 Vol. Recv.:

Parameter	Qualifier	Result	DL	RL	Units	DF	Analyst	Date	Time	Batch	Method
Ion Chromatography Federal											
<i>EPA 314.0 Perchlorate by IC "As Received"</i>											
Perchlorate	HU	ND	0.004	0.012	mg/L	1	MARI	10/18/09	2214	905757	1

The following Analytical Methods were performed

Method	Description	Analyst Comments
1	EPA 314.0 DOE-AL	

Appendix B

Data Validation Sample Findings Summary Sheets for the Perchlorate Data

Memorandum

DATE: September 3, 2009

TO: File

FROM: David Schwent

SUBJECT: General Chemistry Data Review and Validation - SNL
Site: TAG GWM
AR/COC: 612298, 612299, 612300, 612301, 612302, and 612303
SDG: 233746
Laboratory: GEL
Project/Task No: 125778.10.11.01

See the attached Data Validation Worksheets for supporting documentation on the data review and validation. This validation was performed according to SNL/NM ER Project AOP 00-03 Rev 2.

Summary

The samples were prepared and analyzed with accepted procedures using EPA314.0 (perchlorate), EPA353.2 (nitrate/nitrite by Cd reduction), and EPA9056 (anions). No problems were identified with the data package that result in the qualification of data.

Data are acceptable. QC measures appear to be adequate. The following sections discuss the data review and validation.

Holding Times/Preservation

All Analyses: All samples were analyzed within the prescribed holding times and properly preserved.

Calibration

All Analyses: All initial and continuing calibration QC acceptance criteria were met.

Blanks

Anions Analysis: No target analytes were detected in the blanks, except the following. Chloride and sulfate were detected in the equipment blank (EB) (sample 233746-019) at concentrations > the method detection limit (MDL) but < the practical quantitation limit (PQL). However, all associated sample results were detects >5X the EB concentration and will not be qualified. It should be noted that the results of the EB only apply to samples on COC 612301.

All Other Analyses: No target analytes were detected in the blanks.

Laboratory Control Sample/Laboratory Control Sample Duplicate (LCS/LCSD)

All Analyses: All LCS QC acceptance criteria were met. No LCSD analyses were performed. No sample data will be qualified as a result.

Matrix Spike/Matrix Spike Duplicate (MS/MSD)

All Analyses: All MS (PS) QC acceptance criteria were met. No MSD (PSD) analyses were performed. The replicate analyses were used as measures of laboratory precision. No sample data will be qualified as a result.

Replicates

All Analyses: All replicate QC acceptance criteria were met.

Detection Limits/Dilutions

Anions Analysis: All detection limits were properly reported. Samples -003 and -011 were diluted 5X for sulfate, samples -028 and -049 were diluted 10X for chloride and sulfate, and sample -040 was diluted 50X for chloride and sulfate due to high concentrations of the target analytes. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Nitrate/nitrite Analysis: All detection limits were properly reported. Sample -012 was diluted 5X, samples -004, -029, -035, and -050 were diluted 10X, and sample -041 was diluted 25X for nitrate/nitrite due to high concentrations of the target analyte. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Perchlorate Analysis: All detection limits were properly reported. No samples required dilution.

Other QC

All Analyses: No field blanks (FBs) were submitted on the AR/COCs. All relative percent differences (RPDs) of the field duplicates (FDs) (samples -035 and -036) were $< 20\%$. No QC acceptance criteria for the evaluation of FDs are currently in place.

No other specific issues were identified that affect data quality.

Sample Findings Summary

Site: TAG GWM

AR/COC: 612298, 612299, 612300, 612301, 612302 and 612303

Organic, Metals, Gen Chem, Rad

Sample ID	EPA8260B (VOCs):		EPA6020 (ICP-MS):	7429-90-5 (Al)	7440-38-2 (As)	7440-41-7 (Be)	7440-70-2 (Ca)	7440-50-8 (Cu)	7440-48-4 (Co)	7440-02-0 (Ni)	7440-23-5 (Na)	EPA7470A (CVAA):		
	67-64-1 (acetone)	108-05-4 (vinyl acetate)												
087544-001 TA1-W-04	UJ,I4	UJ,C3										All Acceptance criteria met. No sample data will be qualified.		
087544-009 TA1-W-04				J-,MS3,RP2							J,D1			
087545-001 TAG-TB4	UJ,I4	UJ,C3												
087546-001 TA1-W-05	UJ,I4	UJ,C3												
087546-009 TA1-W-05				0.088UJ,B,MS3,RP2							J,D1			
087547-001 TAG-TB5	UJ,I4	UJ,C3												
087548-001 TAG-EB1	UJ,I4	UJ,C3												
087548-009 TAG-EB1				0.088UJ,B,MS3,RP2		0.00052U,B	0.46U,B				J,D1			
087549-001 TAG-TB6	UJ,I4	UJ,C3												
087550-001 TA1-W-06	UJ,I4	UJ,C3												
087550-009 TA1-W-06				J-,MS3,RP2	0.020U,B	0.00052U,B		0.012U,B2	J+,CK2	J+,CK2	J,D1			
087551-001 TA1-W-06	UJ,I4	UJ,C3												
087552-001 TAG-TB7	UJ,I4	UJ,C3												
087553-001 TA1-W-08	UJ,I4	UJ,C3												
087553-009 TA1-W-08				0.088UJ,B,MS3,RP2	0.020U,B	0.00052U,B		J+,CK2	J+,CK2	J+,CK2	J,D1			
087554-001 TAG-TB8	UJ,I4	UJ,C3												
087555-001 TA2-NW1-595	UJ,I4	UJ,C3												
087555-009 TA2-NW1-595				0.088UJ,B,MS3,RP2				J+,CK2		J+,CK2	J,D1			
087556-001 TAG-TB9	UJ,I4	UJ,C3												

Validated By: David Schwartz

Date: 09/16/09

Sample Findings Summary

Site: TAG GWM

AR/COC: 612298, 612299, 612300, 612301, 612302 and 612303

Organic, Metals, Gen Chem, Rad

Sample ID	EPA314.0 (perchlorate)	EPA9056 (Anions):	EPA353.1 (Nitrate/nitrite):	EPA901.1 (Gamma Spec):	86954-36-1 (Am-241)	10045-97-3 (Cs-137)	10198-40-0 (Co-60)	13966-00-2 (K-40)	EPA900.0 (Gross Alpha/Beta):	12587-46-1 (gross alpha)	12587-47-2 (gross beta)	EPA906.0 (Tritium):	10028-17-8 (Tritium)		
087544-033 TA1-W-04	All Acceptance criteria met. No sample data will be qualified.	All Acceptance criteria met. No sample data will be qualified.	All Acceptance criteria met. No sample data will be qualified.		BD,FR3	BD,FR3	BD,FR3	BD,FR3							
087544-036 TA1-W-04														BD,FR3	
087546-033 TA1-W-05							BD,FR3	BD,FR3	BD,FR3	R,Z2					
087546-036 TA1-W-05															BD,FR3
087548-033 TAG-EB1							BD,FR3	BD,Z2	BD,FR3	BD,Z2					
087548-034 TAG-EB1												BD,FR3,MS3	BD,FR3		
087548-036 TAG-EB1															BD,FR3
087550-033 TA1-W-06							BD,FR3	BD,FR3	BD,FR3	BD,FR3					
087550-036 TA1-W-06															BD,FR3
087553-033 TA1-W-08							BD,FR3	BD,FR3	BD,FR3	BD,FR3					
087553-034 TA1-W-08												BD,FR3,MS3	BD,FR3		
087553-036 TA1-W-08															BD,FR3
087555-033 TA2-NW1-595							BD,FR3	BD,FR3	BD,FR3	BD,FR3					
087555-036 TA2-NW1-595															BD,FR3
087544-R34 TA1-W-04														J,FR7	
087546-R34 TA1-W-05														J,FR7	
087550-R34 TA1-W-06												J,FR7	BD,FR3		
087555-R34 TA2-NW1-595												J,FR7	J,FR7		

Validated By:

David Schwartz

Date: 09/16/09

Memorandum

DATE: September 9, 2009

TO: File

FROM: David Schwent

SUBJECT: General Chemistry Data Review and Validation - SNL
Site: TAG GWM
AR/COC: 612297, 612304, 612305, 612306, and 612307
SDG: 234180
Laboratory: GEL
Project/Task No: 125778.10.11.01

See the attached Data Validation Worksheets for supporting documentation on the data review and validation. This validation was performed according to SNL/NM ER Project AOP 00-03 Rev 2.

Summary

The samples were prepared and analyzed with accepted procedures using EPA314.0 (perchlorate), EPA353.2 (nitrate/nitrite by Cd reduction), and EPA9056 (anions). Problems were identified with the data package that result in the qualification of data.

Nitrate/nitrite Analysis:

Blanks: Nitrate/nitrite was detected in the initial calibration blank (ICB) and continuing calibration blank (CCB) at negative concentrations with absolute values > the method detection limit (MDL) but < the practical quantitation limit (PQL). The associated result of sample 234180-035 was a non-detect (ND) and will be qualified "UJ,B4."

Data are acceptable. QC measures appear to be adequate. The following sections discuss the data review and validation.

Holding Times/Preservation

All Analyses: All samples were analyzed within the prescribed holding times and properly preserved.

Calibration

All Analyses: All initial and continuing calibration QC acceptance criteria were met.

Blanks

Anions Analysis: No target analytes were detected in the blanks, except the following. Chloride was detected in the equipment blank (EB) (sample -034) at a concentration > the MDL. The result of the EB only applies to samples on COC 612308, contained in another package.

Nitrate/nitrite Analysis: No target analytes were detected in the blanks, except as noted above in the summary section, and the following. Nitrate/nitrite was detected in the ICB and CCB at negative concentrations with absolute values > MDL but < the PQL. However, the associated results of samples -004, -009, -017, and -026 were detects >5X the MDL and will not be qualified.

Perchlorate Analysis: No target analytes were detected in the blanks.

Laboratory Control Sample/Laboratory Control Sample Duplicate (LCS/LCSD)

All Analyses: All LCS QC acceptance criteria were met. No LCSD analyses were performed. No sample data will be qualified as a result.

Matrix Spike/Matrix Spike Duplicate (MS/MSD)

All Analyses: All MS (PS) QC acceptance criteria were met. No MSD (PSD) analyses were performed. The replicate analyses were used as measures of laboratory precision. No sample data will be qualified as a result. It should be noted that the PS analysis for perchlorate was performed on a QC sample of similar matrix from another SNL SDG. No sample data will be qualified as a result.

Replicates

All Analyses: All replicate QC acceptance criteria were met. It should be noted that the laboratory replicate analysis for perchlorate was performed on a QC sample of similar matrix from another SNL SDG. No sample data will be qualified as a result.

Detection Limits/Dilutions

Anions Analysis: All detection limits were properly reported. Samples -008 and -016 were diluted 5X for sulfate, samples -025 was diluted 10X for chloride and sulfate, and sample -003 was diluted 20X for chloride and sulfate due to high concentrations of the target analytes. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Nitrate/nitrite Analysis: All detection limits were properly reported. Sample -026 was diluted 5X, sample -009 was diluted 25X, and sample -004 was diluted 50X for nitrate/nitrite due to high concentrations of the target analyte and sample -017 was diluted 5X due to matrix interference. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Perchlorate Analysis: All detection limits were properly reported. No samples required dilution.

Other QC

All Analyses: No field blanks (FBs) or field duplicates (FDs) were submitted on the AR/COCs.

No other specific issues were identified that affect data quality.

Sample Findings Summary

Site: TAG GWM

AR/COC: 612297, 612304, 612305, 612306, and 612307

Organic, Metals, Gen Chem, Rad

Sample ID	EPA353.1 (Nitrate/nitrite):	EPA314.0 (perchlorate)	EPA9056 (Anions):	EPA901.1 (Gamma Spec):	86954-36-1 (Am-241)	10045-97-3 (Cs-137)	10198-40-0 (Co-60)	13966-00-2 (K-40)	EPA900.0 (Gross Alpha/Beta):	12587-46-1 (gross alpha)	12587-47-2 (gross beta)	EPA906.0 (Tritium):	10028-17-8 (tritium)		
	N599 (nitrate/nitrite)														
087557-033 WYO-3		All Acceptance criteria met. No sample data will be qualified.	All Acceptance criteria met. No sample data will be qualified.		BD,FR3	BD,FR3	BD,FR3	BD,FR3							
087557-034 WYO-3												J,FR7			
087557-036 WYO-3														BD,FR3	
087559-033 PGS-2							BD,FR3	BD,FR3	BD,FR3	BD,FR3					
087559-034 PGS-2												J,FR7			
087559-036 PGS-2															BD,FR3
087562-033 TA2-W-01							BD,FR3	BD,FR3	BD,Z2	BD,FR3					
087562-034 TA2-W-01											J,FR7	BD,FR3			
087562-036 TA2-W-01															BD,FR3
087564-018 TAG-EB2	UJ,B4														
087564-033 TAG-EB2							BD,FR3	BD,FR3	BD,FR3	BD,FR3					
087564-034 TAG-EB2											BD,FR3	BD,FR3			
087564-036 TAG-EB2															BD,FR3

Validated By:

David Schwartz

Date: 09/10/09

Memorandum

Date: October 4, 2009
To: File
From: Kevin Lambert
Subject: Inorganic Data Review and Validation – SNL
Site: TAG GWM
AR/COC: 612308, 612309, 612310, 612311, and 612312
SDG: 234517
Laboratory: GEL
Project/Task: 125778, 10.11.01
Analysis: General Chemistry

See the attached Data Validation Worksheets for supporting documentation on the data review and validation. This validation was performed according to SNL/NM ER Project AOP 00-03 Rev 2.

Summary

Four samples were prepared and analyzed with accepted procedures using methods EPA 9056 (Br, Cl, F, SO₄ by Ion Chromatography). Five samples were prepared and analyzed with accepted procedures using methods EPA 353.2 (nitrate/nitrite by Cd reduction). Two samples were prepared and analyzed with accepted procedures using methods EPA 314.02 (perchlorate). Data were reported for all required analytes. No problems were identified with the data package that result in the qualification of data.

Data are acceptable and reported QC measures appear to be adequate. The following sections discuss the data review and validation.

Holding Times and Preservation

The samples were analyzed within the prescribed holding times and properly preserved.

Calibration

All initial and continuing calibration met QC acceptance criteria.

Blanks

No target analytes were detected in the blanks except as follows.

Nitrate/nitrite was detected in the method blank (MB) associated with sample 234517-040 at a concentration \geq the method detection limit (MDL) but $<$ the practical quantitation limit (PQL). The associated sample result was a detect $>5X$ the MB result and will not be qualified.

Chloride was detected in the equipment blank (EB) associated with samples -003 and -010 at a concentration \geq the PQL. The associated sample results were detects $>5X$ the EB results and will not be qualified.

Laboratory Control Sample (LCS)

All LCS recoveries met QC acceptance criteria.

Matrix Spike (MS)

All MS recoveries met QC acceptance criteria except as noted above in the summary section and as follows.

Nitrate/Nitrite:

It should be noted that the MS analysis associated with sample -040 was performed on a SNL sample of similar matrix from another SDG. No sample data will be qualified as a result.

Laboratory Replicate

The replicate met all QC acceptance criteria except as noted above in the summary section and as follows.

Nitrate/Nitrite:

It should be noted that the laboratory replicate analysis associated with sample -040 was performed on a SNL sample of similar matrix from another SDG. No sample data will be qualified as a result.

Detection Limits/Dilutions

All detection limits were properly reported. Samples -003, and -013, and -022 were diluted 50X, 20X, and 5X, respectively for chloride and sulfate due to high concentrations for this analysis. Samples -004, -009, -014, and -023 were diluted 10X, 10X, 5X, and 25X, respectively for nitrate/nitrite due to high concentrations for this analysis.

Other QC

EBs and a field duplicate pair were submitted on the AR/COC(s). There are no "required" review criteria for field duplicate analyses comparability; no data will be qualified as a result. It should be noted that the EB associated with samples on AR/COC# 612308 is from another SNL SDG on AR/COC# 612307. Also, it should be noted that the EB on AR/COC# 612311 is associated with samples in another SNL SDG on AR/COC# 612313.

No other specific issues that affect data quality were identified.

Sample Findings Summary

Site: TAG GWM

AR/COC: 612308, 612309, 612310,
612311, 612312

Data Type: Organic, Metals, Gen Chem & Rad

	VOC	108-05-4 (vinyl acetate)	ICP-MS metals	7429-90-5 (aluminum)	7440-36-0 (antimony)	7440-70-2 (calcium)	7440-47-3 (chromium)	7440-48-4 (cobalt)	7440-50-8 (copper)	7439-89-6 (iron)	7440-02-0 (nickel)	7782-49-2 (selenium)	7440-23-5 (sodium)	7440-28-0 (thallium)
087566-001 TA2-W-27		UJ,C3												
087567-001 TA2-W-27		UJ,C3												
087568-001 TAG-TB14		UJ,C3												
087569-001 TJA-3		UJ,C3												
087570-001 TAG-TB15		UJ,C3												
087571-001 TJA-6		UJ,C3												
087572-001 TAG-TB16		UJ,C3												
087573-001 TAG-EB3		UJ,C3												
087574-001 TAG-TB17		UJ,C3												
087575-001 TA2-SW1-320		UJ,C3												
087576-001 TAG-TB18		UJ,C3												
087566-009 TA2-W-27				0.069U,B			J+,CK2	J+,CK2	0.013U, B2		J+,CK2	J-,CK3	J,D1	
087569-009 TJA-3				0.12U,B	0.008U,B ,B3				0.0015U ,B					0.0024U, B3
087571-009 TJA-6				0.12U,B	0.008U,B ,B3				0.0015U ,B					
087573-009 TAG-EB3				0.12U,B	0.008U,B ,B3	0.20U,B				UJ,B4				
087575-009 TA2-SW1-320								0.001U,B 3						

Validated By:

Kevin A Lambert

Kevin A. Lambert

Date: 10/06/09

Memorandum

Date: November 12, 2009

To: File

From: Kevin Lambert

Subject: Inorganic Data Review and Validation – SNL
Site: Burn Site GWM
AR/COC: 612390, 612391, and 612392
SDG: 237978
Laboratory: GEL
Project/Task: 125778,10.11.01
Analysis: General Chemistry

See the attached Data Validation Worksheets for supporting documentation on the data review and validation. This validation was performed according to SNL/NM ER Project AOP 00-03 Rev 2.

Summary

Three samples were prepared and analyzed with accepted procedures using methods EPA 314.0 (perchlorate). Three samples were prepared and analyzed with accepted procedures using methods EPA 9056 (Br, Cl, F, and SO₄ by Ion Chromatography). Five samples were prepared and analyzed with accepted procedures using methods EPA 353.2 (nitrate/nitrite by Cd reduction). Data were reported for all required analytes. Problems were identified with the data package that result in the qualification of data.

1. Perchlorate:

The MS recovery for perchlorate was $\geq 75\%$ but $\geq 30\%$. The perchlorate results for samples 237978-030 and -037 were detects and will be qualified "J-MS3." The other associated sample result was a non-detect and will be qualified "UJ,MS3."

Data are acceptable and reported QC measures appear to be adequate. The following sections discuss the data review and validation.

Holding Times and Preservation

The samples were analyzed within the prescribed holding times and properly preserved.

Calibration

All initial and continuing calibration met QC acceptance criteria.

Blanks

No target analytes were detected in the blanks except as follows.

Ion Chromatography:

Chloride and sulfate were detected in the equipment blank (EB) associated with sample -028 at concentrations \geq the method detection limit (MDL) but $<$ the practical quantitation limit (PQL). The associated sample results were detects $>5X$ the EB result and will not be qualified.

Chloride and sulfate were detected in the EB associated with sample -005 at concentrations \geq the MDL but $<$ the PQL. The associated sample results were detects $>5X$ the EB result and will not be qualified.

Nitrate/Nitrite:

Nitrate/nitrite was detected in the EB associated with samples -006 and -012 at a concentration \geq the MDL but $<$ the PQL. The associated sample results were detects $>5X$ the EB result and will not be qualified.

Laboratory Control Sample (LCS)

All LCS recoveries met QC acceptance criteria.

Matrix Spike (MS)

All MS recoveries met QC acceptance criteria except as noted above in the summary section.

Laboratory Replicate

The replicates met all QC acceptance criteria.

Detection Limits/Dilutions

All detection limits were properly reported. Samples -005 and -028 were diluted 10X for chloride and sulfate due to high concentrations for this analysis. Samples -006 and -012 were diluted 25X and samples -029 and -036 were diluted 50X for nitrate/nitrite due to high concentrations for this analysis. Sample -019 was diluted 5X for nitrate/nitrite due to matrix interference. It should be noted that the relative dilution factors between the samples and associated QC samples were <5 . No sample data will be qualified as a result.

Other QC

EBs and a field duplicate pairs were submitted on the AR/COC(s). There are no "required" review criteria for field duplicate analyses comparability; no data will be qualified as a result. It should be noted that the EB associated with samples -005, -006, and -012 on AR/COC# 612390 are from another SNL SDG (237646) on AR/COC# 612389.

No other specific issues that affect data quality were identified.

Sample Findings Summary

Site: Burn Site GWM

AR/COC: 612390, 612391, 612392

Data Type: Organic, Metals, Gen Chem & Rad

	General Chemistry	Radiochemistry																
	14797-73-0 (perchlorate)	86954-36-1 (americium-241)	10045-97-3 (cesium-137)	10198-40-0 (cobalt-60)	13966-00-2 (potassium-40)	12587-46-1 (gross alpha)	12587-47-2 (gross beta)	10028-17-8 (tritium)										
087732-020 CYN-EB2	UJ,MS3																	
087734-020 CYN-MW6	J-,MS3																	
087735-020 CYN-MW6	J-,MS3																	
087729-033 CYN-MW3		BD,FR3	BD,FR3	BD,FR3	BD,FR3													
087732-033 CYN-EB2		BD,FR3	BD,FR3	BD,FR3	BD,FR3													
087734-033 CYN-MW6		BD,FR3	BD,FR3	BD,FR3	BD,FR3													
087729-034 CYN-MW3						J,FR7	BD,FR3											
087732-034 CYN-EB2						BD,FR3	BD,FR3											
087734-034 CYN-MW6						J,FR7	J,FR7											
087729-036 CYN-MW3								BD,FR3										
087732-036 CYN-EB2								BD,FR3										
087734-036 CYN-MW6								BD,FR3										
DRO, GRO, Ion chromatography, and nitrate/nitrite analyses met QC acceptance criteria. No data will be qualified.																		

Memorandum

DATE: November 11, 2009
TO: File
FROM: David Schwent
SUBJECT: General Chemistry Data Review and Validation - SNL
Site: TAV GWM
AR/COC: 612366, 612367, and 612368
SDG: 237241
Laboratory: GEL
Project/Task No: 125778.10.11.01

See the attached Data Validation Worksheets for supporting documentation on the data review and validation. This validation was performed according to SNL/NM ER Project AOP 00-03 Rev 2.

Summary

The samples were prepared and analyzed with accepted procedures using EPA314.0 (perchlorate), EPA353.2 (nitrate/nitrite by Cd reduction), and EPA9056 (anions). No problems were identified with the data package that result in the qualification of data.

Perchlorate Analysis:

Holding Time/Preservation: The samples were analyzed beyond the method specified holding time, but within 2X the holding time. All associated sample results were non-detects (NDs) and will be qualified "UJ,H1."

MS/MSD: The MS (PS) percent recovery (%R) of perchlorate was <75% but \geq 30%. All associated sample results were NDs and will be qualified "UJ,MS3."

Anions Analysis:

Blanks: Sulfate was detected in the continuing calibration blank (CCB) at a concentration > the method detection limit (MDL) but < the practical quantitation limit (PQL). The associated result of sample 237241-011 was a detect <5X the CCB concentration and will be qualified "1.4U,B3" at 5X the value of the CCB.

Data are acceptable. QC measures appear to be adequate. The following sections discuss the data review and validation.

Holding Times/Preservation

Perchlorate Analysis: All samples were analyzed within the prescribed holding times and properly preserved, except as noted above in the summary section.

All Other Analyses: All samples were analyzed within the prescribed holding times and properly preserved.

Calibration

All Analyses: All initial and continuing calibration QC acceptance criteria were met.

Blanks

Perchlorate Analysis: No target analytes were detected in the blanks.

Anions Analysis: No target analytes were detected in the blanks, except as noted above in the summary section and the following. Chloride was detected in the equipment blank (EB) (sample -011) at a concentration > the MDL but < the PQL. However, all associated sample results were detects >5X the EB concentration and will not be qualified. It should be noted that the sulfate result of the EB was qualified ND "U" due to CCB contamination and, therefore, cannot affect other field sample results. It should also be noted that the results of the EB only apply to samples on COC 612368.

Nitrate/nitrite Analysis: No target analytes were detected in the blanks, except the following. Nitrate/nitrite was detected in the method blank (MB) at a concentration > the MDL but < the PQL. However, all associated sample results were detects >5X the MB concentration and will not be qualified.

Laboratory Control Sample (LCS)

All Analyses: All LCS QC acceptance criteria were met.

Matrix Spike/Matrix Spike Duplicate (MS/MSD)

Perchlorate Analysis: All MS (PS) QC acceptance criteria were met, except as noted above in the summary section. No MSD (PSD) analysis was performed. The replicate analysis was used as a measure of laboratory precision. No sample data will be qualified as a result.

All Other Analyses: All MS (PS) QC acceptance criteria were met. No MSD (PSD) analyses were performed. The replicate analyses were used as measures of laboratory precision. No sample data will be qualified as a result.

Replicates

All Analyses: All replicate QC acceptance criteria were met.

Detection Limits/Dilutions

Perchlorate Analysis: All detection limits were properly reported. No samples required dilution.

Anions Analysis: All detection limits were properly reported. Samples -019 and -027 were diluted 10X for chlorate and sulfate and sample -003 was diluted 25X for chloride and sulfate due to high concentrations of the target analytes. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Nitrate/nitrite Analysis: All detection limits were properly reported. Samples -004, -020, and -028 were diluted 25X for nitrate/nitrite due to high concentration of the target analyte and sample -012 was diluted 5X due to matrix inference. All associated batch QC samples were analyzed at dilution factors that resulted in relative dilution factors to the samples that were $\leq 5X$. No sample data will be qualified as a result.

Other QC

All Analyses: No field blanks (FBs) were submitted on the AR/COCs. All relative percent differences (RPDs) of the field duplicates (FDs) (samples -027, -028, and -029) were $< 20\%$. No QC acceptance criteria for the evaluation of FDs are currently in place.

No other specific issues were identified that affect data quality.

