Allen, Pam, NMENV

ENTERED

From: Maestas, Ricardo, NMENV
Sent: Thursday, June 26, 2014 2:17 PM
To: Allen, Pam, NMENV
Subject: FW: NMED Questions
Attachments: Station A and B Filter Readings 2014.xlsx

March

From: Skibitski, Thomas, NMENV
Sent: Thursday, March 13, 2014 1:27 PM
To: Kliphuis, Trais, NMENV; Flynn, Ryan, NMENV; Kendall, Jeff, NMENV
Cc: Tongate, Butch, NMENV; Winchester, Jim, NMENV; Blaine, Tom, NMENV; Schwender, Erika, NMENV; Kieling, John, NMENV; Nelson, Morgan, NMENV; Maestas, Ricardo, NMENV; Smith, Coleman, NMENV; Holmes, Steve, NMENV; LucasKamat, Susan, NMENV; Turner, Jill, NMENV
Subject: RE: NMED Questions

Please see the attached, tab "combined numbers"
Blue highlighted columns are what we should expect to see IF the design efficiency was indeed 99.97%.

I multiplied the station a data by 0.9997
TS

From: Kliphuis, Trais, NMENV
Sent: Wednesday, March 12, 2014 12:44 PM
To: Flynn, Ryan, NMENV; Kendall, Jeff, NMENV
Cc: Tongate, Butch, NMENV; Winchester, Jim, NMENV; Blaine, Tom, NMENV; Schwender, Erika, NMENV; Skibitski, Thomas, NMENV; Kieling, John, NMENV; Nelson, Morgan, NMENV; Maestas, Ricardo, NMENV; Smith, Coleman, NMENV; Holmes, Steve, NMENV; LucasKamat, Susan, NMENV; Turner, Jill, NMENV
Subject: NMED Questions

Trais Kliphuis
WIPP Staff Manager
Hazardous Waste Bureau
New Mexico Environment Department
2905 Rodeo Park Drive E, Building 1
Santa Fe, New Mexico 87505

Office: 505-476-6051
Front Desk: 505-476-6000

From: Kliphuis, Trais, NMENV
Sent: Wednesday, March 12, 2014 12:44 PM
To: 'Oba Vincent'; 'peake.tom@epa.gov'; 'Edwards, Jonathan'; 'Walsh, Jonathan'; 'Perrin, Alan'; 'Bob.Kehrman@wipp.ws'; 'Rick.Chavez@wipp.ws'; 'Stone.Nick@epa.gov'; Smith, Coleman, NMENV; 'brozowski.george@epa.gov'; 'Fraass, Ron'
Cc: George Basabilvazo - WIPPNet; 'Reynolds, Tammy - NWP (Tammy.Reynolds@wipp.ws)'; 'Pace, Berry (Berry.Pace@wipp.ws)'; 'Alton.Harris@em.doe.gov'; Susan McCauslin; 'Joe Harvill (jharvill@portageinc.com)'; 'Kennedy, Scott - NWP (Scott.Kennedy@wipp.ws)'; 'Jones, Stewart - RES'; 'Berta Oates'
Subject: RE: WIPP Information - for call today

Please see the attached document listing our questions regarding the filtration system. Thanks.

140395

Trais Kliphuis
WIPP Staff Manager
Hazardous Waste Bureau
New Mexico Environment Department
2905 Rodeo Park Drive E, Building 1
Santa Fe, New Mexico 87505

Office: 505-476-6051
Front Desk: 505-476-6000

From: Oba Vincent [mailto:oba.vincent@cbfo.doe.gov]
Sent: Tuesday, March 11, 2014 12:23 PM
To: Kliphuis, Trais, NMENV; 'peake.tom@epa.gov'; 'Edwards, Jonathan'; 'Walsh, Jonathan'; 'Perrin, Alan'; 'Bob.Kehrman@wipp.ws'; 'Rick.Chavez@wipp.ws'; 'Stone.Nick@epa.gov'; Smith, Coleman, NMENV; 'brozowski.george@epa.gov'; 'Fraass, Ron'
Cc: George Basabilvazo - WIPPNet; 'Reynolds, Tammy - NWP (Tammy.Reynolds@wipp.ws)'; 'Pace, Berry (Berry.Pace@wipp.ws)'; 'Alton.Harris@em.doe.gov'; Susan McCauslin; 'Joe Harvill (jharvill@portageinc.com)'; 'Kennedy, Scott - NWP (Scott.Kennedy@wipp.ws)'; 'Jones, Stewart - RES'; 'Berta Oates'
Subject: WIPP Information - for call today

Attached are the tables and graph with the environmental data. Also attached is a revised version of the Consequence Assessment.
Thanks

Oba

Preliminary Information - Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/14/14	2/14/14 0742	2/15/14 0630	A23021414	Tennelec XLB	10 Mins	4.4M	1.2M	021514/0649				WIPP Labs
2/15/14	2/15/14 0630	2/15/14 0840	A23021514	Tennelec XLB	10 Mins	225K	46.8K	021514/0916				WIPP Labs
2/15/14	2/15/14 0840	2/15/14 1510	A23021514 0840	Tennelec XLB	10 Mins	285K	54K	021514/1541				SRS Lab
2/15/14	2/15/14 1510	2/15/14 2330	A23021514 1510	Tennelec XLB	10 Mins	124050	24481	021614/0012				SRS Lab
2/15/14	2/15/14 2330	2/16/14 0850	A23021514 2330	Tennelec XLB	10 Mins	47283	10558	021614/0917				On Site
2/16/14	2/16/14 0850	2/16/14 1648	A23021614 0850	Tennelec XLB	10 Mins	12215	2842	121614/1927				On Site
2/16/14	2/16/14 1648	2/17/14 0015	A23021614 1650	Tennelec XLB	10 Mins	4051	1256	021714/0046				On Site
2/17/14	2/17/14 0015	2/17/14 0820	A23021714 0015	Tennelec XLB	10 Mins	1802	638	021714/0942	1723	573	021714/1012	On Site
2/17/14	2/17/14 0820	2/17/14 1620	A23021714 0820	Tennelec XLB	10 Mins	1048	621	021714/1705				On Site
2/17/14	2/17/14 1620	2/18/14 0010	A23021714 1620	Tennelec XLB	10 Mins	802	633	021814/0051	633 592	230 210	021814/1012 021814/0751	On Site
2/18/14	2/18/14 0010	2/18/14 0820	A23021814 0010	Tennelec XLB	10 Mins	326	338	021814/0928	237 212	157 116	021814/1202 021814/1824	On Site
2/18/14	2/18/14 0820	2/18/14 1605	A23021814 0820	Tennelec XLB	10 Mins	609	780	021814/1624	258	118	021914/0315	On Site
2/18/14	2/18/14 1605	2/19/14 0035	A23021814 1605	Tennelec XLB	10 Mins	346	340	021914/0143	227	143	021914/0547	On Site
2/19/14	2/19/14 0035	2/19/14 0823	A23021914 0040	Tennelec XLB	10 Mins	224	320	021914/0952	136	143	021914/1222	On Site

Preliminary Information – Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/19/14	2/19/14 0823	2/19/14 1600	A23021914 0823	Tennelec XLB	10 Mins	264	443	021914/1708	130	137	021914/2046	On-Site
2/19/14	2/19/14 1600	2/20/14 0018	A23021914 1600	Tennelec XLB	10 Mins	286	378	022014/0124	150	119	02214/0352	On-Site
2/19/14	2/19/14 0018	2/20/14 0817	A23022014 0018	Tennelec XLB	10 Mins	290	219	022014/1010	216	146	022014/1256	On-Site
2/20/14	2/20/14 0817	2/20/14 1624	A23022014 0817	Tennelec XLB	10 Mins	135	131	0222014/1838	107	85	022014/2204	On-Site
2/20/14	2/20/14 1624	2/21/14 0012	A23022014 1624	Tennelec XLB	10 Mins	231	103	022114/0154	203	84	022114/0505	On-Site
2/21/14	2/21/14 0012	2/21/14 0845	A23022114 0012	Tennelec XLB	10 Mins	330	146	022114/1027	286	105	022114/1532	On-Site
2/21/14	2/21/2014 0845	2/21/2014 1620	A230221140845	Tennelec XLB	10 Mins	253	199	022114/1654	175	86	022114/2000	On-Site
2/21/14	2/21/2014 1620	2/22/2014 0050	A230221141620	Tennelec XLB	10 Mins	388	549	022114/0124	215	154	022114/0400	On-Site
2/22/14	2/22/2014 0050	2/22/2014 0830	A230222140050	Tennelec XLB	10 Mins	421	599	022214/0906	180	154	022214/1150	On-Site
2/22/14	2/22/2014 0830	2/22/2014 1650	A230222140830	Tennelec XLB	10 Mins	243	337	022214/1713	140	166	022214/2004	On-Site
2/22/14	2/22/2014 1650	2/23/2014 0011	A230222141650	Tennelec XLB	10 Mins	487	626	022314/0047	208	129	022314/0401	On-Site
2/23/14	2/23/2014 0011	2/23/2014 0830	A230223140011	Tennelec XLB	10 Mins	328	504	022314/0906	162	167	022314/1222	On-Site
2/23/14	2/23/2014 0830	2/23/2014 1615	A230223140830	Tennelec XLB	10 Mins	225	340					On-Site
2/23/14	2/23/2014 1615	2/24/2014 0025	A230223141615	Tennelec XLB	10 Mins	412	696	022414/0048	102	109	022414/0405	On-Site
2/24/14	2/24/2014 0025	2/24/2014 0912	A230224140025	Tennelec XLB	10 Mins	195	309	022414/1137	149	213	022414/1540	On-Site

Preliminary Information - Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/24/14	2/24/2014 0912	2/24/14 1702	A230224140912	Tennelec XLB	10 Mins	437	740	022414/1733	141	214	022414/2031	On-Site
2/24/14	2/24/14 1702	2/25/14 0005	A230224141702	Tennelec XLB	10 Mins	429	796	022514/0029	91	138	022514/0355	On-Site
2/25/14	2/25/14 0005	2/25/14 0830	A230225140005	Tennelec XLB	10 Mins	381	618	022514/0951	138	194	022514/1349	On-Site
2/25/14	2/25/14 0830	2/25/14 1628	A120225140830	Tennelec XLB	10 Mins	544	962	022514/ 1730	165	277	022514/ 2000	On-Site
2/25/14	2/25/14 1628	2/26/14 0025	A230225141628	Tennelec XLB	10 Mins	647	1140	022614/0100	161	263	022614/0407	On-Site
2/26/14	2/26/14 0025	2/26/14 0845	A230226140025	Tennelec XLB	10 Mins	307	487	022614/ 0958	158	225	022614/1354	On-Site
2/26/14	2/26/14 0845	2/26/14 1640	A230226140845	Tennelec XLB	10 Mins	377	579	022614/ 1729				On-Site
2/26/14	2/26/14 1640	2/27/14 0015	A230226141640	Tennelec XLB	10 Mins	458	826	022714/ 0052	114	172	022714/ 0408	On-Site
2/27/14	2/27/14 0015	2/27/14 0903	A230227140015	Tennelec XLB	10 Mins	685	1198	022714/ 0932	191	340	022714/ 1225	On-Site
2/27/14	2/27/2014 0903	2/27/14 1651	A230227140903	Tennelec XLB	10 Mins	457	793	022714/1726	78	103	022814/ 0424	On-Site
2/28/14	2/27/2014 1651	2/28/14 0015	A230227141651	Tennelec XLB	10 Mins	239	423	022812/0046	52	90	022814/ 0401	On-Site
2/28/14	2/28/14 0015	2/28/14 0835	A230228140015	Tennelec XLB	10 Mins	81	136	022814/1032	49	81	022814/ 1417	On-Site
2/28/14	2/28/14 0835	02/28/14 1615	A230228140835	Tennelec XLB	10 Mins	84	127	022814 / 1820	43	91	022814 / 2119	On-Site
3/1/14	2/28/14 1615	3/1/14 0104	A230228141615	Tennelec XLB	10 Mins	133	208	022814 / 0235	60	89	030114 / 0527	On-Site
3/1/14	3/1/14 0104	3/1/14 0855	A230301140104	Tennelec XLB	10 Mins	224	440	030114/0956	73	116	030114/1257	On-Site

Preliminary Information – Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
3/1/14	3/1/14 0855	3/1/14 1656	A230301140855	Tennelec XLB	10 Mins	186	354	030114/ 0536	69	94	030114/ 2109	On-Site
3/1/14	3/1/14 1656	3/2/14 0007	A230301141656	Tennelec XLB	10 Mins	121	213	030214/ 0107	47	55	030214/ 0512	On-Site
3/2/14	3/2/14 0007	3/2/14 0825	A230302140007	Tennelec XLB	10 Mins	918	1638	030214/0836	122	218	030214/ 1155	On-Site
3/2/14	3/2/14 0825	3/2/14 1650	A230302140825	Tennelec XLB	10 Mins	563	973	030214/ 1732	155	311	030214/ 0924	On-Site
3/2/14	3/2/14 1650	3/3/14 0106	A230302141650	Tennelec XLB	10 Mins	359	621	030314/0158	150	258	030314/ 0537	On-Site
3/3/14	3/3/14 0106	3/3/14 0817	A230303140106	Tennelec XLB	10 Mins	264	468	030314/ 0915	118	201	030314/ 1217	On-Site
3/3/14	3/3/14 0817	3/3/2014 1630	A230303140817	Tennelec XLB	10 Mins	380	699	030314/ 1704	97	172	030314/ 2103	On-Site
3/3/14	3/3/2014 1630	3/4/14 0034	A230303141630	Tennelec XLB	10 Mins	191	340	030414/ 0207	93	147	030414/ 0543	On-Site
3/4/14	3/4/14 0034	3/4/14 0817	A230304140034	Tennelec XLB	10 Mins	479	757	030414/ 0900	135	199	030414/1130	On-Site
3/4/14	3/4/14 0817	3/4/14 1557	A230304140817	Tennelec XLB	10 Mins	384	586	030414/ 1639	120	129	030414/ 1957	On-Site
3/4/14	3/4/14 1557	3/5/14 0022	A230304141557	Tennelec XLB	10 Mins	399	753	030514/ 0051	74	143	030514/ 0351	On-Site

Station A (A-2-3) Before the HEPA Filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location

Preliminary Information-Not for Public Release

Station B (B-1-3) Downstream of the HEPA filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/14/14	2/14/14 0754	2/15/14 0835	B13021414	Tennelec XLB	10 Mins	28205	5877	021514/0850				WIPP Labs
2/15/14	2/15/14 0835	2/15/14 1445	B13021514	Tennelec XLB	10 Mins	36194	7340					SRS Labs
2/15/14	2/15/14 1445	2/15/14 2305	B130215141445	Tennelec XLB	10 Mins	671	142	021714/1056				On-Site
2/15/14	2/15/14 2305	2/16/14 0904	B130215142305	Tennelec XLB	10 Mins	300	152	021614/0932	253 245 240	63 59 49	021614/1127 021614/1250 021614/1741	On-Site
2/16/14	2/16/14 0904	2/16/14 1705	B130216140904	Tennelec XLB	10 Mins	144	67	021614/1755				On-Site
2/16/14	2/16/14 1705	2/17/2014 0030	B130216141705	Tennelec XLB	10 Mins	72	54	021714/0046	62	18	021714/1203	On-Site
2/17/14	2/17/14 0030	2/17/14 0805	B130216140030	Tennelec XLB	10 Mins	43	26	021714/0930	30 32	23 16	021714/0955 021714/1400	On-Site
2/17/14	2/17/14 0805	2/17/14 1600	B130217140805	Tennelec XLB	10 Mins	78	35	021714/1650	58 24	20 13	021714/1958 021814/1823	On-Site
2/17/14	2/17/14 1600	2/18/14 0030	B130217141600	Tennelec XLB	10 Mins	65	55	021814/0051	45 36	18 12	021814/0423 021814/0751	On-Site
2/18/14	2/18/14 0030	2/18/14 0901	B130218140030	Tennelec XLB	10 Mins	42	61	021814/0928	23	12	021814/1202	On-Site
2/18/14	2/18/14 0901	2/18/14 1655	B130218140901	Tennelec XLB	10 Mins	41	29	021814/1754	28	7	021914/0315	On-Site
2/18/14	2/18/14 1655	2/19/14 0105	B130218141655	Tennelec XLB	10 Mins	42	36	021914/0144	20	7	021914/0547	On-Site
2/19/14	2/19/14 0105	2/19/14 0900	B130219140105	Tennelec XLB	10 Mins	33	44	021914/0952	20	15	021914/1222	On-Site
2/19/14	2/19/14 0900	2/19/14 1627	B130219140900	Tennelec XLB	10 Mins	36	34	021914/1708	25	10	021914/2036	On-Site

Station B (B-1-3) Downstream of the HEPA filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/19/14	2/19/14 1627	2/20/14 0035	B130219141627	Tennelec XLB	10 Mins	45	46	022014/0107	25	9	022014/0359	On-Site
2/20/14	2/20/14 0035	2/20/14 0852	B130220140035	Tennelec XLB	10 Mins	52	21	022014/1035	38	14	022014/1226	On-Site
2/20/14	2/20/14 0852	2/20/14 1654	B130220140852	Tennelec XLB	10 Mins	98	22	022014/1838	101	23	022014/2211	On-Site
2/20/14	2/20/14 1654	2/21/14 0038	B130220141654	Tennelec XLB	10 Mins	40	19	022114/0204	33	11	022114/0521	On-Site
2/21/14	2/21/14 0038	2/21/14 0820	B130221140038	Tennelec XLB	10 Mins	30	6	022114/1027	27	12	022114/1532	On-Site
2/21/14	2/21/14 0820	2/21/14 1600	B130221140820	Tennelec XLB	10 Mins	37	15	022114/1654	41	12	022114/2028	On-Site
2/21/14	2/21/14 1600	2/22/14 0019	B130221141600	Tennelec XLB	10 Mins	50	28	022214/0125	42	14	022214/0358	On-Site
2/22/14	2/22/14 0019	2/22/14 0810	B130222140019	Tennelec XLB	10 Mins	30	22	022214/0946	19	12	022214/1151	On-Site
2/22/14	2/22/14 0810	2/22/14 1615	B130222140810	Tennelec XLB	10 Mins	28	17	022214/1713	22	10	022214/2004	On-Site
2/22/14	2/22/14 1615	2/22/14 2356	B130222141615	Tennelec XLB	10 Mins	32	33	022314/0047	22	9	022314/0404	On-Site
2/22/14	2/22/14 2356	2/23/14 0810	B130222142356	Tennelec XLB	10 Mins	21	29	022314/0938	19	17	022314/1227	On-Site
2/23/14	2/23/14 0810	2/23/14 1605	B130223140810	Tennelec XLB	10 Mins	7	22	022314/1642	17	7	022314/2010	On-Site
2/23/14	2/23/14 1605	2/23/14 0015	B130223141605	Tennelec XLB	10 Mins	40	54	022414/0054	19	13	022414/0401	On-Site
2/24/14	2/24/14 0015	2/24/14 0846	B130224140015	Tennelec XLB	10 Mins	14	19	022414/1136	14	14	022414/1540	On-Site
2/24/14	2/24/14 0846	2/24/14 1635	B130224140846	Tennelec XLB	10 Mins	22	28	022414/1733	8	8	022414/2031	On-Site

Preliminary Information-Not for Public Release

Station B (B-1-3) Downstream of the HEPA filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
2/24/14	2/24/14 1635	2/25/14 0016	B130224141635	Tennelec XLB	10 Mins	45	72	022514/0029	8	12	022514/0404	On-Site
2/25/14	2/25/14 0016	2/25/14 0902	B130225140016	Tennelec XLB	10 Mins	41	53	022514/ 1012	14	21	022514/1403	On-Site
2/25/14	2/25/14 0902	2/25/14 1652	B130225140902	Tennelec XLB	10 Mins	39	59	022514/ 1742	12	7	022514/ 2000	On-Site
2/25/14	2/25/14 1652	2/26/14 0010	B130225141652	Tennelec XLB	10 Mins	27	41	022614/ 0101	12	10	022614/ 0450	On-Site
2/26/14	2/26/14 0010	2/26/14 0921	B130226140010	Tennelec XLB	10 Mins	26	21	022614/ 1051	23	16	022614/ 1423	On-Site
2/26/14	2/26/14 0921	2/26/2014 1616	B130226140921	Tennelec XLB	10 Mins	22	25	022614/ 1727				On-Site
2/26/14	2/26/14 1616	2/27/14 0030	B130226141616	Tennelec XLB	10 Mins	33	59	022714/ 0129	11	14	022714/0408	On-Site
2/27/14	2/27/14 0030	2/27/14 0806	B130227140030	Tennelec XLB	10 Mins	22	37	022714/ 0929	7	22	022714/1153	On-Site
2/27/14	2/27/14 0806	2/28/14 0012	B130227140806	Tennelec XLB	10 Mins	27	41	022814/ 0046	16	10	022814/0401	On-Site
2/28/14	02/28/14 0012	2/28/14 0927	B130228140012	Tennelec XLB	10 Mins	14	20	022814 / 102	8	5	022814/1408	On-Site
2/28/14	2/28/14 0927	2/28/14 1705	B130228140927	Tennelec XLB	10 Mins	6	7	022814 / 182	5	3	022814/1919	On-Site
3/1/14	2/28/14 1705	3/1/14 0144	B130228141705	Tennelec XLB	10 Mins	16	28	030114 / 023	6	5	030114 / 0528	On-Site
3/1/14	3/1/14 0144	3/1/14 0915	B130301140144	Tennelec XLB	10 Mins	21	35	030114/ 0957	6	8	030114/1257	On-Site
3/1/14	3/1/14 0915	3/1/14 1620	B130301140915	Tennelec XLB	10 Mins	10	10	030114/ 0535	4	1	030114/ 0910	On-Site
3/1/14	3/1/14 1620	3/2/14 0045	B130301141620	Tennelec XLB	10 Mins	17	16	030214/0108	9	5	030214/ 0512	On-Site

Preliminary Information Not for Public Release

Station B (B-1-3) Downstream of the HEPA filters

Date	Time Installed	Time Removed	Filter ID	Inst Model	Count Time	Alpha (dpm)	Beta (dpm)	First Count	Alpha (dpm)	Beta (dpm)	Re-count	Location
3/2/14	3/2/14 0045	3/2/14 0850	B130302140045	Tennelec XLB	10 Mins	51	81	030214/ 0925	19	20	030214/ 1156	On-Site
3/2/14	3/2/14 0850	3/2/14 1630	B130302140850	Tennelec XLB	10 Mins	51	37	030214/ 1723	34	18	030214/ 2122	On-Site
3/2/14	3/2/14 1630	3/3/14 0106	B130302141630	Tennelec XLB	10 Mins	17	28	030314/ 0152	7	13	030314/ 0559	On-Site
3/3/14	3/3/14 0106	3/3/14 0820	B130303140106	Tennelec XLB	10 Mins	26	39	030314/ 0855	9	14	030314/ 1217	On-Site
3/3/14	3/3/14 0820	3/3/14 1620	B130303140820	Tennelec XLB	10 Mins	19	48	030314/ 1812	2	6	030314/ 1812	On-Site
3/3/14	3/3/14 1620	3/4/14 0114	B130303141620	Tennelec XLB	10 Mins	22	33	030414/ 0208	5	8	030414/ 0543	On-Site
3/4/14	3/4/14 0114	3/4/14 0815	B130304140114	Tennelec XLB	10 Mins	31	49	030414/ 0846	8	11	030414/ 1130	On-Site
3/4/14	3/4/14 0815	3/4/14 1610	B130304140815	Tennelec XLB	10 Mins	18	26	030414/ 1639	4	4	030414/ 1957	On-Site
3/4/14	3/4/14 1610	3/5/14 0005	B130304141610	Tennelec XLB	10 Mins	21	34	030514/ 0051	5	5	030514/ 0351	On-Site

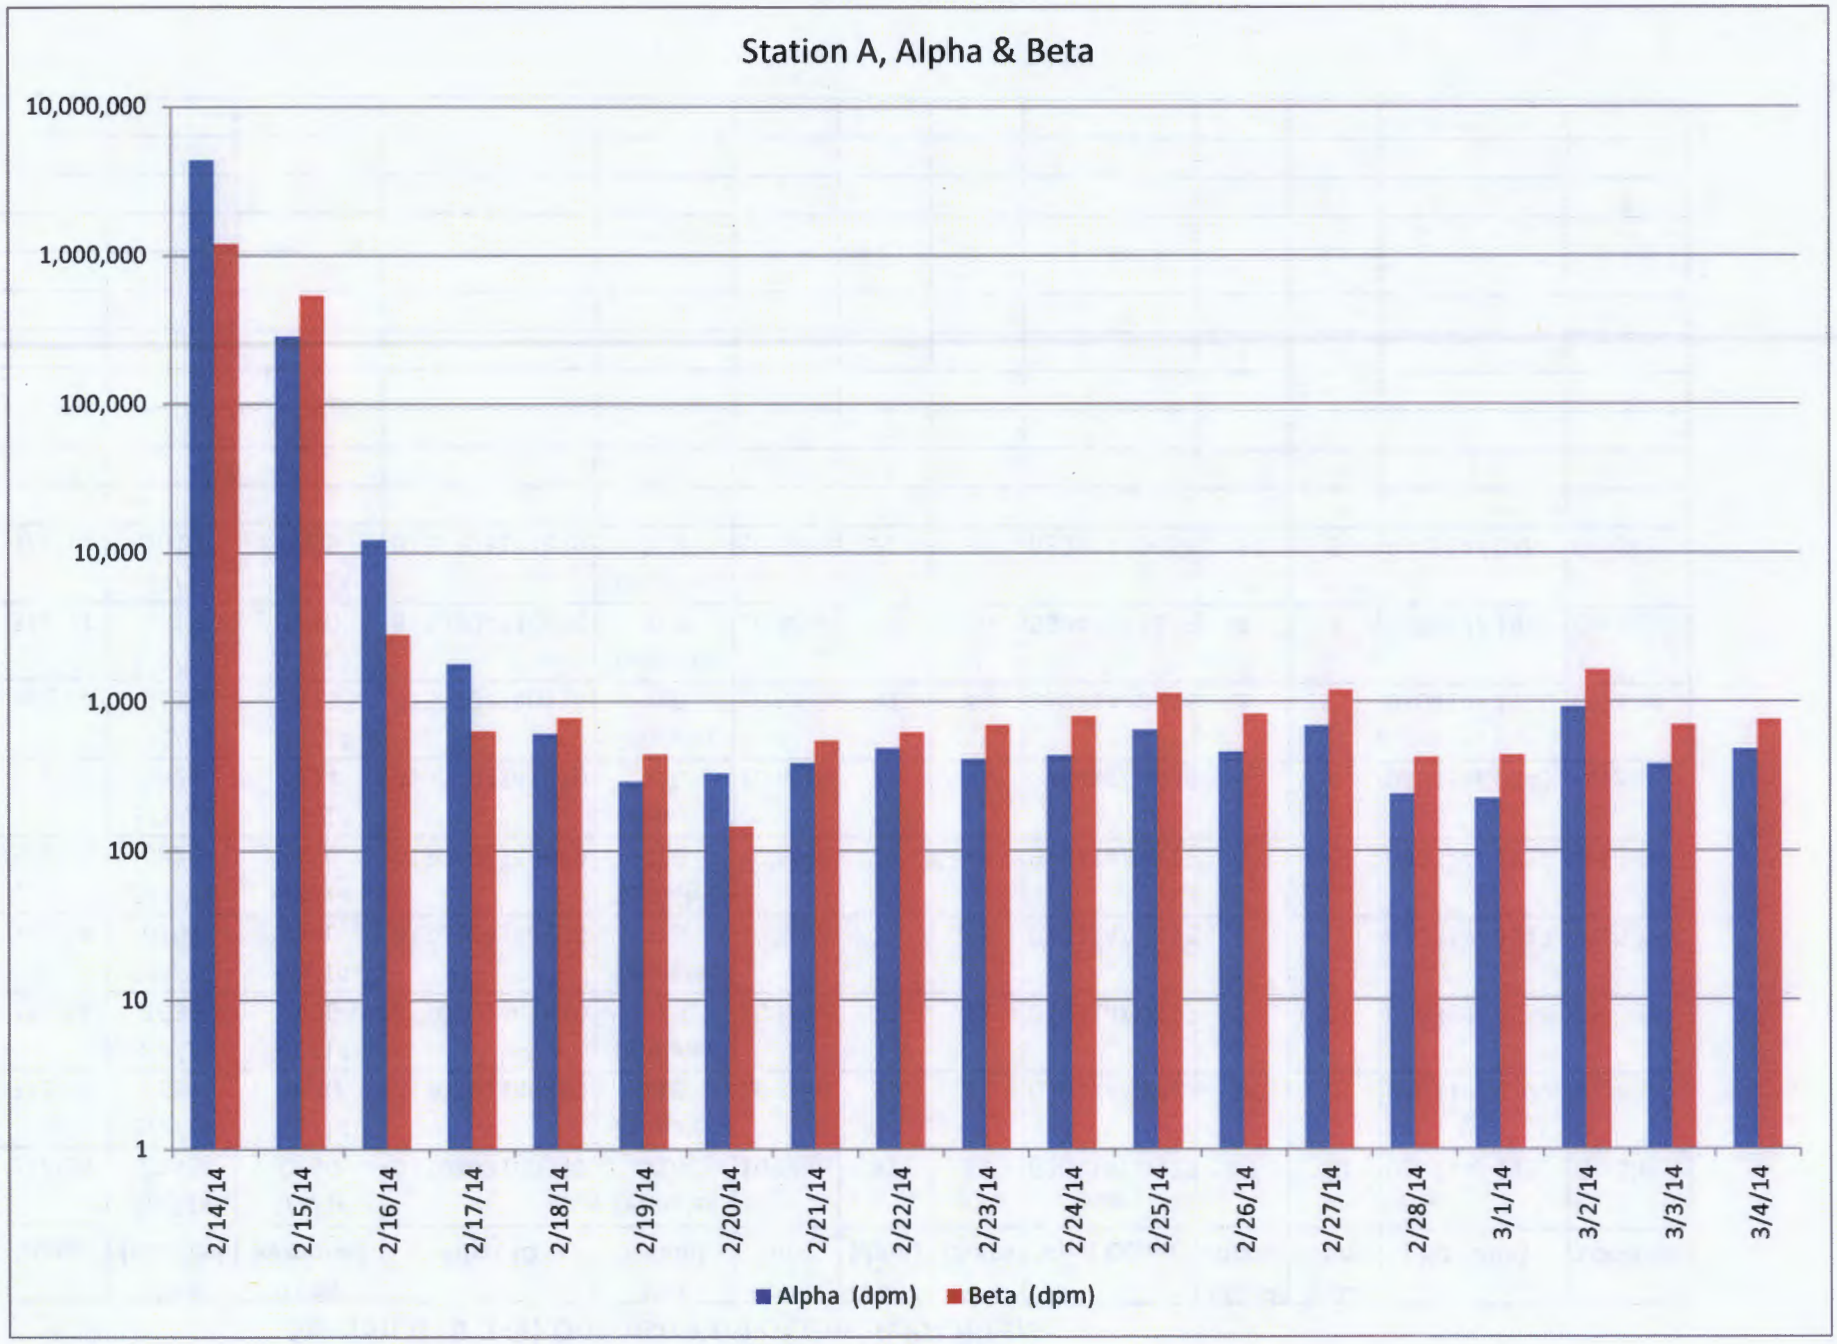
Station A, Alpha & Beta
10,000,000
1,000,000
100,000
10,000
1,000
100
10
1
2/14/14
2/15/14
2/16/14
2/17/14
2/18/14
2/19/14
2/20/14
2/21/14
2/22/14
2/23/14
2/24/14
2/25/14
2/26/14
2/27/14
2/28/14
3/1/14
3/2/14
3/3/14
3/4/14
Alpha (dpm)
Beta (dpm)

Preliminary Information – Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Installed, Date/Time	Removed, Date/Time	(Time) Hours : Minutes	Filter ID	Count Time	Alpha (dpm)	Beta (dpm)	First Count, Date/Time	Alpa (dpm)	Beta (dpm)	Re-count, Date/Time	(Time) Hrs:Min: Sec
2/14/14	2/14/14 7:42	2/15/14 6:30	22:48:00	A23021414	10 Mins	4,400,000	1,200,000	2/15/14 6:49				
2/15/14	2/15/14 6:30	2/15/14 8:40	2:10:00	A23021514	10 Mins	225,000	468,000	2/15/14 9:16				
2/15/14	2/15/14 8:40	2/15/14 15:10	6:30:00	A23021514 0840	10 Mins	285,000	540,000	2/15/14 15:41				
2/15/14	2/15/14 15:10	2/15/14 23:30	8:20:00	A23021514 1510	10 Mins	124,050	24,481	2/16/14 0:12				
2/15/14	2/15/14 23:30	2/16/14 8:50	9:20:00	A23021514 2330	10 Mins	47,283	10,558	2/16/14 9:17				
2/16/14	2/16/14 8:50	2/16/14 16:48	7:58:00	A23021614 0850	10 Mins	12,215	2,842	2/16/14 19:27				
2/16/14	2/16/14 16:48	2/17/14 0:15	7:27:00	A23021614 1650	10 Mins	4,051	1,256	2/17/14 0:46				
2/17/14	2/17/14 0:15	2/17/14 8:20	8:05:00	A23021714 0015	10 Mins	1,802	638	2/17/14 9:42	1,723	573	2/17/14 10:12	0:30:00
2/17/14	2/17/14 8:20	2/17/14 16:20	8:00:00	A23021714 0820	10 Mins	1,048	621	2/17/14 17:05				
2/17/14	2/17/14 16:20	2/18/14 0:10	7:50:00	A23021714 1620	10 Mins	802	633	2/18/14 0:51	592	210	2/18/14 7:51	7:00:00
2/17/14	*2/17/14 16:20*	*2/18/14 0:10*	*7:50:00*	*Recount*				*2/18/14 0:51*	*633*	*230*	*2/18/14 10:12*	*9:21:00*
2/18/14	2/18/14 0:10	2/18/14 8:20	8:10:00	A23021814 0010	10 Mins	326	338	2/18/14 9:28	237	157	2/18/14 12:02	2:34:00
2/18/14	*2/18/14 0:10*	*2/18/14 8:20*	*8:10:00*	*Recount*				*2/18/14 9:28*	*212*	*116*	*2/18/14 18:24*	*8:56:00*
2/18/14	2/18/14 8:20	2/18/14 16:05	7:45:00	A23021814 0820	10 Mins	609	780	2/18/14 16:24	258	118	2/19/14 3:15	10:51:00
2/18/14	2/18/14 16:05	2/19/14 0:35	8:30:00	A23021814 1605	10 Mins	346	340	2/19/14 1:43	227	143	2/19/14 5:47	4:04:00
2/19/14	2/19/14 0:35	2/19/14 8:23	7:48:00	A23021914 0040	10 Mins	224	320	2/19/14 9:52	136	143	2/19/14 12:22	2:30:00
2/19/14	2/19/14 8:23	2/19/14 16:00	7:37:00	A23021914 0823	10 Mins	264	443	2/19/14 17:08	130	137	2/19/14 20:46	3:38:00

Preliminary Information – Not for Public Release
Station A (A-2-3) Before the HEPA Filters

Date	Installed, Date/Time	Removed, Date/Time	(Time) Hours : Minutes	Filter ID	Count Time	Alpha (dpm)	Beta (dpm)	First Count, Date/Time	Alpa (dpm)	Beta (dpm)	Re-count, Date/Time	(Time) Hrs:Min: Sec
2/19/14	2/19/14 16:00	2/20/14 0:18	8:18:00	A23021914 1600	10 Mins	286	378	2/20/14 1:24	150	119	2/21/04 3:52	
2/19/14	2/19/14 0:18	2/20/14 8:17	31:59:00	A23022014 0018	10 Mins	290	219	2/20/14 10:10	216	146	2/20/14 12:56	2:46:00
2/20/14	2/20/14 8:17	2/20/14 16:24	8:07:00	A23022014 0817	10 Mins	135	131	2/20/14 18:38	107	85	2/20/14 22:04	3:26:00
2/20/14	2/20/14 16:24	2/21/14 0:12	7:48:00	A23022014 1624	10 Mins	231	103	2/21/14 1:54	203	84	2/21/14 5:05	3:11:00
2/20/14	2/21/14 0:12	2/21/14 8:45	8:33:00	A23022114 0012	10 Mins	330	146	2/21/14 10:27	286	105	2/21/14 15:32	5:05:00
2/21/14	2/21/14 8:45	2/21/14 16:20	7:35:00	A23022114 0845	10 Mins	253	199	2/21/14 16:54	175	86	2/21/14 20:00	3:06:00
2/21/14	2/21/14 16:20	2/22/14 0:50	8:30:00	A23022114 1620	10 Mins	388	549	2/22/14 1:24	215	154	2/22/14 4:00	2:36:00
2/22/14	2/22/14 0:50	2/22/14 8:30	7:40:00	A23022214 0050	10 Mins	421	599	2/22/14 9:06	180	154	2/22/14 11:50	2:44:00
2/22/14	2/22/14 16:50	2/23/14 0:11	7:21:00	A23022214 1650	10 Mins	487	626	2/23/14 0:47	208	129	2/23/14 4:01	3:14:00
2/23/14	2/23/14 0:11	2/23/14 8:30	8:19:00	A23022314 0011	10 Mins	328	504	2/23/14 9:06	162	167	2/23/14 12:22	3:16:00
2/23/14	2/23/14 8:30	2/23/14 16:15	7:45:00	A23022314 0830	10 Mins	225	340					
2/23/14	2/23/14 16:15	2/24/14 0:25	8:10:00	A23022314 1615	10 Mins	412	696	2/24/14 0:48	102	109	2/24/14 4:05	3:17:00
2/24/14	2/24/14 0:25	2/24/14 9:12	8:47:00	A23022414 0025	10 Mins	195	309	2/24/14 11:37	149	213	2/24/14 15:40	4:03:00
2/24/14	2/24/14 9:12	2/24/14 17:02	7:50:00	A23022414 0912	10 Mins	437	740	2/24/14 17:33	141	214	2/24/14 20:31	2:58:00
2/24/14	2/24/14 17:02	2/25/14 0:05	7:03:00	A23022414 1702	10 Mins	429	796	2/25/14 0:29	91	138	2/25/14 3:55	3:26:00

Preliminary Information – Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Installed, Date/Time	Removed, Date/Time	(Time) Hours : Minutes	Filter ID	Count Time	Alpha (dpm)	Beta (dpm)	First Count, Date/Time	Alpa (dpm)	Beta (dpm)	Re-count, Date/Time	(Time) Hrs:Min: Sec
2/25/14	2/25/14 0:05	2/25/14 8:30	8:25:00	A23022514 0005	10 Mins	381	618	2/25/14 9:51	138	194	2/25/14 13:49	3:58:00
2/25/14	2/25/14 8:30	2/25/14 16:28	7:58:00	A12022514 0830	10 Mins	544	962	2/25/14 17:30	165	277	2/25/14 20:00	2:30:00
2/25/14	2/25/14 16:28	2/26/14 0:25	7:57:00	A23022514 1628	10 Mins	647	1,140	2/26/14 1:00	161	263	2/26/14 4:07	3:07:00
2/26/14	2/26/14 0:25	2/26/14 8:45	8:20:00	A23022614 0025	10 Mins	307	487	2/26/14 9:58	158	225	2/26/14 13:54	3:56:00
2/26/14	2/26/14 8:45	2/26/14 16:40	7:55:00	A23022614 0845	10 Mins	377	579	2/26/14 17:29				
2/26/14	2/26/14 16:40	2/27/14 0:15	7:35:00	A23022614 1640	10 Mins	458	826	2/27/14 0:52	114	172	2/27/14 4:08	3:16:00
2/27/14	2/27/14 0:15	2/27/14 9:03	8:48:00	A23022714 0015	10 Mins	685	1,198	2/27/14 9:32	191	340	2/27/14 12:25	2:53:00
2/27/14	2/27/14 9:03	2/27/14 16:51	7:48:00	A23022714 0903	10 Mins	457	793	2/27/14 17:26	78	103	2/28/14 4:24	10:58:00
2/28/14	2/27/14 16:51	2/28/14 0:15	7:24:00	A23022714 1651	10 Mins	239	423	2/28/14 0:46	52	90	2/28/14 4:01	3:15:00
2/28/14	2/28/14 0:15	2/28/14 8:35	8:20:00	A23022814 0015	10 Mins	81	136	2/28/14 10:32	49	81	2/28/14 14:17	3:45:00
2/28/14	2/28/14 8:35	2/28/14 16:15	7:40:00	A23022814 0835	10 Mins	84	127	2/28/14 18:20	43	91	2/28/14 21:19	2:59:00
3/1/14	2/28/14 16:15	3/1/14 1:04	8:49:00	A23022814 1615	10 Mins	133	208	2/28/14 2:35	60	89	3/1/14 5:27	26:52:00
3/1/14	3/1/14 1:04	3/1/14 8:55	7:51:00	A23030114 0104	10 Mins	224	440	3/1/14 9:56	73	116	3/1/14 12:57	3:01:00
3/1/14	3/1/14 8:55	3/1/14 16:56	8:01:00	A23030114 0855	10 Mins	186	354	3/1/14 5:36	69	94	3/1/14 21:09	15:33:00
3/1/14	3/1/14 16:56	3/2/14 0:07	7:11:00	A23030114 1656	10 Mins	121	213	3/2/14 1:07	47	55	3/2/14 5:12	4:05:00

Preliminary Information – Not for Public Release

Station A (A-2-3) Before the HEPA Filters

Date	Installed, Date/Time	Removed, Date/Time	(Time) Hours : Minutes	Filter ID	Count Time	Alpha (dpm)	Beta (dpm)	First Count, Date/Time	Alpa (dpm)	Beta (dpm)	Re-count, Date/Time	(Time) Hrs:Min: Sec
3/2/14	3/2/14 0:07	3/2/14 8:25	8:18:00	A23030214 0007	10 Mins	918	1,638	3/2/14 8:36	122	218	3/2/14 11:55	3:19:00
3/2/14	3/2/14 8:25	3/2/14 16:50	8:25:00	A23030214 0825	10 Mins	563	973	3/2/14 17:32	155	311	3/3/14 9:24	15:52:00
3/2/14	3/2/14 16:50	3/3/14 1:06	8:16:00	A23030214 1650	10 Mins	359	621	3/3/14 1:58	150	258	3/3/14 5:37	3:39:00
3/3/14	3/3/14 1:06	3/3/14 8:17	7:11:00	A23030314 0106	10 Mins	264	468	3/3/14 9:15	118	201	3/3/14 12:17	3:02:00
3/3/14	3/3/14 8:17	3/3/14 16:30	8:13:00	A23030314 0817	10 Mins	380	699	3/3/14 17:04	97	172	3/3/14 21:03	3:59:00
3/3/14	3/3/14 16:30	3/4/14 0:34	8:04:00	A23030314 1630	10 Mins	191	340	3/4/14 2:07	93	147	3/4/14 5:43	3:36:00
3/4/14	3/4/14 0:34	3/4/14 8:17	7:43:00	A23030414 0034	10 Mins	479	757	3/4/14 9:00	135	199	3/4/14 11:30	2:30:00
3/4/14	3/4/14 8:17	3/4/14 15:57	7:40:00	A23030414 0817	10 Mins	384	586	3/4/14 16:39	120	129	3/4/14 19:57	3:18:00
3/4/14	3/4/14 15:57	3/5/14 0:22	8:25:00	A23030414 1557	10 Mins	399	753	3/5/14 0:51	74	143	3/5/14 3:51	3:00:00

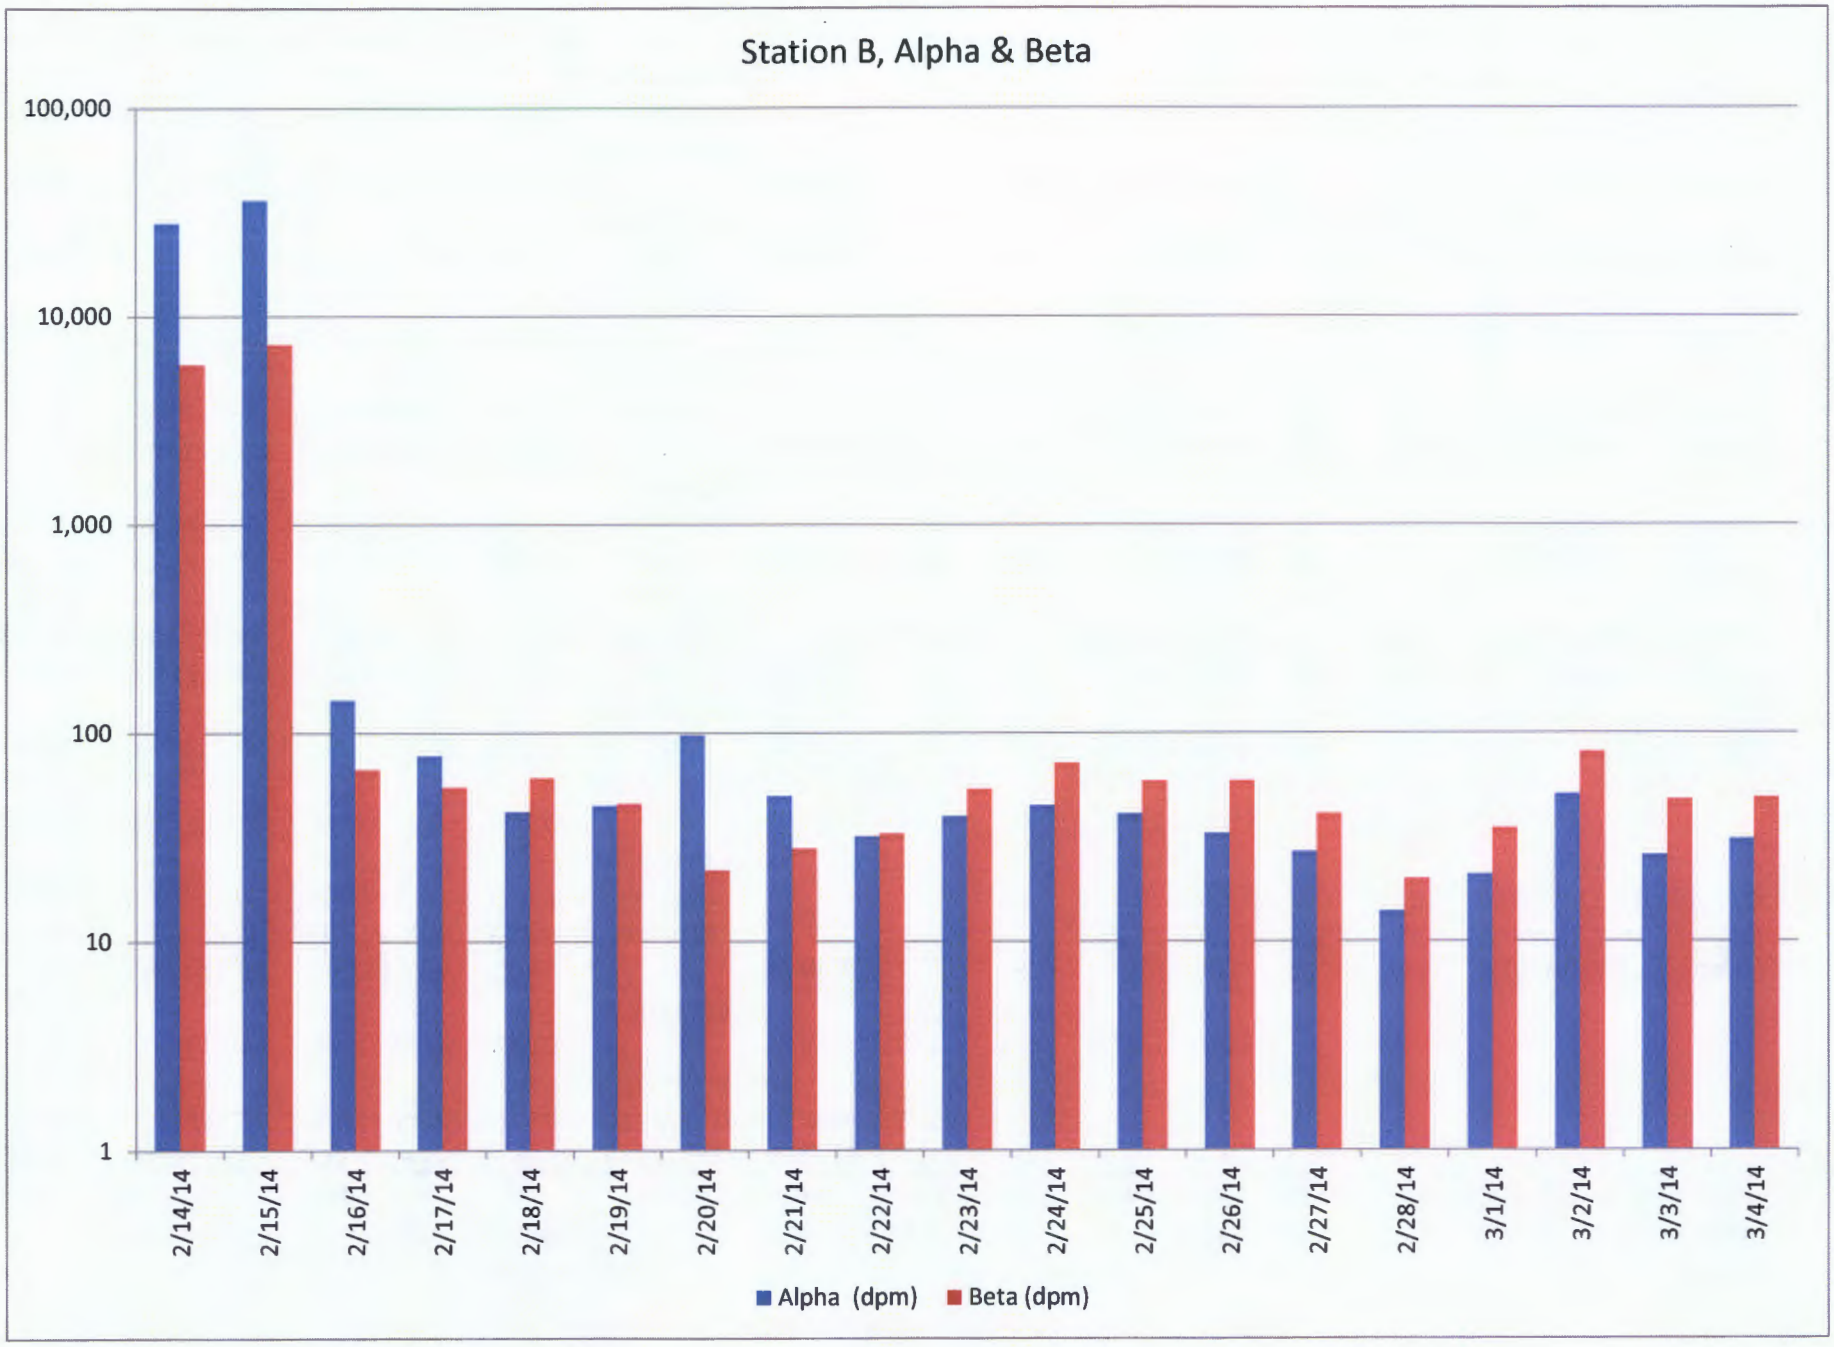
Station B, Alpha & Beta
100,000
10,000
1,000
100
10
1
2/14/14
2/15/14
2/16/14
2/17/14
2/18/14
2/19/14
2/20/14
2/21/14
2/22/14
2/23/14
2/24/14
2/25/14
2/26/14
2/27/14
2/28/14
3/1/14
3/2/14
3/3/14
3/4/14
Alpha (dpm)
Beta (dpm)

Preliminary Information - Not for Public Release
Station B (B-1-3) Downstream of the HEPA Filters

Date	Installed, Date/Time	Removed, Date/Time	(Time) Hrs:Min: Sec	Filter ID	Count Time	Alpha (dpm)	Beta (dpm)	First Count, Date/Time	Alpha (dpm)	Beta (dpm)	Re-count	(Time) Hrs:Min:Sec
2/14/14	2/14/14 7:54	2/15/14 8:35	24:41:00	B13021414	10 Mins	28,205	5,877	2/15/14 8:50				
2/15/14	2/15/14 8:35	2/15/14 14:45	6:10:00	B13021514	10 Mins	36,194	7,340					
2/15/14	2/15/14 14:45	2/15/14 23:05	8:20:00	B130215141 445	10 Mins	671	142	2/17/14 10:56				
2/15/14	2/15/14 23:05	2/16/14 9:04	9:59:00	B130215142 305	10 Mins	300	152	2/16/14 9:32	253	63	2/16/14 11:27	1:55:00
2/15/14	*2/15/14 23:05*	*2/16/14 9:04*	*9:59:00*	*Recount*				*2/16/14 9:32*	*245*	*59*	*2/16/14 12:50*	*3:18:00*
2/15/14	*2/15/14 23:05*	*2/16/14 9:04*	*9:59:00*	*Recount*				*2/16/14 9:32*	*240*	*49*	*2/16/14 17:41*	*8:09:00*
2/16/14	2/16/14 9:04	2/16/14 17:05	8:01:00	B130216140 904	10 Mins	144	67	2/16/14 17:55				
2/16/14	2/16/14 17:05	2/17/14 0:30	7:25:00	B130216141 705	10 Mins	72	54	2/17/14 0:46	62	18	2/17/14 12:03	11:17:00
2/17/14	2/17/14 0:30	2/17/14 8:05	7:35:00	B130216140 030	10 Mins	43	26	2/17/14 9:30	30	23	2/17/14 9:55	0:25:00
2/17/14	*2/17/14 0:30*	*2/17/14 8:05*	*7:35:00*	*Recount*				*2/17/14 9:30*	*32*	*16*	*2/17/14 14:00*	*4:30:00*
2/17/14	2/17/14 8:05	2/17/14 16:00	7:55:00	B130217140 805	10 Mins	78	35	2/17/14 16:50	58	20	2/17/14 19:58	3:08:00
2/17/14	2/17/14 8:05	2/17/14 16:00	7:55:00	*Recount*				*2/17/14 16:50*	*24*	*13*	*2/18/14 18:23*	*25:33:00*
2/17/14	2/17/14 16:00	2/18/14 0:30	8:30:00	B130217141 600	10 Mins	65	55	2/18/14 0:51	45	18	2/18/14 4:23	3:32:00
2/17/14	2/17/14 16:00	2/18/14 0:30	8:30:00	*Recount*				*2/18/14 0:51*	*36*	*12*	*2/18/14 7:51*	*7:00:00*
2/18/14	2/18/14 0:30	2/18/14 9:01	8:31:00	B130218140 030	10 Mins	42	61	2/18/14 9:28	23	12	2/18/14 12:02	2:34:00
2/18/14	2/18/14 9:01	2/18/14 16:55	7:54:00	B130218140 901	10 Mins	41	29	2/18/14 17:54	28	7	2/19/14 3:15	9:21:00
2/18/14	2/18/14 16:55	2/19/14 1:05	8:10:00	B130218141 655	10 Mins	42	36	2/19/14 1:44	20	7	2/19/14 5:47	4:03:00
2/19/14	2/19/14 1:05	2/19/14 9:00	7:55:00	B130219140 105	10 Mins	33	44	2/19/14 9:52	20	15	2/19/14 12:22	2:30:00
2/19/14	2/19/14 9:00	2/19/14 16:27	7:27:00	B130219140 900	10 Mins	36	34	2/19/14 17:08	25	10	2/19/14 20:36	3:28:00

2/19/14	2/19/14 16:27	2/20/14 0:35	8:08:00	B130219141627	10 Mins	45	46	2/20/14 1:07	25	9	2/20/14 3:59	2:52:00
2/20/14	2/20/14 0:35	2/20/14 8:52	8:17:00	B130220140035	10 Mins	52	21	2/20/14 10:35	38	14	2/20/14 12:26	1:51:00
2/20/14	2/20/14 8:52	2/20/14 16:54	8:02:00	B130220140852	10 Mins	98	22	2/20/14 18:38	101	23	2/20/14 22:11	3:33:00
2/20/14	2/20/14 16:54	2/21/14 0:38	7:44:00	B130220141654	10 Mins	40	19	2/21/14 2:04	33	11	2/21/14 5:21	3:17:00
2/21/14	2/21/14 0:38	2/21/14 8:20	7:42:00	B130221140038	10 Mins	30	6	2/21/14 10:27	27	12	2/21/14 15:32	5:05:00
2/21/14	2/21/14 8:20	2/21/14 16:00	7:40:00	B130221140820	10 Mins	37	15	2/21/14 16:54	41	12	2/21/14 20:28	3:34:00
2/21/14	2/21/14 16:00	2/22/14 0:19	8:19:00	B130221141600	10 Mins	50	28	2/22/14 1:25	42	14	2/22/14 3:58	2:33:00
2/22/14	2/22/14 0:19	2/22/14 8:10	7:51:00	B130222140019	10 Mins	30	22	2/22/14 9:46	19	12	2/22/14 11:51	2:05:00
2/22/14	2/22/14 8:10	2/22/14 16:15	8:05:00	B130222140810	10 Mins	28	17	2/22/14 17:13	22	10	2/22/14 20:04	2:51:00
2/22/14	2/22/14 16:15	2/22/14 23:56	7:41:00	B130222141615	10 Mins	32	33	2/23/14 0:47	22	9	2/23/14 4:04	3:17:00
2/22/14	2/22/14 23:56	2/23/14 8:10	8:14:00	B130222142356	10 Mins	21	29	2/23/14 9:38	19	17	2/23/14 12:27	2:49:00
2/23/14	2/23/14 8:10	2/23/14 16:05	7:55:00	B130223140810	10 Mins	7	22	2/23/14 16:42	17	7	2/23/14 20:10	3:28:00
2/23/14	2/23/14 16:05	2/24/14 0:15	8:10:00	B130223141605	10 Mins	40	54	2/24/14 0:54	19	13	2/24/14 4:01	3:07:00
2/24/14	2/24/14 0:15	2/24/14 8:46	8:31:00	B130224140015	10 Mins	14	19	2/24/14 11:36	14	14	2/24/14 15:40	4:04:00
2/24/14	2/24/14 8:46	2/24/14 16:35	7:49:00	B130224140846	10 Mins	22	28	2/24/14 17:33	8	8	2/24/14 20:31	2:58:00
2/24/14	2/24/14 16:35	2/25/14 0:16	7:41:00	B130224141635	10 Mins	45	72	2/25/14 0:29	8	12	2/25/14 4:04	3:35:00

2/25/14	2/25/14 0:16	2/25/14 9:02	8:46:00	B130225140016	10 Mins	41	53	2/25/14 10:12	14	21	2/25/14 14:03	3:51:00
2/25/14	2/25/14 9:02	2/25/14 16:52	7:50:00	B130225140902	10 Mins	39	59	2/25/14 17:42	12	7	2/25/14 20:00	2:18:00
2/25/14	2/25/14 16:52	2/26/14 0:10	7:18:00	B130225141652	10 Mins	27	41	2/26/14 1:01	12	10	2/26/14 4:50	3:49:00
2/26/14	2/26/14 0:10	2/26/14 9:21	9:11:00	B130226140010	10 Mins	26	21	2/26/14 10:51	23	16	2/26/14 14:23	3:32:00
2/26/14	2/26/14 9:21	2/26/14 16:16	6:55:00	B130226140921	10 Mins	22	25	2/26/14 17:27				
2/26/14	2/26/14 16:16	2/27/14 0:30	8:14:00	B130226141616	10 Mins	33	59	2/27/14 1:29	11	14	2/27/14 4:08	2:39:00
2/27/14	2/27/14 0:30	2/27/14 8:06	7:36:00	B130227140030	10 Mins	22	37	2/27/14 9:29	7	22	2/27/14 11:53	2:24:00
2/27/14	2/27/14 8:06	2/28/14 0:12	16:06:00	B130227140806	10 Mins	27	41	2/28/14 0:46	16	10	2/28/14 4:01	3:15:00
2/28/14	2/28/14 0:12	2/28/14 9:27	9:15:00	B130228140012	10 Mins	14	20	2/28/14 10:24	8	5	2/28/14 14:08	3:44:00
2/28/14	2/28/14 9:27	2/28/14 17:05	7:38:00	B130228140927	10 Mins	6	7	2/28/14 18:25	5	3	2/28/14 19:19	0:54:00
3/1/14	2/28/14 17:05	3/1/14 1:44	8:39:00	B130228141705	10 Mins	16	28	3/1/14 2:35	6	5	3/1/14 5:28	2:53:00
3/1/14	3/1/14 1:44	3/1/14 9:15	7:31:00	B130301140144	10 Mins	21	35	3/1/14 9:57	6	8	3/1/14 12:57	3:00:00
3/1/14	3/1/14 9:15	3/1/14 16:20	7:05:00	B130301140915	10 Mins	10	10	3/1/14 5:35	4	1	3/1/14 9:10	3:35:00
3/1/14	3/1/14 16:20	3/2/14 0:45	8:25:00	B130301141620	10 Mins	17	16	3/2/14 1:08	9	5	3/2/14 5:12	4:04:00
3/2/14	3/2/14 0:45	3/2/14 8:50	8:05:00	B130302140045	10 Mins	51	81	3/2/14 9:25	19	20	3/2/14 11:56	2:31:00
3/2/14	3/2/14 8:50	3/2/14 16:30	7:40:00	B130302140850	10 Mins	51	37	3/2/14 17:23	34	18	3/2/14 21:22	3:59:00

				B130302141								
3/2/14	3/2/14 16:30	3/3/14 1:06	8:36:00	630	10 Mins	17	28	3/3/14 1:52	7	13	3/3/14 5:59	4:07:00
				B130303140								
3/3/14	3/3/14 1:06	3/3/14 8:20	7:14:00	106	10 Mins	26	39	3/3/14 8:55	9	14	3/3/14 12:17	3:22:00
				B130303140								
3/3/14	3/3/14 8:20	3/3/14 16:20	8:00:00	820	10 Mins	19	48	3/3/14 18:12	2	6	3/3/14 18:12	0:00:00
				B130303141								
3/3/14	3/3/14 16:20	3/4/14 1:14	8:54:00	620	10 Mins	22	33	3/4/14 2:08	5	8	3/4/14 5:43	3:35:00
				B130304140								
3/4/14	3/4/14 1:14	3/4/14 8:15	7:01:00	114	10 Mins	31	49	3/4/14 8:46	8	11	3/4/14 11:30	2:44:00
				B130304140								
3/4/14	3/4/14 8:15	3/4/14 16:10	7:55:00	815	10 Mins	18	26	3/4/14 16:39	4	4	3/4/14 19:57	3:18:00
				B130304141								
3/4/14	3/4/14 16:10	3/5/14 0:05	7:55:00	610	10 Mins	21	34	3/5/14 0:51	5	5	3/5/14 3:51	3:00:00

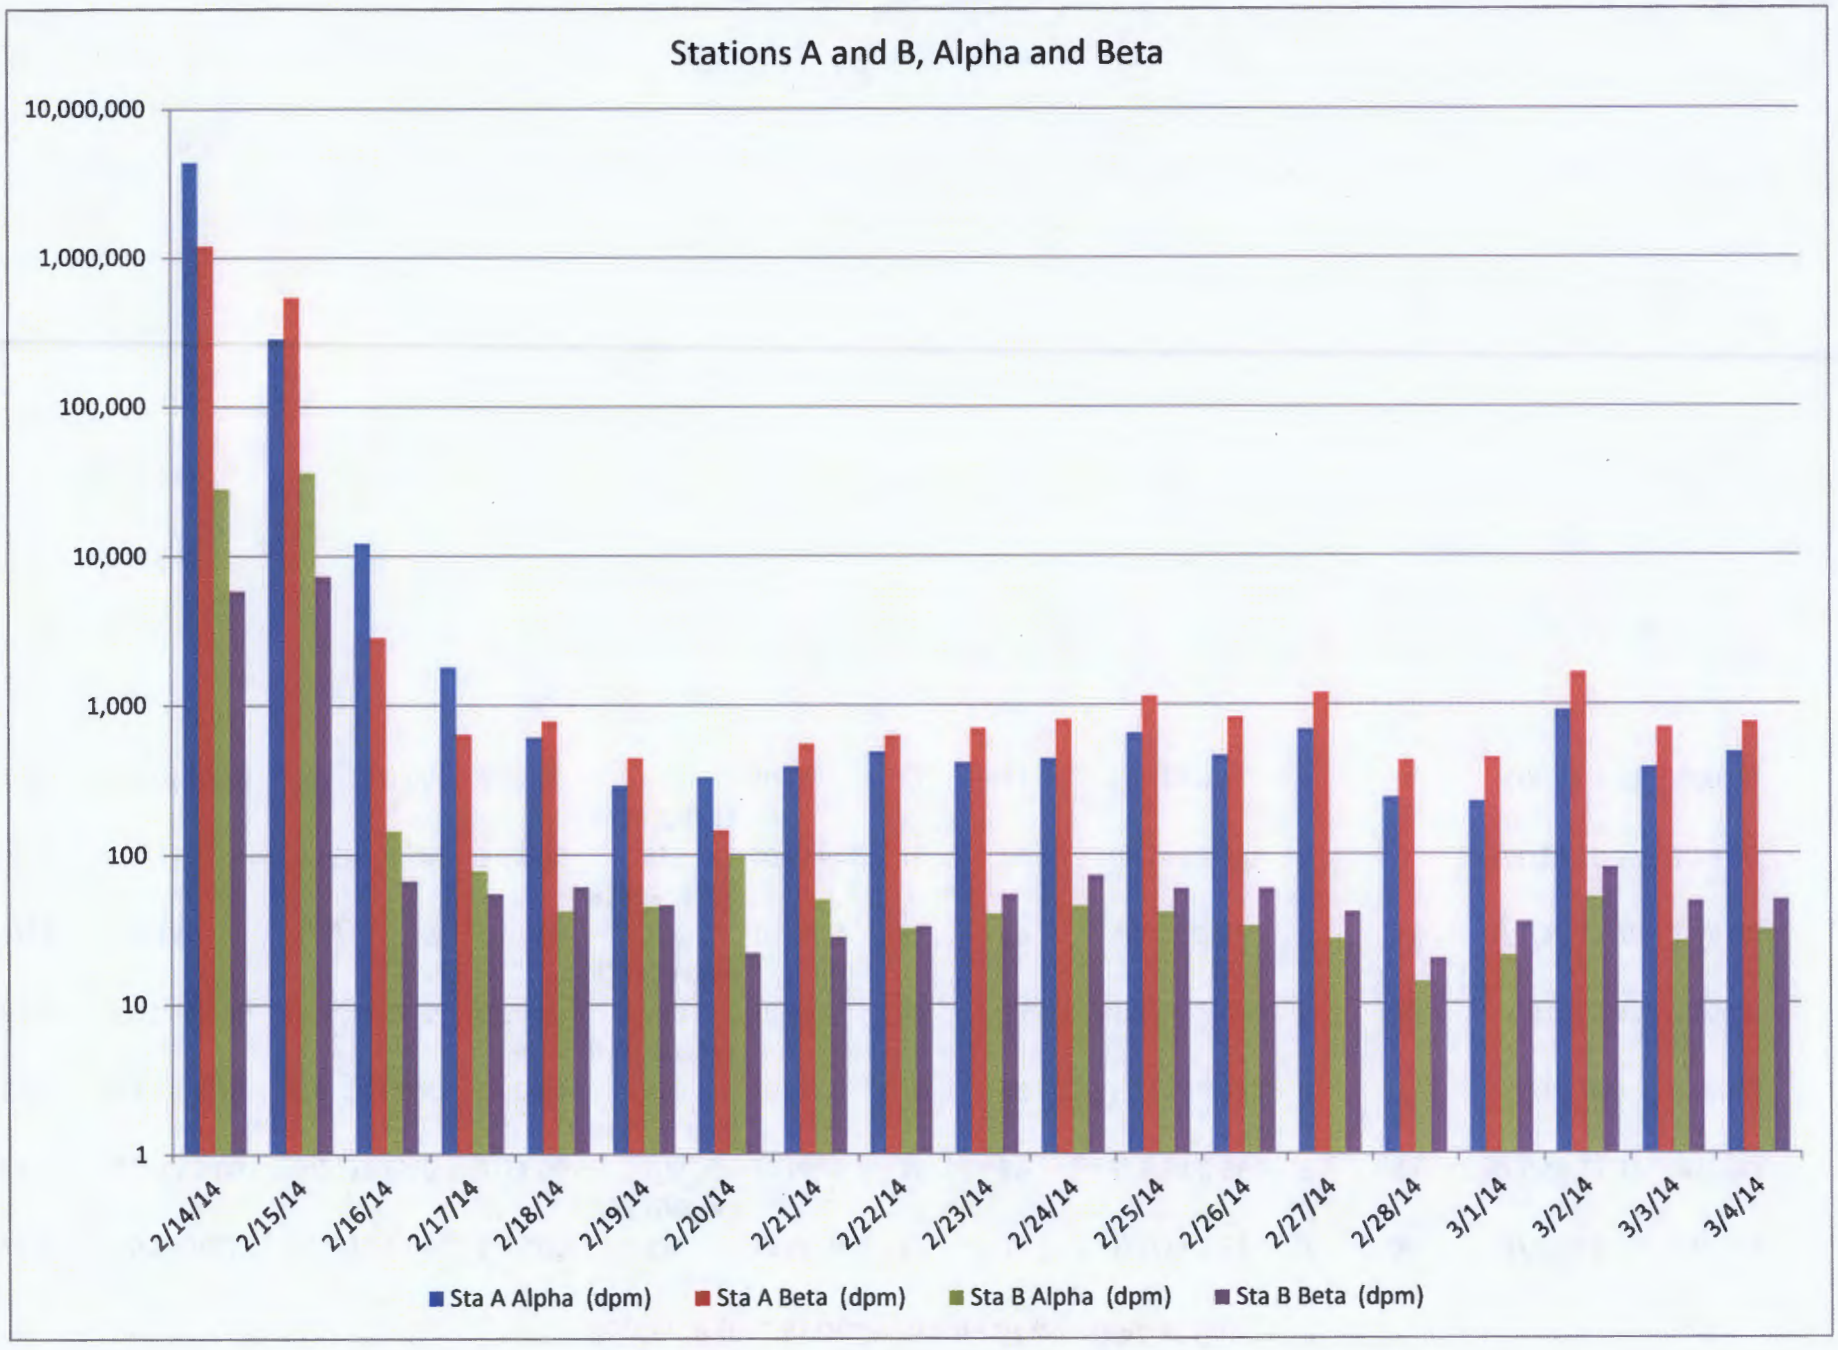
Stations A and B, Alpha and Beta
10,000,000
1,000,000
100,000
10,000
1,000
100
10
1
2/14/14
2/15/14
2/16/14
2/17/14
2/18/14
2/19/14
2/20/14
2/21/14
2/22/14
2/23/14
2/24/14
2/25/14
2/26/14
2/27/14
2/28/14
3/1/14
3/2/14
3/3/14
3/4/14
Sta A Alpha (dpm)
Sta A Beta (dpm)
Sta B Alpha (dpm)
Sta B Beta (dpm)

Date	Sta A Alpha (dpm)	Sta A Beta (dpm)	Sta B Alpha (dpm)	Sta B Beta (dpm)	% Difference Alpha	% Difference Beta	Design Efficiency Alpha	Design Efficiency Beta	If <0 Then 0 Alpha	If <0 Then 0 Beta
2/14/14	4,400,000	1,200,000	28,205	5,877	99.36%	99.51%	1,320.00	360.00	1320	360
2/15/14	225,000	468,000	36,194	7,340	83.91%	98.43%	67.50	140.40	67.5	140.4
2/15/14	285,000	540,000	671	142	99.76%	99.97%	85.50	162.00	85.5	162
2/15/14	124,050	24,481	300	152	99.76%	99.38%	37.21	7.34	37.215	7.3443
2/15/14	47,283	10,558					14.18	3.17	14.1849	3.1674
2/16/14	12,215	2,842	144	67	98.82%	97.64%	3.66	0.85	3.6645	0.8526
2/16/14	4,051	1,256	72	54	98.22%	95.70%	1.22	0.38	1.2153	0.3768
2/17/14	1,802	638	43	26	97.61%	95.92%	0.54	0.19	0.5406	0.1914
2/17/14	1,048	621					0.31	0.19	0.3144	0.1863
2/17/14	802	633	78	35	90.27%	94.47%	0.24	0.19	0.2406	0.1899
2/17/14			65	55			0.00	0.00	0	0
2/18/14	326	338	42	61	87.12%	81.95%	0.10	0.10	0.0978	0.1014
2/18/14	609	780	41	29	93.27%	96.28%	0.18	0.23	0.1827	0.234
2/18/14	346	340	42	36	87.86%	89.41%	0.10	0.10	0.1038	0.102
2/19/14	224	320	33	44	85.27%	86.25%	0.07	0.10	0.0672	0.096
2/19/14	264	443	36	34	86.36%	92.33%	0.08	0.13	0.0792	0.1329
2/19/14	286	378	45	46	84.27%	87.83%	0.09	0.11	0.0858	0.1134
2/19/14	290	219					0.09	0.07	0.087	0.0657
2/20/14	135	131	52	21	61.48%	83.97%	0.04	0.04	0.0405	0.0393
2/20/14	231	103	98	22	57.58%	78.64%	0.07	0.03	0.0693	0.0309
2/20/14	330	146	40	19	87.88%	86.99%	0.10	0.04	0.099	0.0438
2/21/14	253	199	30	6	88.14%	96.98%	0.08	0.06	0.0759	0.0597
2/21/14	388	549	37	15	90.46%	97.27%	0.12	0.16	0.1164	0.1647
2/21/14			50	28			0.00	0.00	0	0
2/22/14	421	599	30	22	92.87%	96.33%	0.13	0.18	0.1263	0.1797
2/22/14	487	626	28	17	94.25%	97.28%	0.15	0.19	0.1461	0.1878
2/22/14			32	33			0.00	0.00	0	0
2/22/14			21	29			0.00	0.00	0	0
2/23/14	328	504	7	22	97.87%	95.63%	0.10	0.15	0.0984	0.1512
2/23/14	225	340	40	54	82.22%	84.12%	0.07	0.10	0.0675	0.102
2/23/14	412	696					0.12	0.21	0.1236	0.2088
2/24/14	195	309	14	19	92.82%	93.85%	0.06	0.09	0.0585	0.0927
2/24/14	437	740	22	28	94.97%	96.22%	0.13	0.22	0.1311	0.222
2/24/14	429	796	45	72	89.51%	90.95%	0.13	0.24	0.1287	0.2388
2/25/14	381	618	41	53	89.24%	91.42%	0.11	0.19	0.1143	0.1854
2/25/14	544	962	39	59	92.83%	93.87%	0.16	0.29	0.1632	0.2886
2/25/14	647	1,140	27	41	95.83%	96.40%	0.19	0.34	0.1941	0.342
2/26/14	307	487	26	21	91.53%	95.69%	0.09	0.15	0.0921	0.1461
2/26/14	377	579	22	25	94.16%	95.68%	0.11	0.17	0.1131	0.1737
2/26/14	458	826	33	59	92.79%	92.86%	0.14	0.25	0.1374	0.2478
2/27/14	685	1,198	22	37	96.79%	96.91%	0.21	0.36	0.2055	0.3594
2/27/14	457	793	27	41	94.09%	94.83%	0.14	0.24	0.1371	0.2379
2/28/14	239	423	14	20	94.14%	95.27%	0.07	0.13	0.0717	0.1269
2/28/14	81	136	6	7	92.59%	94.85%	0.02	0.04	0.0243	0.0408
2/28/14	84	127					0.03	0.04	0.0252	0.0381
3/1/14	133	208	16	28	87.97%	86.54%	0.04	0.06	0.0399	0.0624
3/1/14	224	440	21	35	90.63%	92.05%	0.07	0.13	0.0672	0.132
3/1/14	186	354	10	10	94.62%	97.18%	0.06	0.11	0.0558	0.1062
3/1/14	121	213	17	16	85.95%	92.49%	0.04	0.06	0.0363	0.0639
3/2/14	918	1,638	51	81	94.44%	95.05%	0.28	0.49	0.2754	0.4914
3/2/14	563	973	51	37	90.94%	96.20%	0.17	0.29	0.1689	0.2919
3/2/14	359	621	17	28	95.26%	95.49%	0.11	0.19	0.1077	0.1863
3/3/14	264	468	26	39	90.15%	91.67%	0.08	0.14	0.0792	0.1404
3/3/14	380	699	19	48	95.00%	93.13%	0.11	0.21	0.114	0.2097
3/3/14	191	340	22	33	88.48%	90.29%	0.06	0.10	0.0573	0.102
3/4/14	479	757	31	49	93.53%	93.53%	0.14	0.23	0.1437	0.2271
3/4/14	384	586	18	26	95.31%	95.56%	0.12	0.18	0.1152	0.1758
3/4/14	399	753	21	34	94.74%	95.48%	0.12	0.23	0.1197	0.2259
				Average	90.88%	93.38%				
				Min	57.58%	78.64%				
				Max	99.76%	99.97%				

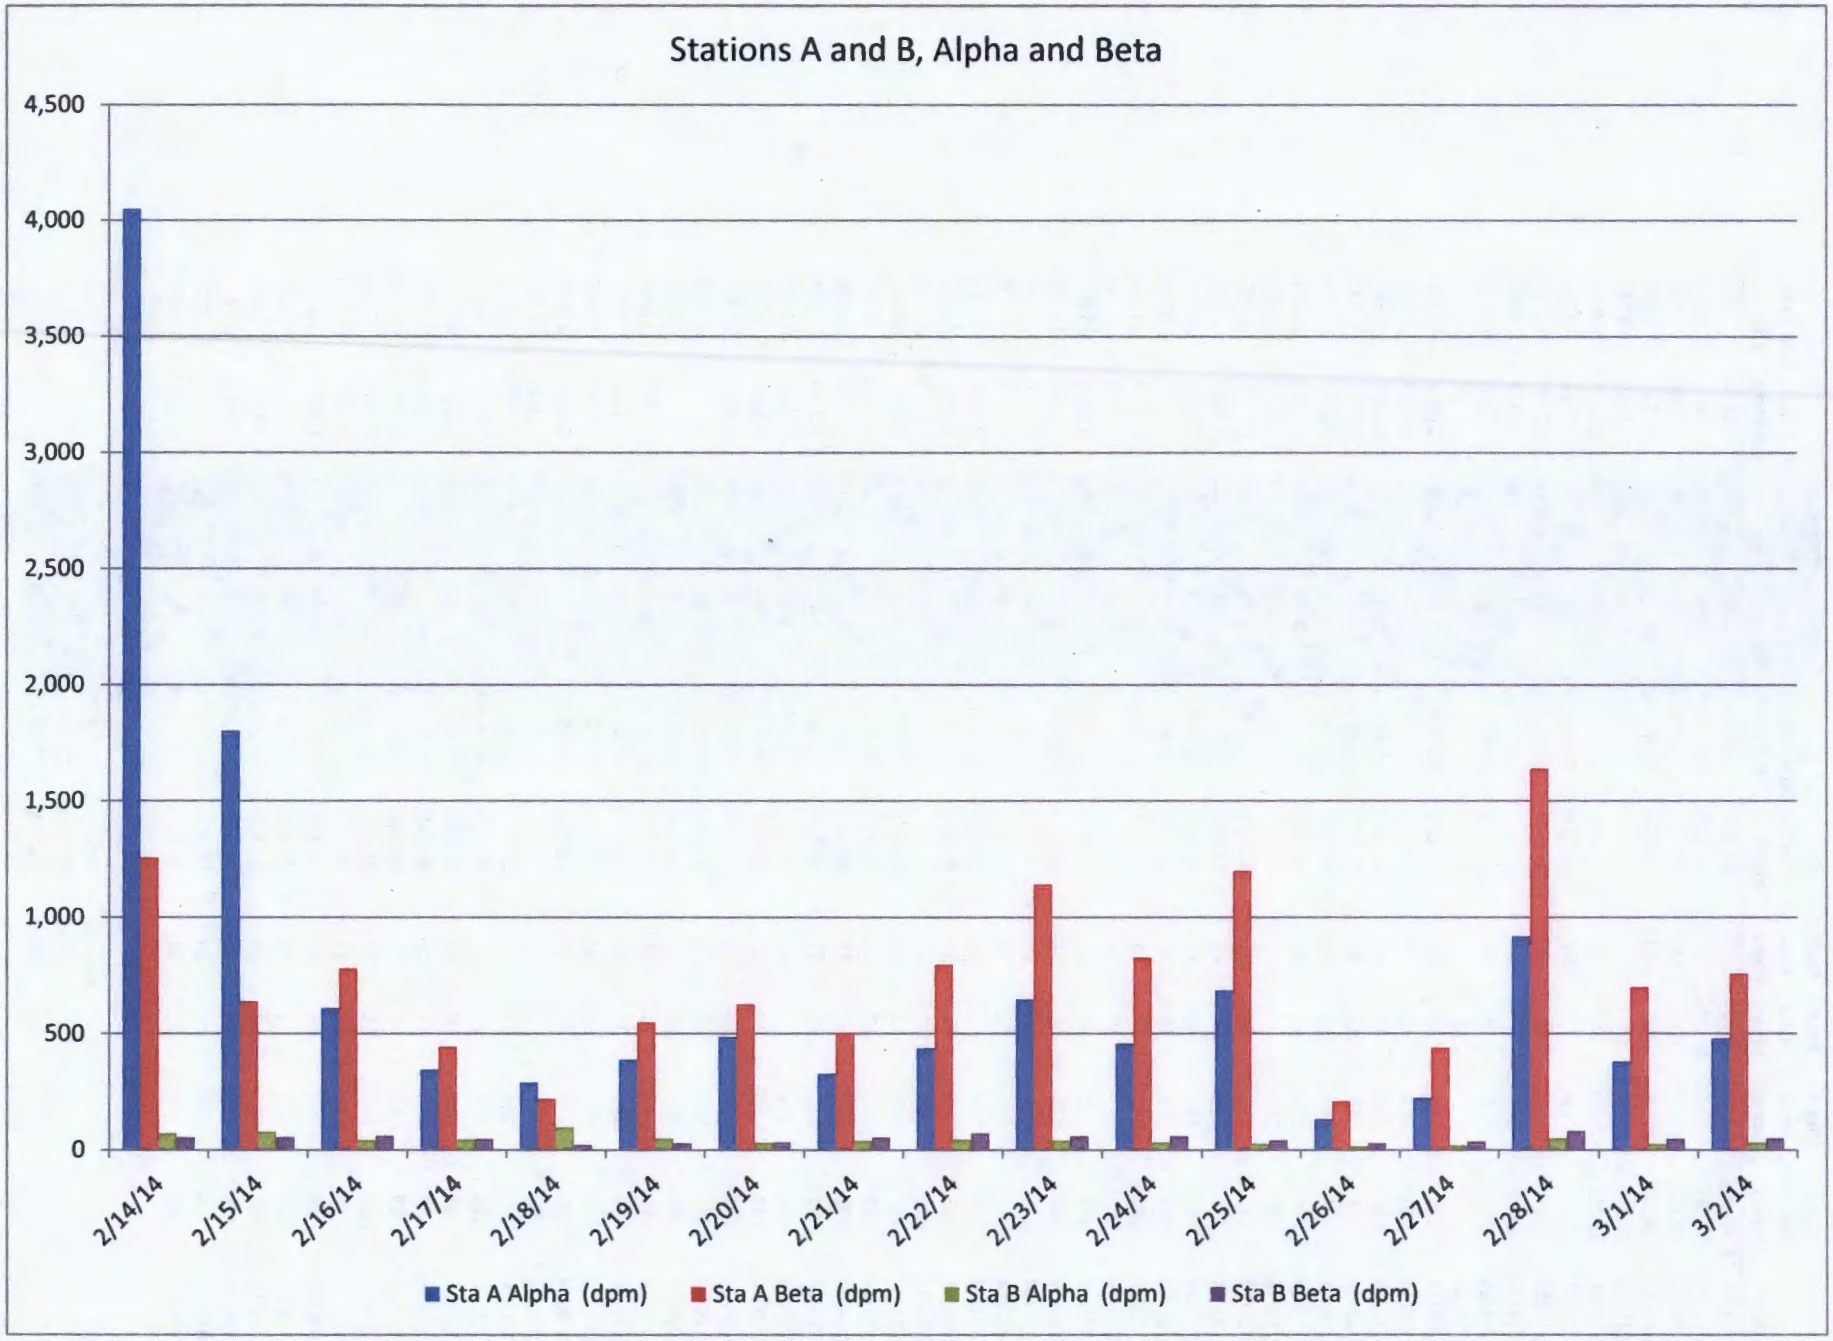
Stations A and B, Alpha and Beta
4,500
4,000
3,500
3,000
2,500
2,000
1,500
1,000
500
0
2/14/14
2/15/14
2/16/14
2/17/14
2/18/14
2/19/14
2/20/14
2/21/14
2/22/14
2/23/14
2/24/14
2/25/14
2/26/14
2/27/14
2/28/14
3/1/14
3/2/14
Sta A Alpha (dpm)
Sta A Beta (dpm)
Sta B Alpha (dpm)
Sta B Beta (dpm)
