



DEPARTMENT OF THE AIR FORCE
HEADQUARTERS 377TH AIR BASE WING (AFMC)

ENTERED

SEP 16 2011

Mr. Thomas Berardinelli
377 ABW/DS
2000 Wyoming Blvd SE
Kirtland AFB NM 87117-5606

Mr. John Kieling, Manager
RCRA Permits Management Program
Hazardous Waste Bureau (HWB)
New Mexico Environment Department (NMED)
2905 Rodeo Park Road
Santa Fe New Mexico 87505

Dear Mr. Kieling

Please find the Kirtland Air Force Base Indoor Air Work Plan Schedule, September 2011 (attachment 1), an NMED requirement referenced in the NMED letter dated 18 August 2011, Re: Submittal of Indoor Air Risk Evaluation Work Plan for Petroleum Hydrocarbon Fuel Compounds in Sub-Slab Soil Vapor – Bulk Fuels Facility, KAFB, EPA ID#NM9570024423 HWB-KAFB-MISC.

Please contact Mr. L. Wayne Bitner, (505) 853-3484 or ludie.bitner@kirtland.af.mil, if you have any questions.

Sincerely


THOMAS F. BERARDINELLI
Director of Staff

2 Attachments:

1. KAFB Indoor Air Work Plan, September 2011
2. KAFB Indoor Air Work Plan, September 2011 Document Certification

cc:


NMED-RPD (J. Davis)
NMED-HWB (W. Moats; W. McDonald; B. Salem; S. Brandwein)
NMED-GWQB (J. Schoeppner)
NMED-OGC (L. Barnhart)
EPA Region 6 (L. King)
HQ AFMC/A7AQ (Mr. McCann)
HQ AFMC/A7A1 (Mr. Fort)
AFCEE/CMSE (Mr. Oyelowo)
AFCEE/EXEC (Mr. Urrutia)
Public Info Repository (Central New Mexico)
Community College Montoya Campus
File

KAFB3799



Kirtland Air Force Base
Bulk Fuels Facility

ID	Task Name	Duration	Start	Finish	August 21		October 1		December		January 2		March 11		May 1		June 21		August 11		
					8/7	8/28	9/18	10/9	0/3	1/2	2/1	1/1	1/22	2/12	3/4	3/25	4/15	5/6	5/27	6/17	7/8
1	Receive requirements from NMED	0 days	Mon 10/3/11	Mon 10/3/11																	
2	Prepare work plan	60 days	Mon 10/3/11	Fri 12/23/11																	
3	Submit work plan to USACE/KAFB	0 days	Fri 12/23/11	Fri 12/23/11																	
4	USACE/KAFB review of work plan	30 days	Mon 12/26/11	Fri 2/3/12																	
5	Revise work plan	15 days	Mon 2/6/12	Fri 2/24/12																	
6	Submit work plan to NMED	0 days	Fri 2/24/12	Fri 2/24/12																	
7	NMED review of work plan	45 days	Mon 2/27/12	Fri 4/27/12																	
8	Receive NMED comments on work plan	0 days	Fri 4/27/12	Fri 4/27/12																	
9	Revise work plan/RTCs	15 days	Mon 4/30/12	Fri 5/18/12																	
10	Submit revised work plan to USACE/KAFB	0 days	Fri 5/18/12	Fri 5/18/12																	
11	USACE/KAFB review of work plan	15 days	Mon 5/21/12	Fri 6/8/12																	
12	Revise work plan	5 days	Mon 6/11/12	Fri 6/15/12																	
13	Submit Final work plan to NMED	0 days	Fri 6/15/12	Fri 6/15/12																	
14	NMED review or work plan	45 days	Mon 6/18/12	Fri 8/17/12																	
15	NMED approval of work plan	0 days	Fri 8/17/12	Fri 8/17/12																	

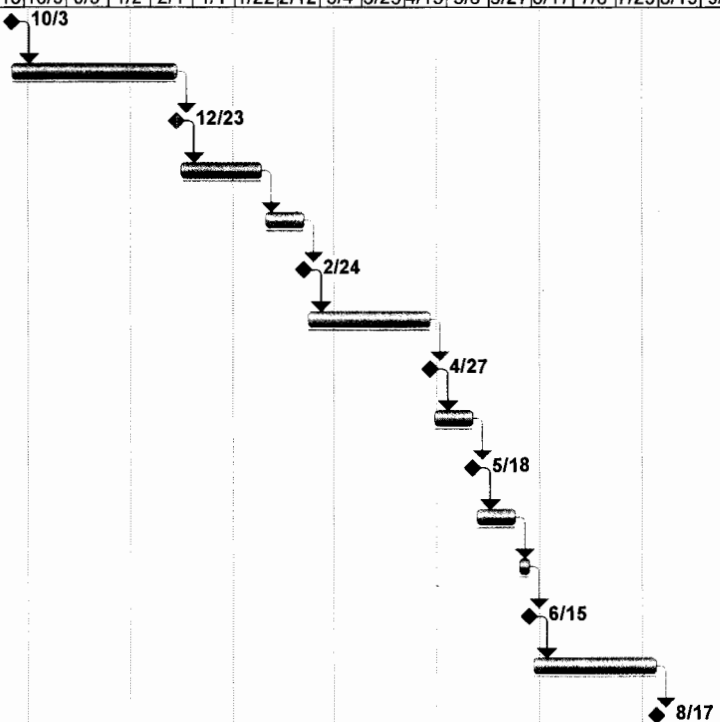


Project: KAFB Indoor Air Work Plan
Date: Mon 9/12/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


**40 CFR 270.11
DOCUMENT CERTIFICATION
SEPTEMBER 2011**

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision according to a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.



DAVID J. HORNYAK, Colonel, USAF
Commander

This document has been approved for public release in accordance with Department of Defense Directives and Air Force Instructions.



KIRTLAND AIR FORCE BASE
377th ABW Public Affairs
