



DEPARTMENT OF THE AIR FORCE
HEADQUARTERS 27TH SUPPORT GROUP (ACC)
CANNON AIR FORCE BASE NEW MEXICO



4 MAY 1999

Colonel James A. Thomas III
Commander, 27th Support Group
100 S DL Ingram Blvd Suite 100
Cannon AFB NM 88103-5214

Mr. James Bearzi, Chief
Hazardous and Radioactive Materials Bureau
New Mexico Environment Department
2044 Galisteo
P O Box 26110
Santa Fe NM 87502

*Polker -
Plz handle
-1722*

Dear Mr. Bearzi

Enclosed for your review and approval is the schedule requested by the New Mexico Environment Department for revising Cannon AFB Phase I RCRA Facility Investigation for Melrose Air Force Range.

Questions regarding this schedule or the Cannon AFB Restoration Program may be addressed to Mr. Sanford D. Hutsell of my Civil Engineer Environmental Flight at (505) 784-1092. I look forward to the continued cooperation between our organizations in addressing the environmental restoration concerns of Cannon AFB.

Sincerely

JAMES A. THOMAS III, Colonel, USAF

Attachments:
Proposed Timeline for Action

cc:
EPA (B. Sturdivant)
NMED HRWB (C. Will)
NMED Water Quality Bureau (J. Jacobs)
HQ ACC CES/ESVW w/o atch (M. Patterson)

**Cannon Air Force Base
Melrose Air Force Range RFI Report Finalization**

ID	Task Name	Duration	Start	Finish	September 1999				October 1999				November 19						
					9/5	9/12	9/19	9/26	10/3	10/10	10/17	10/24	10/31	11/7	11/14				
1	Finalization of Melrose Air Force Range RFI Report	200d	9/6/99	6/9/00	[Task bar from 9/6/99 to 6/9/00]														
2	Acknowledgment of Comments and Concurrence from NMED on scope	1d	9/6/99	9/6/99	[Task bar from 9/6/99 to 9/6/99]														
3	Planning	48d	9/6/99	11/10/99	[Task bar from 9/6/99 to 11/10/99]														
4	Unarchiving information and software conversion of electronic	30d	9/6/99	10/15/99	[Task bar from 9/6/99 to 10/15/99]														
5	Preparation of Letter Work Plan for field work	14d	9/14/99	10/1/99	[Task bar from 9/14/99 to 10/1/99]														
6	Review of Letter Work Plan by USACE and Cannon AFB	28d	10/4/99	11/10/99	[Task bar from 10/4/99 to 11/10/99]														
7	Procurement of field equipment and laboratory services	14d	10/22/99	11/10/99	[Task bar from 10/22/99 to 11/10/99]														
8	Field Operations	20d	11/15/99	12/10/99	[Task bar from 11/15/99 to 12/10/99]														
9	Chemistry Support (data mgmt, data validation)	40d	12/13/99	2/4/00	[Task bar from 12/13/99 to 2/4/00]														
10	Report Finalization	139d	11/29/99	6/8/00	[Task bar from 11/29/99 to 6/8/00]														
11	Report preparation	95d	11/29/99	4/7/00	[Task bar from 11/29/99 to 4/7/00]														
12	Review of final report by USACE and Cannon AFB	28d	4/10/00	5/17/00	[Task bar from 4/10/00 to 5/17/00]														
13	Report revisons based on USACE and Cannon AFB comments	16d	5/18/00	6/8/00	[Task bar from 5/18/00 to 6/8/00]														
14	Submittal of Final Report to USACE and Cannon AFB for NMED	1d	6/9/00	6/9/00	[Task bar from 6/9/00 to 6/9/00]														

Project: Melrose RFI Final Report
Date: 5/11/99

Task [bar] Summary [bar] Rolled Up Progress [bar]
 Progress [bar] Rolled Up Task [bar]
 Milestone [diamond] Rolled Up Milestone [diamond]

15:02
 FOSTER WHEELER ENV
 TEL 59803539
 P. 002

**Cannon Air Force Base
Melrose Air Force Range RFI Report Finalization**

ID	Task Name	Duration	December 1999					January 2000				February 2000						
			11/21	11/28	12/5	12/12	12/19	12/26	1/2	1/9	1/16	1/23	1/30	2/6	2/13	2/20	2/27	
1	Finalization of Melrose Air Force Range RFI Report	200d	[Redacted]															
2	Acknowledgment of Comments and Concurrence from NMED on scope	1d	[Redacted]															
3	Planning	48d	[Redacted]															
4	Unarchiving information and software conversion of electronic	30d	[Redacted]															
5	Preparation of Letter Work Plan for field work	14d	[Redacted]															
6	Review of Letter Work Plan by USACE and Cannon AFB	28d	[Redacted]															
7	Procurement of field equipment and laboratory services	14d	[Redacted]															
8	Field Operations	20d	[Redacted]															
9	Chemistry Support (data mgmt, data validation)	40d	[Redacted]															
10	Report Finalization	139d	[Redacted]															
11	Report preparation	95d	[Redacted]															
12	Review of final report by USACE and Cannon AFB	28d	[Redacted]															
13	Report revisions based on USACE and Cannon AFB comments	16d	[Redacted]															
14	Submittal of Final Report to USACE and Cannon AFB for NMED	1d	[Redacted]															

12/10

12/13

2/4


11/29

Project: Melrose RFI Final Report
Date: 5/11/99

Task [Redacted] Summary [Redacted] Rolled Up Progress [Redacted]
 Progress [Redacted] Rolled Up Task [Redacted]
 Milestone ◆ Rolled Up Milestone ◇

TEL 59805539
 FOSTER WHEELER ENV
 5/11/99 15:02
 P. 005

**Cannon Air Force Base
Melrose Air Force Range RFI Report Finalization**

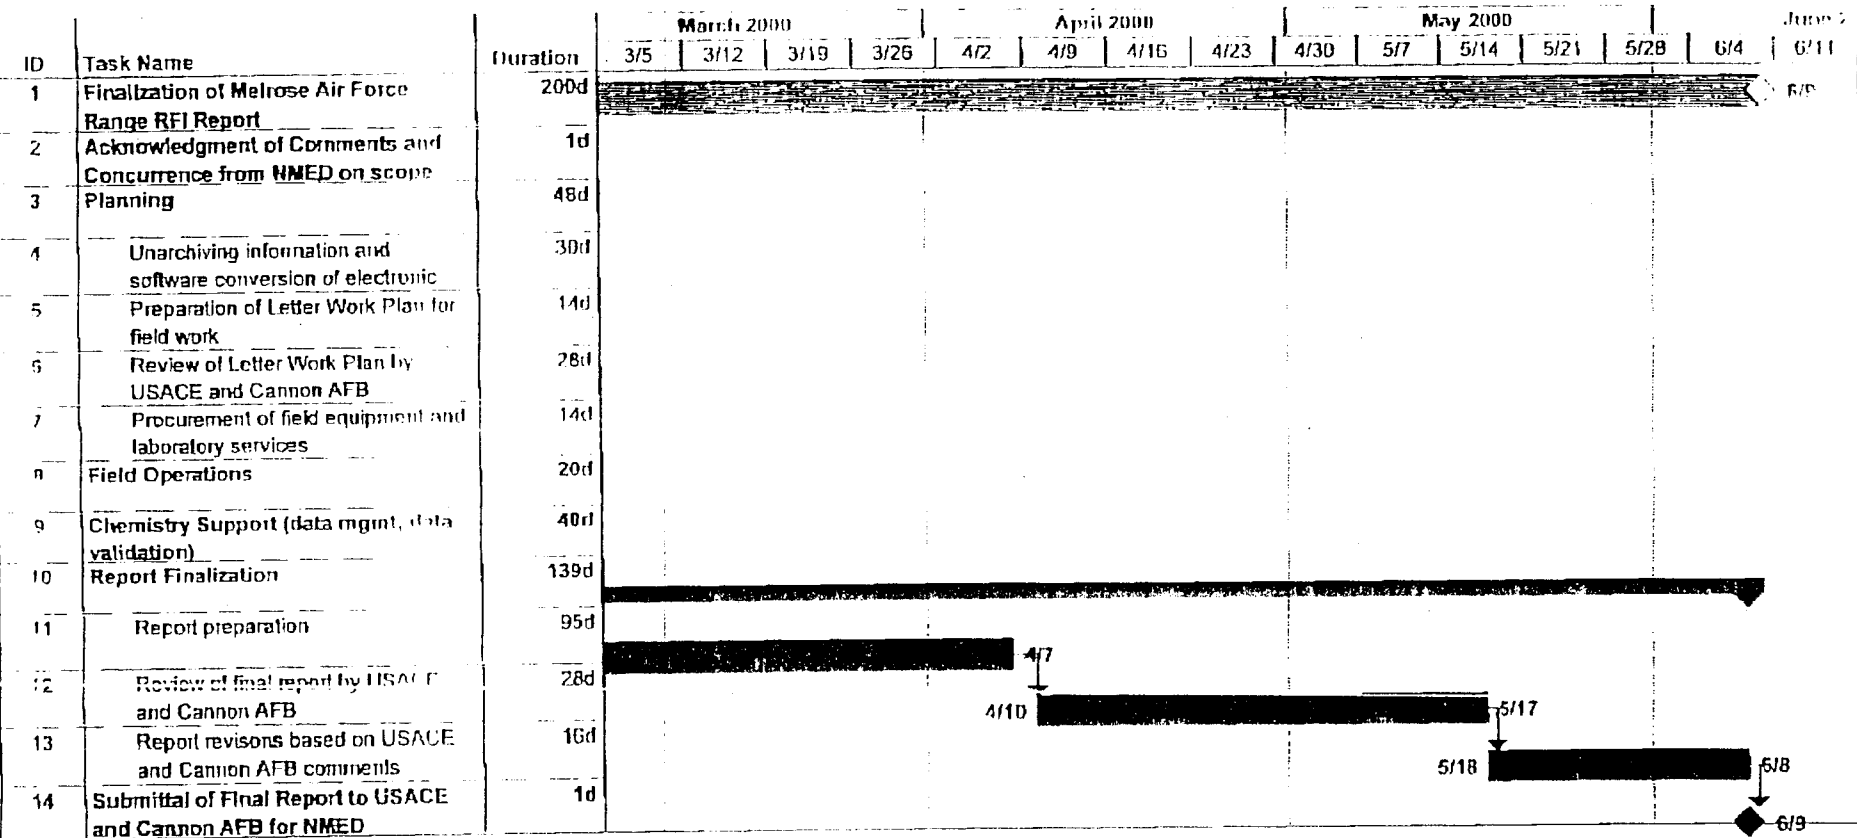

Project: Melrose RFI Final Report
Date: 5/11/99

Task		Summary		Rolled Up Progress	
Progress		Rolled Up Task			
Milestone		Rolled Up Milestone			

EAST WHEELER ENV TEL 59805559
